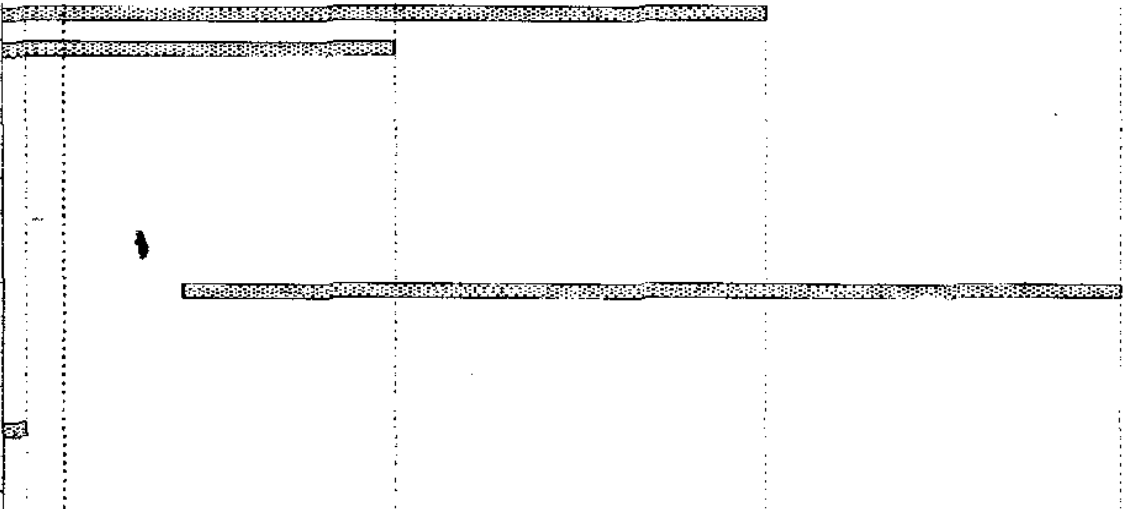


# Appendix J

## Tentative Construction Programme

ID	Activities	July 2003							August 2003							September 2003							O										
		29	02	05	08	11	14	17	20	23	26	29	01	04	07	10	13	16	19	22	25	28		31	03	06	09	12	15	18	21	24	27
1	<b>Reclamation Works</b>																																
2	Vertical Seawall																																
3	Type 2 Rock (completed)																																
4	Sloping Seawall																																
5	Type 3 Rock																																
6	Deep Compaction (completed)																																
7	Surcharge Placing (completed)																																
8	Surcharge Removal																																
9	Seawall Coving																																
10																																	
11	<b>Bridge Construction</b>																																
12	Bored Pile Construction (completed)																																
13	Retaining Wall & Pile Cap 1 & 3 (completed)																																
14	Pile Cap 2 (completed)																																
15	Pile Cap 4																																
16	Bridge Deck Construction																																
17	Pile Head Trimming (completed)																																
18																																	
19	<b>CW Intake &amp; Outfall (Remaining Portion)</b>																																
20	No.4 CW Intake																																
21	No.3 CW Outfall																																
22	No.4 CW Outfall (completed)																																
<b>Lamma Power Station Extension - Site Formation 3-Month Programme</b>		Scheduled Activity 																															

ID	Task Name	Start	Finish	July					August				September				Oct
				29/6	6/7	13/7	20/7	27/7	3/8	10/8	17/8	24/8	31/8	7/9	14/9	21/9	28/9
1	<b>Civil Works</b>																
2	<u>Within Lamma Power Station</u>																
3	Construction of Cable Ducts	Mon 5/1/04	Sat 14/5/05														
4	Construction of Cable Trenches	Wed 2/2/05	Sat 14/5/05														
5																	
6	<u>Yung Shue Wan South</u>																
7	Construction of Cable Landing Points	Sat 3/1/04	Sat 30/10/04														
8	Construction of Cable Ducts	Fri 2/1/04	Sat 14/5/05														
9																	
10	<u>Pak Kok San Tsuen</u>																
11	Construction of Cable Landing Points	Fri 2/1/04	Fri 29/10/04														
12	Construction of Cable Trenches	Tue 1/3/05	Tue 12/7/05														
13	Construction of Cable Duct	Fri 2/1/04	Mon 11/7/05														
14																	
15	<u>Pak Kok Tsui</u>																
16	Construction of Cable Landing Points	Fri 2/1/04	Tue 14/12/04														
17	Construction of Cable Ducts	Fri 2/1/04	Mon 11/7/05														

Additional Transmission System for Lamma Power Station  
 275kV Cable Route from Lamma Island to Cyberport  
 3-Month Programme

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress



Project Summary



Deadline

