


Revised Works Programme for 2no. DN1800 CW Outlet Pipes Installation - Culvert Outfall No. 4 + GRS Works

No.4 Outfall A&A+GRS (Rev.17) (26-10-2021)

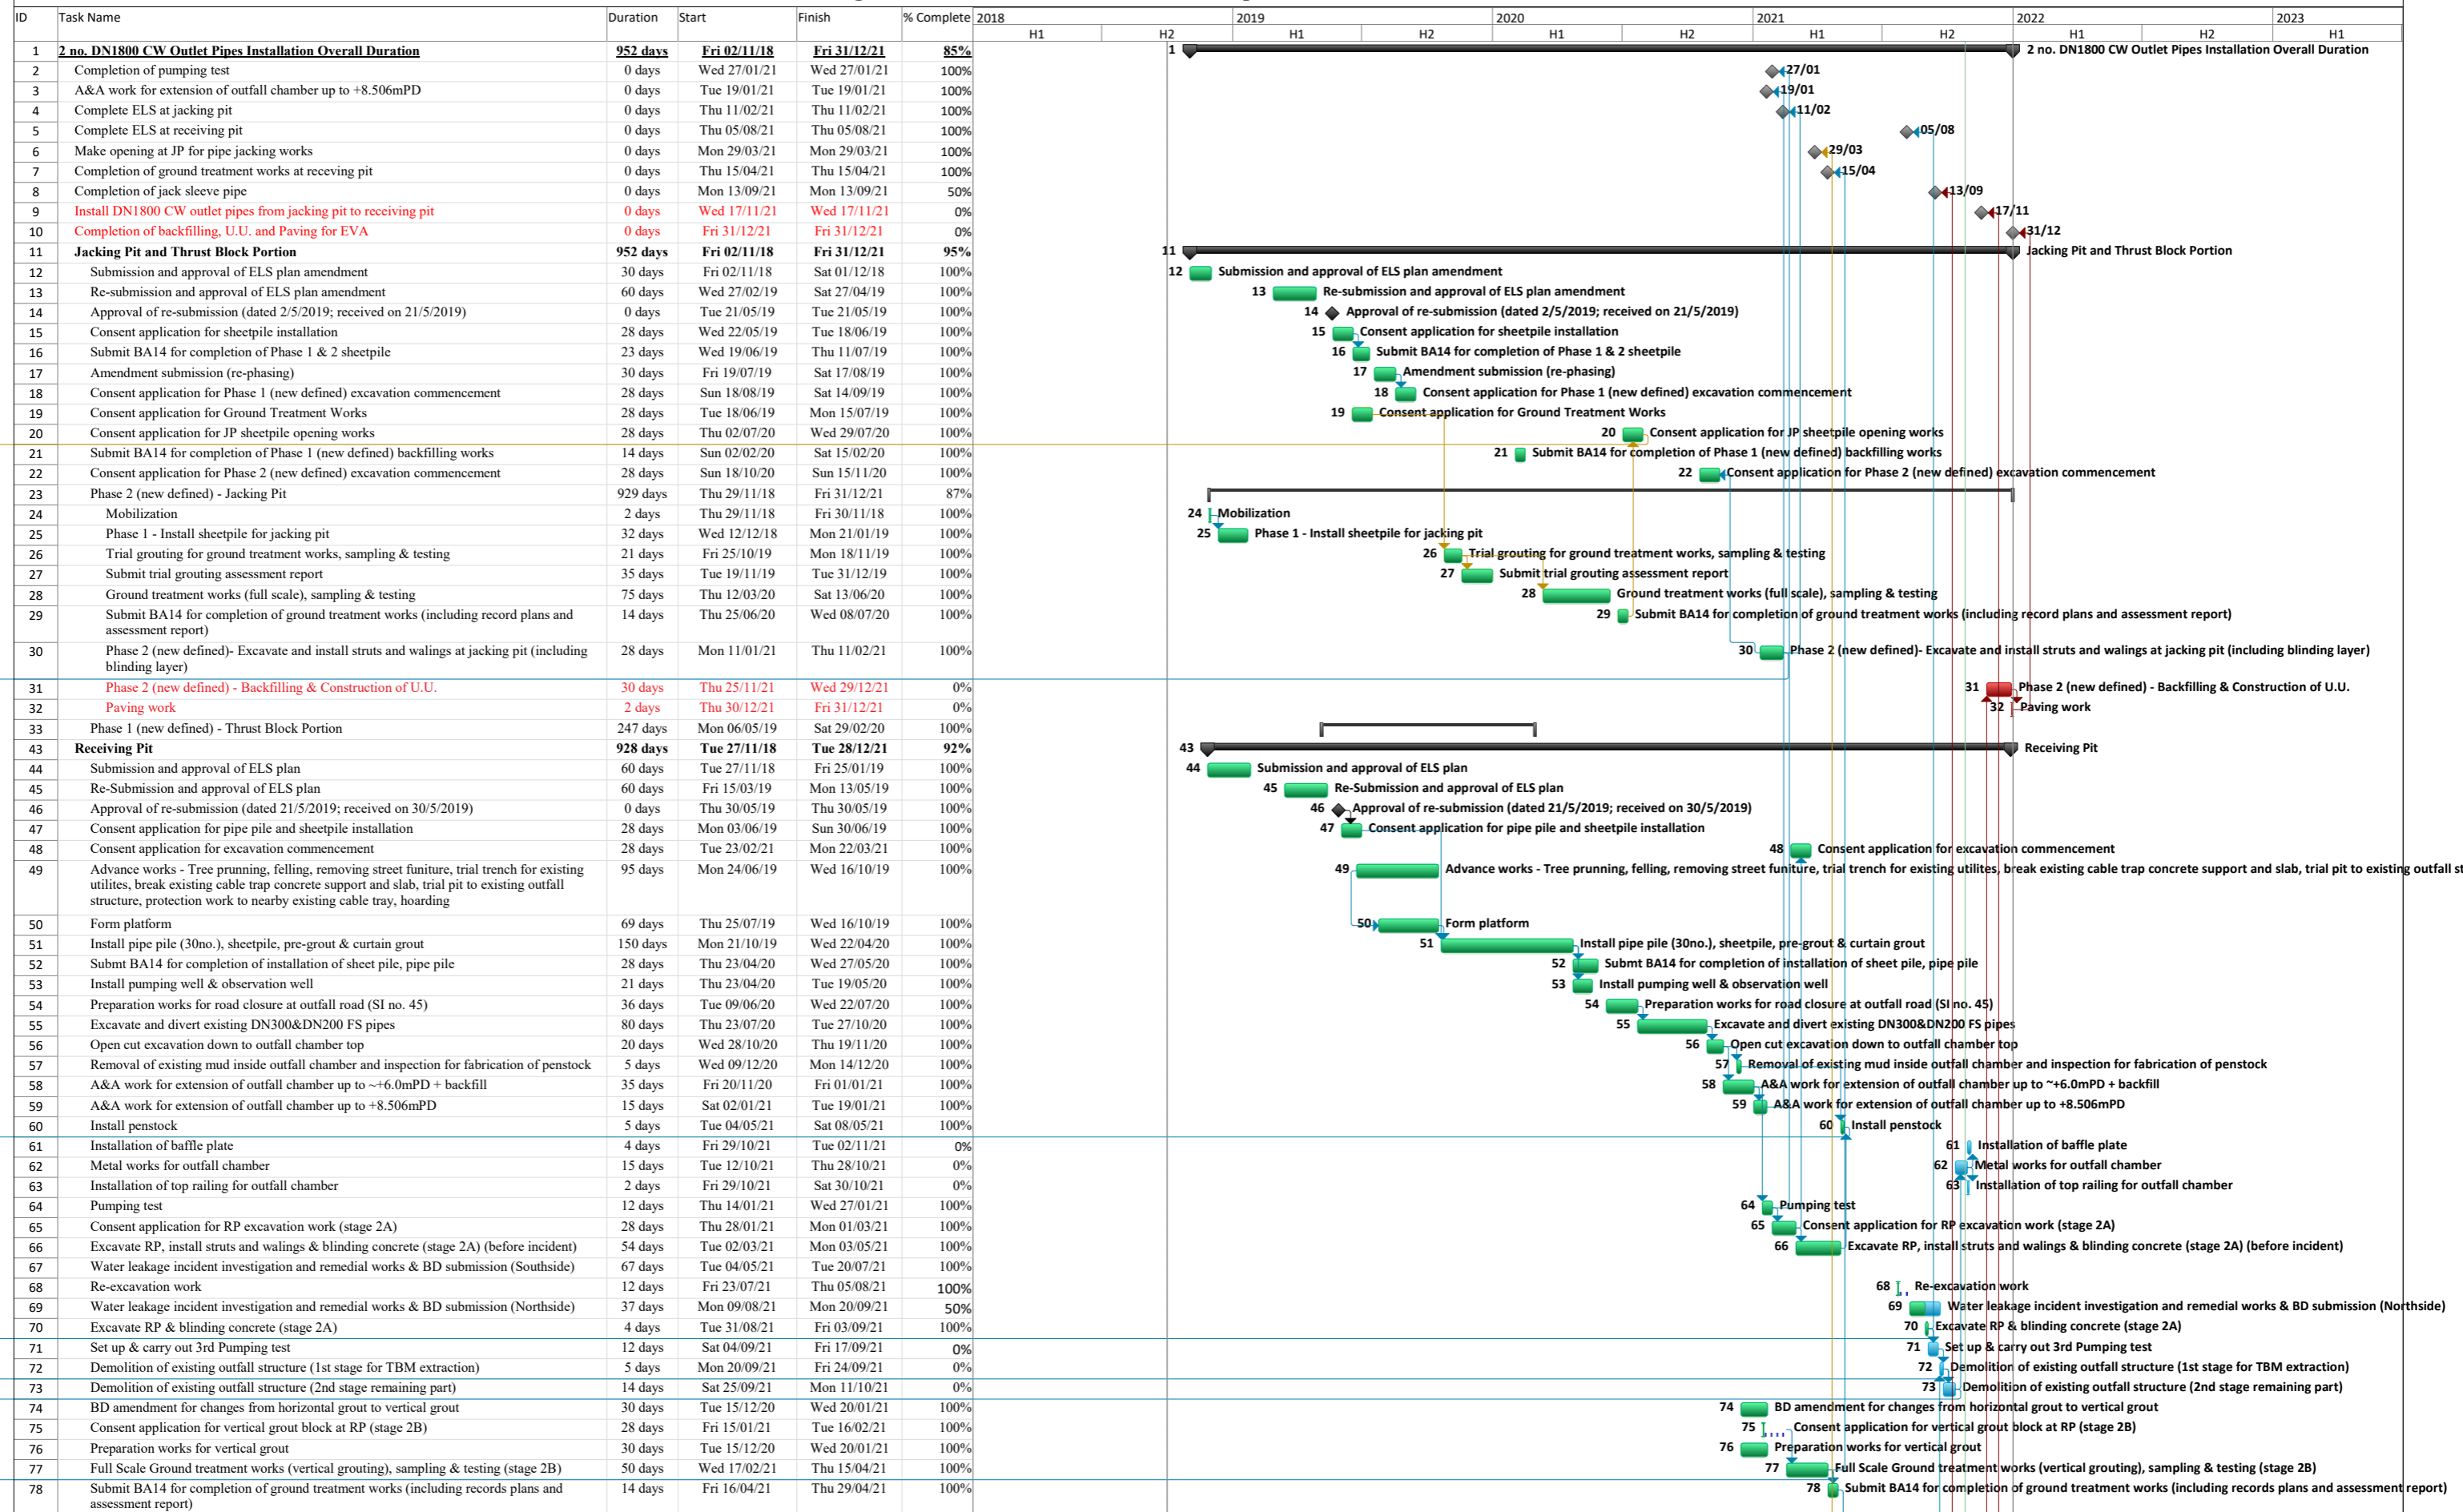


Paul Y Construction Co., Ltd.

Task Split Milestone Summary Project Summary External Tasks Critical Critical Split Progress

Revised Works Programme for 2no. DN1800 CW Outlet Pipes Installation - Culvert Outfall No. 4 + GRS Works


No.4 Outfall A&A+GRS (Rev.17) (26-10-2021)

ID	Task Name	Duration	Start	Finish	% Complete	2018		2019		2020		2021		2022		2023
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
79	Consent application for pipe pile opening works	28 days	Fri 23/04/21	Thu 20/05/21	100%											
80	Pipe pile opening works	5 days	Sat 04/09/21	Thu 09/09/21	0%											
81	Extraction of TBM (1st pipe)	4 days	Sat 25/09/21	Wed 29/09/21	0%											
82	RP - Backfilling	14 days	Mon 13/12/21	Tue 28/12/21	0%											
83	Pipe Jacking (2 no.)	226 days	Sat 20/02/21	Wed 10/11/21	78%											
84	Set up for pipe jacking works	20 days	Sat 20/02/21	Mon 15/03/21	100%											
85	Make opening at JP for pipe jacking works	2 days	Tue 16/03/21	Wed 17/03/21	100%											
86	Jack sleeve pipe no. 1 (first 40m of 70m)	30 days	Thu 18/03/21	Wed 21/04/21	100%											
87	Jack sleeve pipe no. 1 (final 30m of 70m) [Ground treatment works at RP shall be completed according to JP approval plan.]	20 days	Thu 22/04/21	Fri 14/05/21	100%											
88	Pick up TBM from receiving pit and re-setup at jacking pit	2 days	Thu 30/09/21	Fri 01/10/21	0%											
89	Jack sleeve pipe no. 2 (70m)	15 days	Thu 21/10/21	Sun 07/11/21	0%											
90	Pick up TBM from receiving pit	3 days	Mon 08/11/21	Wed 10/11/21	0%											
91	CW pipes installation and Inspection Manhole at Jacking Pit	48 days	Thu 21/10/21	Wed 15/12/21	0%											
92	Modify existing outfall structure for connection of CW pipe at outfall	30 days	Thu 11/11/21	Wed 15/12/21	0%											
93	Install DN1800 CW outlet pipes from jacking pit to receiving pit (1st pipe)	6 days	Thu 28/10/21	Wed 03/11/21	0%											
94	Install DN1800 CW outlet pipes from jacking pit to receiving pit (2nd pipe)	6 days	Thu 11/11/21	Wed 17/11/21	0%											
95	Annulus grout (1st pipe)	5 days	Thu 04/11/21	Tue 09/11/21	0%											
96	Annulus grout (2nd pipe)	5 days	Thu 18/11/21	Tue 23/11/21	0%											
97	Demolition of thrust block, cut sheet pile for connection of CW pipes to dog house at Jacking	3 days	Thu 18/11/21	Sat 20/11/21	0%											
98	CW pipes connection at Jacking Pit to existing portion	3 days	Mon 22/11/21	Wed 24/11/21	0%											
99	CW pipes connection to existing outfall structure at Receiving Pit	15 days	Thu 25/11/21	Sat 11/12/21	0%											
100	Gas pipe support foundation and pipe trench and associated external works at Area E14	247 days	Mon 17/02/20	Sat 12/12/20	72%											
109	L12&L13 Outlet culvert(Connection to Jacking Pit) at Area E15(A) and associated external works at area E15(B)	357 days	Sat 15/02/20	Wed 21/04/21	59%											
117	Gas Receiving Station and L11 Gas Receiving Station Equipment Room(GRS) area extension at Area E16	202 days	Thu 12/03/20	Sat 14/11/20	90%											

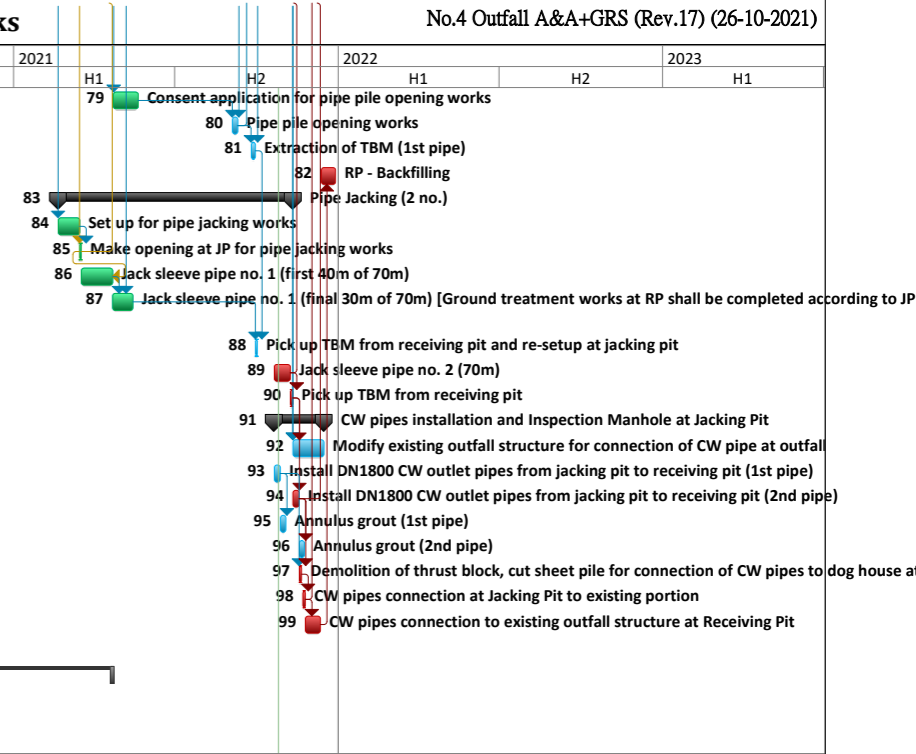

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

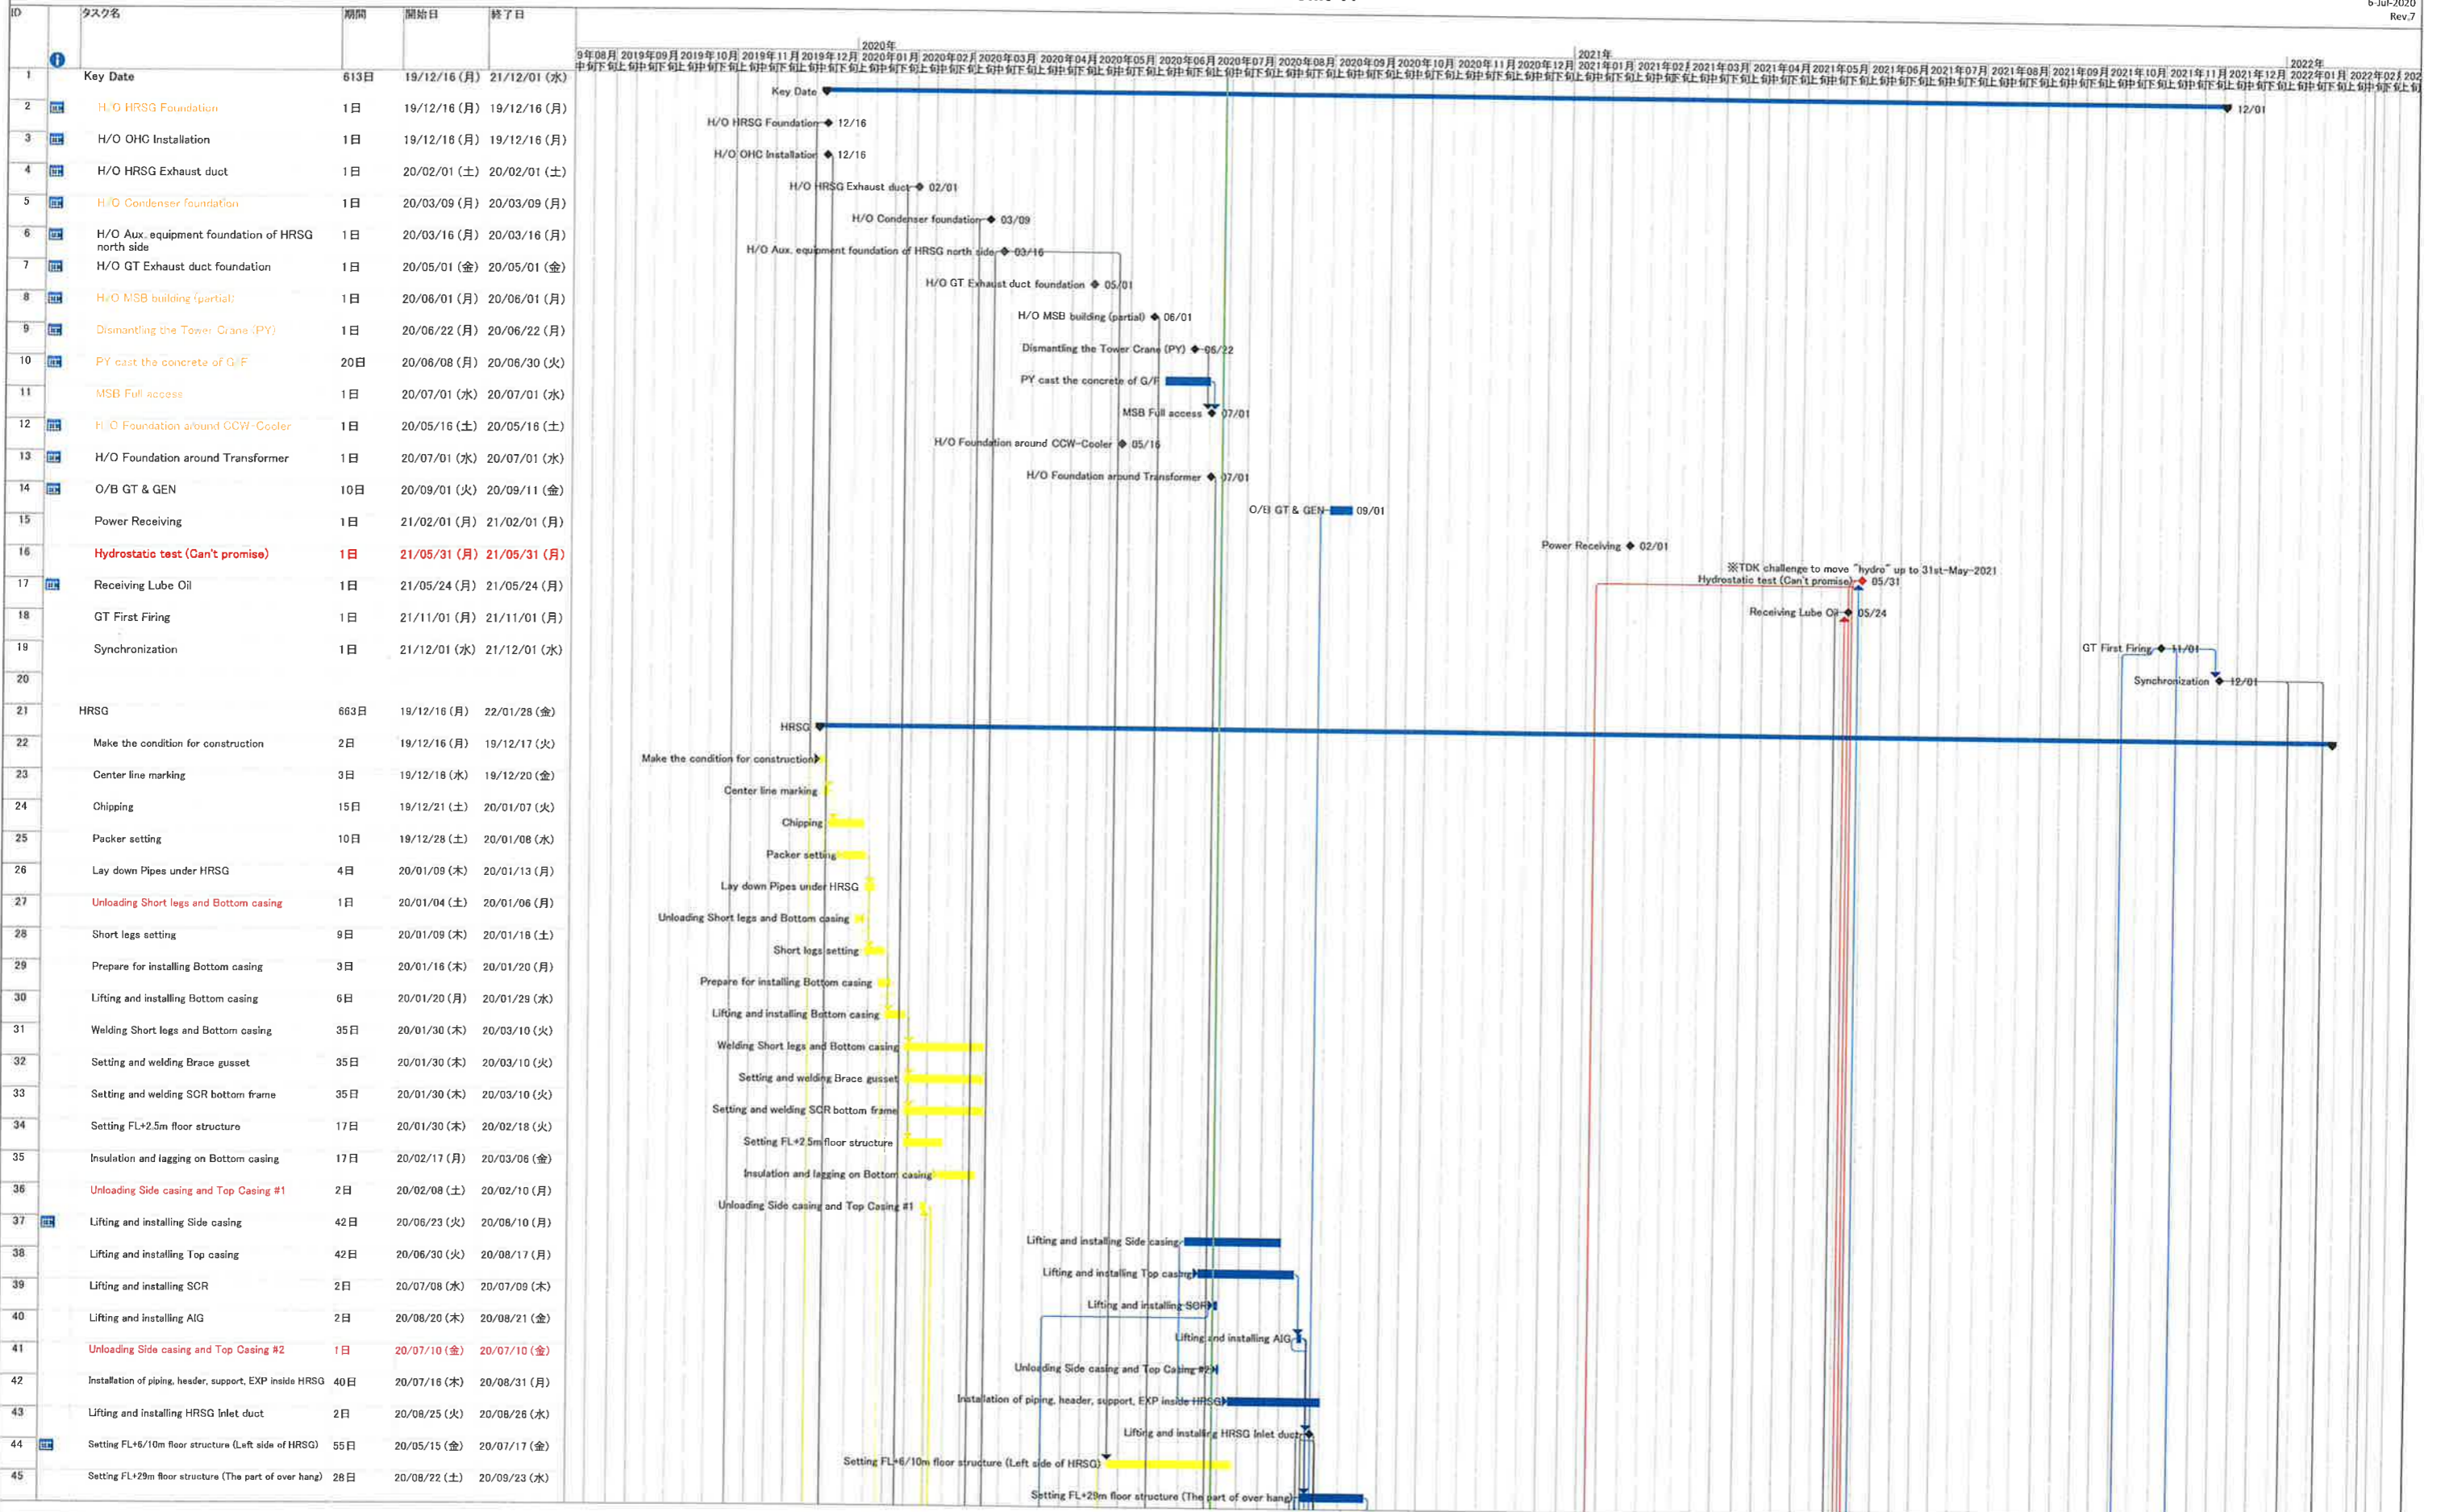


1. Change the starting date of installation below
 - ・ Installation HRSFG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15th-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

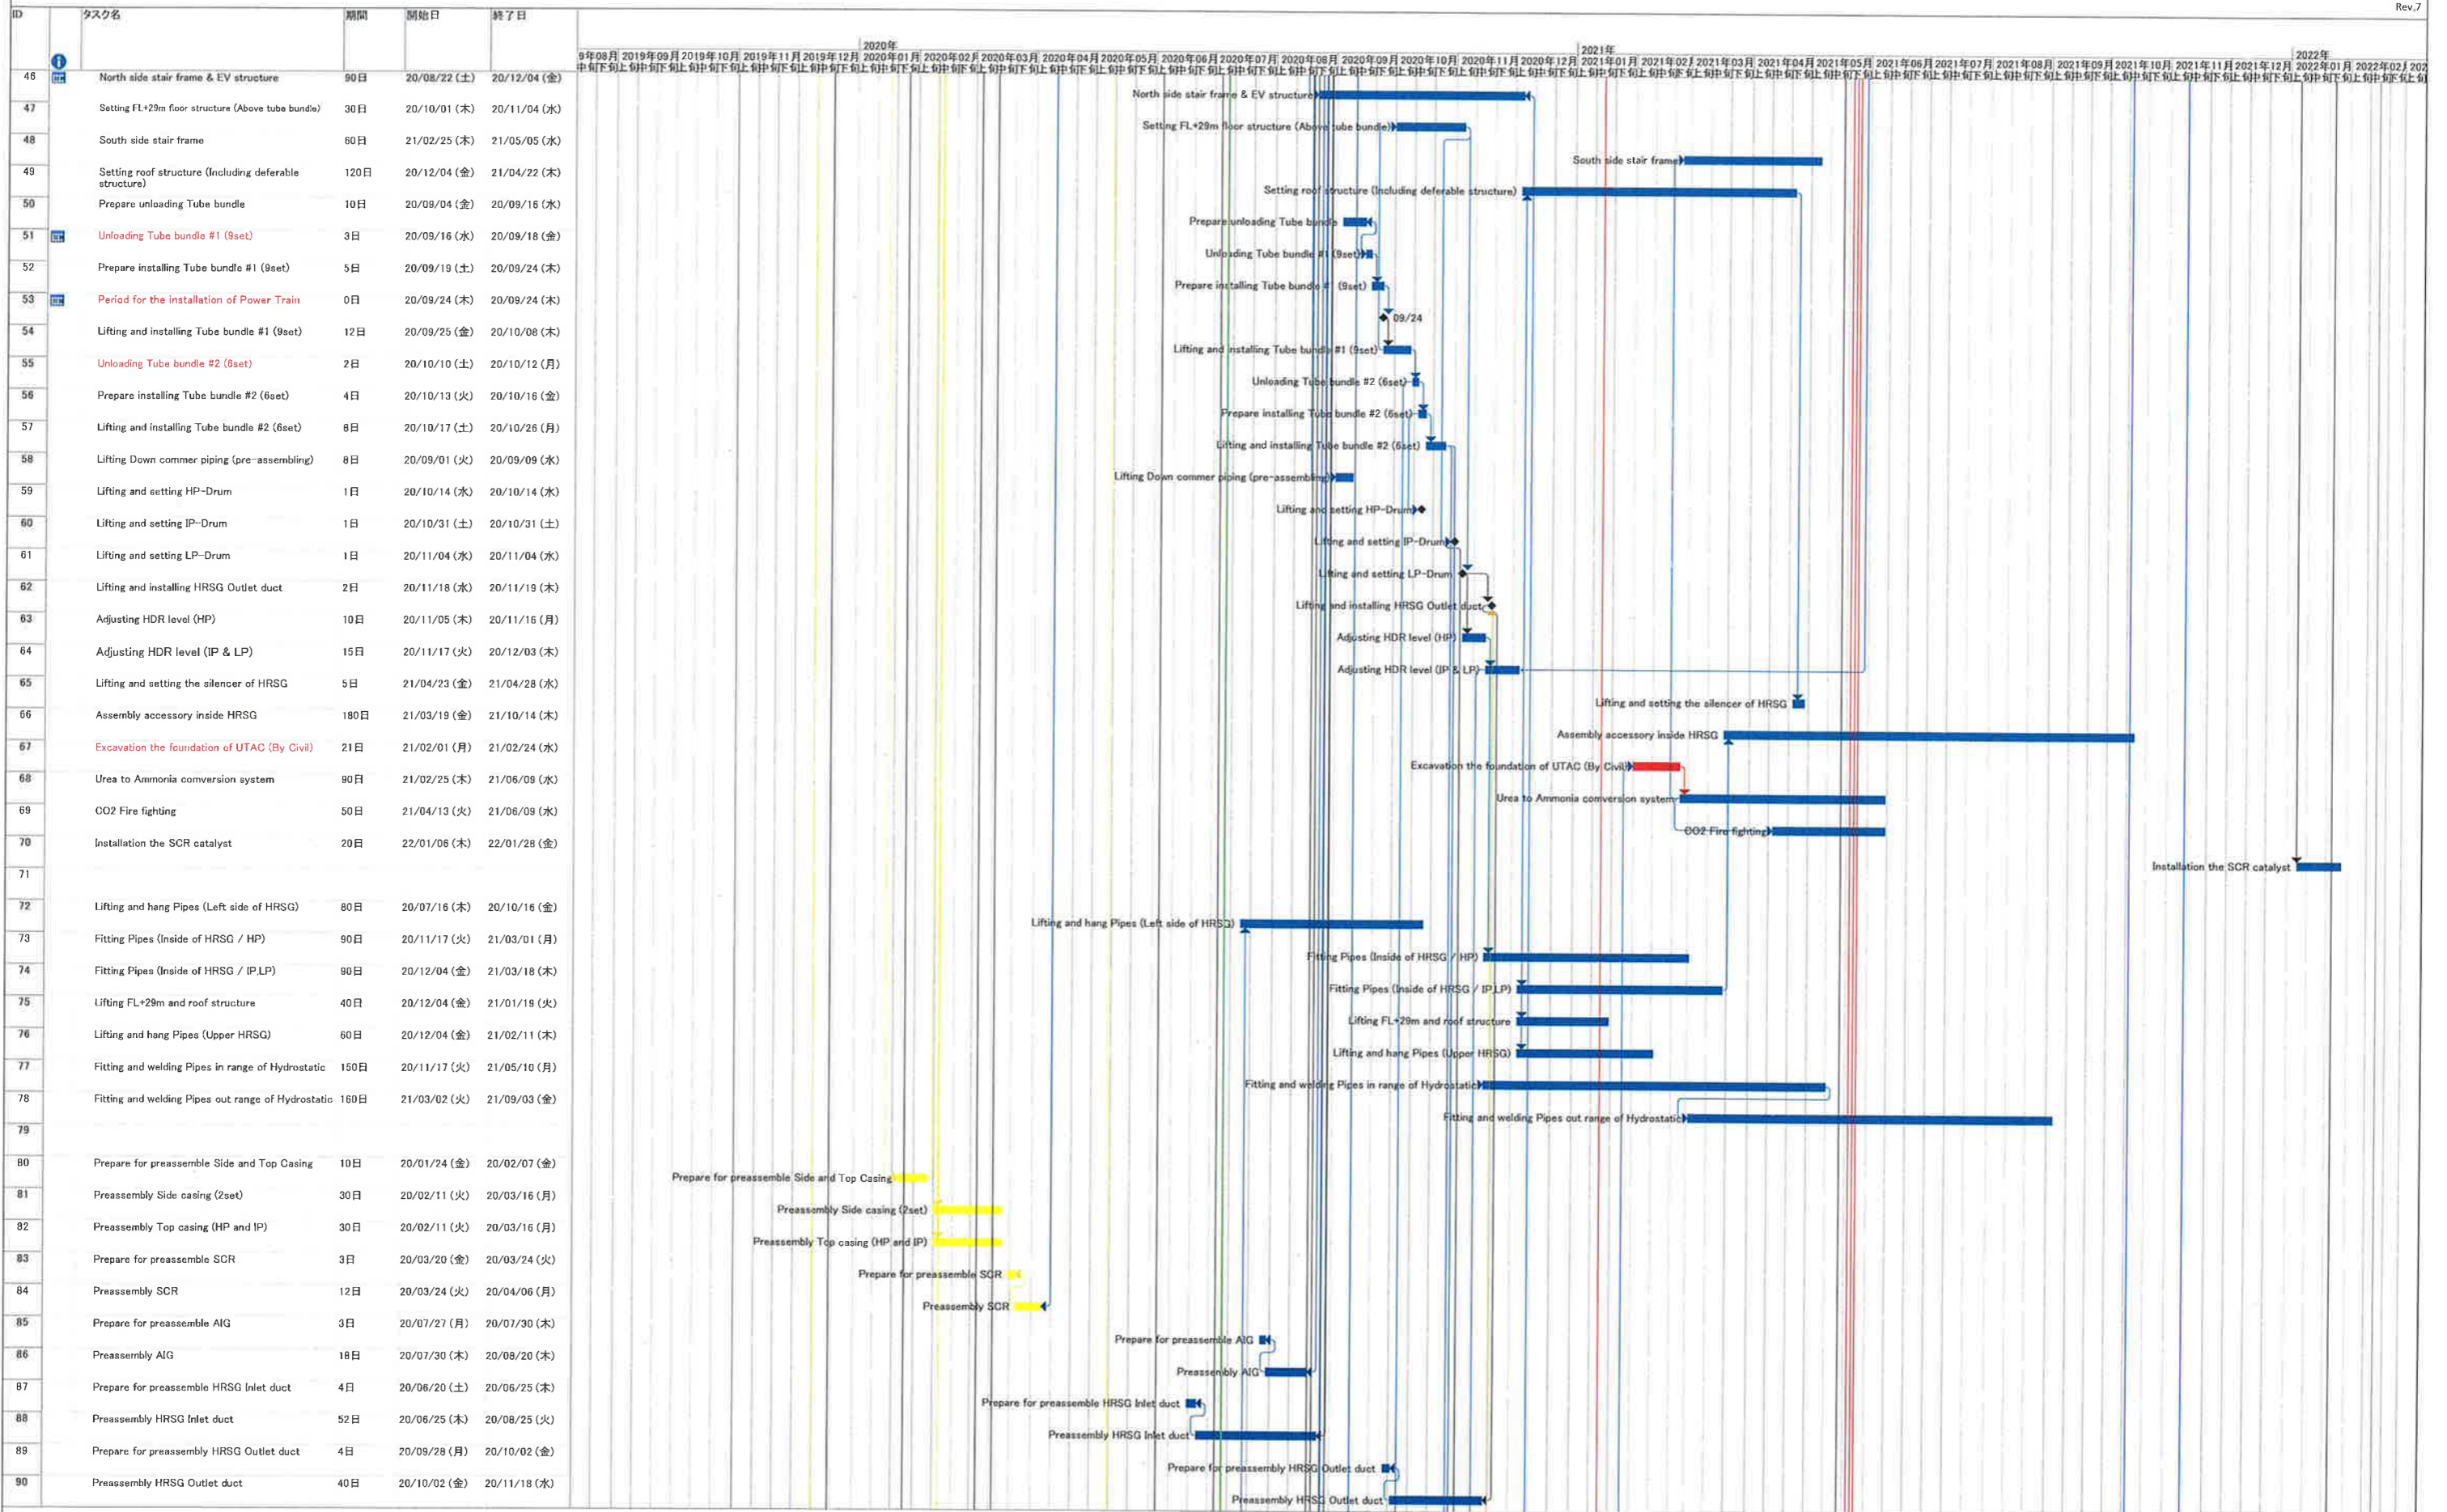


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

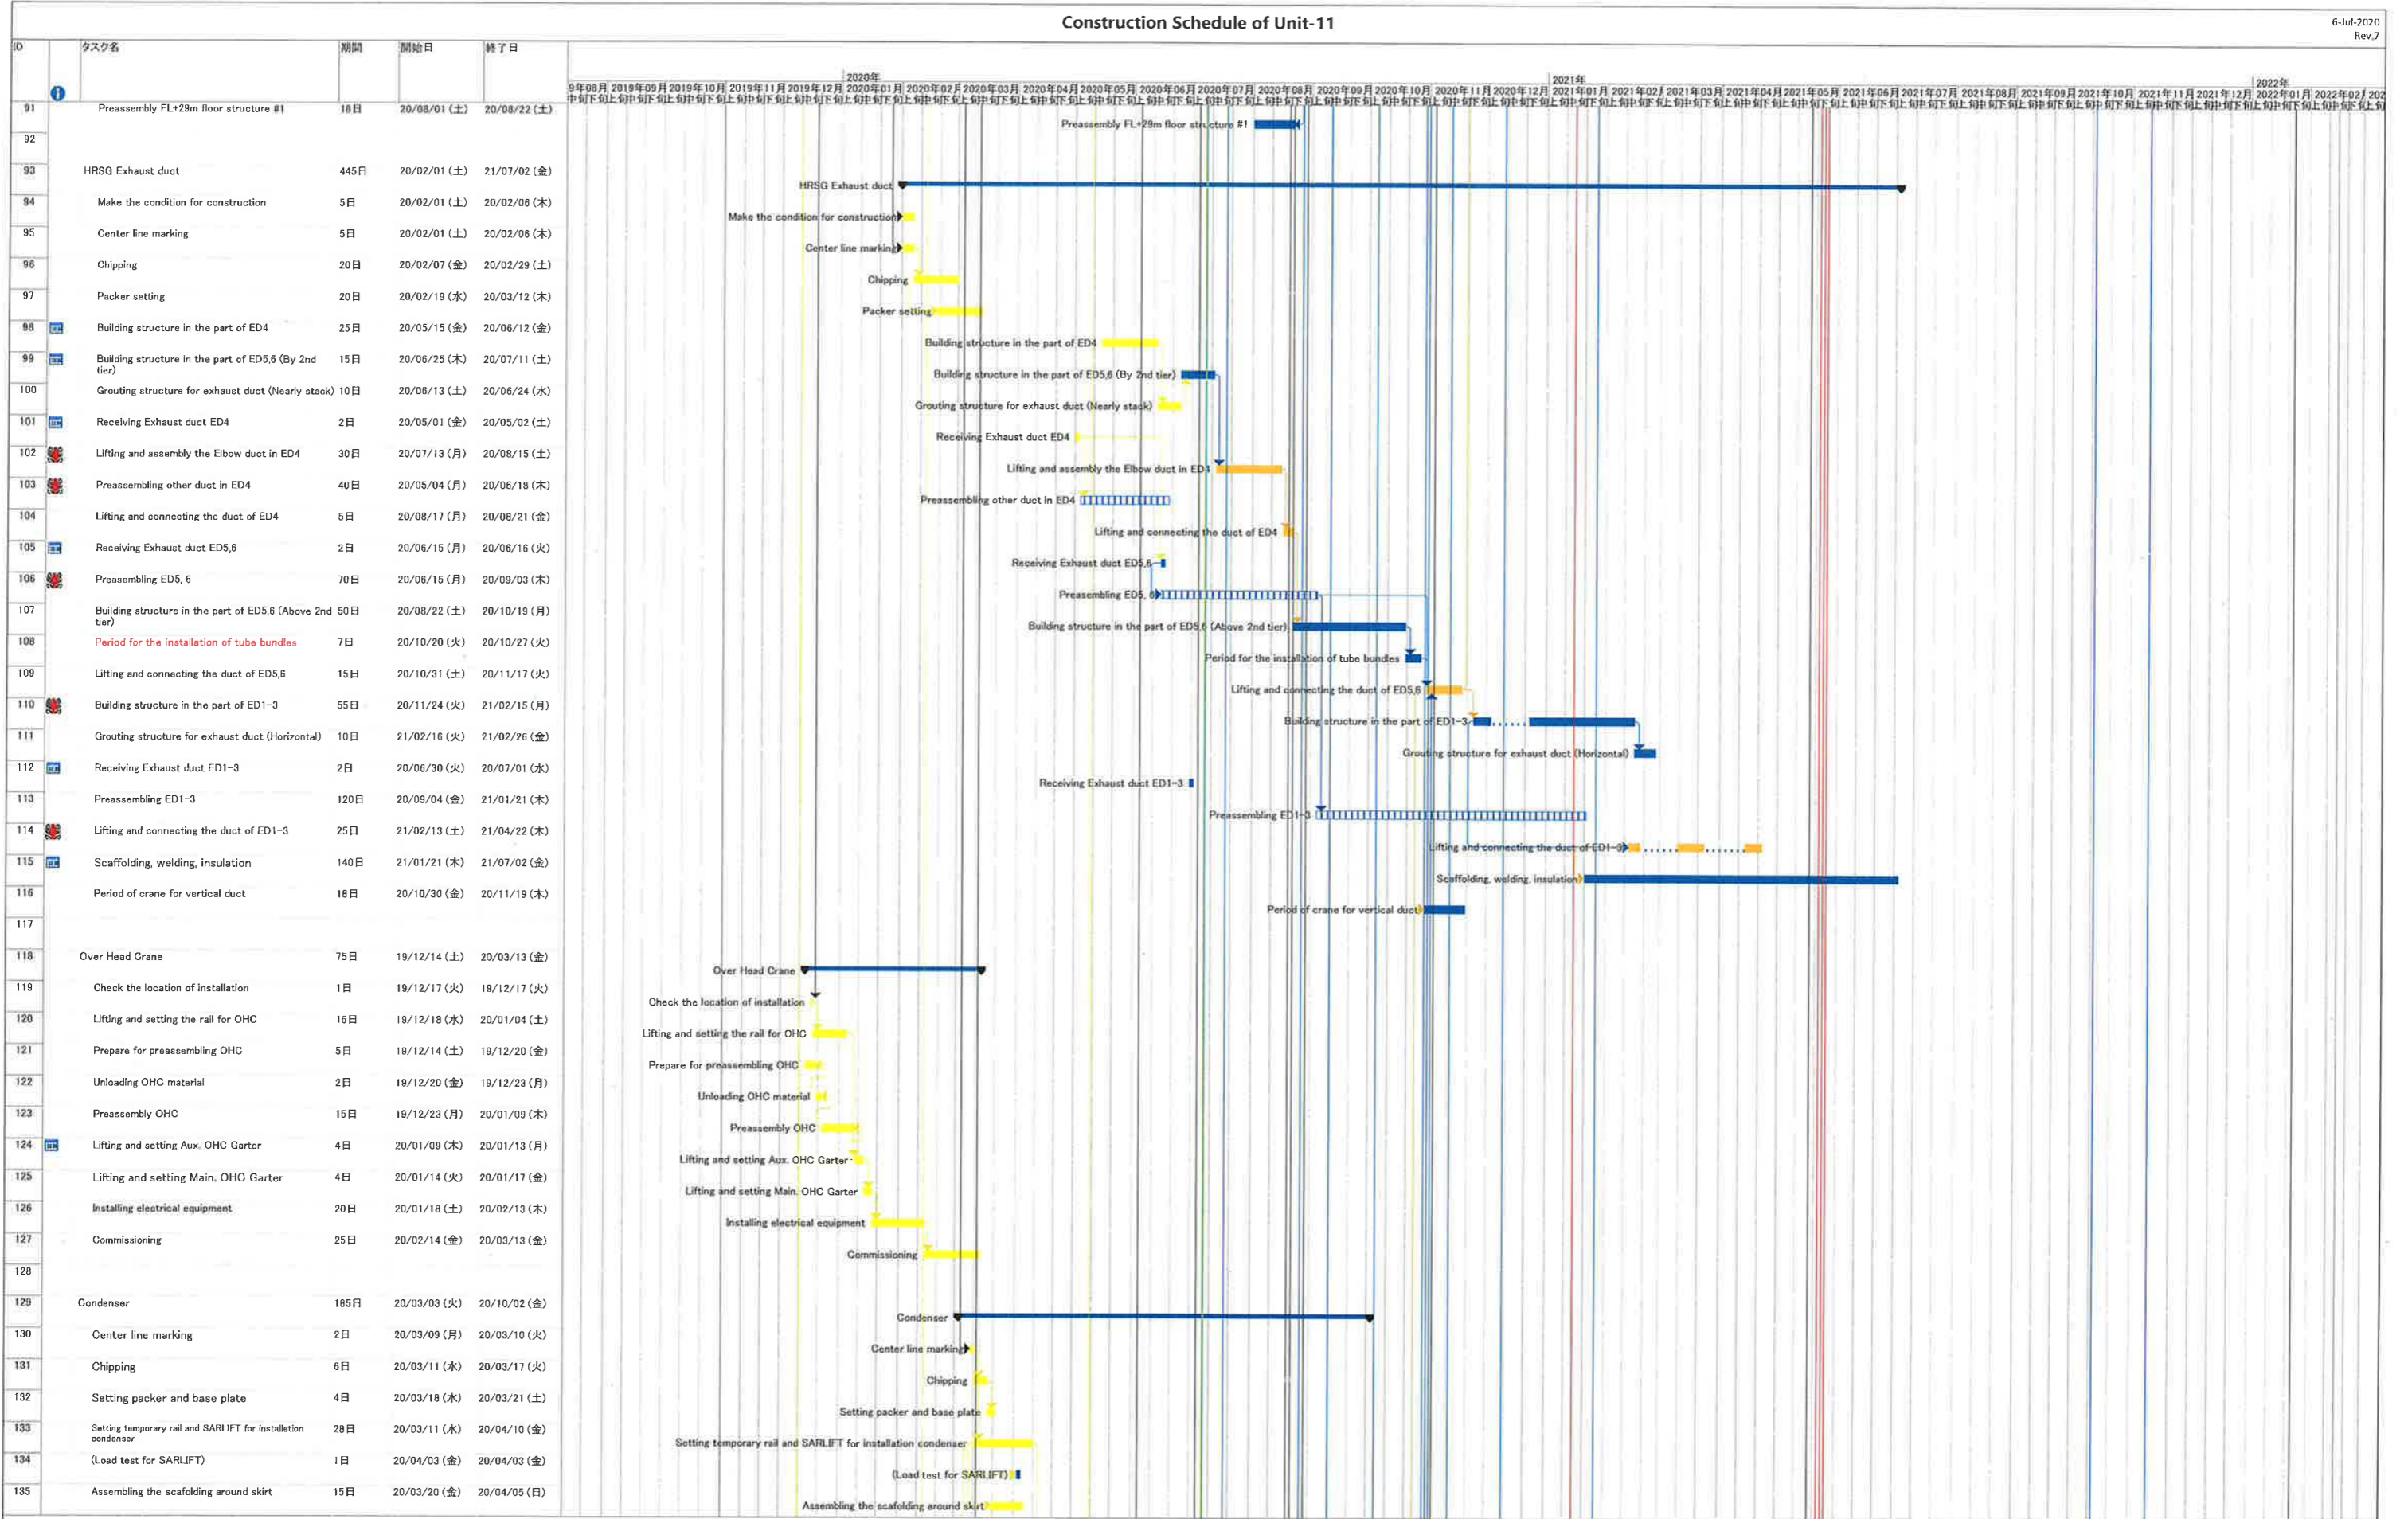


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

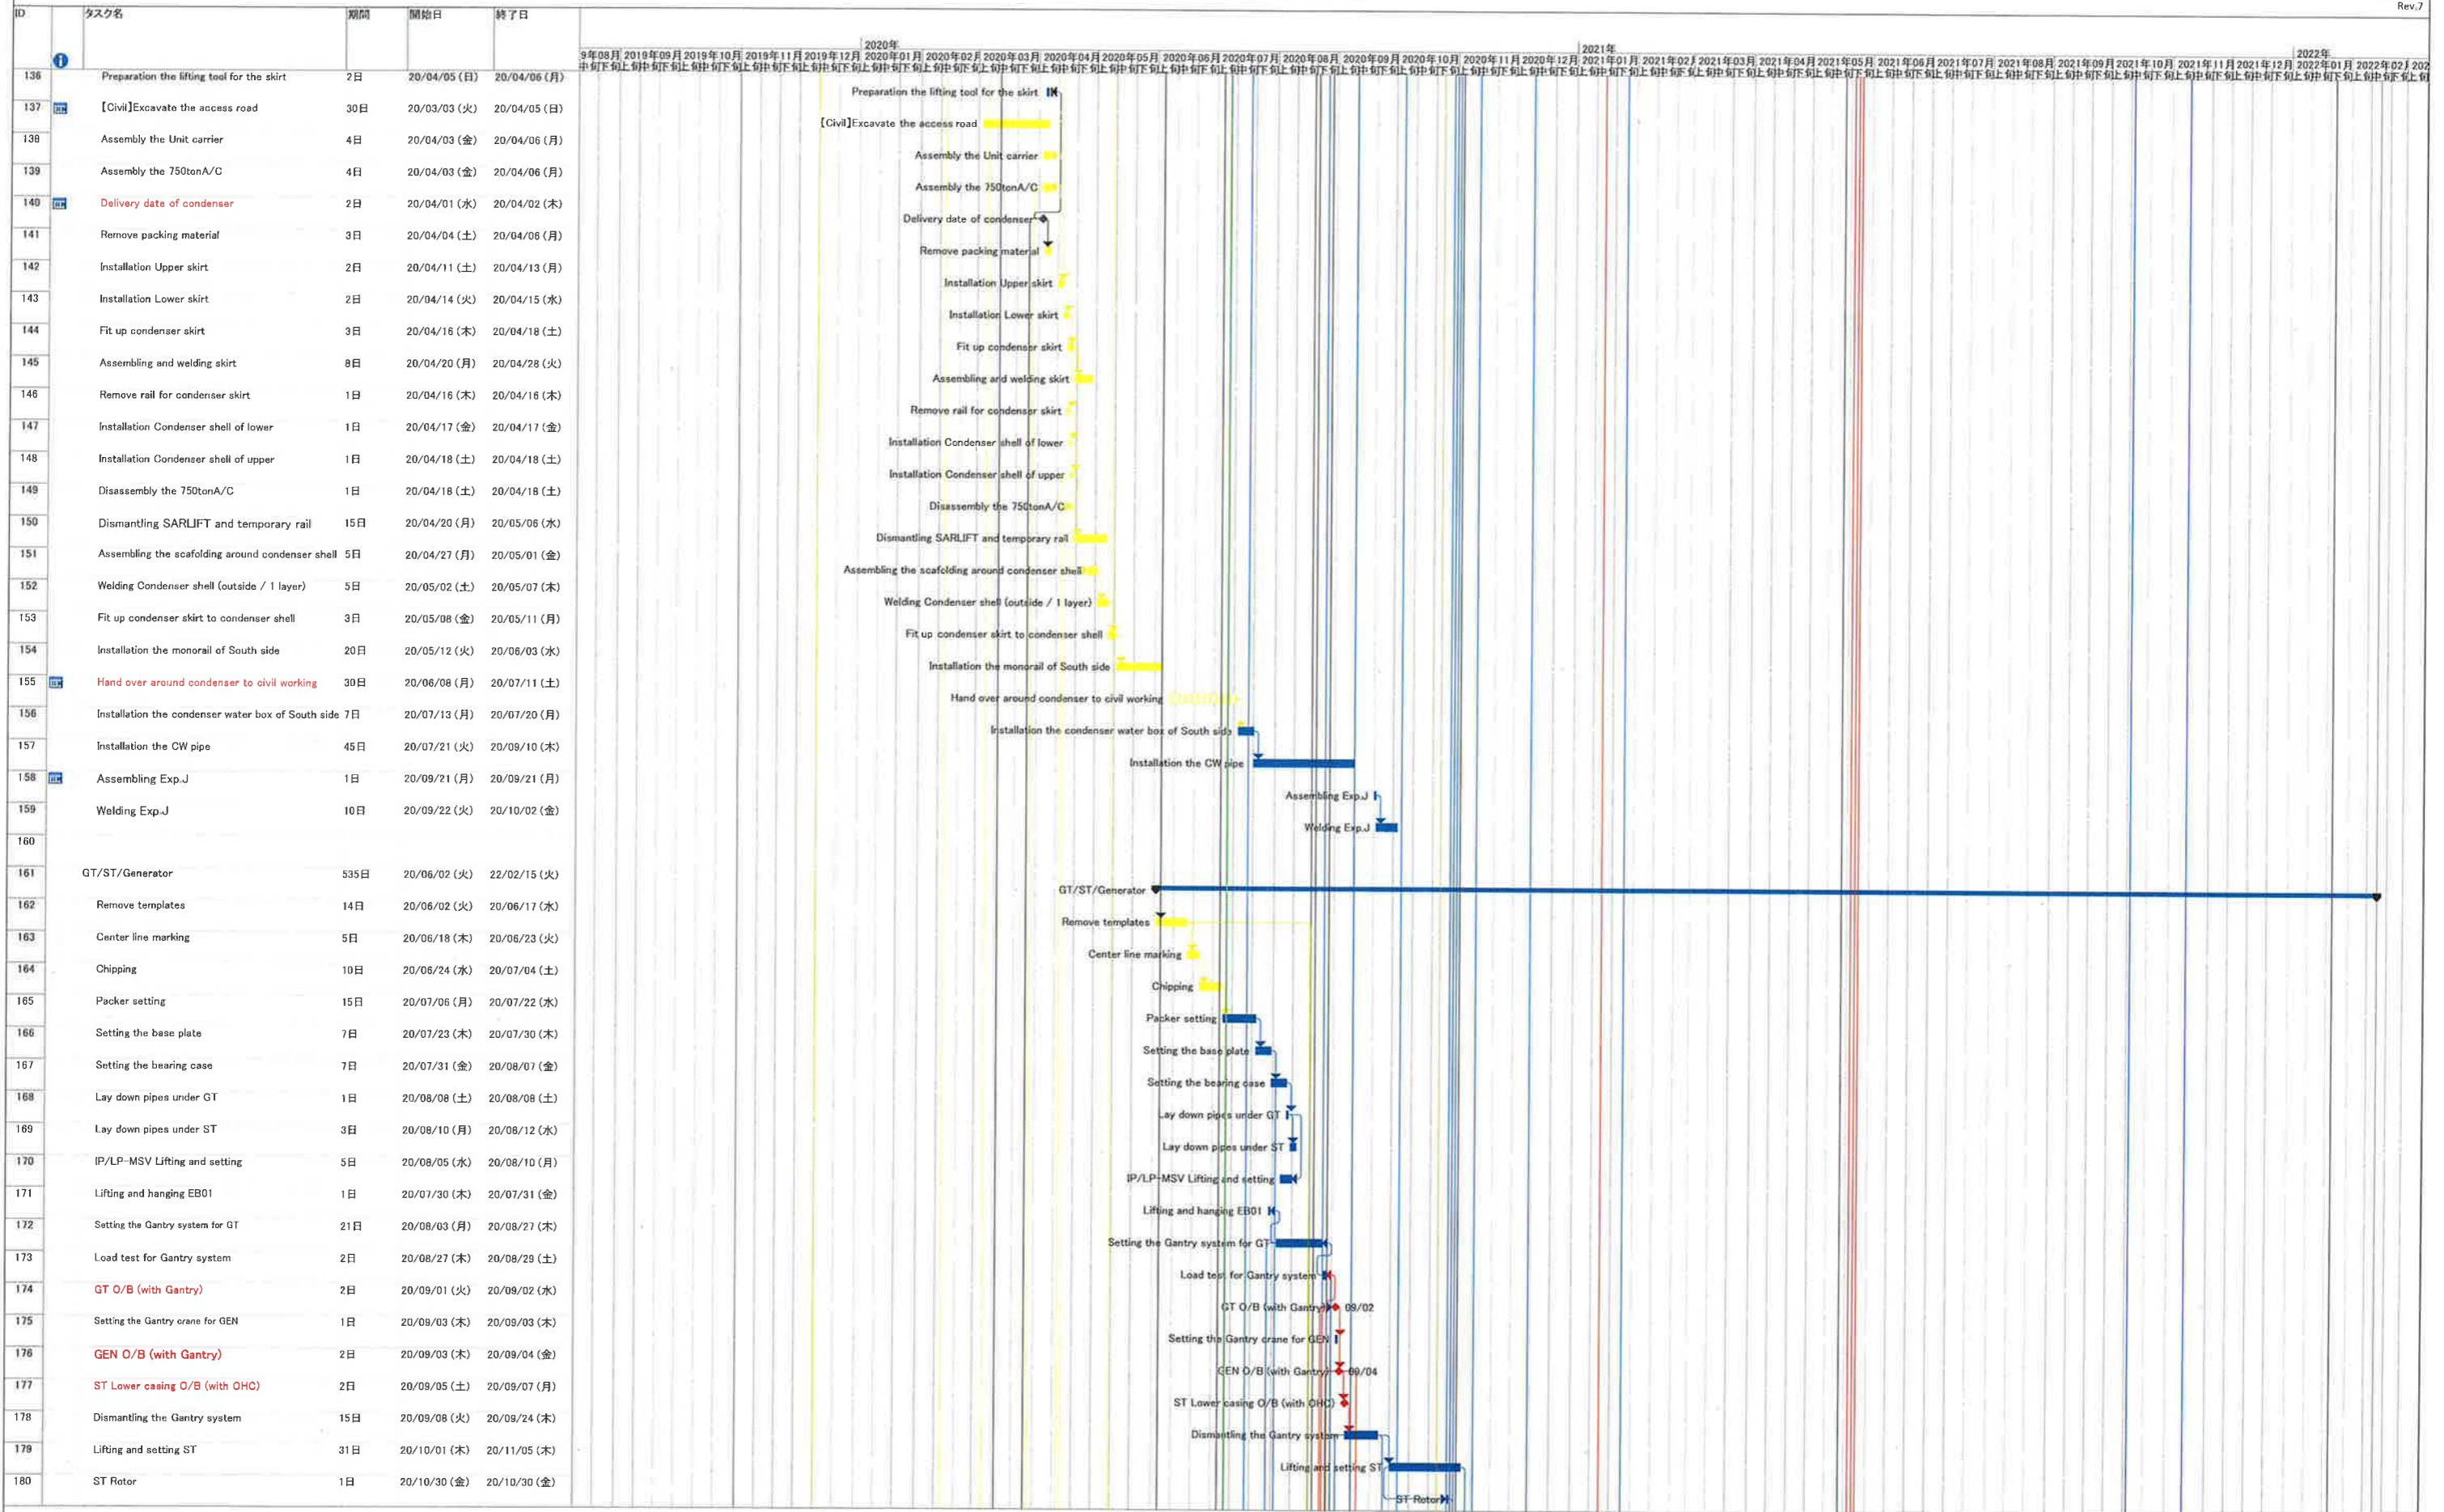


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

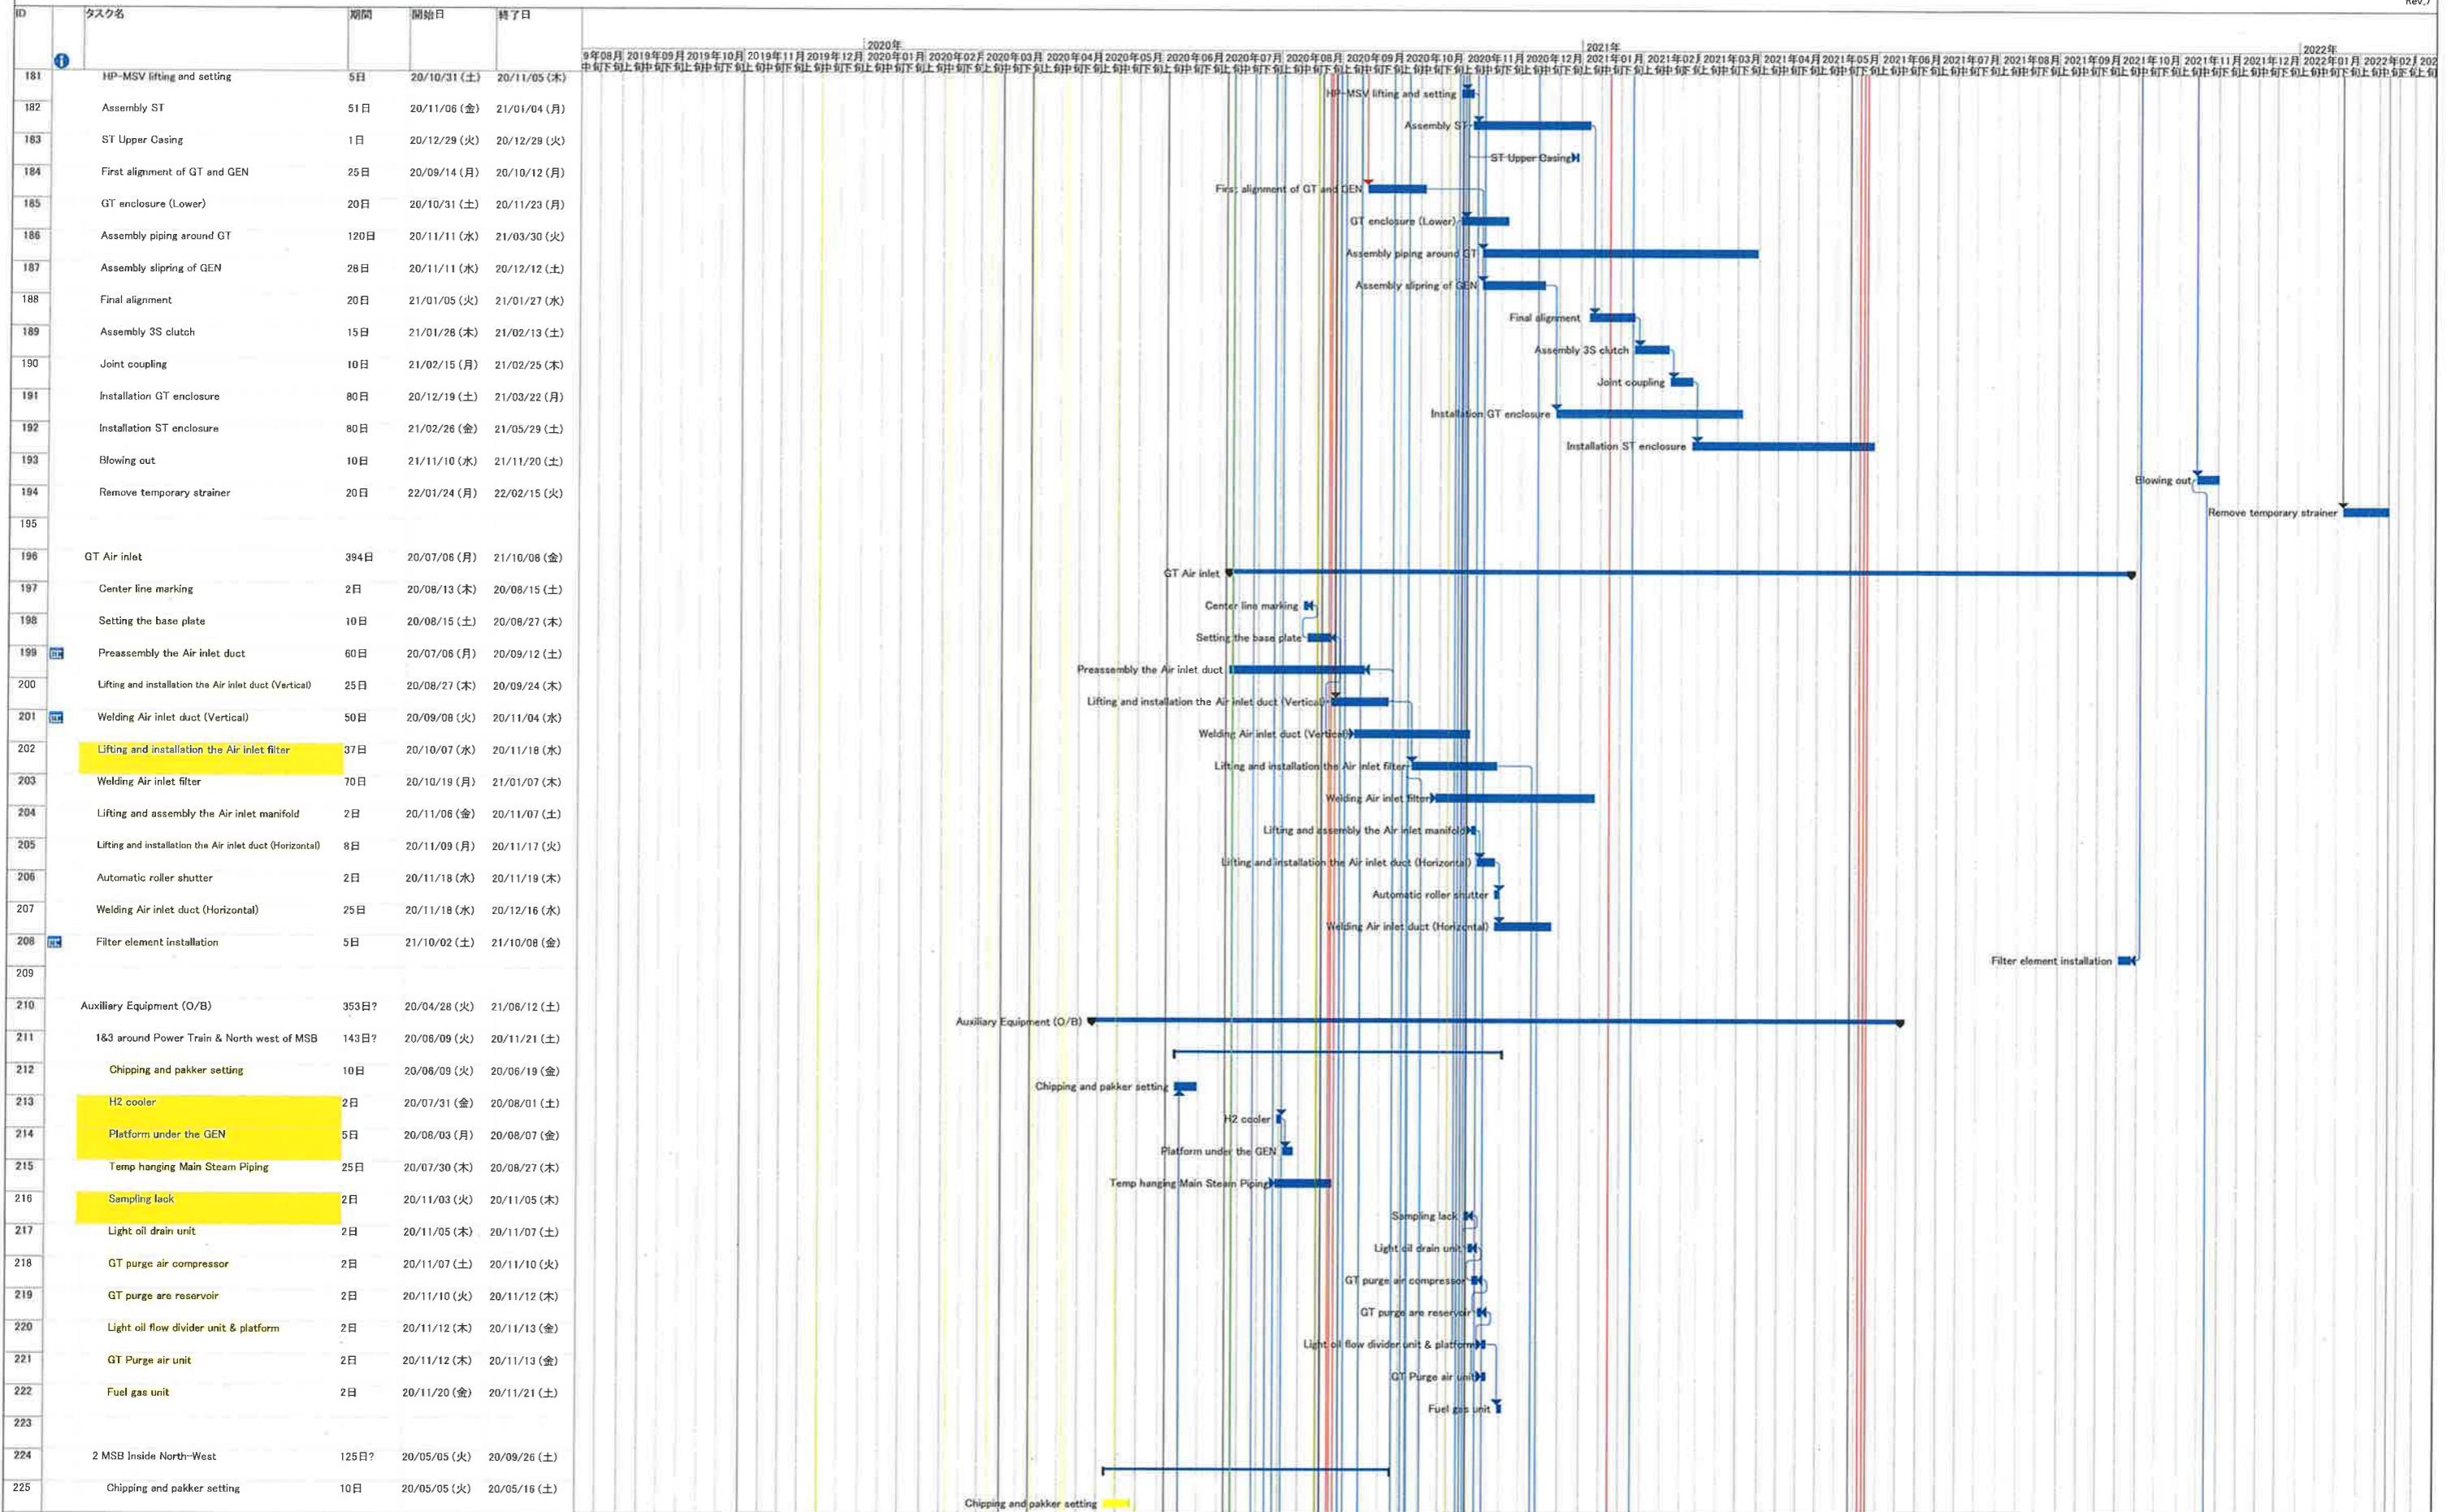


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020 Rev.7

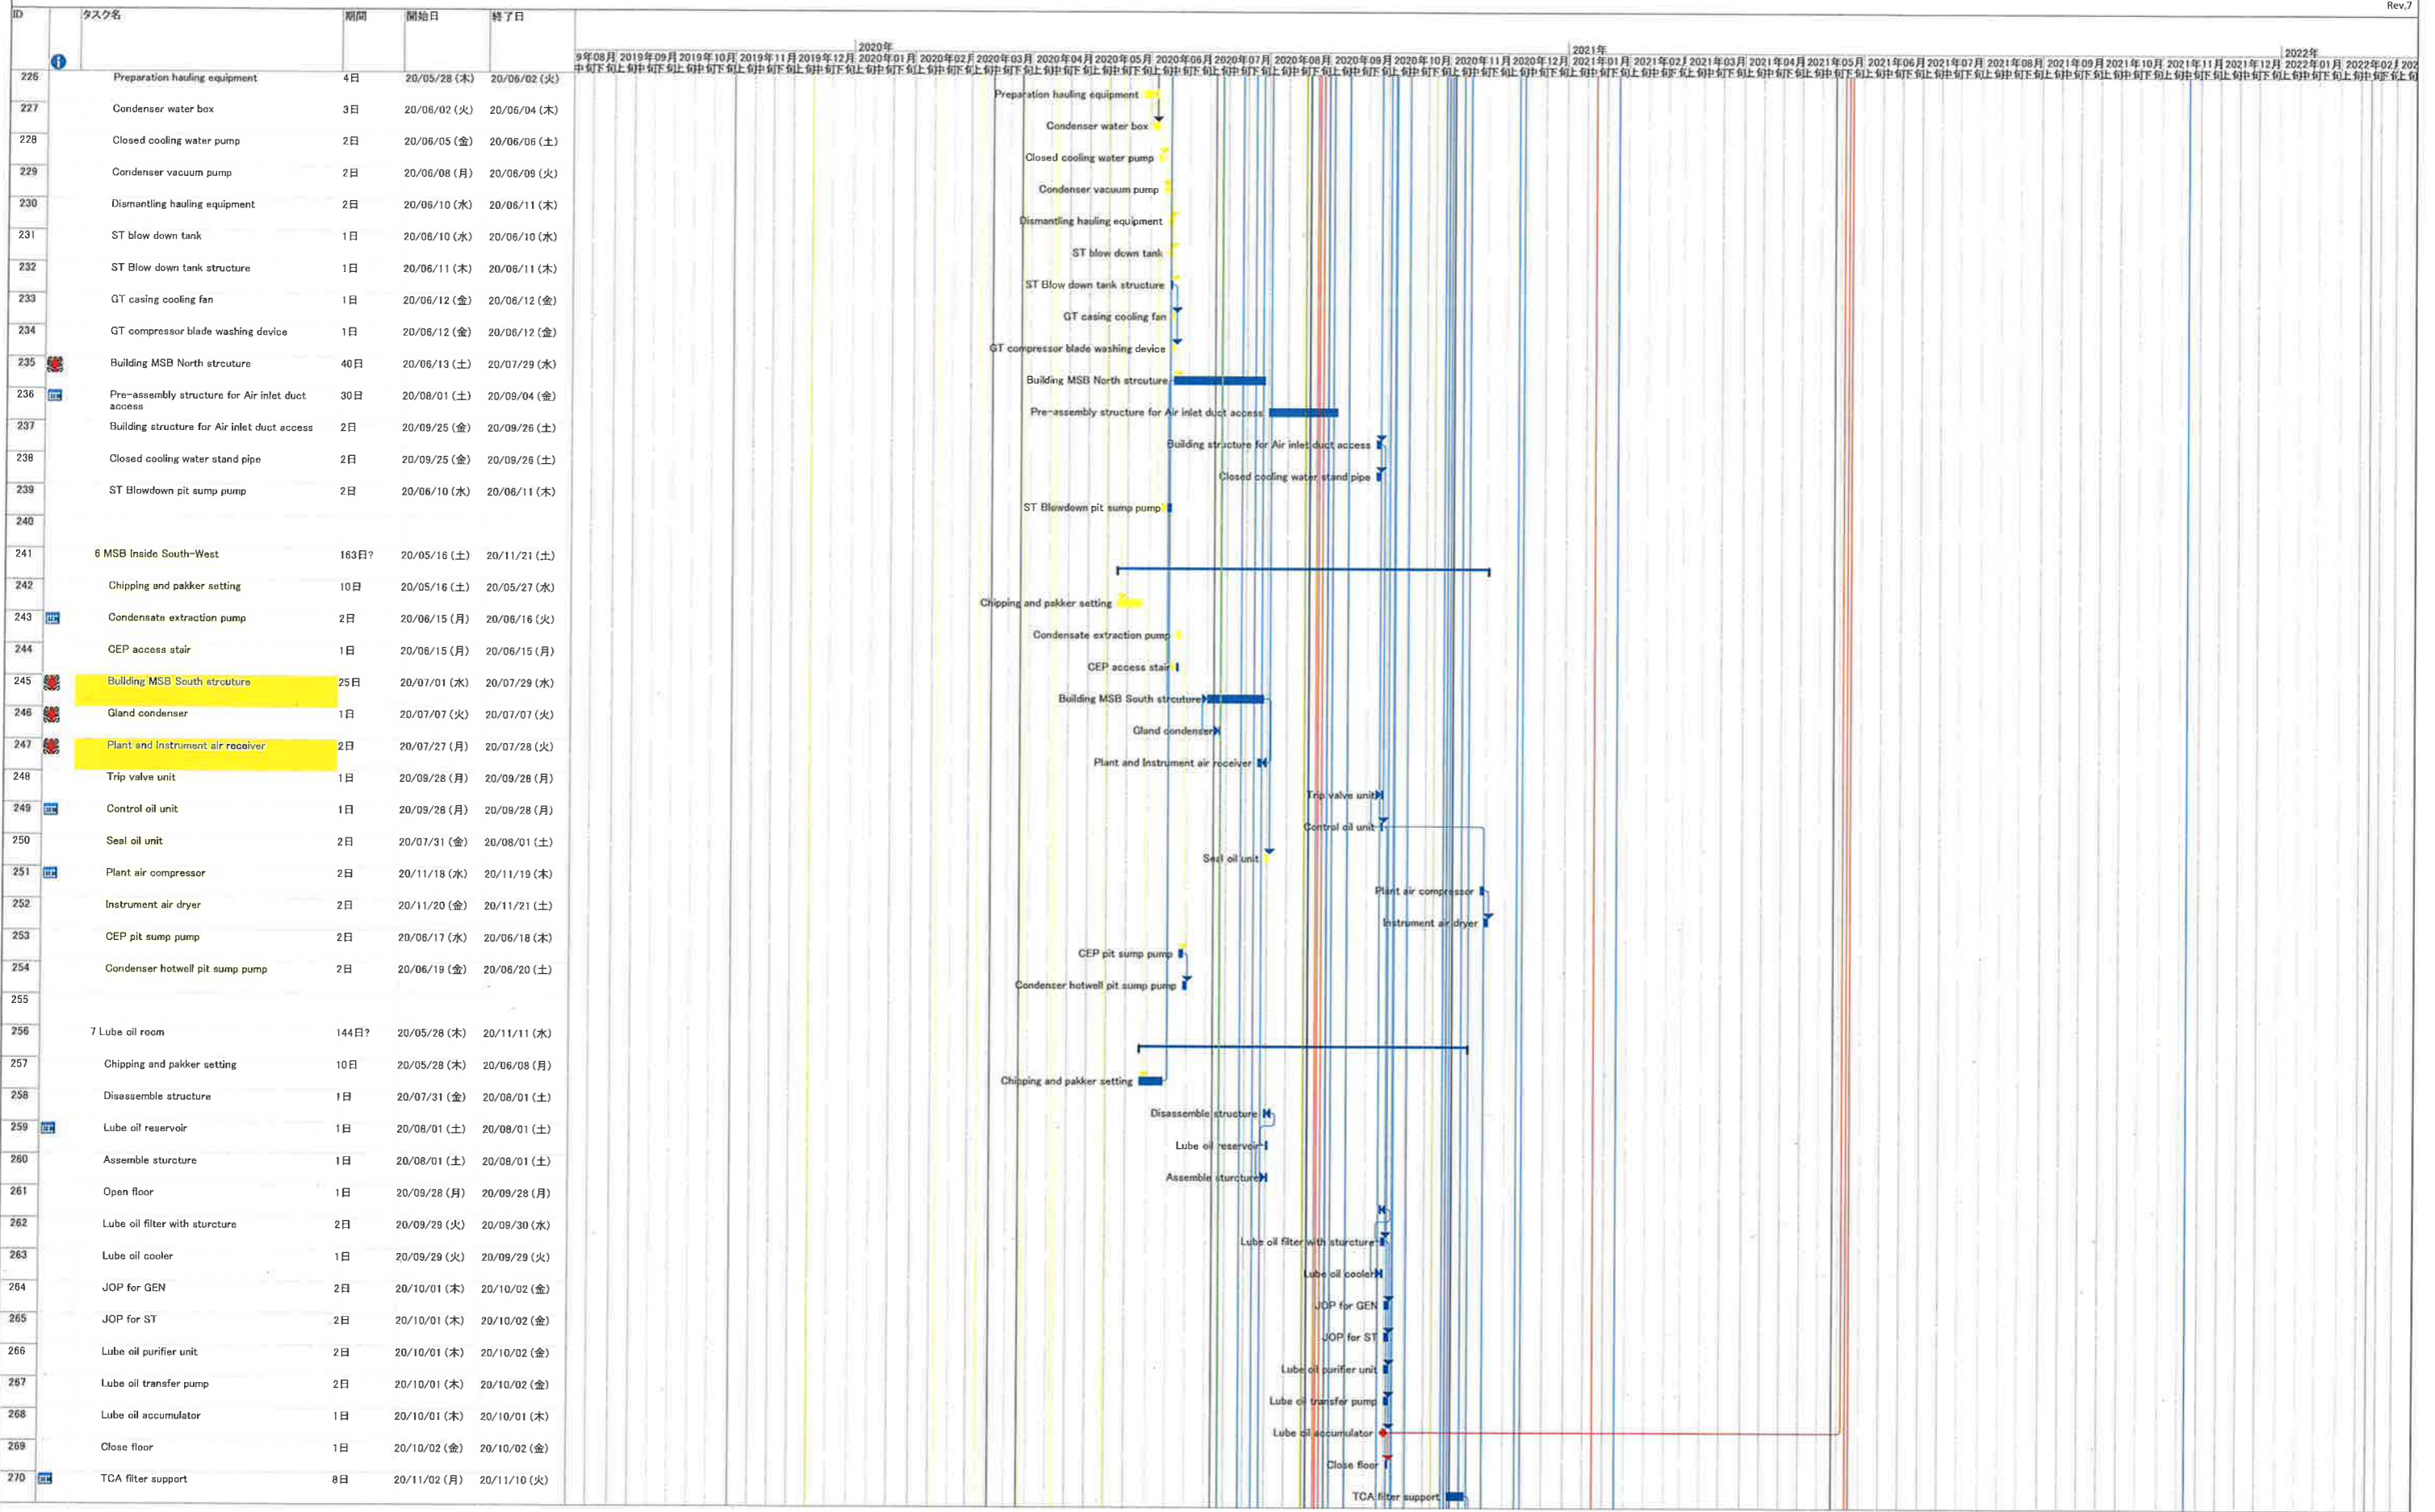


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15th-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

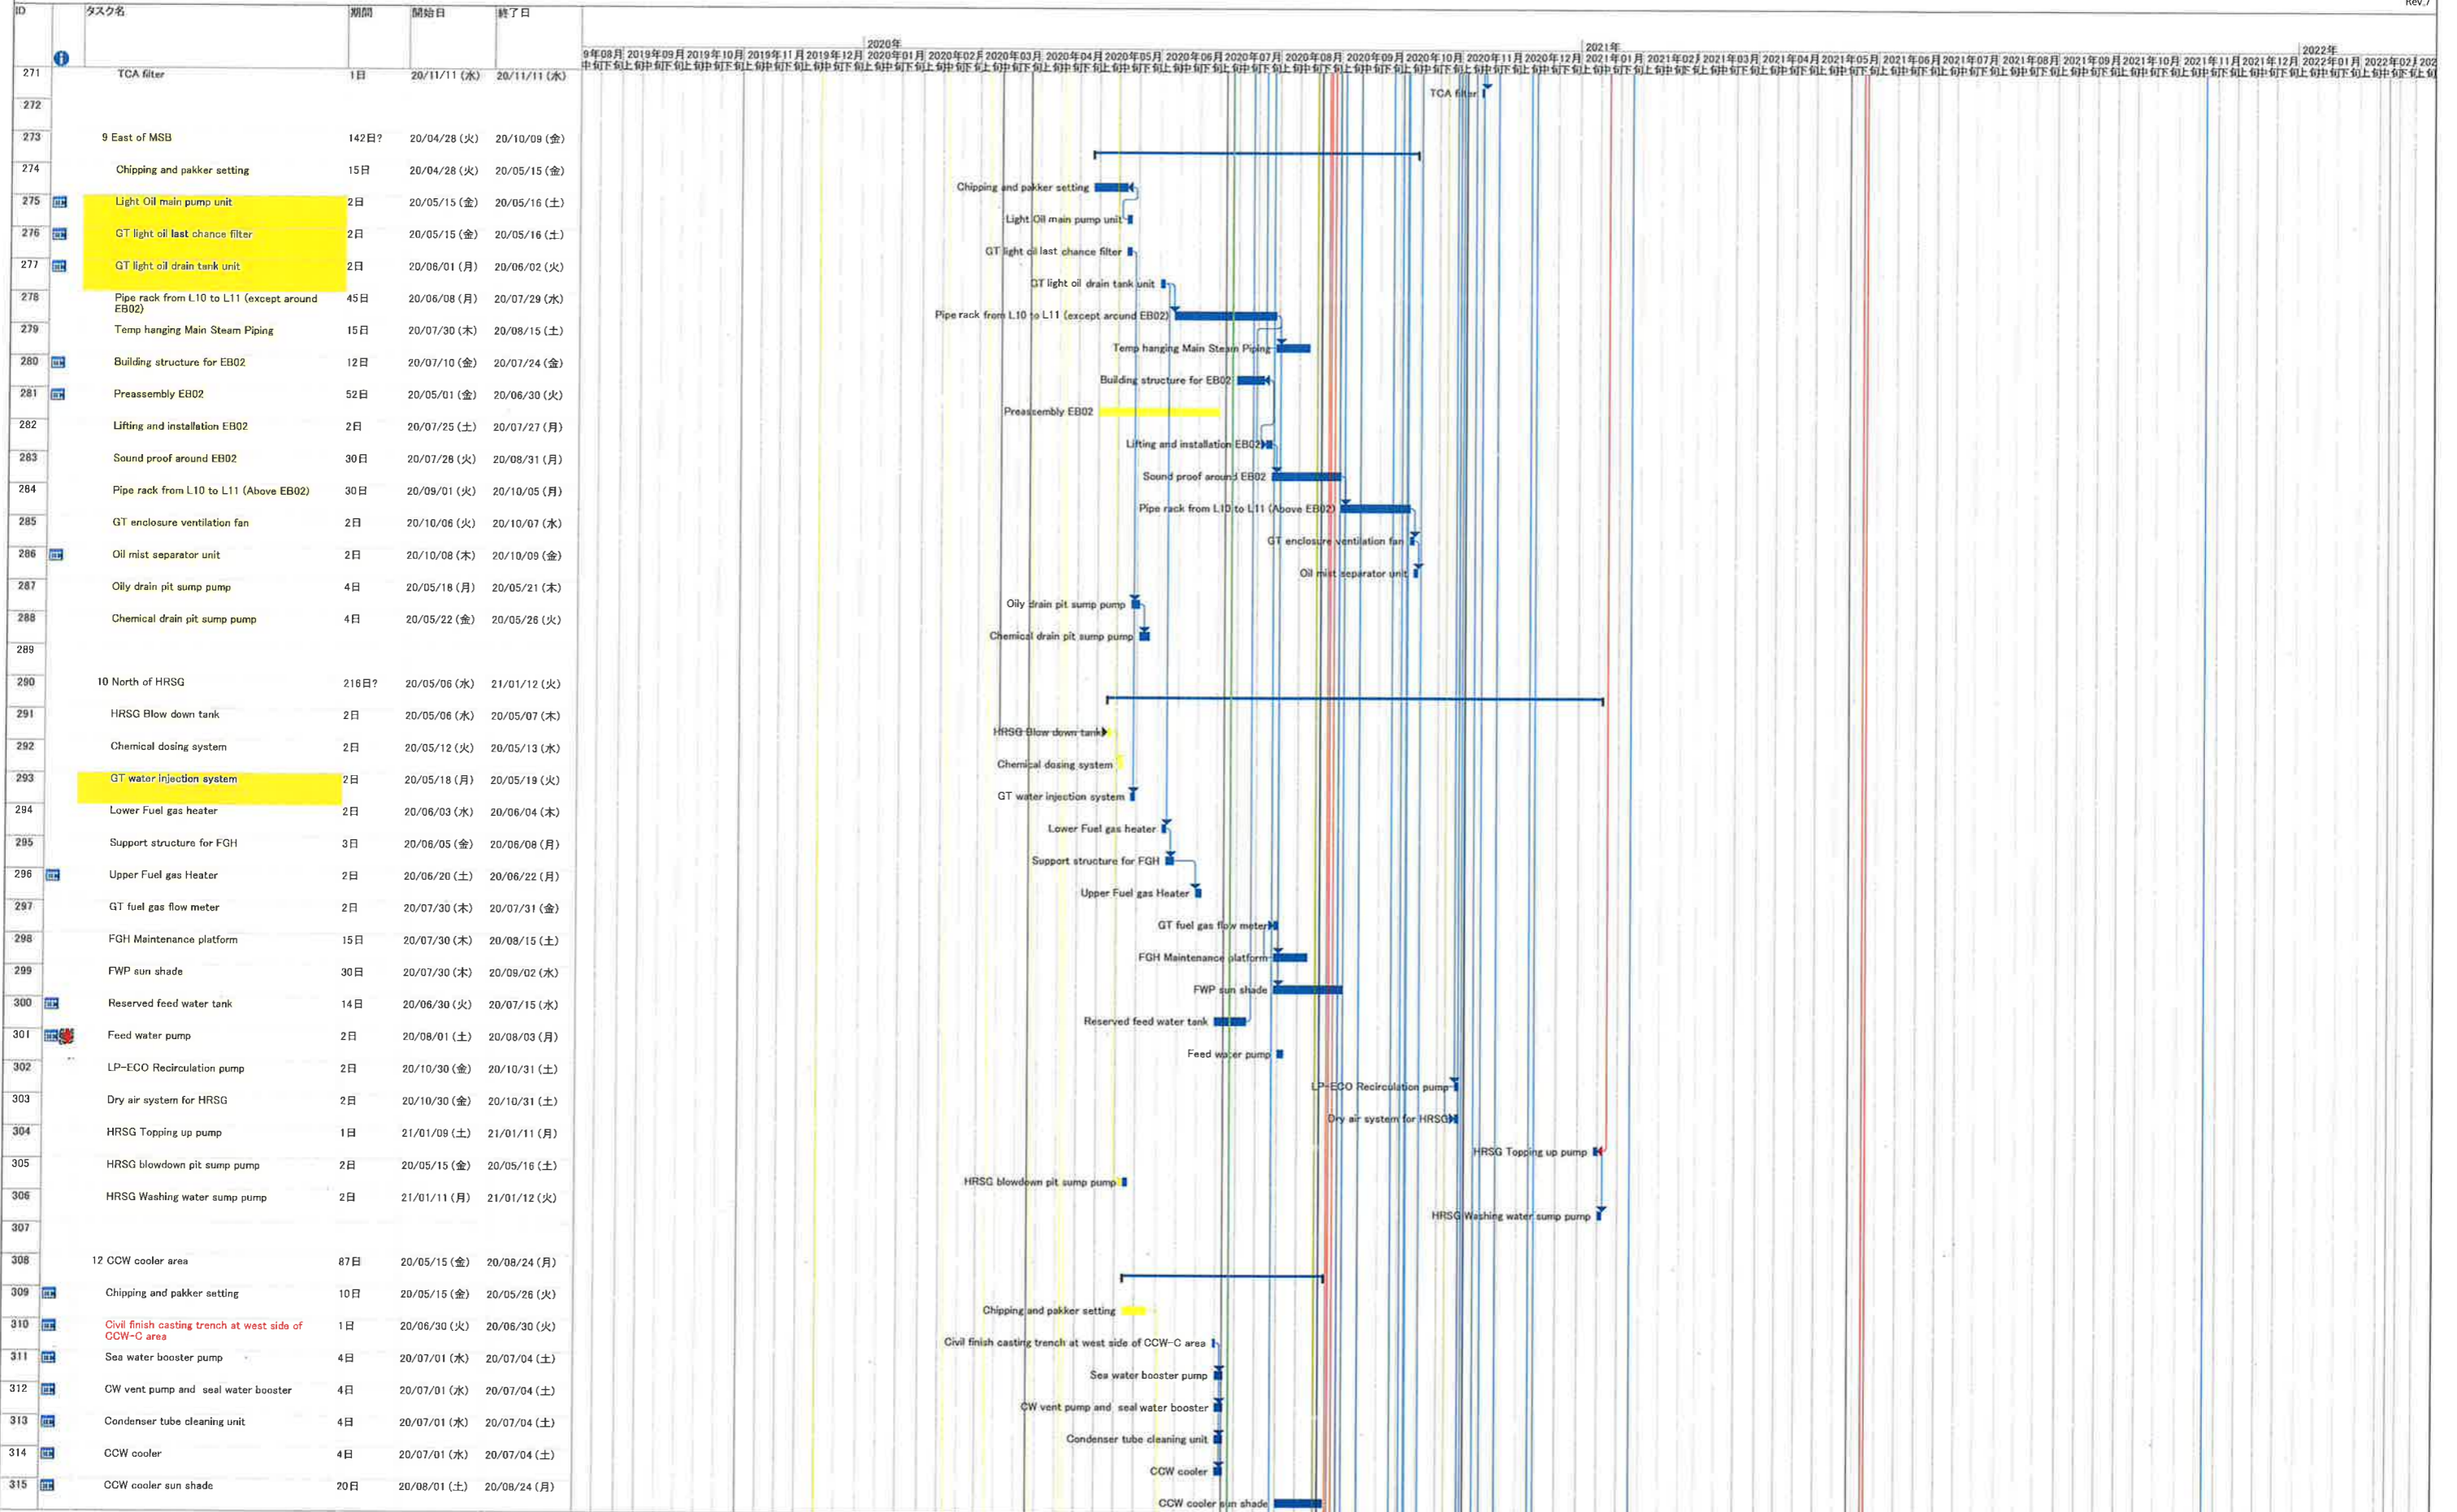


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

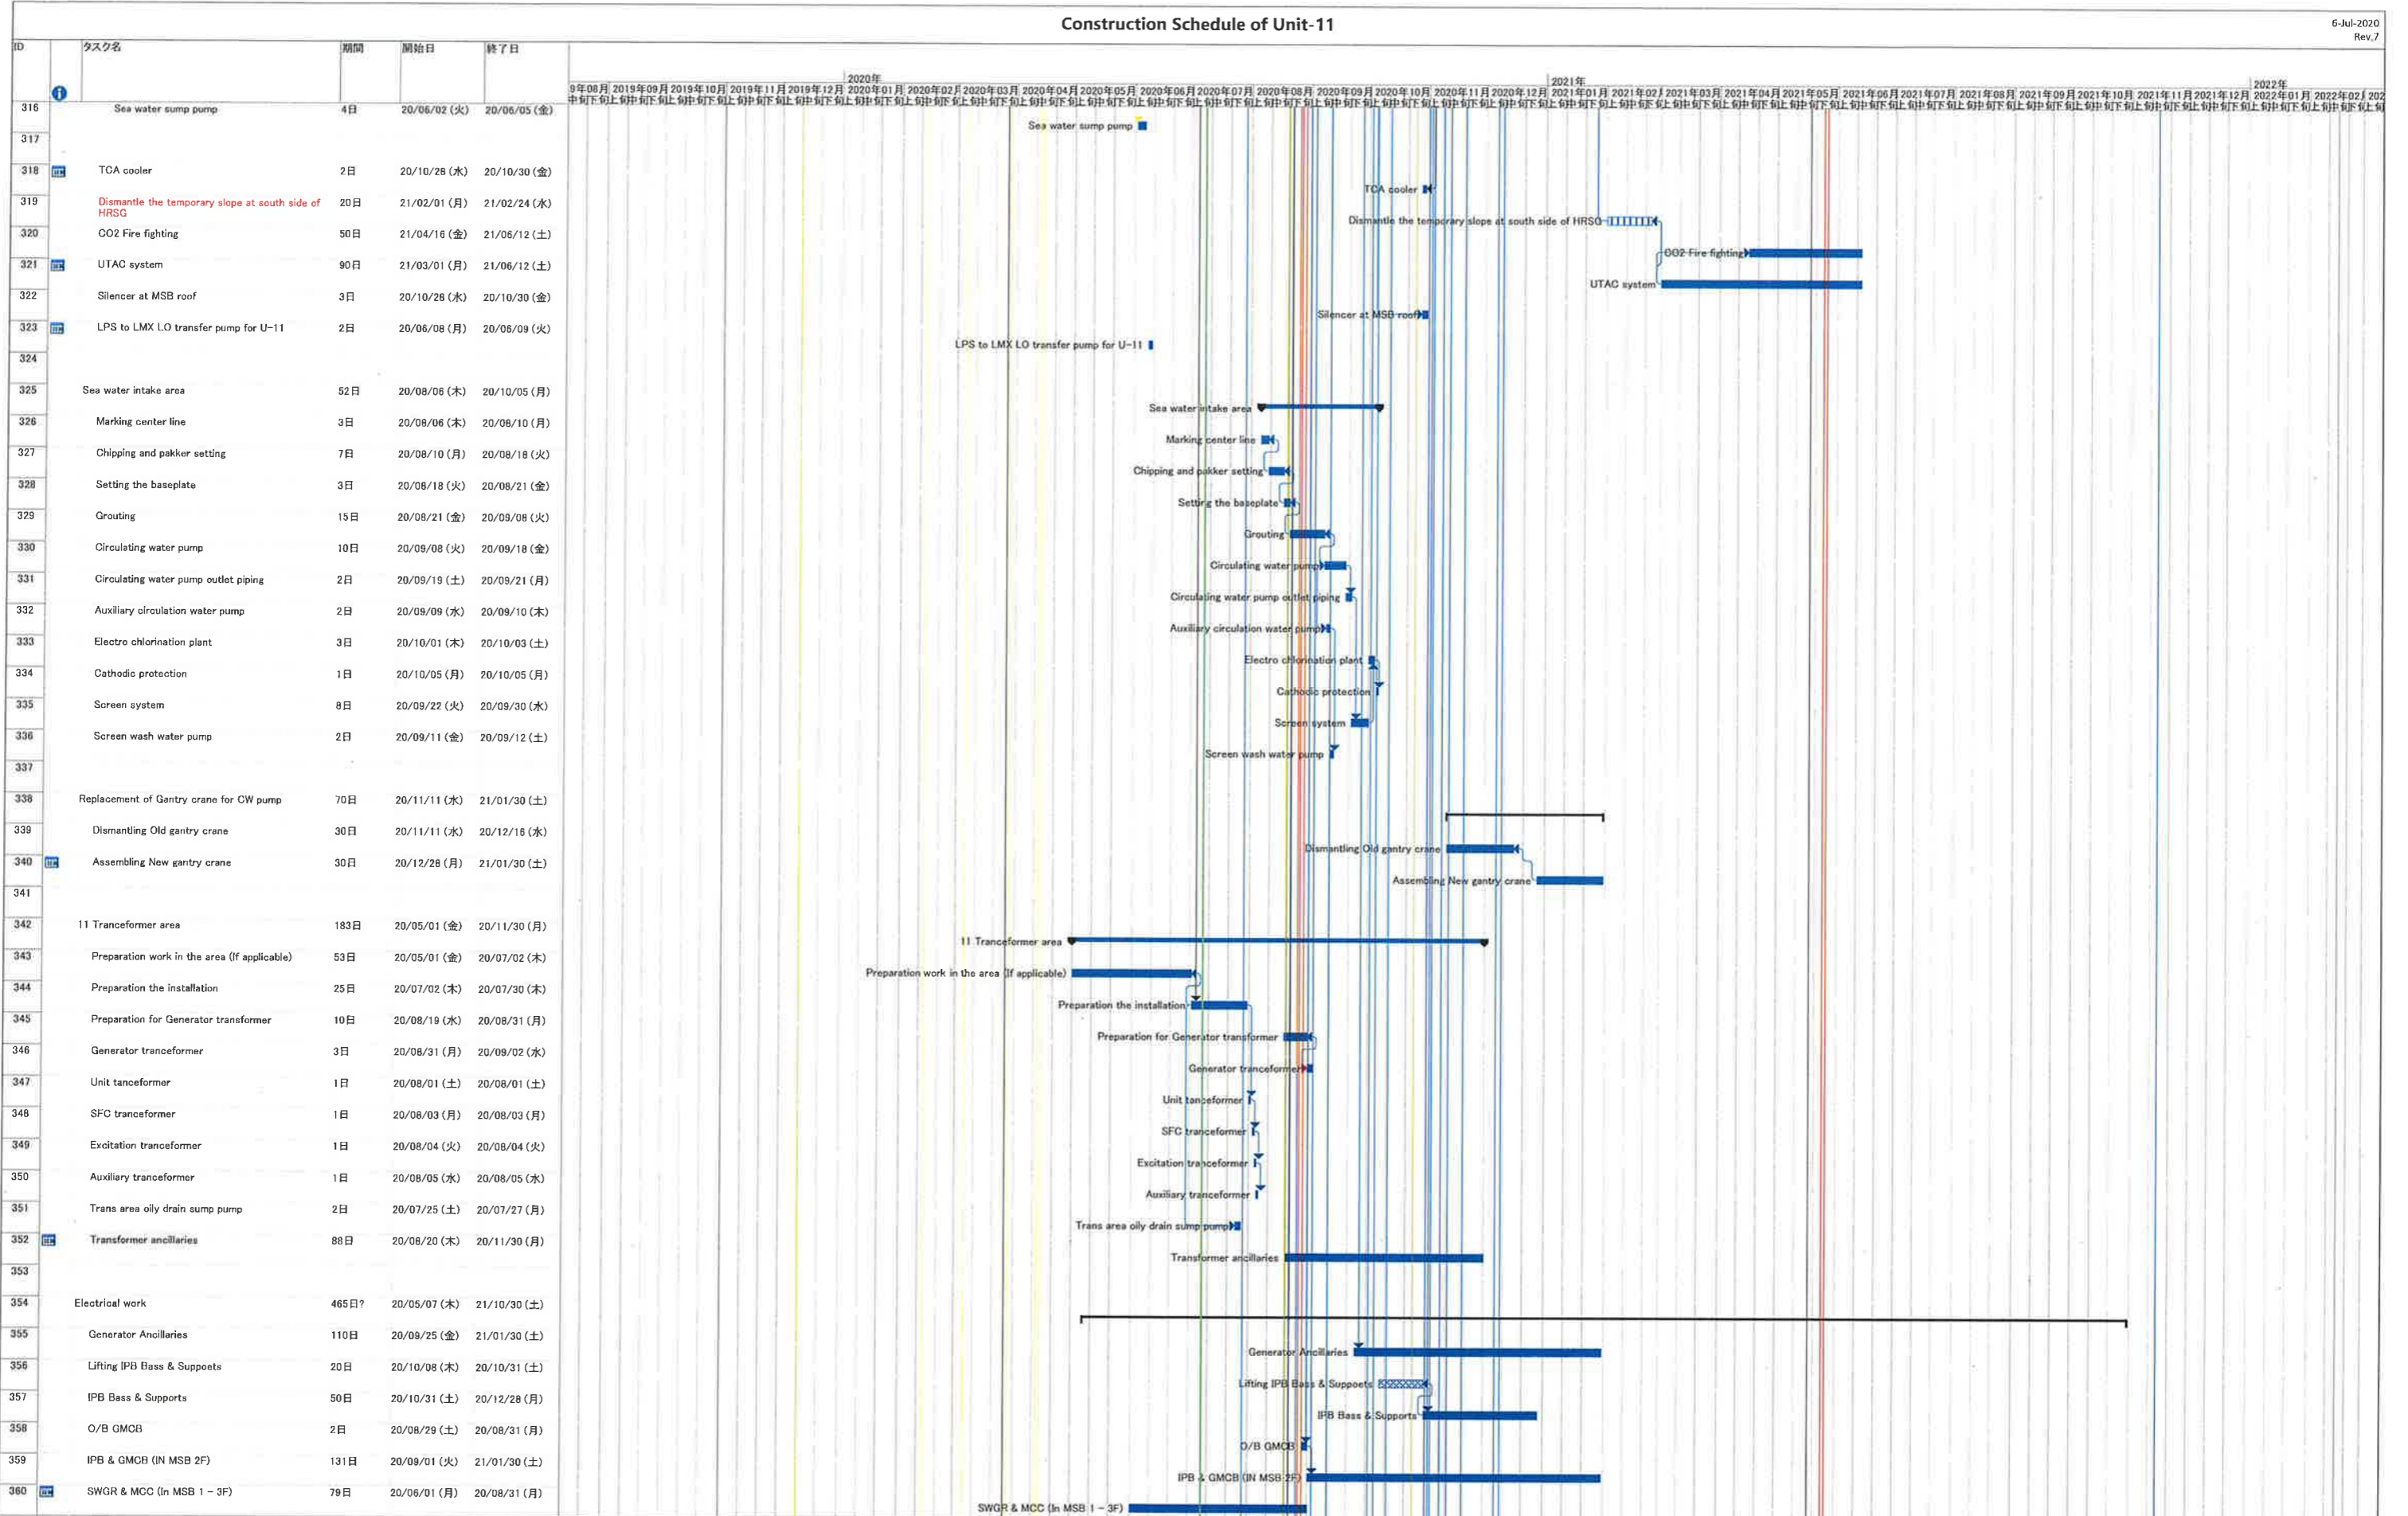


1. Change the starting date of installation below
 ・ Installation HRSG was re-started from 23rd-Jun
 ・ Installation Exhaust duct was re-started from 15st-May
 2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
 5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

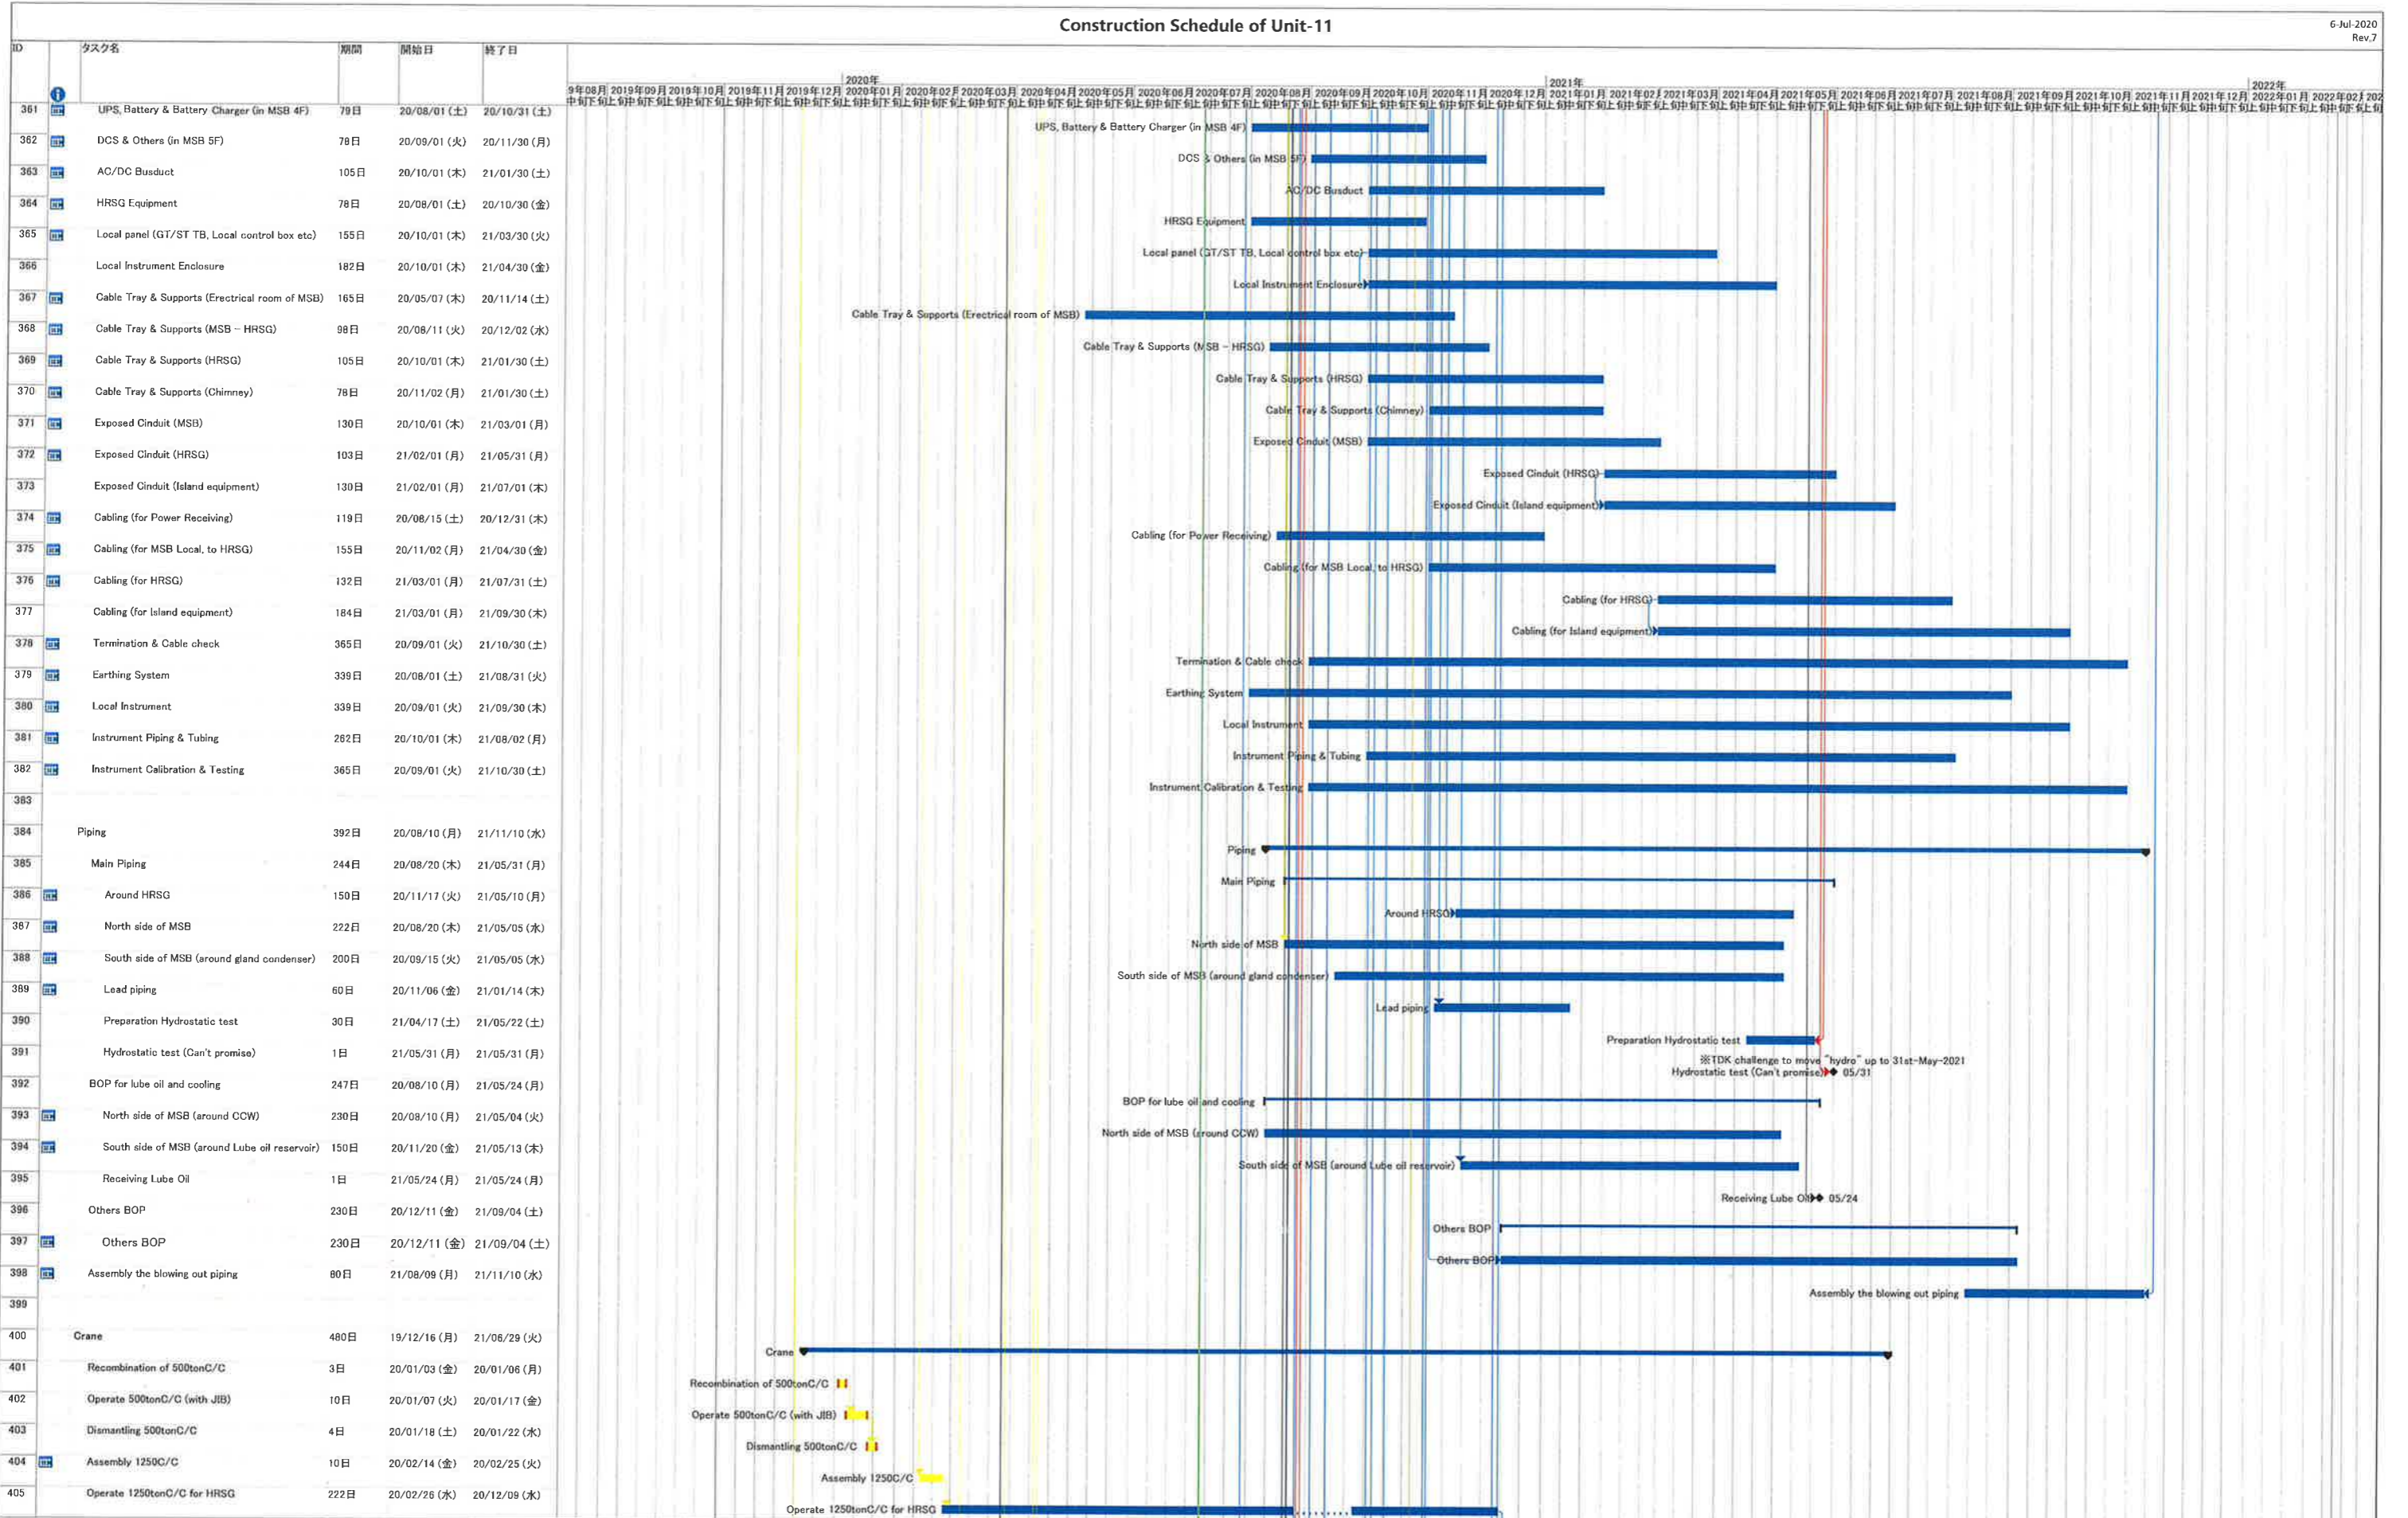


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15th-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

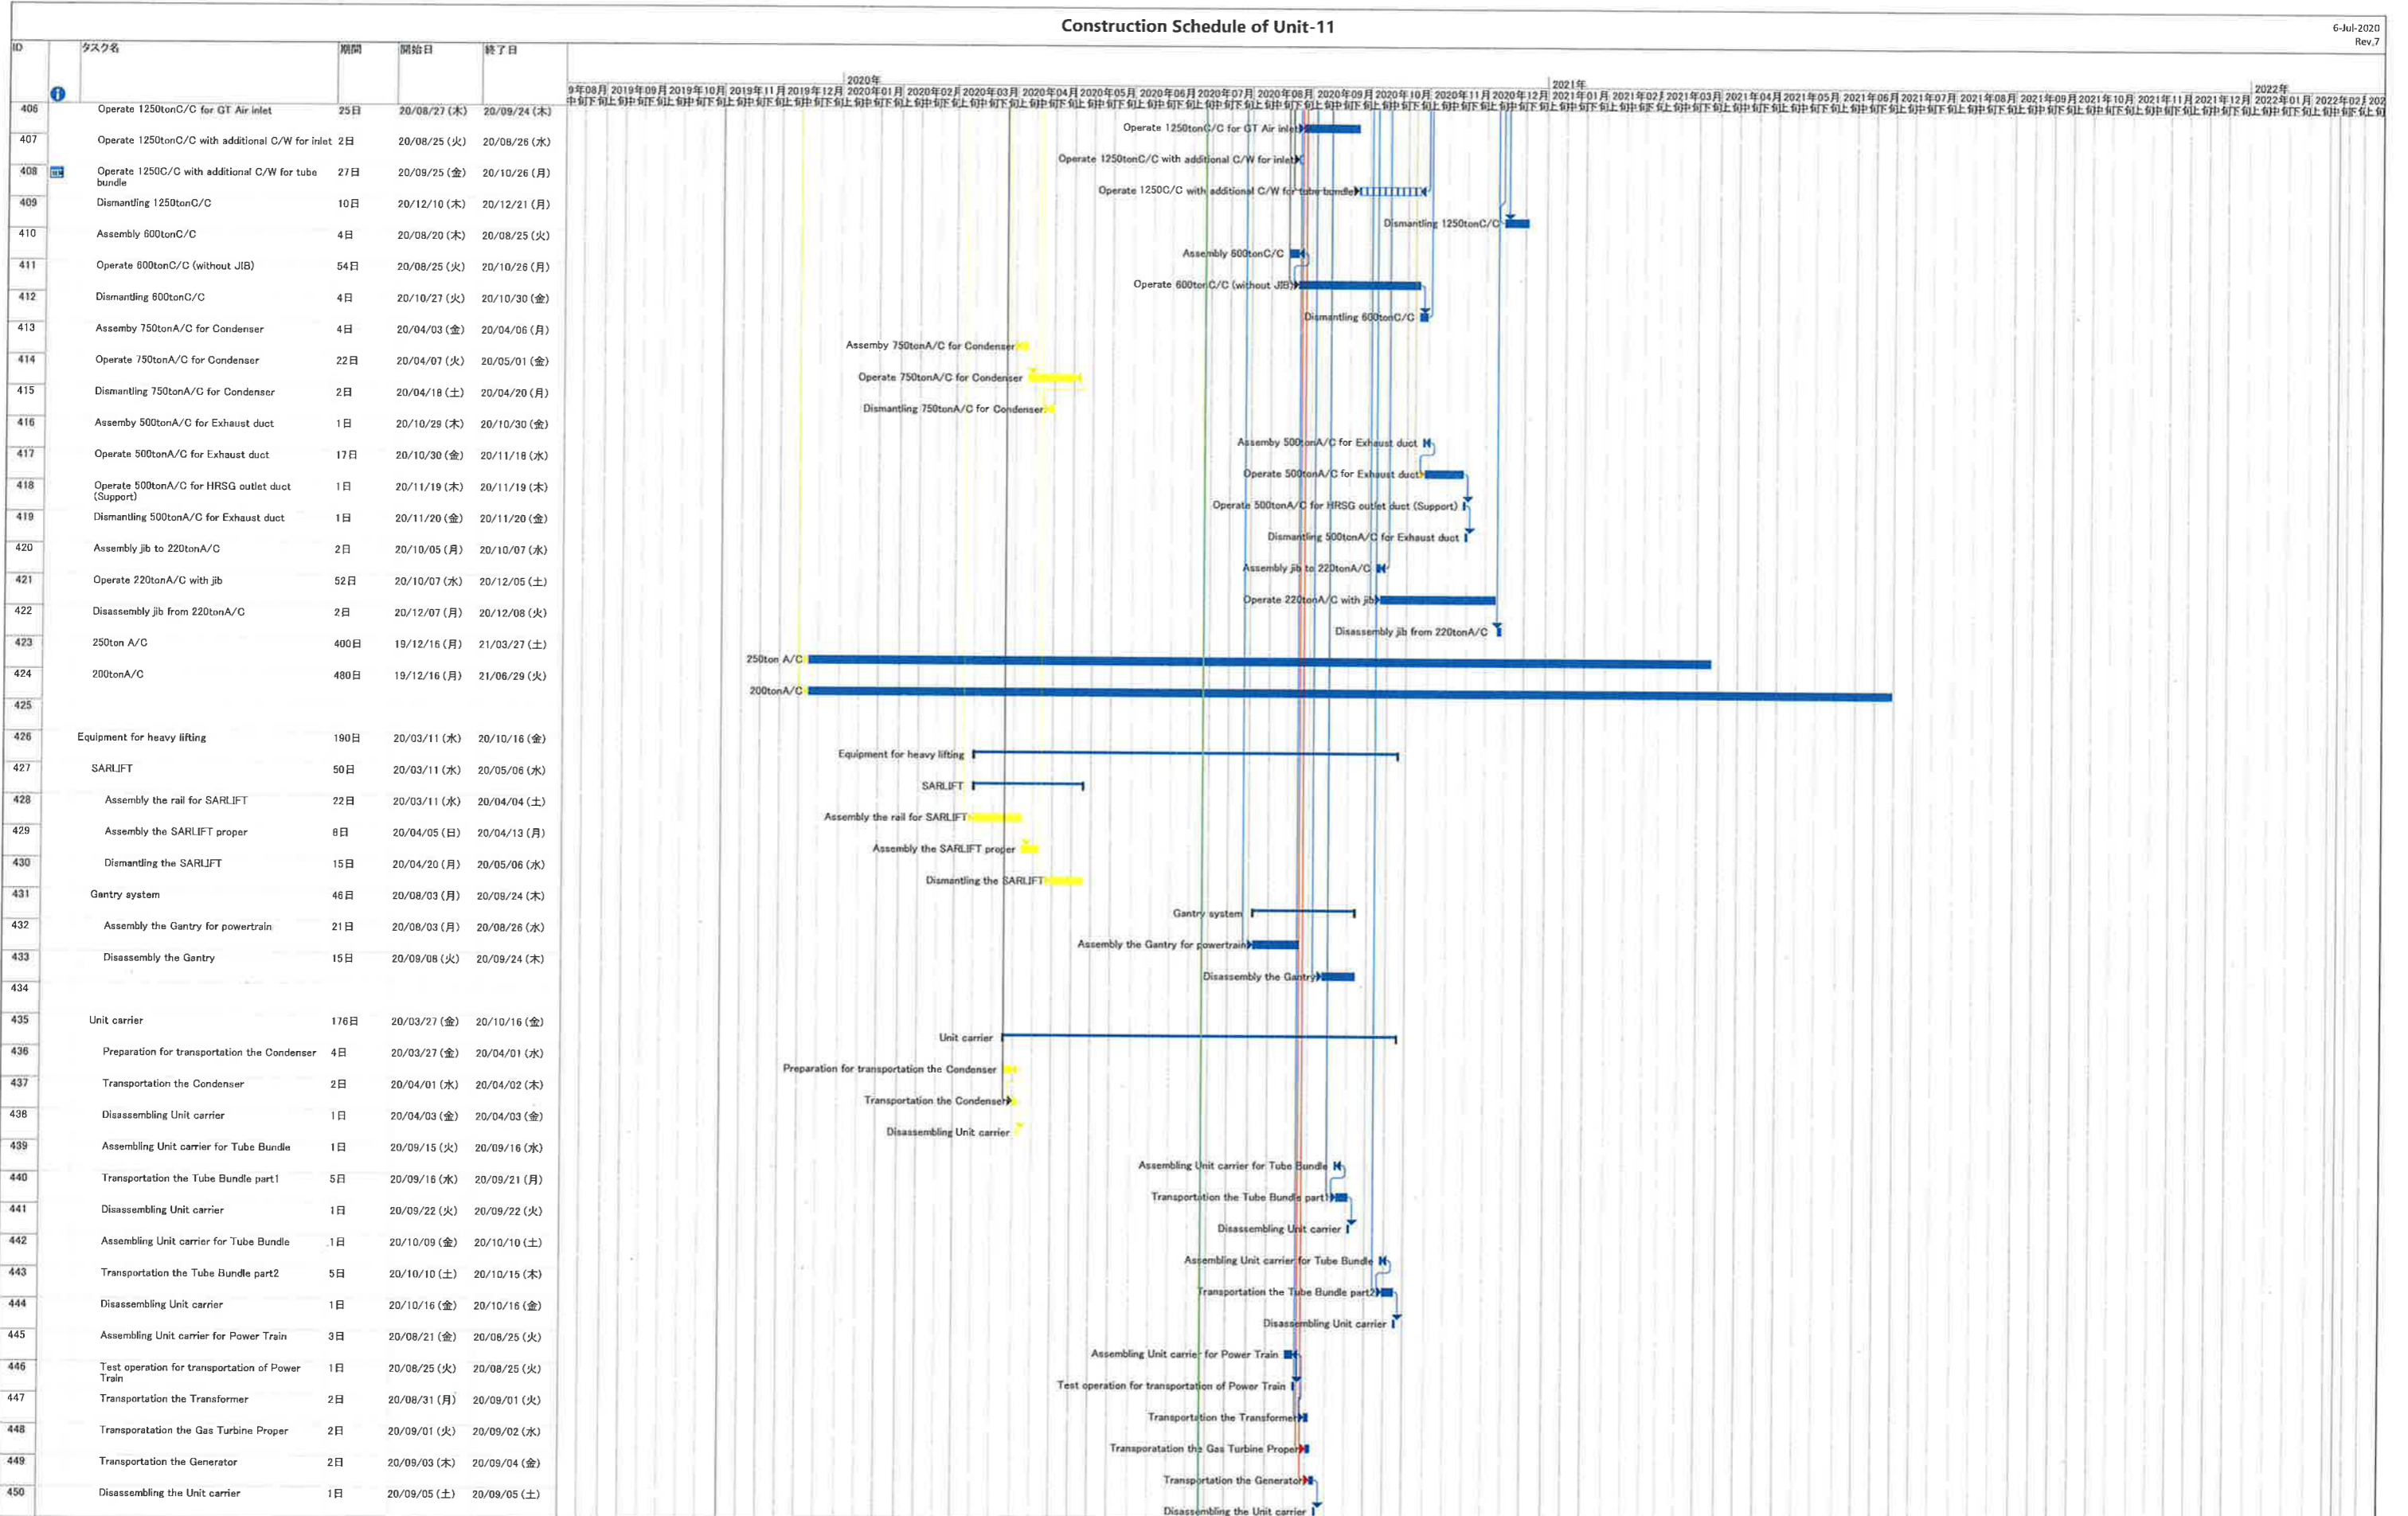

1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12

Master Programme

Table with columns: ID, Task Name, Duration, Start, Finish, Apr, May, Jun, 2022. It lists various construction and completion tasks such as 'KEY DATES & MILESTONES', 'SITE POSSESSION DATES', and 'COMPLETION DATES as per PS1.4.2 Time for Completion'.

MASTER PROGRAMME Rev 1-B 23 Aug 2021 PaulY logo

Task Legend: Split (green bar), Milestone (diamond), Summary (orange bar)

Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12

Master Programme

ID	Task Name	Duration	Start	Finish	Apr	May	Jun	2022
136	Excavation & Construct Pile Caps & Tie Beams & Piers	86 days	Mon 8/3/21	Thu 19/8/21				
137	Installation of Pipe Pile for HRSG foundation (VO)	48 days	Thu 25/3/21	Tue 11/5/21				
138	Construction HRSG & Gas Duct foundations	112 days	Fri 7/5/21	Fri 3/9/21				
139	Construction of HRSG Equipment Room incl. ABWF & BS (except T&C)	64 days	Tue 4/5/21	Thu 30/9/21				
140	Construction underground utilities within HRSG	55 days	Mon 19/7/21	Sat 11/9/21				
141	Backfill & Construction on-grade slabs & RC plinths on top	14 days	Fri 30/7/21	Mon 27/9/21				
142	Backfill and Temporary paving	21 days	Fri 10/9/21	Thu 30/9/21				
143	Section B2 (ii) - Remaining northern part of L12 HRSG area and its surrounding at Area F6A and F6C	319 days	Fri 1/1/21	Mon 15/11/21				
144	Area Possession and Clearance at Area F6A	30 days	Fri 1/1/21	Sat 30/1/21				
145	Subletting / Fabrication / Delivery (for Area F6A and F6C civil)	90 days	Sat 2/1/21	Thu 1/4/21				
146	Construction of Underground pits (HRSG Blowdown sump pit)	110 days	Sat 2/1/21	Wed 21/4/21				
147	Excavation & Construct Pile Caps & Tie Beams & Piers	139 days	Mon 1/2/21	Sat 10/7/21				
148	Construction underground utilities within HRSG	55 days	Mon 19/7/21	Sat 11/9/21				
149	Construction of Underground pits (GT Oil & Chemical drain pits)	15 days	Thu 5/8/21	Thu 19/8/21				
150	Backfill & Construction on-grade slabs & RC plinths on top	45 days	Sun 12/9/21	Tue 26/10/21				
151	Construct RC Walls	90 days	Thu 22/4/21	Tue 20/7/21				
152	Construction of Underground utilities at F6C	21 days	Tue 19/10/21	Mon 8/11/21				
153	Backfill and Temporary paving	7 days	Tue 9/11/21	Mon 15/11/21				
154	Section B2 - (iii) L12 Turbo Block foundation including the L12 MSB ground floor together with the equipment foundations between GL 12-F to 12-H and 12-1 to 12-6 for the installation of power generator, air inlet duct and lube oil reservoir	452 days	Fri 4/12/20	Mon 28/2/22				
155	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21				
156	Subletting / Fabrication / Delivery (Civil+ABWF+BS for MSBL12)	150 days	Fri 25/12/20	Sun 23/5/21				
157	Complete excavation at Type A&C Construction Area	0 days	Sun 21/3/21	Sun 21/3/21				
158	Excavation & Pile Caps & Tie Beams + Slabs (Turbo Block North)	75 days	Sun 31/1/21	Thu 15/4/21				
159	Backfill and construction turbine block & equipment foundation	85 days	Tue 1/6/21	Tue 24/8/21				
160	Excavation & Pile Caps & Tie Beams + Slabs (Turbo Block South)	45 days	Sat 17/4/21	Mon 31/5/21				
161	Construction of internal drainage & on-grade slab	90 days	Wed 1/9/21	Mon 29/11/21				
162	Construction turbine block columns and upper portion for plant embed installation	83 days	Wed 25/8/21	Mon 15/11/21				
163	Concrete Turbine upper part foundation	15 days	Fri 31/12/21	Fri 14/1/22				
164	Construction of Lube Oil Room	14 days	Tue 30/11/21	Fri 28/1/22				
165	Concrete RC walls	115 days	Tue 7/9/21	Thu 30/12/21				
166	ABFW Works	60 days	Thu 4/11/21	Sun 2/1/22				
167	Building Services Works	45 days	Sat 15/1/22	Mon 28/2/22				
168	Remove temporary falsework and scaffolding for installation of power generator	13 days	Mon 7/2/22	Sat 19/2/22				
169	Section B2 - (iv) G/F of L12 MSB including the Condenser Pit, Circulating Water Pipe Pit and equipment foundations between GL 12-B to 12-C and 12-1 to 12-6 for the installation of condenser	377 days	Fri 4/12/20	Wed 15/12/21				
170	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21				
171	Subletting / Fabrication / Delivery (for MSB L12 civil)	150 days	Fri 25/12/20	Sun 23/5/21				
172	Excavation to foundation level at ELS SP Type A & C	80 days	Fri 1/1/21	Sun 21/3/21				
173	Install CW Outlet pipe	85 days	Mon 22/3/21	Mon 14/6/21				
174	Construction of CW Outlet Box + lowest tie beam & caps	40 days	Mon 22/3/21	Fri 30/4/21				
175	Construction of pile caps & tie beams & sump pits up to +2.7mPD	26 days	Sat 1/5/21	Wed 26/5/21				
176	Backfill & Construction of CW Inlet Box + tie beams	71 days	Thu 27/5/21	Thu 5/8/21				
177	Construction of pile caps & tie beams at SunShadeCover Area	45 days	Tue 15/6/21	Thu 29/7/21				
178	Backfill and Construction ground beams & trenches	28 days	Thu 27/5/21	Mon 5/7/21				
179	Construction of indoor underground drainage	14 days	Fri 13/8/21	Thu 26/8/21				
180	Backfill & construction on-grade slabs	60 days	Sun 1/8/21	Wed 29/9/21				
181	Construction Column casting and RC walls & equipment foundations	50 days	Thu 30/9/21	Thu 18/11/21				
182	ABFW Works	15 days	Fri 19/11/21	Fri 3/12/21				
183	Building Services Works	20 days	Fri 26/11/21	Wed 15/12/21				
184	Mis. Works and Ready for condenser move in	25 days	Wed 17/11/21	Wed 15/12/21				
185	Section C - (i) Roads and external grounds surrounding L12 MSB and L12 HRSG in addition to the southern & eastern areas mentioned above in Area F5	408 days	Fri 4/12/20	Sat 15/1/22				
186	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21				
187	Subletting / Fabrication / Delivery	210 days	Fri 25/12/20	Thu 22/7/21				
188	Complete substructure & Steel Erection works for MSB	0 days	Tue 17/8/21	Tue 17/8/21				
189	Construction all utilities deeper than 2m from future road level	30 days	Wed 18/8/21	Thu 16/9/21				
190	Construction of cable trenches	30 days	Fri 17/9/21	Sat 16/10/21				
191	Backfill and lay temporary paving	91 days	Sun 17/10/21	Sat 15/1/22				
192	Section C - (ii) Whole of L12 MSB including the pipe and cable rack along south façade of L12 MSB with all underground utilities at Area F4 including C.W. Inlet and Outlet Culvert except the deferred works	483 days	Fri 4/12/20	Thu 31/3/22				
193	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21				
194	Subletting / Fabrication / Delivery	120 days	Fri 25/12/20	Fri 23/4/21				
195	Construction of pile caps & tie beams at Transformer Area	180 days	Sun 31/1/21	Thu 29/7/21				
196	Backfill and on-grade slab at transformer Area	160 days	Sun 11/4/21	Thu 7/10/21				
197	Construction of Fire Walls at Transformer Area	45 days	Fri 8/10/21	Sun 21/11/21				
198	Excavation & Construction Blow Down Sum pit (SP Type B)	140 days	Wed 14/4/21	Tue 31/8/21				
199	Preparation for S.Steelwork Erection	7 days	Sat 5/6/21	Fri 11/6/21				
200	Structural Delivery & Erection (Turbine Hall North fr G.L. 1-3/H->B)	67 days	Sat 12/6/21	Tue 17/8/21				
201	Structural Delivery & Erection (Equipment Floors)	33 days	Wed 18/8/21	Sun 19/9/21				
202	Structural Delivery & Erection (Turbine Hall South + East Elevation)	47 days	Mon 20/9/21	Mon 15/11/21				
203	Joint Tightening and touch up coating	99 days	Sat 3/7/21	Wed 24/11/21				
204	External Scaffolding Erection	97 days	Thu 15/7/21	Mon 22/11/21				
205	Construction 1/F RC Slab	14 days	Mon 20/9/21	Sun 3/10/21				
206	Construction 2/F RC Slab	7 days	Mon 27/9/21	Sun 10/10/21				
207	Construction 3/F RC Slab	18 days	Thu 30/9/21	Sun 17/10/21				
208	Construction 4/F RC Slab	7 days	Thu 7/10/21	Sun 24/10/21				
209	Construction 5/F RC Slab	44 days	Mon 25/10/21	Tue 7/12/21				
210	Construction 6/F RC Slab	14 days	Wed 1/12/21	Tue 14/12/21				
211	Construction Upper Roof RC Slab	10 days	Sun 12/12/21	Fri 24/12/21				
212	Construction Main Roof RC Slab	39 days	Tue 12/10/21	Fri 19/11/21				
213	Construction Defer Roof RC Slab (G.L. G-H)	14 days	Wed 1/12/21	Tue 14/12/21				
214	Construction of Staircase ST-01 & lift shaft & machine room	130 days	Fri 27/8/21	Mon 3/1/22				
215	Construction M/F RC Slab	14 days	Wed 1/9/21	Tue 14/9/21				
216	Lift Installation	60 days	Tue 4/1/22	Fri 4/3/22				
217	Construction of Staircase ST-02 except defer work	68 days	Mon 11/10/21	Fri 24/12/21				
218	Construction of RC plinth, kerbs & parapet Walls	40 days	Sat 20/11/21	Wed 29/12/21				
219	Erection of Skylight & Roof Features	50 days	Fri 26/11/21	Fri 14/1/22				
220	Waterproofing & Flooring at Roof	34 days	Thu 30/12/21	Thu 17/2/22				
221	ABFW Works	100 days	Fri 8/10/21	Sat 15/1/22				
222	Building Services Works	105 days	Tue 16/11/21	Mon 28/2/22				
223	Metal Cladding, Windows and Louvres incl. roof feature	185 days	Mon 23/8/21	Wed 23/2/22				
224	Removal of external scaffolding	90 days	Wed 1/12/21	Mon 28/2/22				
225	Installation of Catwalk at south elevation	26 days	Mon 31/1/22	Tue 1/3/22				
226	Cladding, ABWF & BS Works	30 days	Wed 2/3/22	Thu 31/3/22				
227	Removal of temporary works & clearance for plant erection contractor	30 days	Sun 30/1/22	Mon 28/2/22				
228	Section C - (iii) Link Bridge between L11 and L12 MSB including their associated A&A at L11 MSB	493 days	Fri 4/12/20	Sun 10/4/22				
229	BD Consent	0 days	Fri 4/12/20	Fri 4/12/20				
230	Subletting / Fabrication / Delivery (For BS and ABWF)	250 days	Fri 25/12/20	Tue 31/8/21				
231	Clearing Works and plant set-up	30 days	Fri 3/12/21	Sat 1/1/22				
232	Dismantle of north scaffold for link bridge erection	0 days	Tue 25/1/22	Tue 25/1/22				
233	A&A works at South of L11 MSB	30 days	Fri 3/12/21	Sat 1/1/22				
234	Erection of link bridge structural steel	30 days	Sun 2/1/22	Mon 31/1/22				
235	Casting of bridge deck	11 days	Tue 1/2/22	Fri 11/2/22				
236	Metal roofing installation	24 days	Sat 12/2/22	Mon 7/3/22				
237	ABWF work	30 days	Sun 20/2/22	Mon 21/3/22				
238	BS Works	20 days	Tue 22/3/22	Sun 10/4/22				
239	Ready for power cable laying work by others	0 days	Sun 10/4/22	Sun 10/4/22				
240	Section D - (ii) No. 5 Chimney with L12 Steel Flue Liner	810 days	Fri 1/1/21	Tue 21/3/23				
241	Area Possession & Clearance	45 days	Fri 1/1/21	Sun 14/2/21				
242	Subletting / Fabrication / Delivery (For Civil and BS for Microwave Antenna and Equipment)	120 days	Fri 8/1/21	Fri 7/5/21				
243	Excavation & Pile Cap & Backfill	90 days	Sat 2/1/21	Thu 1/4/21				
244	Tower Crane erection	30 days	Tue 11/5/21	Wed 9/6/21				
245	Construction of Wind Shiled + clearance for internal floors and flue+Ground slab	308 days	Fri 2/4/21	Mon 4/4/22				
246	Structural steel fabrication & Delivery for floors and staircase	201 days	Mon 3/1/22	Fri 22/7/22				
247	Erection of steel floors	79 days	Tue 19/4/22	Wed 6/7/22				
248	Construction of G/F room incl. Microwave Antenna Rm	45 days	Thu 7/7/22	Sat 20/8/22				
249	Construction of 1/F RC slab	8 days	Sat 13/8/22	Sat 20/8/22				
250	Construction of 2/F RC Slab	8 days	Fri 5/8/22	Fri 12/8/22				
251	Construction of 3/F RC slab	8 days	Thu 28/7/22	Thu 4/8/22				
252	Construction of 4/F RC slab	8 days	Thu 7/7/22	Thu 14/7/22				
253	Construction of Roof RC slab	61 days	Tue 21/6/22	Sat 20/8/22				
254	Removal of tower Crane	7 days	Sun 21/8/22	Sat 27/8/22				
255	Steel Flue fabrication and delivery	145 days	Sat 5/3/22	Wed 27/7/22				
256	Set up for steel flue installation	60 days	Tue 5/7/22	Fri 2/9/22				
257	Lift & install steel flue liner + cladding works	161 days	Thu 28/7/22	Wed 4/1/23				
258	Lift installation	100 days	Mon 12/12/22	Tue 21/3/23				
259	Installation Louvre & Doors	30 days	Thu 5/1/23	Fri 3/2/23				
260	Mis works, Demobilization and ready for gas duct connection	17 days	Thu 5/1/23	Sat 21/1/23				
261	Section D (i) - ABWF and BS Works at Microwave Antenna Room and Chimney Windshield for installation of microwave and antenna	102 days	Tue 1/3/22	Fri 10/6/22				
262	Completion of Microwave Antenna Room	0 days	Tue 1/3/22	Tue 1/3/22				
263	Remaining ABWF & BS Works	100 days	Thu 3/3/22	Fri 10/6/22				
264	Section E - (i) Administration and Control Building (Transformer Room)	332 days	Fri 4/12/20	Sun 31/10/21				
265	Area Possession & Clearance + BD consent	60 days	Fri 4/12/20					

Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12


Master Programme

ID	Task Name	Duration	Start	Finish	Apr	May	Jun
281	Construction of RC up to R/F incl. staircases	25 days	Thu 30/9/21	Sun 24/10/21			
282	Construction of RC up to lift machine room	21 days	Mon 25/10/21	Sun 14/11/21			
283	Construction of RC up to UR/F	21 days	Mon 15/11/21	Sun 5/12/21			
284	External Wall Finish, Cladding + Windows and Louvres + Features	138 days	Thu 30/9/21	Mon 14/2/22			
285	ABWF at 1/F	95 days	Fri 8/10/21	Mon 10/1/22			
286	ABWF at 2/F	96 days	Fri 15/10/21	Tue 18/1/22			
287	Building Services Works at G/F, 1/F, 2/F & Hoisting Well	147 days	Tue 5/10/21	Mon 28/2/22			
288	Section E (iii) Whole of Administration and Control Building	544 days	Fri 4/12/20	Tue 31/5/22			
289	Subletting / Fabrication / Delivery (For BS+ABWF)	127 days	Sat 23/10/21	Sun 20/3/22			
290	Construction of New UG Grey Water Tank	60 days	Mon 20/3/23	Thu 18/5/23			
291	Submission of WW046 for commencement	60 days	Wed 19/1/22	Sat 19/3/22			
292	ABWF at 3/F	120 days	Mon 25/10/21	Mon 21/2/22			
293	ABWF at 4/F	90 days	Wed 24/11/21	Mon 21/2/22			
294	ABWF at R/F	60 days	Wed 15/12/21	Sat 12/2/22			
295	ABWF at UR/F + Lift Machine Room	45 days	Wed 5/1/22	Fri 18/2/22			
296	Bridge Erection & Connection	28 days	Mon 7/2/22	Mon 28/3/22			
297	Installation of Raised floors	60 days	Fri 7/1/22	Fri 29/4/22			
298	Removal of external scaffolding	39 days	Mon 24/1/22	Wed 9/3/22			
299	Waterproofing & screeding	60 days	Mon 6/12/21	Thu 3/2/22			
300	Removal of Tower Crane	7 days	Thu 10/3/22	Wed 16/3/22			
301	External utilities and road work	45 days	Tue 8/2/22	Thu 14/4/22			
302	Building Services Works	160 days	Tue 7/12/21	Sun 15/5/22			
303	False ceiling after BS works	54 days	Tue 29/3/22	Sat 21/5/22			
304	Submission of WW046 for completion	30 days	Thu 9/3/22	Thu 7/4/22			
305	Submission of FS inspection	14 days	Fri 13/5/22	Thu 26/5/22			
306	Submission for OP Inspection	14 days	Wed 18/5/22	Tue 31/5/22			
307	Section F (i) - Gas Receiving Station and L12 Gas Receiving Station Equipment Room (GRS) Area Extension at Area F14	548 days	Tue 1/6/21	Wed 30/11/22			
308	Area Possession & Clearance + BD consent	90 days	Tue 1/6/21	Sun 29/8/21			
309	Subletting / Fabrication / Delivery	30 days	Tue 22/6/21	Wed 21/7/21			
310	Installation of pipe pile at north of GRS (VO)	134 days	Mon 5/7/21	Mon 15/11/21			
311	Construction Equipment room extension	145 days	Sun 31/10/21	Thu 24/3/22			
312	Modification of existing drainage	45 days	Fri 25/3/22	Sun 8/5/22			
313	Excavation & earthing for Skid foundations	21 days	Mon 9/5/22	Sun 29/5/22			
314	Construction of Skid foundation	45 days	Mon 30/5/22	Wed 13/7/22			
315	Construct underground utilities and drainage	45 days	Thu 14/7/22	Sat 27/8/22			
316	Backfill and road works	60 days	Sun 28/8/22	Wed 26/10/22			
317	Relocate / install new fencing for completion	21 days	Thu 27/10/22	Wed 16/11/22			
318	Mis. Work and ready for OP inspection	14 days	Thu 17/11/22	Wed 30/11/22			
319	Section F (ii) - Pipe and Cable rack and external work at Area F9A and F9B	515 days	Sat 2/1/21	Tue 31/5/22			
320	BD consent + Site Possession at Area F9A & F9B	90 days	Sat 2/1/21	Thu 1/4/21			
321	Excavation & Plate load test	30 days	Mon 1/11/21	Tue 30/11/21			
322	Construction new footing for pipe rack	30 days	Wed 1/12/21	Thu 30/12/21			
323	Underground utilities and road works for completion	11 days	Thu 31/3/22	Tue 31/5/22			
324	Structural Steel fabrication & Delivery	90 days	Sat 2/10/21	Thu 30/12/21			
325	Erection of new pipe rack	70 days	Fri 31/12/21	Thu 10/3/22			
326	Mis. Work and ready for OP inspection	21 days	Wed 11/5/22	Tue 31/5/22			
327	Section F (iii) - No. 5 CW Equipment Room, pipe and cable rack, external works at Area F10	457 days	Tue 1/6/21	Wed 31/8/22			
328	Area Possession & Clearance + BD consent	90 days	Tue 1/6/21	Sun 29/8/21			
329	Subletting / Fabrication / Delivery For ABWF + BS	150 days	Wed 2/6/21	Fri 29/10/21			
330	Installation of Sheet Pile (VO)	85 days	Tue 1/6/21	Tue 24/8/21			
331	Consent for ELS Works	28 days	Wed 25/8/21	Tue 21/9/21			
332	Excavation & Plate load test	30 days	Wed 22/9/21	Thu 21/10/21			
333	Construction new footing for equipment room	68 days	Thu 23/12/21	Mon 28/2/22			
334	Superstructure for equipment room	60 days	Tue 1/3/22	Fri 29/4/22			
335	ABWF Works	45 days	Sat 30/4/22	Mon 13/6/22			
336	BS Works	30 days	Wed 1/6/22	Thu 30/6/22			
337	Construction RC Wall & plinths & drainage at Chlorinator area	45 days	Wed 30/3/22	Fri 13/5/22			
338	External wall finish & remove scaffolding	30 days	Sat 14/5/22	Sun 12/6/22			
339	Excavation & Plate load test for pipe rack extension (For F45-47 & F49)	30 days	Sat 16/10/21	Sun 14/11/21			
340	Construction new footing for pipe rack (For F45-47 & F49)	45 days	Mon 15/11/21	Wed 29/12/21			
341	Underground utilities and road works for completion	60 days	Thu 30/12/21	Sun 27/2/22			
342	Structural Steel fabrication & Delivery	90 days	Sun 12/12/21	Fri 11/3/22			
343	Backfilling and prepare for steel erection	12 days	Mon 28/2/22	Fri 11/3/22			
344	Excavation & Plate Load test for pipe rack extension (For F48 F56)	14 days	Wed 30/3/22	Tue 12/4/22			
345	Construction of new footing for pipe rak (For F48 & F56)	14 days	Wed 13/4/22	Tue 26/4/22			
346	Erection of new pipe rack (For F48 & F56)	65 days	Tue 3/5/22	Wed 6/7/22			
347	Erection of new pipe rack (For F45-47 & F49)	70 days	Sat 12/3/22	Fri 20/5/22			
348	Mis. Work and ready for OP inspection	56 days	Thu 7/7/22	Wed 31/8/22			
349	Section G (i) - External Work surrounding Area F11	145 days	Sat 4/6/22	Wed 26/10/22			
350	Area Possession & Clearance after handover from No. 5 Intake Contractor	30 days	Sat 4/6/22	Sun 3/7/22			
351	Subletting / Fabrication / Delivery	30 days	Sat 4/6/22	Sun 3/7/22			
352	Submission WW0046 for commencement	30 days	Sat 4/6/22	Sun 3/7/22			
353	Construct Underground utilities and drainage	30 days	Mon 20/6/22	Tue 19/7/22			
354	Install new FS Hydrant	20 days	Mon 20/6/22	Sat 9/7/22			
355	Submission WW0046 for completion	30 days	Sat 30/7/22	Sun 28/8/22			
356	Construction Road extension	58 days	Sat 30/7/22	Sun 25/9/22			
357	Construction road paving and install fencing	30 days	Mon 26/9/22	Tue 25/10/22			
358	Ready for OP inspection	14 days	Thu 13/10/22	Wed 26/10/22			
359	Section G (ii) - External Works at Area F12 & F13	666 days	Fri 4/12/20	Fri 30/9/22			
360	Area Possession & Clearance after handover from other	45 days	Fri 4/12/20	Sun 17/1/21			
361	Subletting / Fabrication / Delivery	180 days	Thu 4/3/21	Mon 30/8/21			
362	Excavation	21 days	Sat 23/10/21	Fri 12/11/21			
363	Submission WW0046 for commencement	30 days	Sat 13/11/21	Sun 12/12/21			
364	Construct Underground utilities and drainage	90 days	Mon 13/12/21	Sat 12/3/22			
365	Install new FS Hydrant	30 days	Sun 13/3/22	Mon 11/4/22			
366	Submission WW0046 for completion	30 days	Tue 12/4/22	Wed 11/5/22			
367	Construction Road extension	127 days	Thu 12/5/22	Thu 15/9/22			
368	Complete with Mis. Works for completion	15 days	Fri 16/9/22	Fri 30/9/22			
369	Section G (iii) - FS Modification works along South Seafront Road at Area F15	183 days	Fri 1/4/22	Fri 30/9/22			
370	Area Possession & Clearance after handover from other	45 days	Fri 1/4/22	Sun 15/5/22			
371	Subletting / Fabrication / Delivery	21 days	Fri 1/4/22	Thu 21/4/22			
372	Temporary Traffic Arrangement approval	14 days	Fri 1/4/22	Thu 14/4/22			
373	Utilities scanning and expose existing FS	14 days	Fri 15/4/22	Thu 28/4/22			
374	Determine new FS alignment	21 days	Fri 29/4/22	Thu 19/5/22			
375	Submission to FSD	14 days	Fri 20/5/22	Thu 2/6/22			
376	Modification of FS	60 days	Fri 3/6/22	Mon 1/8/22			
377	Backfill and reinstatement + report to FSD	60 days	Tue 2/8/22	Fri 30/9/22			
378	Section G (iv) - 275kV cable trenches and External Works at Area F16	518 days	Sat 1/5/21	Fri 30/9/22			
379	Area Possession & Clearance	60 days	Sat 1/5/21	Tue 29/6/21			
380	Subletting / Fabrication / Delivery	210 days	Wed 17/11/21	Tue 14/6/22			
381	Temporary Traffic Arrangement approval	60 days	Sat 1/5/21	Tue 29/6/21			
382	Removal of aboveground services	60 days	Wed 30/6/21	Sat 28/8/21			
383	Utilities scanning and expose existing UU	30 days	Sun 29/8/21	Mon 27/9/21			
384	Arrange of diversion existing UG utilities	90 days	Tue 29/9/21	Sun 26/12/21			
385	Construct new cable trenches	173 days	Mon 27/12/21	Fri 17/6/22			
386	Realignment / install new UG utilities	60 days	Sat 18/6/22	Tue 16/8/22			
387	Backfill and reinstatement + ready for cable laying by others	45 days	Wed 17/8/22	Fri 30/9/22			
388	Section G (v) - Shunt Reactor Compound and External Works at Area F17	666 days	Fri 4/12/20	Fri 30/9/22			
389	Temporary Traffic Arrangement approval	45 days	Fri 4/12/20	Sun 17/1/21			
390	Subletting / Fabrication / Delivery	100 days	Fri 25/12/20	Sat 3/4/21			
391	BD approval & consent for pipe pile installation	90 days	Fri 4/12/20	Wed 3/3/21			
392	Area Possession & Clearance	14 days	Thu 4/3/21	Wed 17/3/21			
393	Removal of aboveground services	21 days	Thu 18/3/21	Wed 7/4/21			
394	Utilities scanning and expose existing UU	15 days	Thu 8/4/21	Thu 22/4/21			
395	Arrange of diversion existing UG utilities	45 days	Fri 23/4/21	Sun 6/6/21			
396	Install pipe piles	61 days	Sun 23/5/21	Thu 22/7/21			
397	BA14 for pipepile and BD consent for ELS	28 days	Fri 23/7/21	Thu 19/8/21			
398	Excavation & install earthing	35 days	Fri 20/8/21	Thu 23/9/21			
399	Construct Pile Caps and Tie Beams	45 days	Fri 24/9/21	Sun 7/11/21			
400	Backfill & Erect scaffold	21 days	Mon 8/11/21	Sun 28/11/21			
401	Construction of SRC Walls	75 days	Mon 29/11/21	Fri 11/2/22			
402	Wall finish and remove scaffolding	24 days	Sat 12/2/22	Mon 7/3/22			
403	Construct new cable trenches	60 days	Tue 8/3/22	Fri 6/5/22			
404	Install new UG Utilities, Backfill and reinstatement + ready for cable laying by Others for DAX1	55 days	Thu 7/4/22	Tue 31/5/22			
405	Realignment / install new UG utilities (for DAX2, APX1 & APX3)	117 days	Sat 7/5/22	Wed 31/8/22			
406	Backfill and reinstatement + ready for cable laying by others (for DAX2, APX1, & APX3)	30 days	Thu 1/9/22	Fri 30/9/22			
407	Section G (vi) - 275kV cable trenches and External Works at Area F18	397 days	Sat 1/5/21	Wed 1/6/22			
408	Temporary Traffic Arrangement approval	45 days	Sat 1/5/21	Mon 14/6/21			
409	Subletting / Fabrication / Delivery	60 days	Tue 15/6/21	Fri 13/8/21			
410	Area Possession & Clearance	15 days	Sat 1/5/21	Sat 15/5/21			
411	Removal of aboveground services	30 days	Sun 16/5/21	Mon 14/6/21			
412	Utilities scanning and expose existing UU	45 days	Tue 15/6/21	Thu 29/7/21			
413	Arrange of diversion existing UG utilities	60 days	Fri 30/7/21	Mon 27/9/21			
414	Construct new cable trenches	172 days	Tue 28/9/21	Fri 18/3/22			
415	Realignment / install new UG utilities	45 days	Sat 19/3/22	Mon 25/2/22			
416	Backfill and reinstatement + ready for cable laying by others	30 days	Tue 3/5/22	Wed 1/6/22			
417	Section G (vii) - Flood wall at No. 5 CW Intake Area along HUA at Area F20A	521 days	Fri 4/12/20	Sun 8/5/22			
418	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21			
419	Subletting / Fabrication / Delivery	60 days	Fri 25/12/20	Mon 22/2/21			
420	Temporary Traffic Arrangement approval	300 days	Fri 4/12/20	Wed 29/9/21			
421	ELS BD approval & consent</						

Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12

Master Programme


ID	Task Name	Duration	Start	Finish	Apr	May	Jun	2022
435	Demolition of existing carriageway	60 days	Fri 1/10/21	Mon 29/11/21				
436	Removal of aboveground services	21 days	Tue 30/11/21	Mon 20/12/21				
437	Utilities scanning and expose existing UU	21 days	Tue 21/12/21	Mon 10/1/22				
438	Arrange of diversion existing UG utilities	30 days	Tue 1/1/22	Wed 9/2/22				
439	Install Sheetpiles	55 days	Thu 10/2/22	Tue 5/4/22	Install Sheetpiles			
440	BA14 for sheetpile and BD consent for ELS	28 days	Wed 6/4/22	Tue 3/5/22		BA14 for sheetpile and BD consent for ELS		
441	Excavation and construction of new Flood wall	90 days	Wed 4/5/22	Mon 1/8/22				
442	Realignment / install new UG utilities	30 days	Tue 2/8/22	Wed 31/8/22				
443	Backfill and construct new carriageway	21 days	Thu 1/9/22	Wed 21/9/22				
444	Mis. Work for completion	9 days	Thu 22/9/22	Fri 30/9/22				
445	Section G (ix) - Bund wall modification works at South Seafront Road at Area F21	316 days	Fri 4/12/20	Fri 15/10/21				
446	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21				
447	Subletting / Fabrication / Delivery	90 days	Fri 25/12/20	Wed 24/3/21				
448	Temporary Traffic Arrangement approval	165 days	Fri 4/12/20	Mon 17/5/21				
449	ELS BD approval & consent	0 days	Thu 17/12/20	Thu 17/12/20				
450	Demolition of existing carriageway	14 days	Tue 18/5/21	Mon 31/5/21				
451	Removal of aboveground services	14 days	Tue 1/6/21	Mon 14/6/21				
452	Utilities scanning and expose existing UU	21 days	Tue 15/6/21	Mon 5/7/21				
453	Arrange of diversion existing UG utilities (include FS pipe under 17/8002)	40 days	Tue 6/7/21	Sat 14/8/21				
454	Excavation and expose existing bund wall & demolish	18 days	Wed 28/7/21	Sat 14/8/21				
455	Construction new bund wall for road junction	21 days	Sat 4/9/21	Fri 24/9/21				
456	Realignment / install new UG utilities (include FS pipe under 17/8002)	60 days	Sun 1/8/21	Wed 29/9/21				
457	Backfill and construct new carriageway	16 days	Thu 30/9/21	Fri 15/10/21				
458	Mis. Work for completion	5 days	Mon 11/10/21	Fri 15/10/21				
459	Section G (x) - DAX Cable Diversion Works (from Part I to Part IV)	758 days	Fri 4/12/20	Sat 31/12/22				
460	Temporary Traffic Arrangement approval	14 days	Fri 4/12/20	Thu 17/12/20				
461	Subletting / Fabrication / Delivery	90 days	Fri 25/12/20	Wed 24/3/21				
462	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21				
463	Identification of existing cable trench	7 days	Mon 18/1/21	Sun 24/1/21				
464	Part 1 Re-excavation works incl.construction of joint bay (at Water Reservoir Road)	246 days	Mon 25/1/21	Mon 27/9/21				
465	Part 1 Re-excavation works incl construction of joint bay (other than Reservoir road base on revised routing)	310 days	Mon 25/1/21	Tue 30/11/21				
466	Part 2 Re-excavation works incl. joint bay	120 days	Mon 1/11/21	Mon 28/2/22				
467	Part 3 Re-excavation works incl. joint bay	242 days	Mon 1/11/21	Thu 30/6/22				
468	Part 4 Re-excavation works incl. joint bay & new oil tank pits	92 days	Sat 1/10/22	Sat 31/12/22				
469	Backfill & Reinstatement Part 1	61 days	Mon 1/11/21	Fri 31/12/21				
470	Backfill & Reinstatement Part 2	61 days	Sun 1/5/22	Thu 30/6/22				
471	Backfill & Reinstatement Part 3	61 days	Thu 1/9/22	Mon 31/10/22				
472	Section H - All remaining works shall be completed for reporting completion to BD and ready for OP inspection (PS1.4.4)	775 days	Wed 17/11/21	Sun 31/12/23				
473	Deferred works (MSB & HRS) Listed in PS 1.4.4	272 days	Wed 17/11/21	Mon 15/8/22				
474	Construction of L12 MSB roof between GL12-G to 12-H and 12-2 to 12-6 after the overhead crane installation by the Employer's Specialist Contractors	38 days	Wed 17/11/21	Fri 7/1/22				
475	Construction of walls of L12 MSB below 1/F along GL 12-6 from GL12-B to 12-C and the associated staircases including the enclosure walls between G/F and 1/F. The Contractor shall allow access for the Employer's Specialist Contractors to use the hoisting we	92 days	Mon 16/5/22	Mon 15/8/22				
476	Provision in associated with hoisting well	21 days	Mon 6/6/22	Sun 26/6/22				
477	Construction of internal partition wall at 1/F of L12 MSB along GL 12-C from GL 12-2 to 12-3 AND North Façade at 1/F of L12 MSB along GL 12-1 from GL 12-B to 12-C	30 days	Sat 16/4/22	Sun 15/5/22				
478	Construction of metal fence and the associated Fire Services (F.S.) installations and installation of removable shelter at Transformer Area	92 days	Mon 16/5/22	Mon 15/8/22				
479	Deferred works (DAX1 and DAX2) Listed in PS 1.4.4	334 days	Wed 1/2/23	Sun 31/12/23				
480	Backfilling of whole DAX1 compartment inside existing joint bay "STJ12" and the new oil tank pit A located aside existing joint bay "STJ12".	59 days	Wed 1/2/23	Fri 31/3/23				
481	Re-excavation of whole DAX2 compartment inside existing joint bay "STJ12".	61 days	Tue 1/8/23	Sat 30/9/23				
482	Backfilling of whole DAX2 compartment inside existing joint bay "STJ12" and the new oil tank pit B located aside existing joint bay "STJ12".	61 days	Wed 1/11/23	Sun 31/12/23				
483	Deferred works (External Work) Listed in PS 1.4.4	121 days	Thu 1/12/22	Fri 31/3/23				
484	Final reinstatement of access roads and pavement surrounding and within L12 MSB and L12 HRS area	62 days	Thu 1/12/22	Tue 31/1/23				
485	Installation of trench cover and road reinstatement of gas pipe and cable trenches within Area F5, F14, F16, F17 and F18.	90 days	Sun 1/1/23	Fri 31/3/23				
486	Backfilling and road-reinstatement of 275kV cable trenches	90 days	Sun 1/1/23	Fri 31/3/23				
487	All Remaining work ready for OP inspection	0 days	Tue 28/2/23	Tue 28/2/23				
488	STATUTORY SUBMISSION, INSPECTION & APPROVAL	560 days	Tue 16/11/21	Mon 29/5/23				
489	WSD Statutory Submission, Inspection and Approval WWO Part I to III Submission / Approval	256 days	Tue 16/11/21	Fri 29/7/22				
490	WSD: Submit to WSD Form WWO 046 Part I to II - FOR ACB Building (for Ext Works at later stage)	0 days	Tue 16/11/21	Tue 16/11/21				
491	WSD: Vetting Form WWO 046 Part I and II Submission	90 days	Wed 17/11/21	Mon 14/2/22				
492	WSD: Issued of Form WWO 046 Part III by WSD - FOR ACB Building	0 days	Tue 15/2/22	Tue 15/2/22				
493	WSD: Prepare for 1st Amendment for Plumbing Plan	60 days	Tue 15/2/22	Fri 15/4/22				
494	WSD: Submit to WSD 1st Amendment for Plumbing Plan	0 days	Fri 15/4/22	Fri 15/4/22				
495	WSD: Vetting of Plumbing Plan by WSD	60 days	Sat 16/4/22	Tue 14/6/22				
496	WSD: 1st Approval for Plumbing Plan by WSD	0 days	Tue 14/6/22	Tue 14/6/22				
497	WSD: Prepare and Submit for Final Amendment for Plumbing Plan	45 days	Wed 15/6/22	Fri 29/7/22				
498	WSD: Vetting and Final Approval for Plumbing Plan by WSD	0 days	Fri 29/7/22	Fri 29/7/22				
499	WSD Statutory Submission, Inspection and Approval WWO Part IV to V Fire Services Water Submission / Approval	33 days	Fri 29/7/22	Wed 31/8/22				
500	WSD: Form WWO 046 Part IV Submission (FS)	0 days	Fri 29/7/22	Fri 29/7/22				
501	WSD: WSD Received Form WWO046 Part IV and arrange for inspection (FS)	7 days	Sat 30/7/22	Fri 5/8/22				
502	WSD: WSD Inspection (FS)	7 days	Sat 6/8/22	Fri 12/8/22				
503	WSD: WWO 046 Part V Endorsement by WSD (FS)	12 days	Sat 13/8/22	Wed 24/8/22				
504	WSD: WSD Processing Water Supply Connection Certificate (FS)	7 days	Thu 25/8/22	Wed 31/8/22				
505	WSD: Issue by WSD Water Supply Connection Certificate (FS)	0 days?	Wed 31/8/22	Wed 31/8/22				
506	WSD Statutory Submission, Inspection and Approval WWO Part IV to V Potable /Flush Water Submission / Approval	60 days	Fri 19/8/22	Tue 18/10/22				
507	WSD: Form WWO 046 Part IV Submission (Fresh/Flush)	0 days	Fri 19/8/22	Fri 19/8/22				
508	WSD: WSD Acknowledge Form WWO 046	6 days	Sat 20/8/22	Thu 25/8/22				
509	WSD: WSD Inspection with Testing to lead (Fresh/Fluhs)	12 days	Fri 26/8/22	Tue 6/9/22				
510	WSD: Cleansing/Disinfecting Water Tanks / Piping System (Fresh/Flush)	6 days	Wed 7/9/22	Mon 12/9/22				
511	WSD: Collection of Sample for Testing at Accredited Lab (Fresh/Flush)	12 days	Tue 13/9/22	Sat 24/9/22				
512	WSD: Accredited Lab Testing Report of Sample to WSD	12 days	Sun 25/9/22	Thu 6/10/22				
513	WSD: Vetting of Test Report by WSD	6 days	Fri 7/10/22	Wed 12/10/22				
514	WSD: Issue of WWO 046 Part V (Fresh/Flush)	0 days	Wed 12/10/22	Wed 12/10/22				
515	WSD: WSD Processing WWO1005 Water Certification (Fresh/Flush)	6 days	Thu 13/10/22	Tue 18/10/22				
516	WSD: Issue by WSD WWO 1005 Water Certification (Fresh/Flush)	0 days	Tue 18/10/22	Tue 18/10/22				
517	EMSD LIFT Statutory Submission, Inspection and Approval	45 days	Sat 26/3/22	Mon 9/5/22				
518	EMSD: Submission of Lift Form LE5 to EMSD	12 days	Sat 26/3/22	Wed 6/4/22				
519	EMSD: EMSD Makes arrangement for Lift Installation	5 days	Thu 7/4/22	Mon 11/4/22				
520	EMSD: EMSD Inspection to Lift Installation	14 days	Tue 12/4/22	Mon 25/4/22				
521	EMSD: Processing Lift Certificate (Form LE6)	14 days	Tue 26/4/22	Mon 9/5/22				
522	EMSD: Lift Issuance of Form 6 (Lift Certificate)	0 days	Mon 9/5/22	Mon 9/5/22				
523	HKE Transformer Final Inspection	120 days	Thu 30/6/22	Thu 27/10/22				
524	TX Room: Invite HKE For Transformer Room Inspection	7 days	Thu 30/6/22	Wed 6/7/22				
525	TX Room: Give Access to Transformer Room for HKE Contractor	0 days	Wed 6/7/22	Wed 6/7/22				
526	TX Room: Move-IN HKE Transformer Equipments	5 days	Thu 7/7/22	Mon 11/7/22				
527	TX Room: Install HKE Transformer, MEP Works & Testing	90 days	Tue 12/7/22	Sun 9/10/22				
528	TX Room: HKE Power Energization / Inspection	6 days	Mon 10/10/22	Sat 15/10/22				
529	TX Room: Metering Installation	12 days	Sun 16/10/22	Thu 27/10/22				
530	TX Room: HKE Power-ON Date	0 days	Thu 27/10/22	Thu 27/10/22				
531	DSD Drainage Completion Memo	65 days	Sun 2/10/22	Mon 5/12/22				
532	DSD: CCTV Survey Report on Completed Drainage	30 days	Sun 2/10/22	Mon 31/10/22				
533	DSD: Submitted CCTV Report & Form HPB1 of Completed Drainage to DSD For Technical Audit	7 days	Tue 1/11/22	Mon 7/11/22				
534	DSD: Completed Drainage System including TMC Inspection/Technical Audit by DSD	14 days	Tue 8/11/22	Mon 21/11/22				
535	DSD: Preparation of Drainage Connection Completion Memo by DSD	14 days	Tue 22/11/22	Mon 5/12/22				
536	DSD: Issue of Drainage Connection Completion Memo by DSD	0 days	Mon 5/12/22	Mon 5/12/22				
537	EPD Submission, Inspection and Approval	60 days	Thu 30/6/22	Mon 29/8/22				
538	EPD: License Application to EPD under APCO (Cap 311) for Generator Sets	0 days	Thu 30/6/22	Thu 30/6/22				
539	EPD: Vetting of Application by EPD under APCO (Cap 311) for Generator Sets	60 days	Fri 1/7/22	Mon 29/8/22				
540	EPD: Approval from EPD under APCO (Cap 311) for Generator Sets Installation	0 days	Mon 29/8/22	Mon 29/8/22				
541	FSD VAC Statutory Submission, Inspection and Approval	150 days	Wed 20/7/22	Fri 16/12/22				
542	Preparation of FSD VAC Drawings and Submission to HEC	60 days	Wed 20/7/22	Sat 17/9/22				
543	HEC: Review and Approval	30 days	Sun 18/9/22	Mon 17/10/22				
544	Preparation of VAC Drawings and Submission to FSD	30 days	Tue 18/10/22	Wed 16/11/22				
545	FSD: Review and Approval	30 days	Thu 17/11/22	Fri 16/12/22				
546	FSD Statutory Submission, Inspection and Approval	91 days	Tue 28/2/23	Mon 29/5/23				
547	Testing and Commissioning (Individual System - FSI Related)	45 days	Tue 28/2/23	Thu 13/4/23				
548	FSD: All Sections FS Ingration Test by NSC BS	15 days	Fri 14/4/23	Fri 28/4/23				
549	FSD: Completion of FS Integration Test by NSC BS for FS314/501	0 days	Fri 28/4/23	Fri 28/4/23				
550	FSD: Submit Form 213/314 & Form 501 Request for Inspection	0 days	Fri 28/4/23	Fri 28/4/23				
551	FSD: FSD Makes Arrangement for Inspection	7 days	Sat 29/4/23	Fri 5/5/23				
552	FSD: FSD Inspection	12 days	Sat 6/5/23	Wed 17/5/23				
553	FSD: Completion of FS Inspection	0 days	Wed 17/5/23	Wed 17/5/23				
554	FSD: FSD Processing FS Certificate Form 172	12 days	Thu 18/5/23	Mon 29/5/23				
555	FSD: Issue of Fire Services FS Certificate Form 172	0 days	Mon 29/5/23	Mon 29/5/23				
556	PRACTICAL COMPLETION	216 days	Tue 30/5/23	Sun 31/12/23				
557	BD Inspection	97 days	Tue 30/5/23	Sun 3/9/23				
558	BD: Application Form BA13 for OP Application	21 days	Tue 30/5/23	Mon 19/6/23				

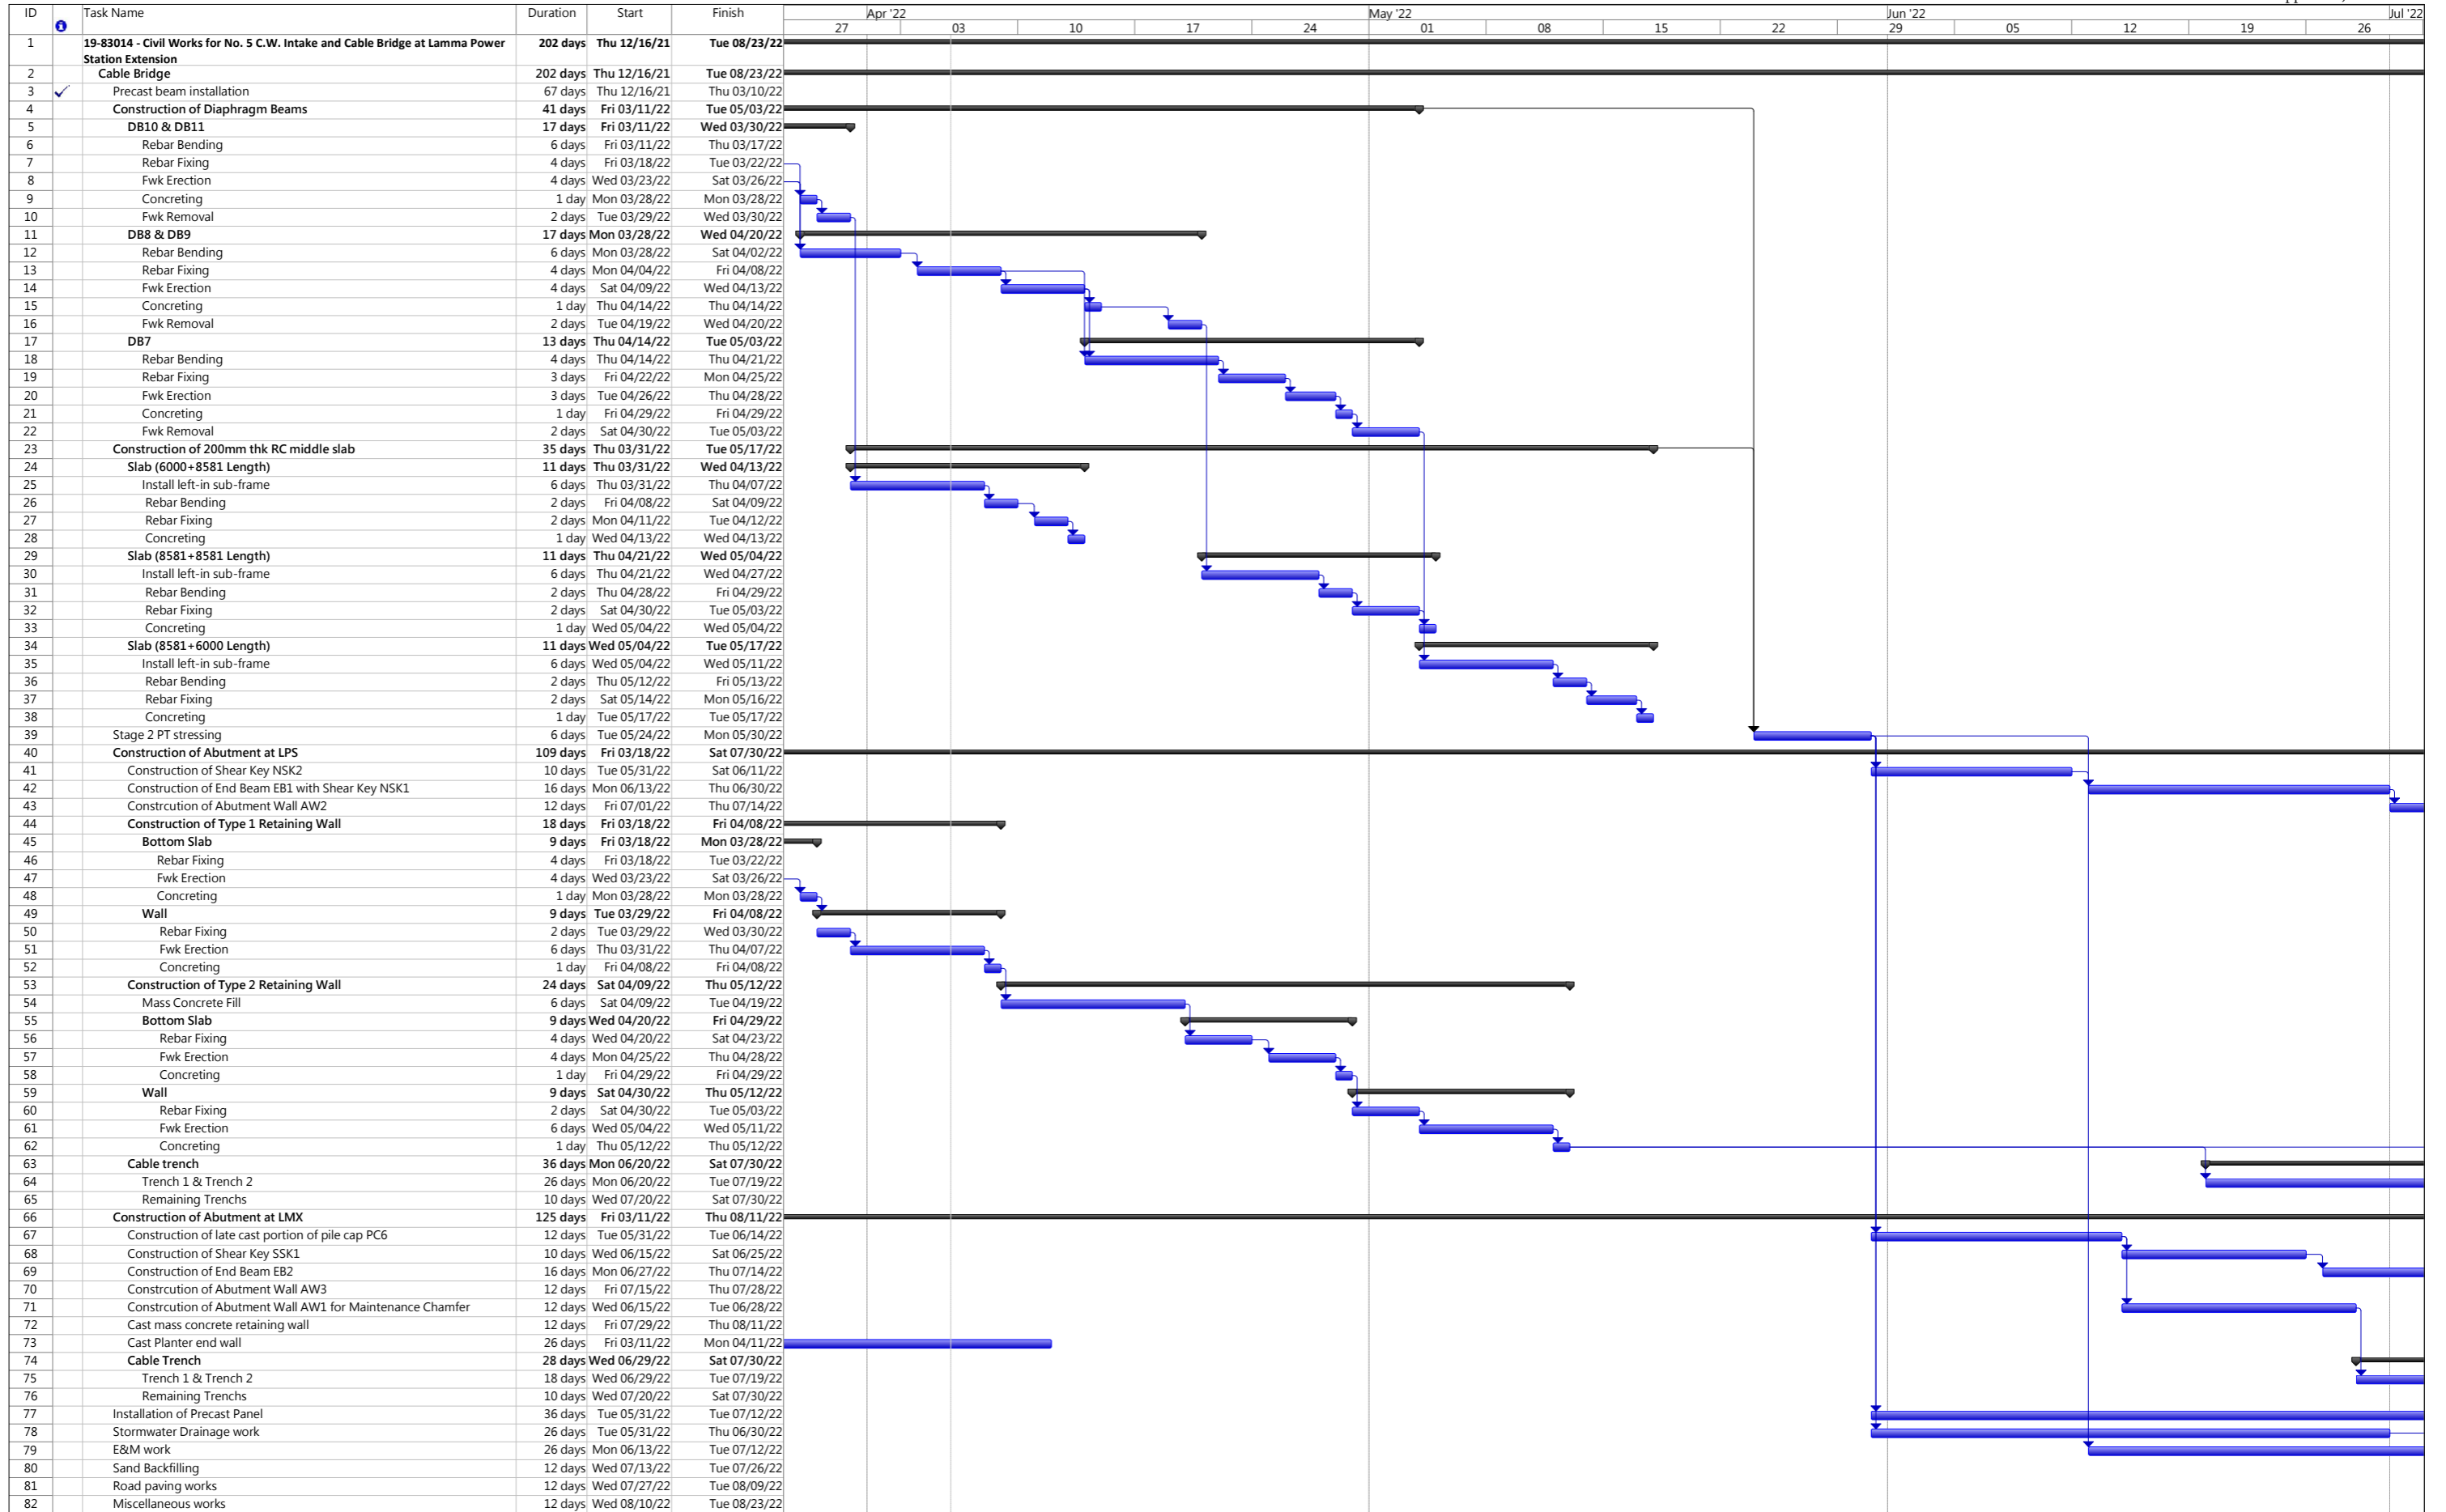

Project: 19-83014 - No. 5 Intake and Cable Br
 Date: 15 Mar 2022
 Rev. 6 - Programme for Cable Bridge

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Milestone
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Progress	Milestone
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Deadline	Milestone

Construction Schedule of Unit-12

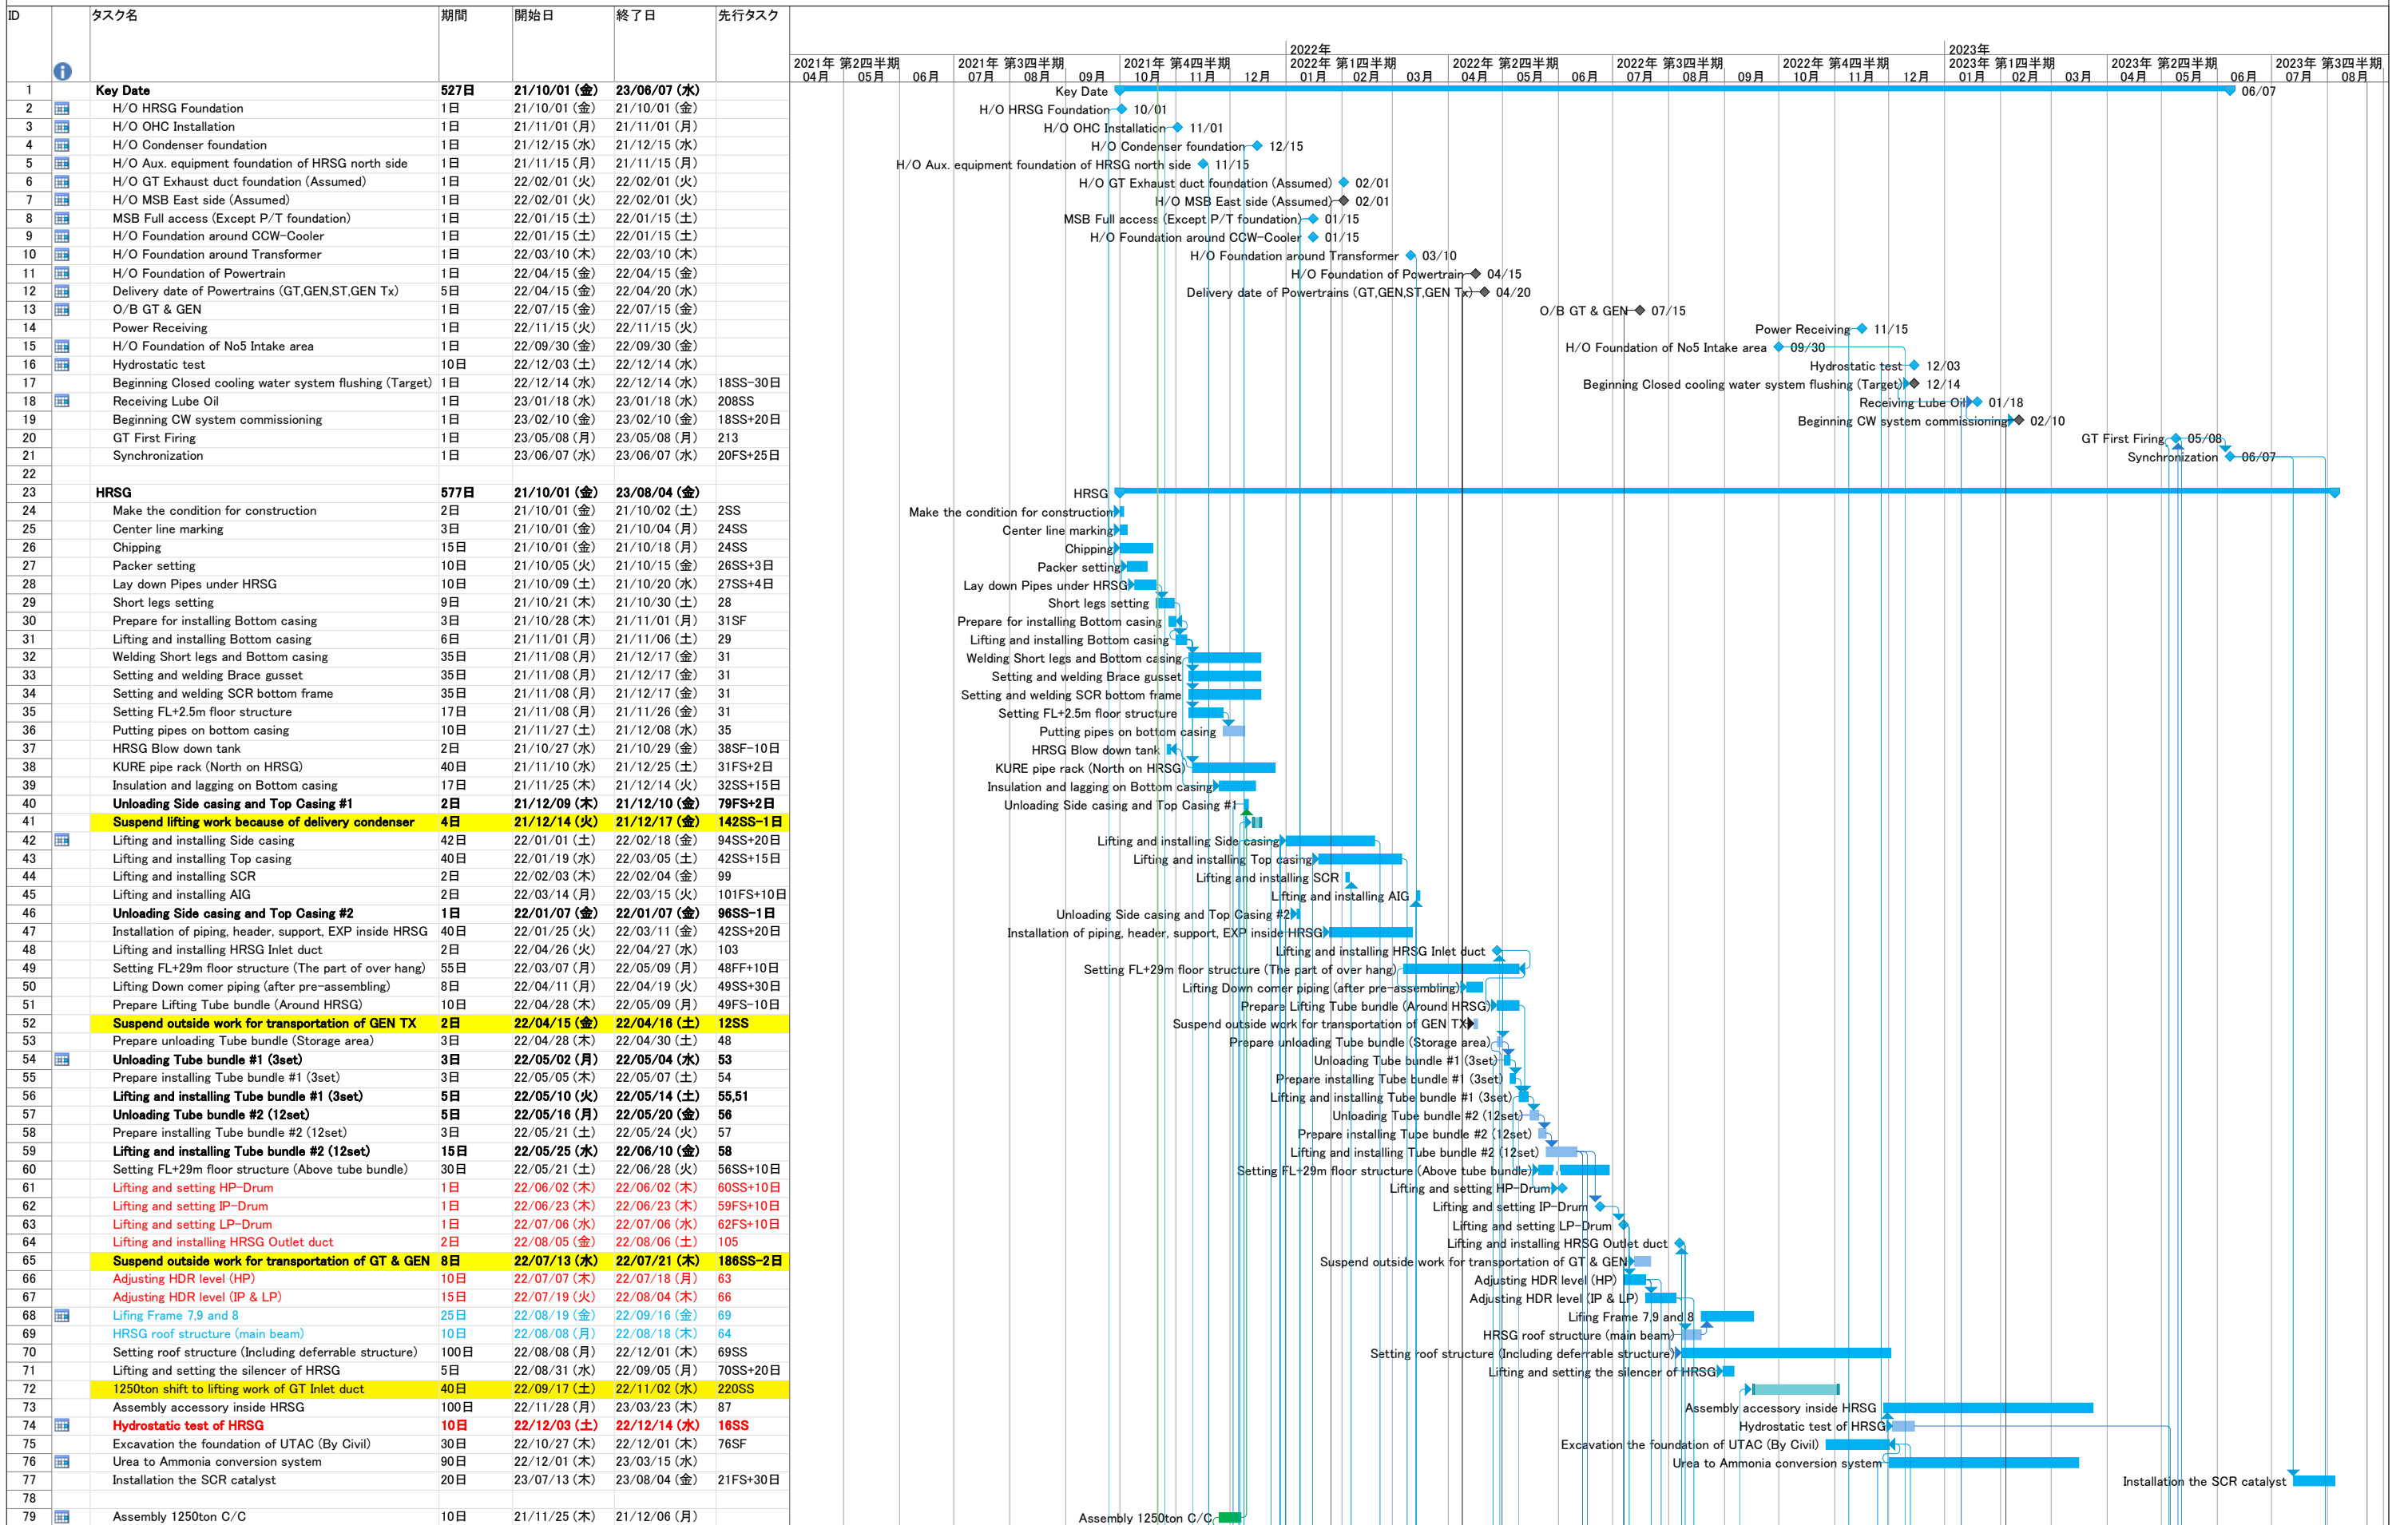

NOTE
 1. The key date is subjected in the KOM held on 30th-Sep.
 2. The east area on the MSB is assumed to be handedover before B-Feb-2022 according to the above key date changed.

3.Considered the affection of KURE's schedule belows;
 i) Because of delaying the side casing,installation Inlet duct is postponed.
 ii) Because of delivery 12 TBs in one time, no enough area for pre-ass'y Outlet duct and GT Inlet duct on schedule.

