



Table with columns: ID, Task Name, Duration, Start, Finish, and Gantt chart area with dates from Oct 2019 to Dec 2022. Includes task details like 'Construction of RC up to R/F incl. staircases' and 'Section E (iii) Whole of Administration and Control Building'.



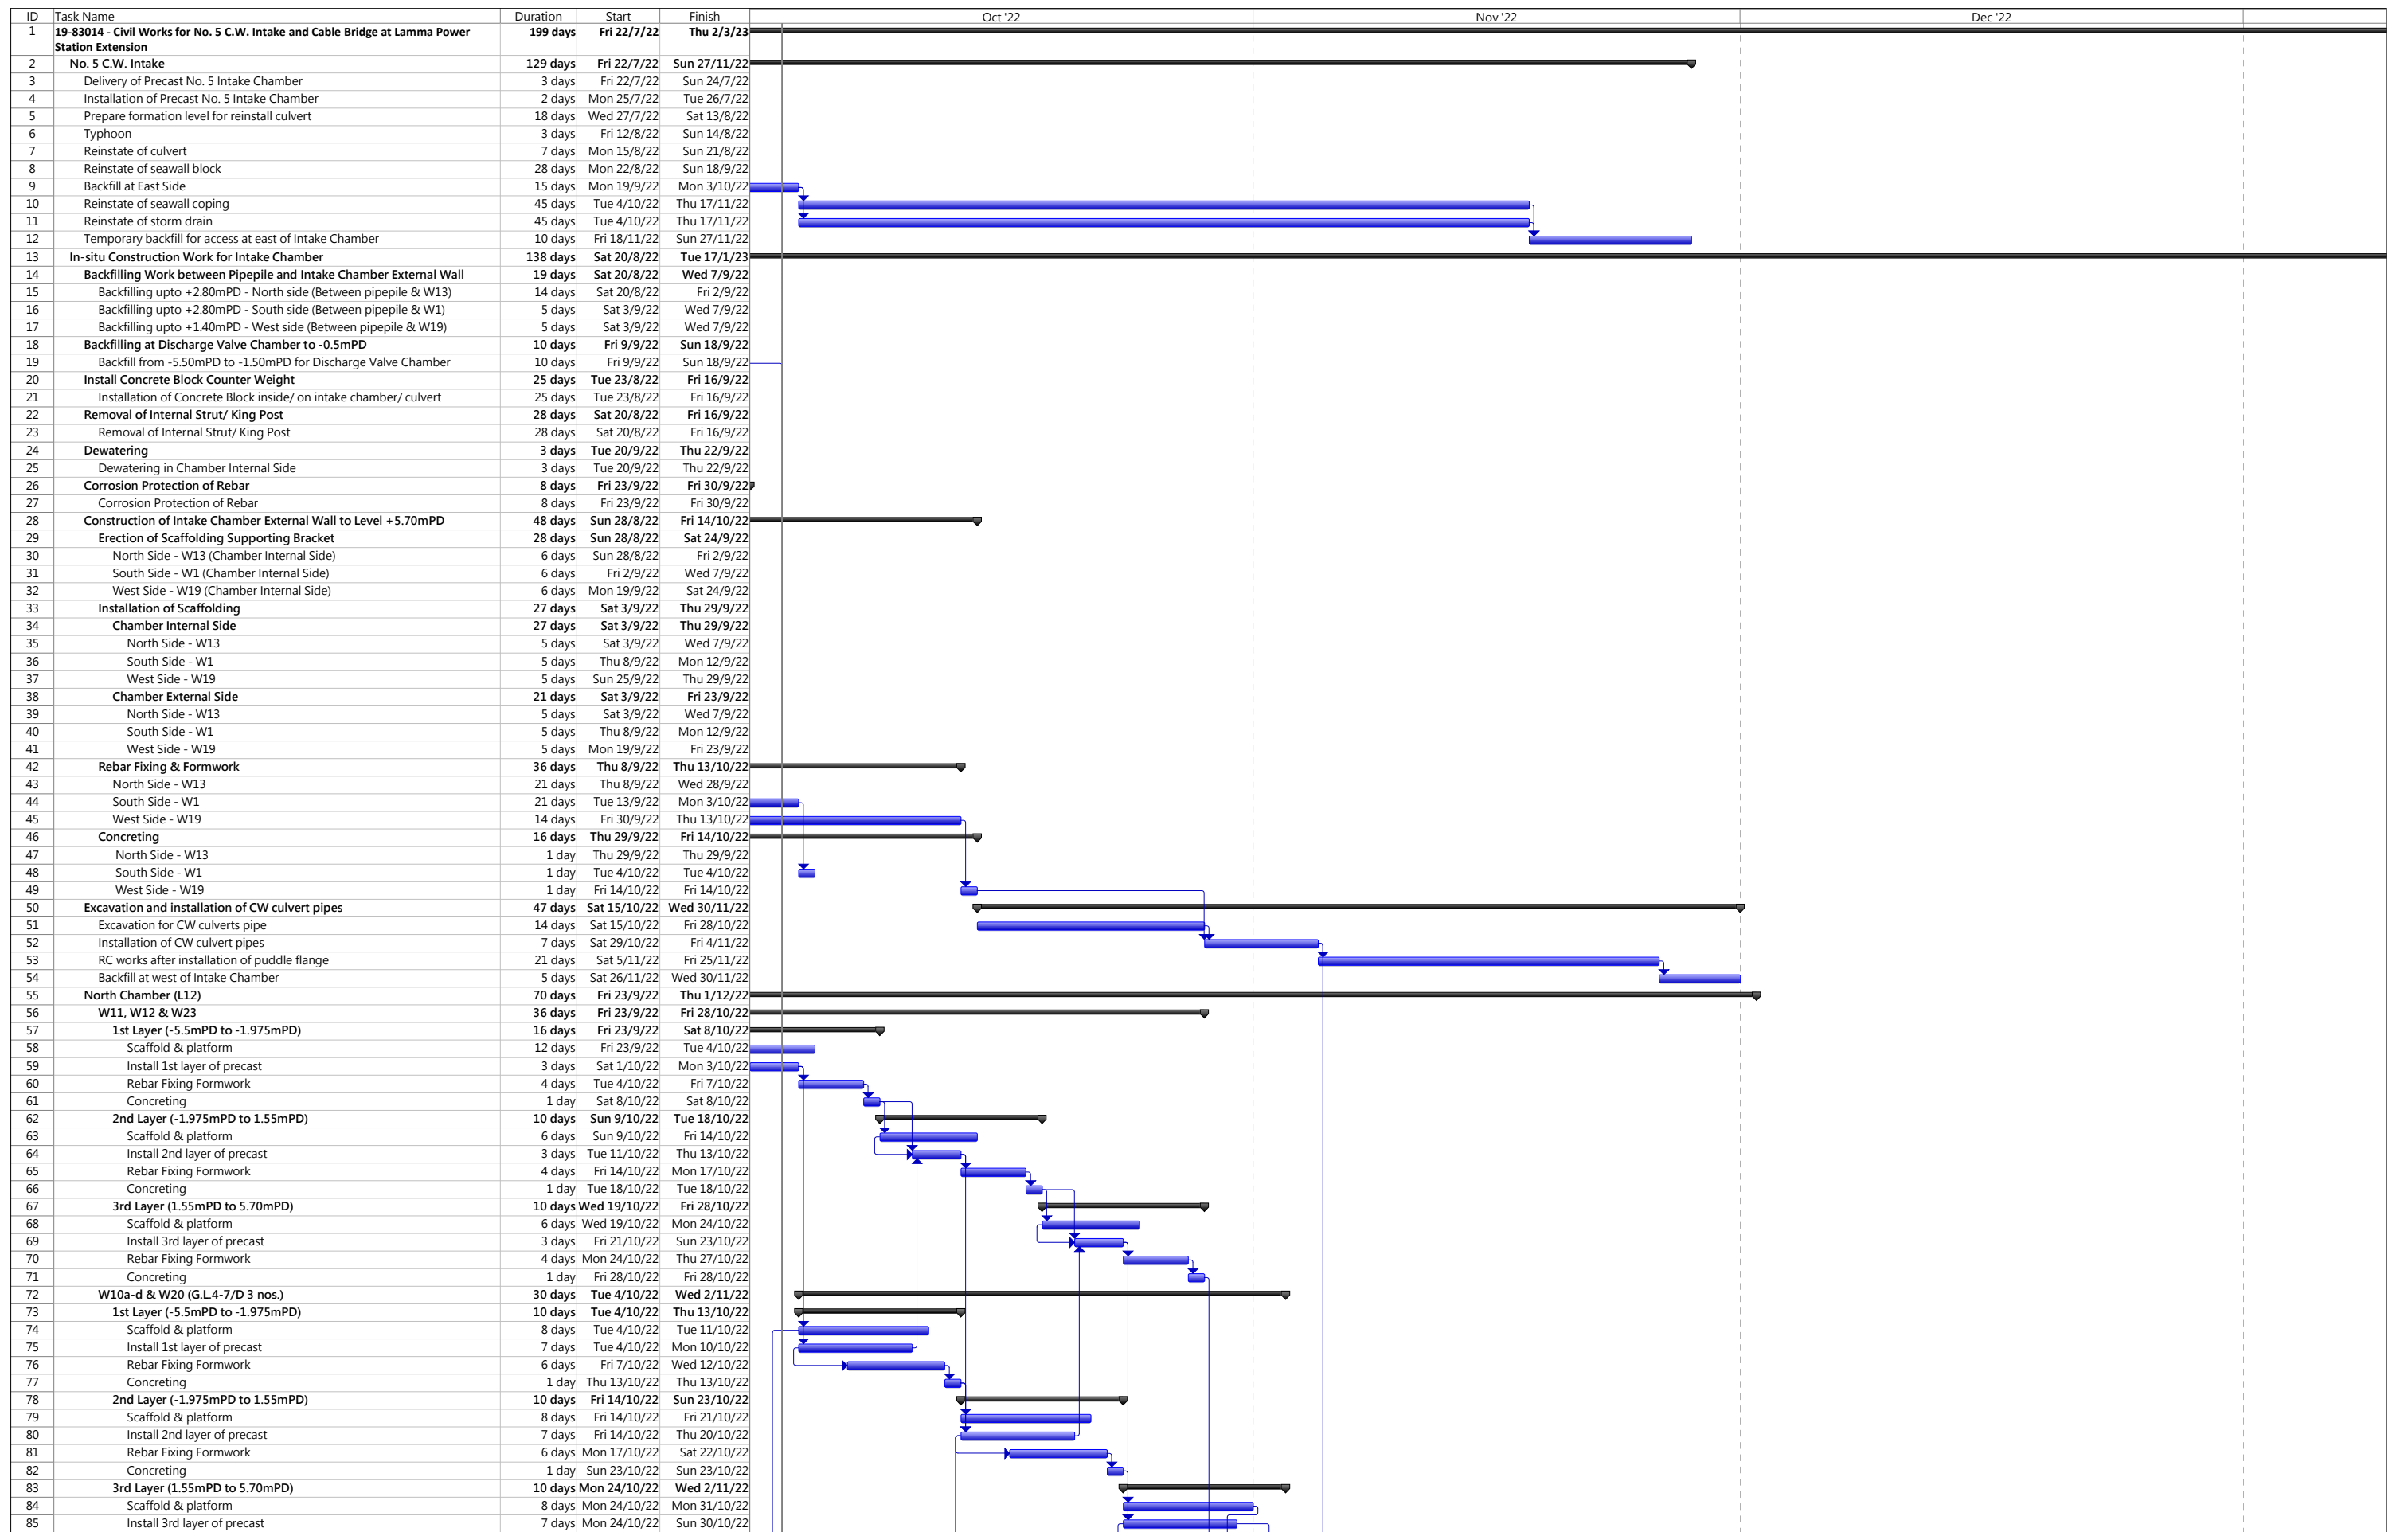

Project: 19-83014 - No. 5 Intake and Cable Br
 Date: 12 Aug 2022
 Rev. 8 - Programme for No. 5 C.W. Intake (D)

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Progress
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline	Start-only
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Deadline	Start-only

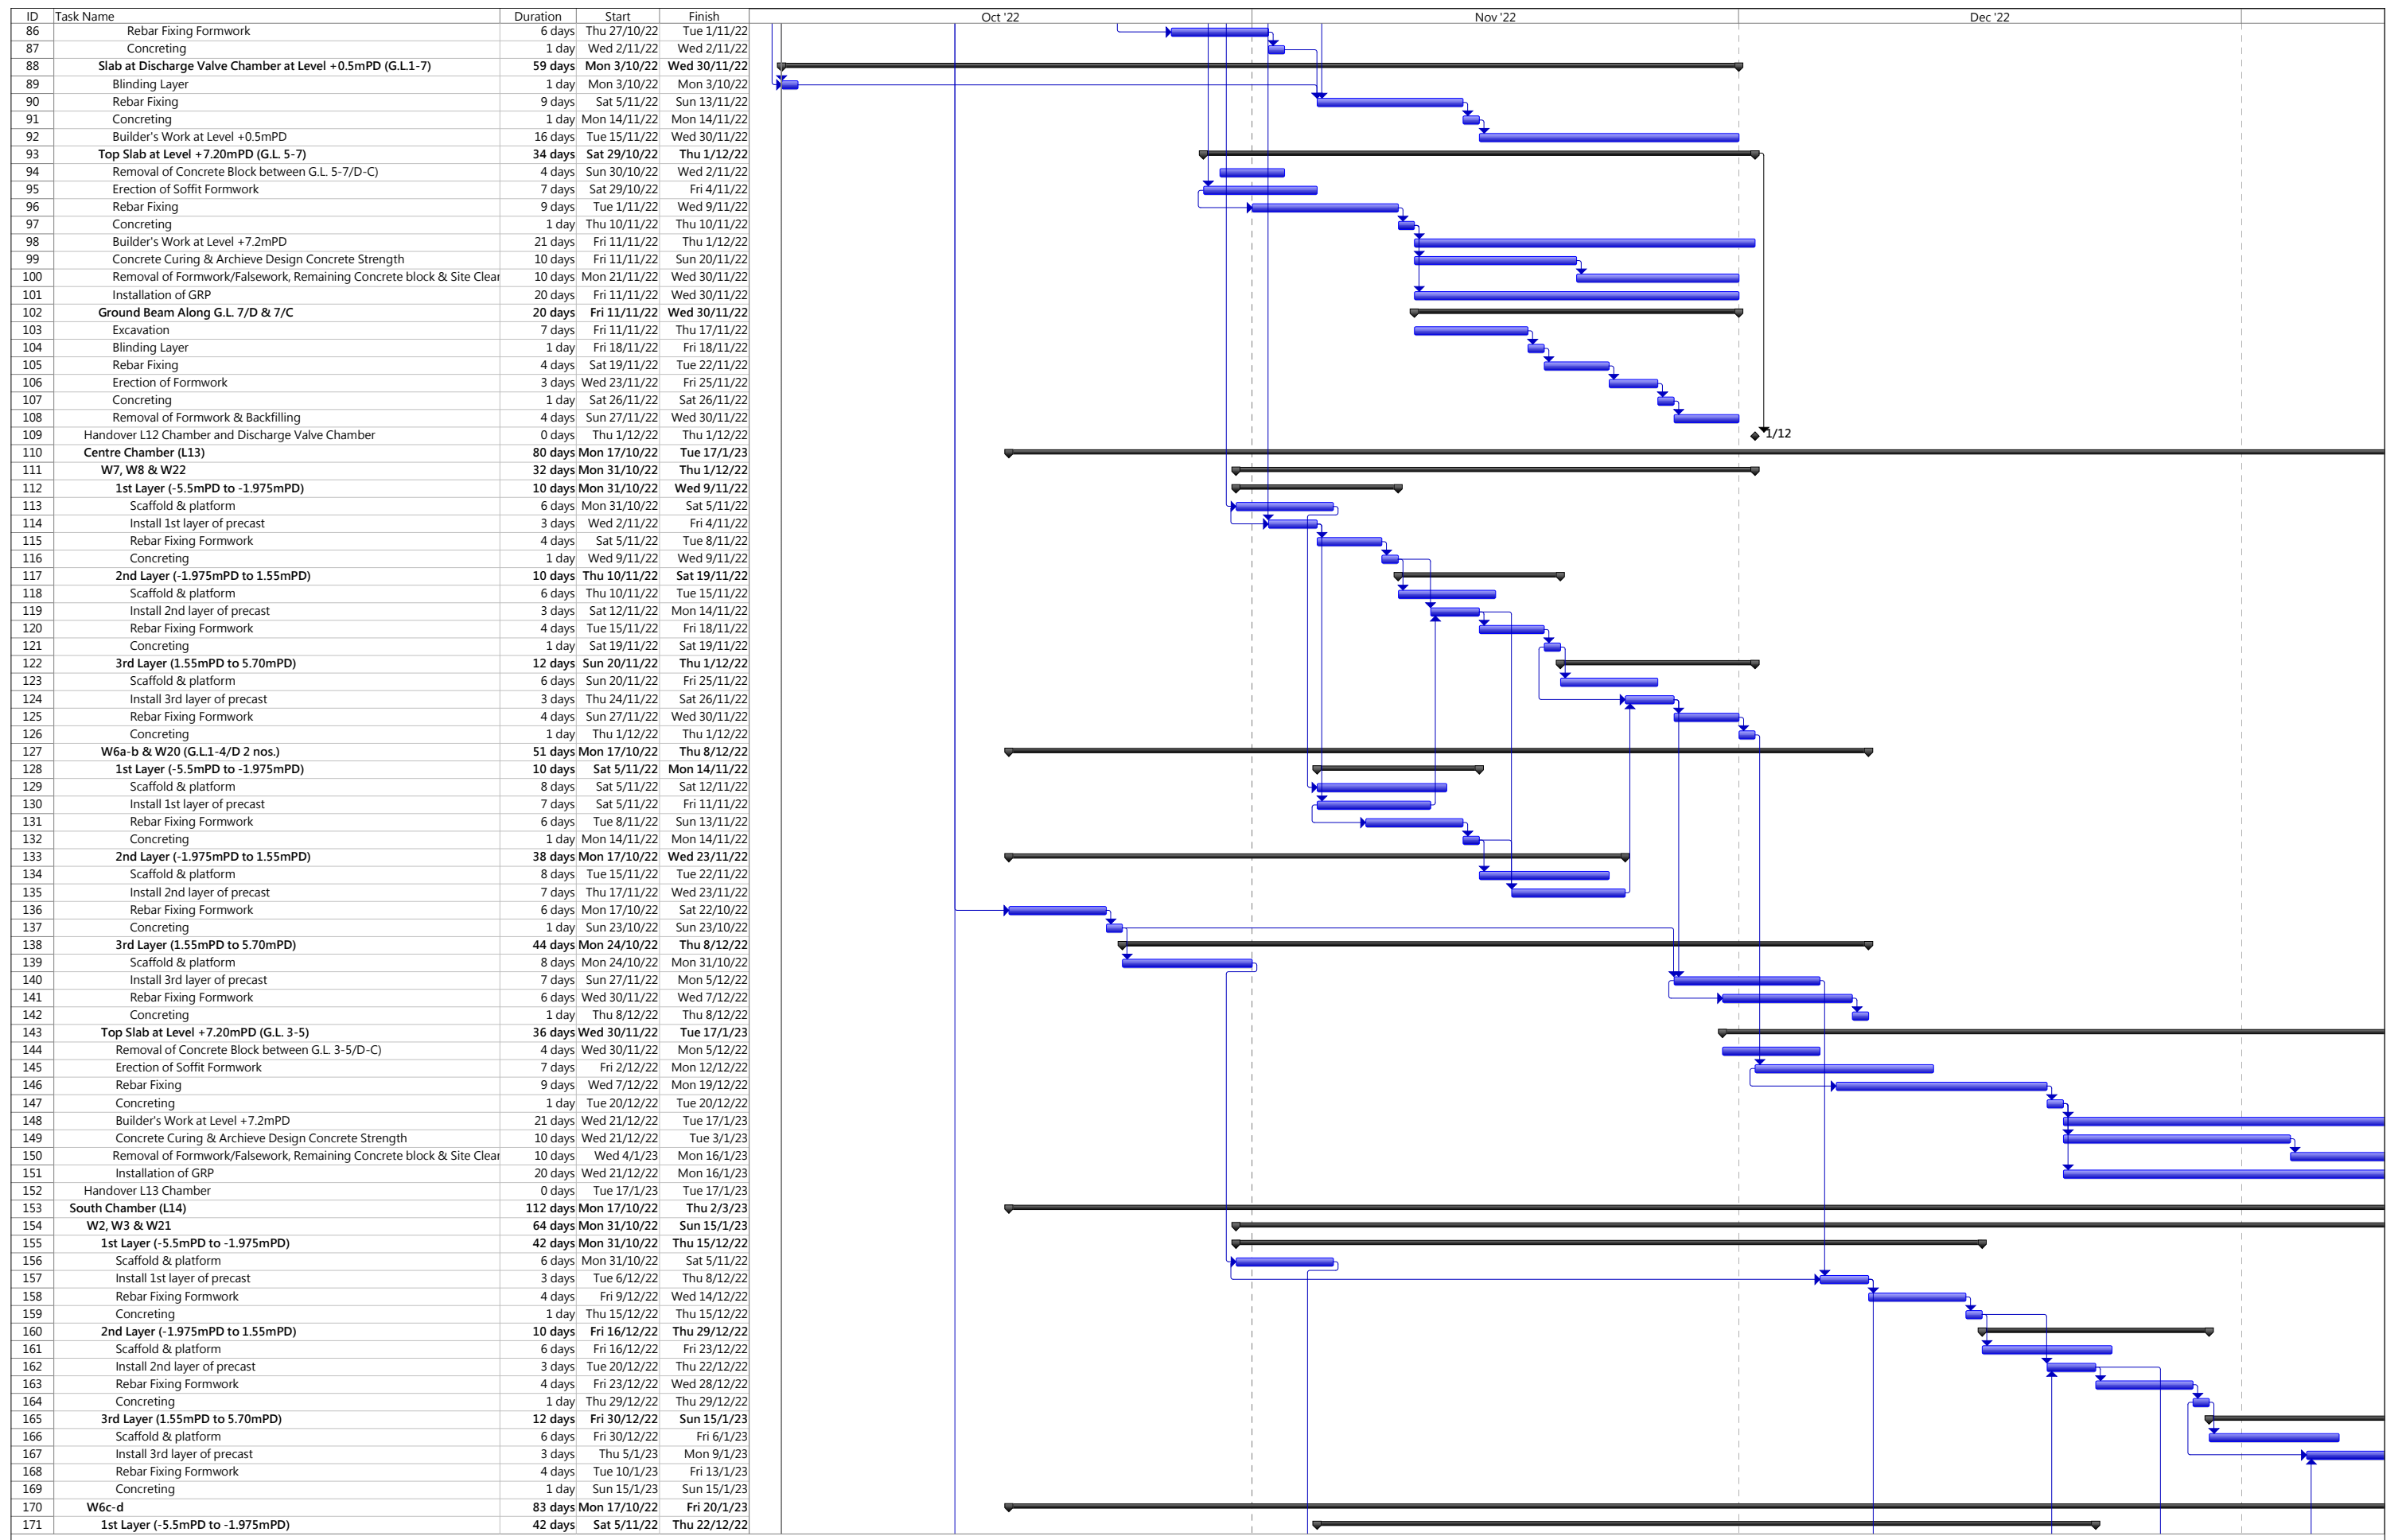


Project: 19-83014 - No. 5 Intake and Cable Br
 Date: 12 Aug 2022
 Rev. 8 - Programme for No. 5 C.W. Intake (D)

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Progress	Start-only
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Deadline	Start-only


Page 2

ID	Task Name	Duration	Start	Finish
172	Scaffold & platform	8 days	Sat 5/11/22	Sat 12/11/22
173	Install 1st layer of precast	7 days	Fri 9/12/22	Mon 19/12/22
174	Rebar Fixing Formwork	6 days	Wed 14/12/22	Wed 21/12/22
175	Concreting	1 day	Thu 22/12/22	Thu 22/12/22
176	2nd Layer (-1.975mPD to 1.55mPD)	70 days	Mon 17/10/22	Wed 4/1/23
177	Scaffold & platform	8 days	Fri 23/12/22	Tue 3/1/23
178	Install 2nd layer of precast	7 days	Tue 27/12/22	Wed 4/1/23
179	Rebar Fixing Formwork	6 days	Mon 17/10/22	Sat 22/10/22
180	Concreting	1 day	Sun 23/10/22	Sun 23/10/22
181	3rd Layer (1.55mPD to 5.70mPD)	76 days	Mon 24/10/22	Fri 20/1/23
182	Scaffold & platform	8 days	Mon 24/10/22	Mon 31/10/22
183	Install 3rd layer of precast	7 days	Tue 10/1/23	Tue 17/1/23
184	Rebar Fixing Formwork	6 days	Fri 13/1/23	Thu 19/1/23
185	Concreting	1 day	Fri 20/1/23	Fri 20/1/23
186	Top Slab at Level +7.20mPD (G.L. 1-3)	35 days	Sun 15/1/23	Thu 2/3/23
187	Removal of Concrete Block between G.L. 1-3/D-C)	4 days	Sun 15/1/23	Wed 18/1/23
188	Erection of Soffit Formwork	7 days	Mon 16/1/23	Tue 24/1/23
189	Rebar Fixing	9 days	Thu 19/1/23	Tue 31/1/23
190	Concreting	1 day	Wed 1/2/23	Wed 1/2/23
191	Builder's Work at Level +7.2mPD	21 days	Thu 2/2/23	Thu 2/3/23
192	Concrete Curing & Archieve Design Concrete Strength	10 days	Thu 2/2/23	Wed 15/2/23
193	Removal of Formwork/Falsework, Remaining Concrete block & Site Clearan	10 days	Thu 16/2/23	Wed 1/3/23
194	Installation of GRP	20 days	Thu 2/2/23	Wed 1/3/23
195	Handover L14 Chamber	0 days	Thu 2/3/23	Thu 2/3/23

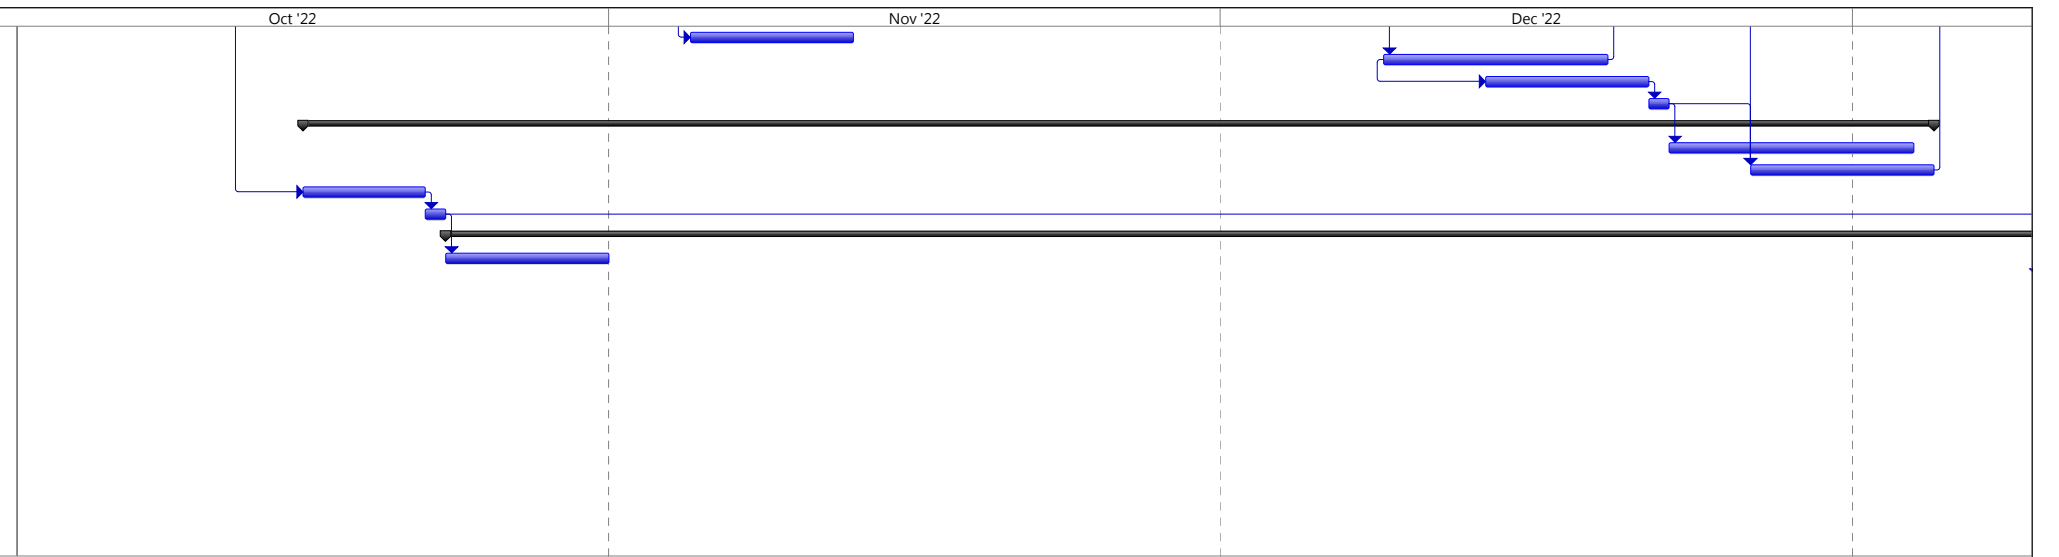

Project: 19-83014 - No. 5 Intake and Cable Br
 Date: 12 Aug 2022
 Rev. 8 - Programme for No. 5 C.W. Intake (D)

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Progress	Deadline
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Deadline	Deadline

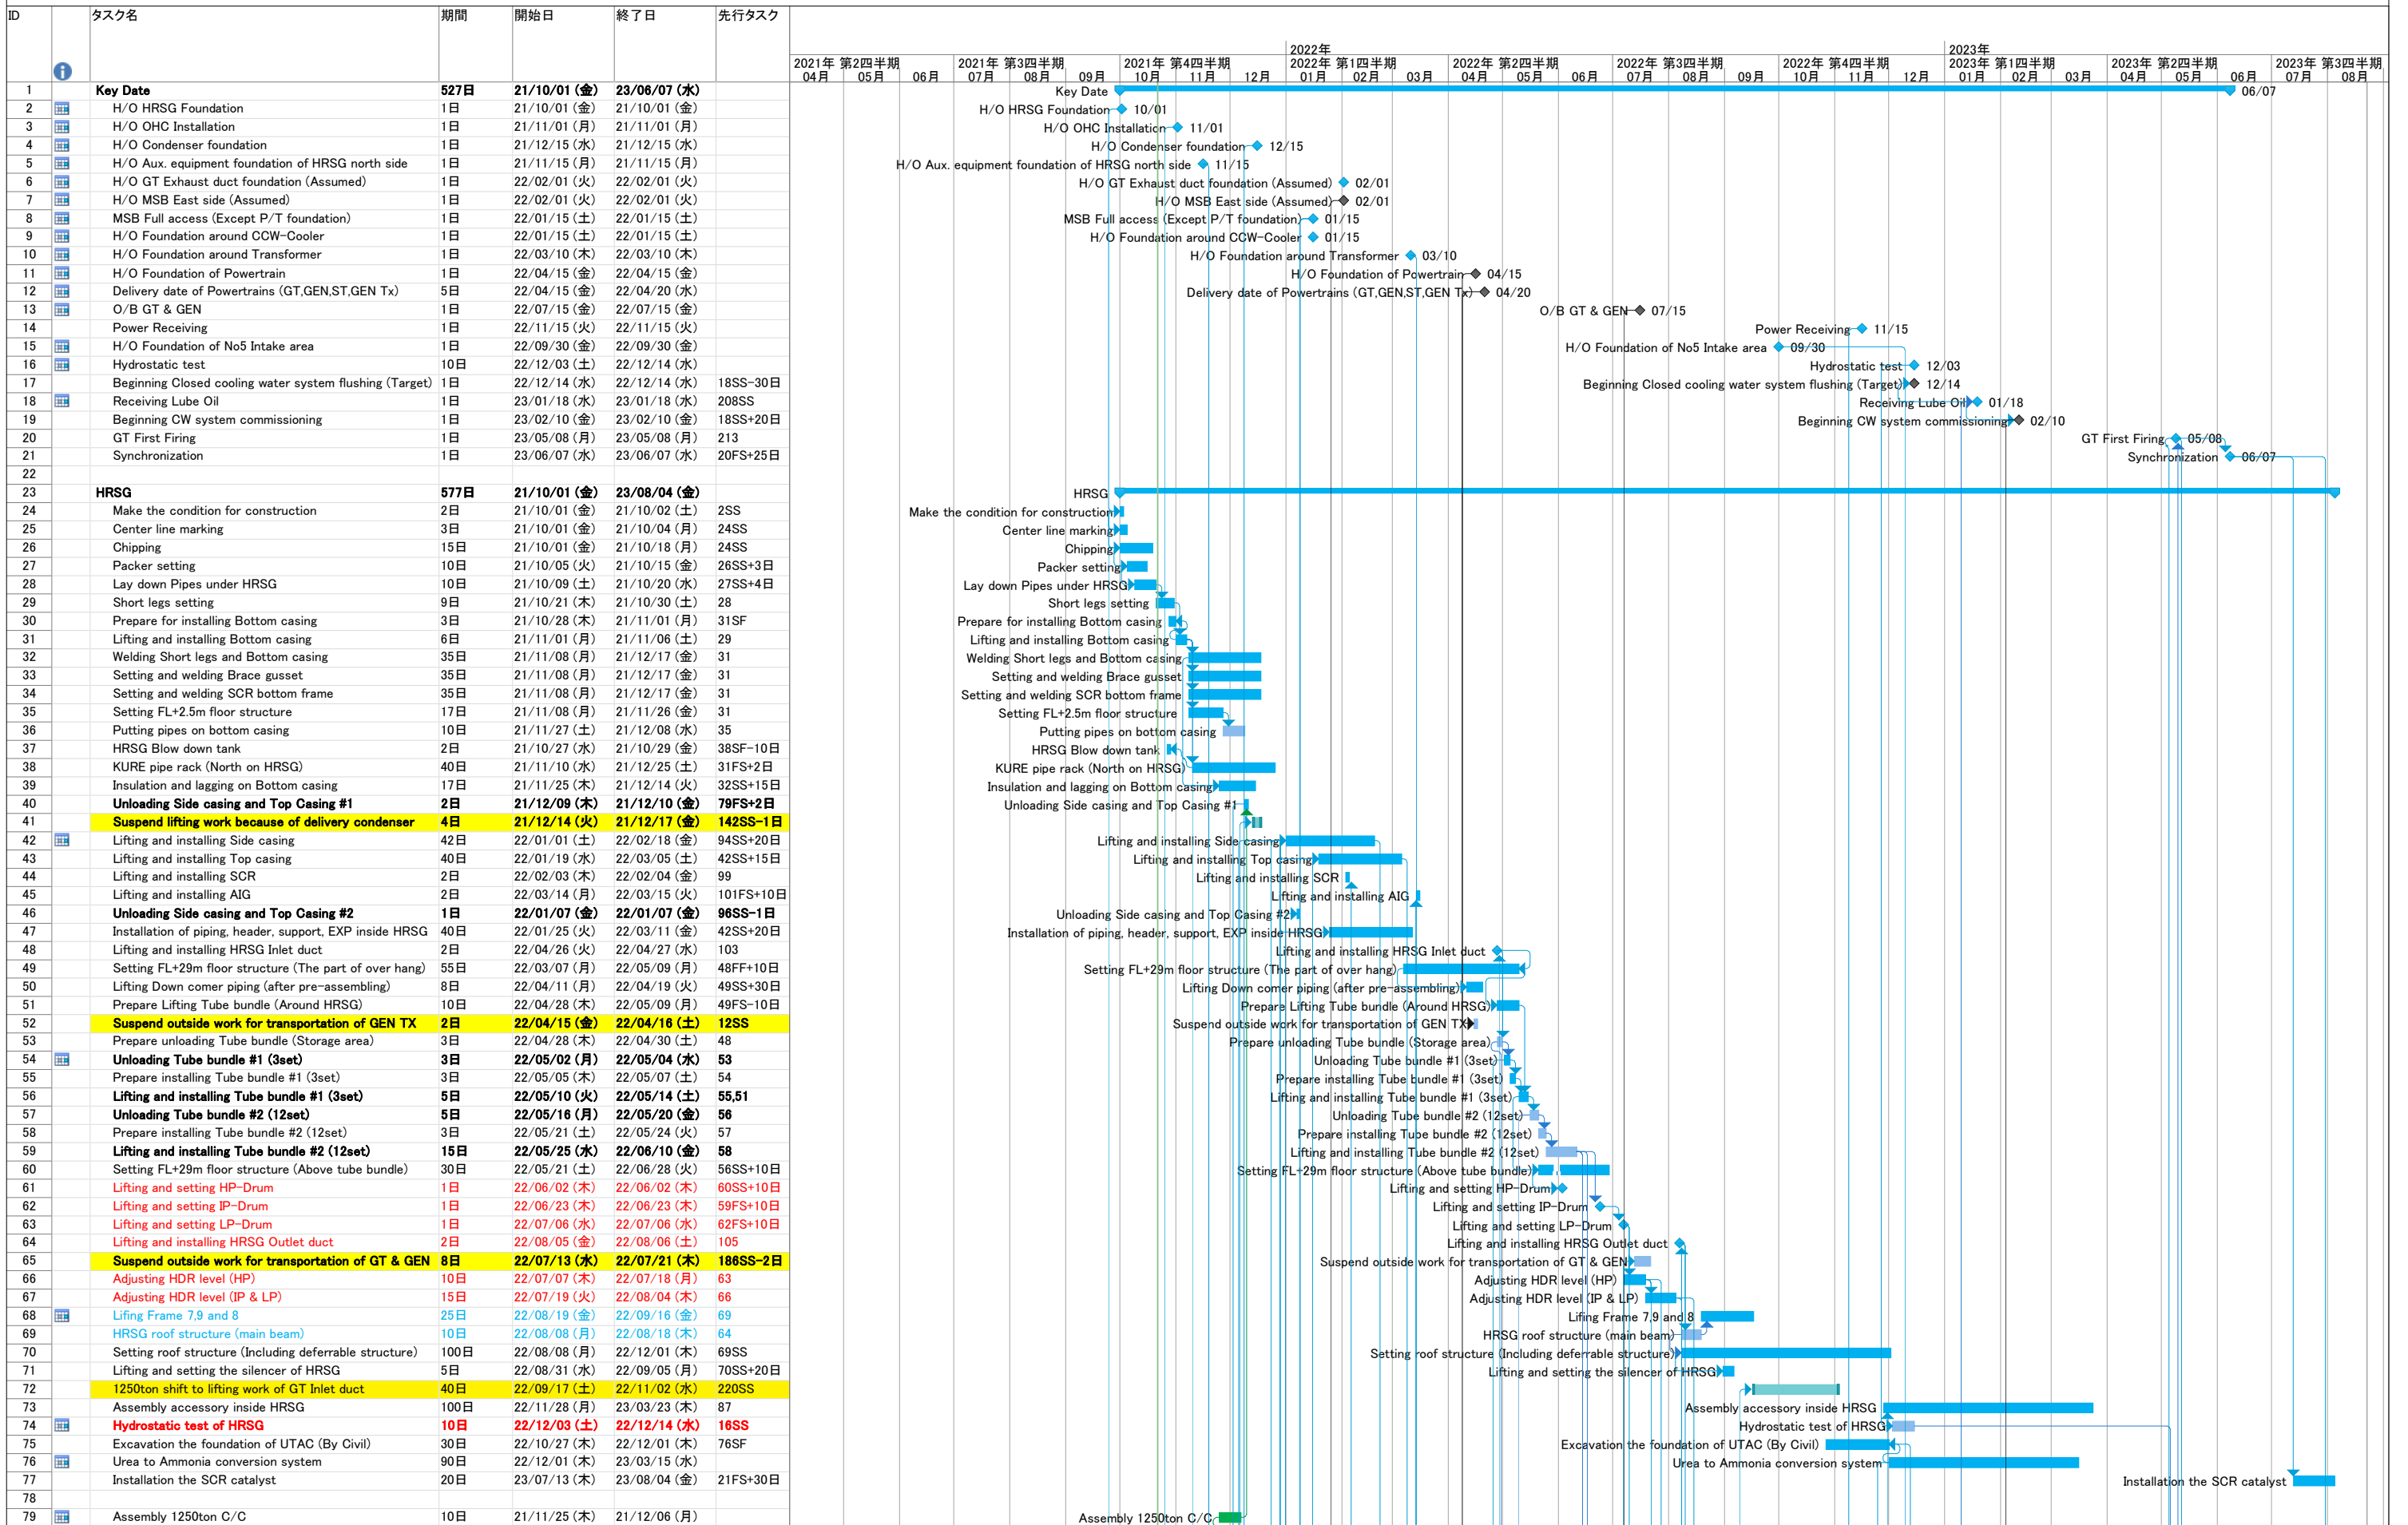

NOTE
 1. The key date is subjected in the KOM held on 30th-Sep.
 2. The east area on the MSB is assumed to be handedover before B-Feb-2022 according to the above key date changed.

3.Considered the affection of KURE's schedule belows;
 i) Because of delaying the side casing,installation Inlet duct is postponed.
 ii) Because of delivery 12 TBs in one time, no enough area for pre-ass'y Outlet duct and GT Inlet duct on schedule.

