

香港電燈有限公司
The Hongkong Electric Co., Ltd.



**Lamma Power Station Extension
Construction Phase
Monthly Environmental Monitoring & Audit Report**

August 2021

香港電燈有限公司
The Hongkong Electric Co., Ltd.



ENVIRONMENTAL IMPACT ASSESSMENT (EIA) ORDINANCE, CAP. 499

ENVIRONMENTAL PERMIT NO. EP-071/2000/D

**LAMMA POWER STATION EXTENSION
ENVIRONMENTAL MONITORING & AUDIT PROGRAMME
AT CONSTRUCTION PHASE**


Report Title	Lamma Power Station Extension – Unit L11 & L12 Monthly EM&A Report (August 2021)
Date	14 September 2021
Certified by	 (Mr. CHAN Hon Yeung, Environmental Team Leader)
Verified by	 Mr. Y T Tang (AECOM Asia Company Limited, Independent Environmental Checker)

TABLE OF CONTENT

EXECUTIVE SUMMARY

1.	INTRODUCTION	1
1.1	Background	1
1.2	Project Organisation	1
1.3	Construction Works undertaken during the Reporting Month	1
1.4	Summary of EM&A Requirements	4
2.	AIR QUALITY	6
2.1	Monitoring Requirements	6
2.2	Monitoring Locations	6
2.3	Monitoring Equipment	6
2.4	Monitoring Parameters, Frequency and Duration	6
2.5	Monitoring Procedures and Calibration Details	7
2.6	Results and Observations	8
3.	NOISE.....	10
3.1	Monitoring Requirements	10
3.2	Monitoring Locations	10
3.3	Monitoring Equipment	10
3.4	Monitoring Parameters, Frequency and Duration	10
3.5	Monitoring Procedures and Calibration Details	11
3.6	Results and Observations	11
4.	ENVIRONMENTAL AUDIT	13
4.1	Review of Environmental Monitoring Procedures	13
4.2	Assessment of Environmental Monitoring Results	13
4.3	Waste Management	13
4.4	Site Environmental Audit	14
4.5	Status of Environmental Licensing and Permitting	14
4.6	Implementation Status of Environmental Mitigation Measures	15
4.7	Implementation Status of Event/Action Plans	15
4.8	Implementation Status of Environmental Complaint Handling Procedures	15
5.	FUTURE KEY ISSUES	17
5.1	Key Issues for the Coming Month	17
5.2	Monitoring Schedules for the Next 3 Months	18
5.3	Construction Program for the Next 3 Months	18
6.	CONCLUSION	19

LIST OF TABLES

Table 1.1	Construction Activities and Their Corresponding Environmental Mitigation Measures
Table 2.1	Air Quality Monitoring Locations
Table 2.2	Air Quality Monitoring Equipment
Table 2.3	Air Quality Monitoring Parameter, Duration and Frequency
Table 3.1	Noise Monitoring Equipment
Table 3.2	Noise Monitoring Duration and Parameter
Table 4.1	Summary of AL Level Exceedances on Monitoring Parameters
Table 4.2	Estimated Amounts of Waste in August 2021
Table 4.3	Summary of Environmental Licensing and Permit Status
Table 4.4	Environmental Complaints Received in August 2021
Table 4.5	Outstanding Environmental Complaints Carried Over

LIST OF FIGURES

Figure 1.1	Layout of Work Site
Figure 2.1	Location of Air Quality Monitoring Stations
Figure 3.1	Location of Noise Monitoring Stations

APPENDICES

Appendix A	Organization Chart
Appendix B	Action and Limit Levels for Air Quality and Noise
Appendix C	Environmental Monitoring Schedule
Appendix D	Air Quality Monitoring Results for August 2021
Appendix E	Noise Monitoring Results for August 2021
Appendix F	The QA/QC Procedures and Results
Appendix G	Event/Action Plans
Appendix H	Site Audit Summary
Appendix I	Summary of EMIS
Appendix J	Tentative Construction Programme
Appendix K	Monthly Waste Flow Table for August 2021

EXECUTIVE SUMMARY

This is the 136th monthly Environmental Monitoring and Audit (EM&A) report for the Project “Construction of Lamma Power Station Extension” prepared by the Environmental Team (ET). This report presents the results of impact monitoring on air quality and noise for the said project in August 2021.

The reclamation and submarine pipeline works were completed with the first gas-fired combined cycle unit (viz. Unit L9) commissioned in October 2006, working currently on base load operation. To cope with the scheduled retirement of the existing units at Lamma Power Station, the second gas-fired combined cycle unit (viz. Unit L10) L10 was commissioned for reliable operation in February 2020. The operational EM&A work for L9 and L10 is recorded in the separate monthly EM&A report for the Project “Operation of Lamma Power Station Extension”.

In September 2016, the Government approved HK Electric to construct the third combined cycle gas-fired generating unit (L11) to implement the 2020 Fuel Mix Target. L11 is planned for commercial operation in 2022 and the associated construction work commenced in November 2016.

With the Government’s approval to build the fourth combined cycle gas-fired generating unit (L12) in July 2018, the associated construction work commenced in April 2019. When L12 is commissioned in 2023, the total gas-fired electricity generation will further rise to reach about 70% of our total output.

Air and noise monitoring were performed. The results were checked against the established Action/Limit (AL) levels. An on-site audit was conducted once per week. The implementation status of the environmental mitigation measures, Event/Action Plan and environmental complaint handling procedures were also checked.

Construction Activities Undertaken

Construction activities for Lamma Extension during the reporting month are tabulated as follows:

Item	Construction Activities
Unit L11 Civil and Building Works	275kV Station Building Extension works, Main Station Building external works, and construction of receiving pit
Unit L11 Mechanical Erection	Condenser installation, HRSG installation and turbine block installation
Unit L11 Electrical, Instrumentation & Control Erection	Cable installation
Unit L12 Civil and Building Works	Installation of columns and beam for Main Station Building, construction of No. 5 Chimney, construction of superstructure for ACB, sheet piling and installation of pipe for No. 5 C.W. Culvert, and pile cap construction for Cable Bridge (South)

Environmental Monitoring Works

All monitoring work at designated stations was performed as scheduled satisfactorily.

Air Quality

No exceedance of Action/Limit levels on 1-hour TSP and 24-hour TSP for air quality was recorded in the month.

Noise

No exceedance of Action and Limit levels for noise arising from the construction of Lamma Extension was recorded in the month.

Site Environmental Audit

EPD officials from Regional Office (South) visited Lamma Power Station on 24/8/2021. There was no adverse comment from EPD regarding the construction site.

Site audits were carried out on a weekly basis to monitor environmental issues on the construction site. The site conditions were generally satisfactory.

Environmental Licensing and Permitting

Description	Permit No.	Valid Period		Issued To	Date of Issuance
		From	To		
Varied Environmental Permit	EP-071/2000/D	28/09/20	-	HK Electric	28/09/20
Construction Noise Permit	GW-RS0072-21	08/02/21	07/08/21	Contractor	05/02/21
Construction Noise Permit	GW-RS0436-21	01/07/21	31/12/21	Contractor	15/06/21
Construction Noise Permit	GW-RS0600-21	08/08/21	07/02/22	Contractor	06/08/21
WPCO Discharge Licence	WT00034006-2019	08/08/19	31/08/24	Contractor	22/08/19
WPCO Discharge Licence	WT00037613-2021	15/04/21	30/04/26	Contractor	15/04/21
Registration of Chemical Waste Producer	WPN5213-912-P2781-22	22/02/16	-	Contractor	22/02/16
Registration of Chemical Waste Producer	WPN5517-912-T2007-02	17/03/05	-	Contractor	17/03/05
Waste Disposal Billing Account	Account No.: 7031135	21/06/18	-	Contractor	21/06/18
Waste Disposal Billing Account	Account No.: 7027672	24/04/17	-	Contractor	24/04/17
Waste Disposal Billing Account	Account No.: 7038672	27/10/20	-	Contractor	27/10/20
Waste Disposal Billing Account	Account No.: 7039272	08/01/21	-	Contractor	08/01/21

Implementation Status of Environmental Mitigation Measures

Environmental mitigation measures for the construction activities as recommended in the EM&A manual were implemented in the reporting month.

Environmental Complaints

No complaint against the construction activities was received in the reporting month.

Future Key Issues

The future key issues to be considered in the coming month are as follows:

Unit L11 Civil and Building Works

- to continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the performance;
- to monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary;
- to treat wastewater in sedimentation pit and tanks before discharge and to ensure compliance with the WPCO discharge licence already obtained.

Unit L11 Mechanical Erection

- to continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained;
- to continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the performance;
- to monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

Unit L11 Electrical, Instrumentation & Control Erection

- to continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained;
- to continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the performance;
- to monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

Unit L12 Civil and Building Works

- to continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained;
- to monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary;
- to treat wastewater in sedimentation pit and tanks before discharge and to ensure compliance with the WPCO discharge licence already obtained;
- to provide silt curtain as preventive measures at Northern Cable Bridge area.

Concluding Remarks

The environmental performance of the project was generally satisfactory.

1. INTRODUCTION

1.1 Background

The Environmental Team (hereinafter called the “ET”) was formed within the Hongkong Electric Co. Ltd (HEC) to undertake Environmental Monitoring and Audit for “Construction of Lamma Power Station Extension” (hereinafter called the “Project”). Under the requirements of Section 6 of Environmental Permit EP-071/2000/D, an EM&A programme for impact environmental monitoring set out in the EM&A Manual (Construction Phase) is required to be implemented. In accordance with the EM&A Manual, environmental monitoring of air quality, noise and water quality and regular environmental audits are required for the Project. With the completion of reclamation and submarine pipeline works, no further marine water quality monitoring would be required.

The Project involves the construction of a gas-fired power station employing combined cycled gas turbine technology, forming an extension to the existing Lamma Power Station. The key elements of the Project including the construction activities associated with the transmission system and submarine gas pipeline are outlined as follows.

- dredging and reclamation to form approximately 22 hectares of usable area;
- construction of six 300MW class gas-fired combined cycle units;
- construction of a gas receiving station;
- construction of a transmission system linking the Lamma Extension to load centres on Hong Kong Island;
- laying of a gas pipeline for the supply of natural gas to the new power station

This report summarizes the environmental monitoring and audit work for the Project for the month of August 2021.

1.2 Project Organisation

An Environmental Management Committee (EMC) has been set up in HEC to oversee the Project. The management structure includes the following:

- Environmental Protection Department (The Authority);
- Environmental Manager (The Chairman of the Environmental Management Committee);
- Engineer;
- Independent Environmental Checker (IEC);
- Environmental Team (ET);
- Contractor.

The project organisation chart for the construction EM&A programme is shown in [Appendix A](#).

1.3 Construction Works undertaken during the Reporting Month

Construction activities for Unit L11 civil and building works were, 275kV Station Building Extension works, Main Station Building external works and construction of receiving pit. Construction activities for Unit L11 mechanical erection were condenser installation, HRSG installation and turbine block installation. Construction activity for Unit L11 electrical, instrumentation & control erection was cable installation. Construction activities for Unit L12 civil and building works were, installation of columns and beam for Main Station Building,

construction of No.5 Chimney, construction of superstructure for ACB, sheet piling and installation of pipe for No. 5 C.W. Culvert, and pile cap construction for Cable Bridge (South). Layout plan for construction site is shown in [Figure 1.1](#).

The main construction activities carried out during the reporting month and the corresponding environmental mitigation measures are summarized in [Table 1.1](#). The implementation of major mitigation measures in the month is provided in [Appendix I](#).

Table 1.1 Construction Activities and Their Corresponding Environmental Mitigation Measures

Item	Construction Activities	Environmental Mitigation Measures
Unit L11 Civil and Building Works		
1.	275kV Station Building Extension Works	<p>Air</p> <ul style="list-style-type: none"> - All regulated machine attached with valid exception/approval NRMM labels. - Water spraying on haul road. <p>Waste Management</p> <ul style="list-style-type: none"> - Scrape metal would be recycled.
2.	Main Station Building external works and construction of receiving pit	<p>Air</p> <ul style="list-style-type: none"> - All regulated machine attached with valid exception/approval NRMM labels. - Water truck and water sprinkler system was used. - Excavated slope and soil stock covered with cement or tarpaulin. - Backfilled surface was compacted. - Wheel washing facility was provided. <p>Wastewater</p> <ul style="list-style-type: none"> - Wastewater should be treated in desilting pit and tanks before discharge. Solution should be added to speed up the sedimentation process. Sediment in pit and tanks must be removed regularly. The frequency would be from every other day to weekly basis depends on the volume of sediment accumulated in order to maintain sufficient volume for wastewater treatment. <p>Waste Management</p> <ul style="list-style-type: none"> - Excavated soil was temporary stored for backfilling. - Scrape metal would be recycled. - Timber would be reused as much as possible.

Item	Construction Activities	Environmental Mitigation Measures
Unit L11 Mechanical Erection		
3.	Condenser installation HRSG installation Turbine block installation	<p>Air</p> <ul style="list-style-type: none"> – Dust suppression measures implemented according to the EMP. <p>Noise</p> <ul style="list-style-type: none"> – General noise mitigation measures employed at all work sites throughout the construction phase. <p>Waste Management</p> <ul style="list-style-type: none"> – Waste Management Plan submitted and implemented
Unit L11 Electrical, Instrumentation & Control Erection		
4.	Cable installation	<p>Air</p> <ul style="list-style-type: none"> – Dust suppression measures implemented according to the EMP. <p>Noise</p> <ul style="list-style-type: none"> – General noise mitigation measures employed at all work sites throughout the construction phase. <p>Waste Management</p> <ul style="list-style-type: none"> – Waste Management Plan submitted and implemented.
Unit L12 Civil and Building Works		
5.	<u>Unit L12 Main Station Building</u> Installation and Columns of beam Construction of No.5 Chimney <u>ACB</u> Construction of superstructure <u>No.5 C.W. Culvert</u> Sheet piling and installation of pipe	<p>Air</p> <ul style="list-style-type: none"> – All regulated machine attached with valid exception/approval NRMM labels. – Water truck, water sprinkler system and mist cannon would be used. – Water spraying for concrete breaking works. – Soil stock would be covered with cement or tarpaulin or keep the entire surface wet. Wheel washing facility was provided. <p>Noise</p> <ul style="list-style-type: none"> – Works conducted during restricted hours should comply with the valid CNP. – Noise emission label was provided for air compressor. <p>Wastewater</p>

Item	Construction Activities	Environmental Mitigation Measures
		<ul style="list-style-type: none"> – Wastewater should be treated in desilting pit and tanks before discharge. Solution should be added to speed up the sedimentation process. Sediment in pit and tanks must be removed regularly. The frequency would be in weekly basis depends on the volume of sediment accumulated in order to maintain sufficient volume for wastewater treatment. <p>Waste Management</p> <ul style="list-style-type: none"> – Excavated soil was temporary stored for backfilling and reuse in other projects. – Scrape metal would be recycled. – Chemical waste should be collected by licensed collector.
6.	Cable Bridge (South): Pile Cap Construction	<p>Air</p> <ul style="list-style-type: none"> – All regulated machine attached with valid exception/approval NRMM labels. – Soil stockpile covered with tarpaulin. – Wheel washing facilities was provided. – Water spraying on haul road and during concrete breaking. <p>Waste Management</p> <ul style="list-style-type: none"> – Excavated soil would be stored for backfilling. <p>Wastewater</p> <ul style="list-style-type: none"> - Wastewater would be treated in desilting tanks before discharge - Silt curtain was provided as preventive measures at Southern Cable Bridge area

1.4 Summary of EM&A Requirements

The detailed EM&A monitoring work for air quality and noise are described in Sections 2 and 3 respectively. Regular environmental site audits for air quality, noise, water quality and waste management were carried out.

The following environmental audits are summarized in Section 4 of this report:

- Environmental monitoring results;
- Waste Management Records;
- Weekly site audit results;
- The status of environmental licensing and permits for the Project;
- The implementation status of environmental protection and pollution control/ mitigation measures.

Future key issues will be reported in Section 5 of this report.

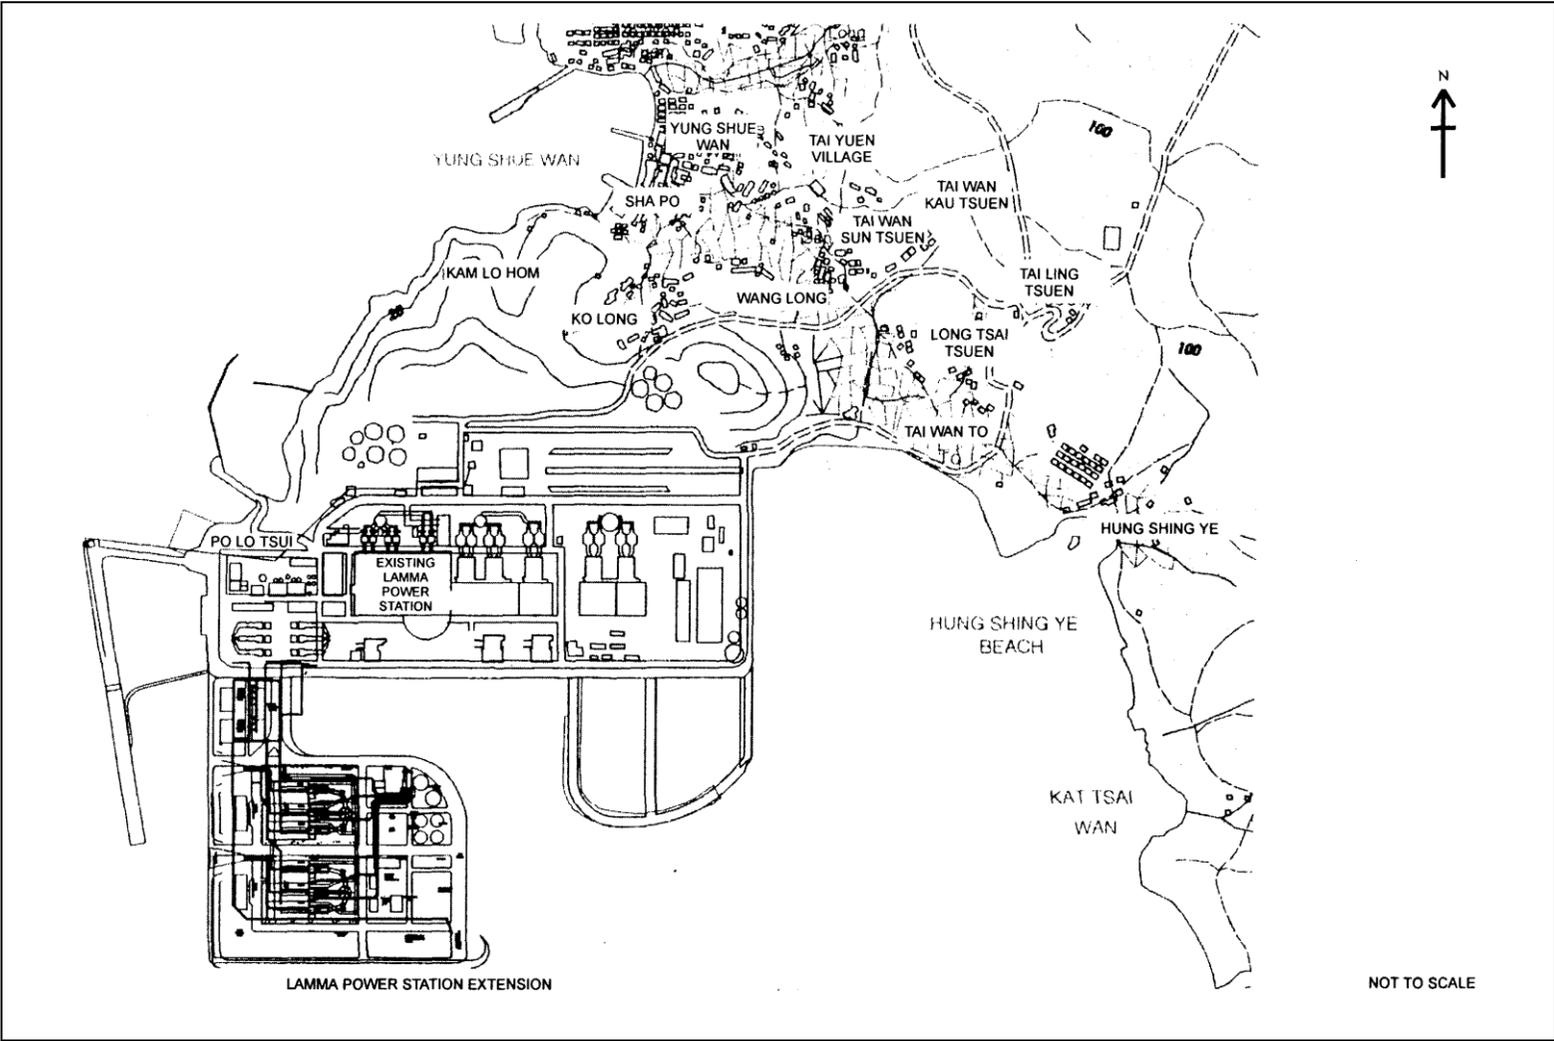


Figure 1.1 Layout of Work Site

2. AIR QUALITY

2.1 Monitoring Requirements

1-hour and 24-hour TSP monitoring at agreed frequencies were conducted to monitor air quality. The impact monitoring data were checked against the Action/Limit Levels as determined in the Baseline Monitoring Report (Construction Phase). [Appendix B](#) shows the established Action/Limit Levels for Air Quality.

2.2 Monitoring Locations

Three dust monitoring locations were selected for 1-hour TSP sampling (AM1, AM2 & AM3) while four monitoring locations were selected for 24-hour TSP sampling (AM1, AM2, AM3 and AM4). [Table 2.1](#) tabulates the monitoring stations. The locations of the monitoring stations are shown in [Figure 2.1](#).

Table 2.1 Air Quality Monitoring Locations

Location I.D.	Description
AM1	Reservoir
AM2	East Gate
AM3	Ash Lagoon
AM4	Tai Yuen Village

2.3 Monitoring Equipment

It is agreed with EPD that continuous 24-hour TSP air quality monitoring would be performed using TEOM continuous dust monitor and the MINIVOL Portable Sampler at AM1,2&3 and AM4 respectively. TEOM continuous dust monitors were used to carry out 1-hour TSP monitoring at AM1, AM2 and AM3. [Table 2.2](#) summarises the equipment used in dust monitoring.

Table 2.2 Air Quality Monitoring Equipment

Equipment	Model and Make
<i>24-hour sampling:</i>	
Continuous TSP Dust Meter	TEOM continuous dust monitor Thermo Scientific
MINIVOL Portable Sampler	AIRMETRICS
<i>1-hour sampling:</i>	
Continuous TSP Dust Meter	TEOM continuous dust monitor Thermo Scientific

2.4 Monitoring Parameters, Frequency and Duration

[Table 2.3](#) summarises the monitoring parameters, duration and frequency of air quality monitoring. The monitoring schedule for the reporting month is shown in [Appendix C](#).

Table 2.3 Air Quality Monitoring Parameter, Duration and Frequency

Monitoring Stations	Parameter	Duration	Frequency
AM1	1-hour TSP	1	3 hourly samples every 6 days
	24-hour TSP	24	Once every 6 days
AM2	1-hour TSP	1	3 hourly samples every 6 days
	24-hour TSP	24	Once every 6 days
AM3	1-hour TSP	1	3 hourly samples every 6 days
	24-hour TSP	24	Once every 6 days
AM4	24-hour TSP	24	Once every 6 days

2.5 Monitoring Procedures and Calibration Details

MINIVOL (24- hour TSP Monitoring):

Preparation of Filter Papers

- Visual inspection of filter papers was carried out to ensure that there were no pinholes, tears and creases;
- The filter papers were then labeled before sampling.
- The filter papers were equilibrated at room temperature and relative humidity < 50% for at least 24 hours before weighing.

Field Monitoring

- During collection of the sampled filter paper, the information on the elapse timer was logged. Site observations around the monitoring stations, which might have affected the monitoring results, were also recorded. Major pollution sources, if any, would be identified and reported.
- The post-sampling filter papers were removed carefully from the filter holder and folded to avoid loss of fibres or dust particles from the filter papers;
- The filter holder and its surrounding were cleaned;
- A pre-weighed blank filter paper for the next sampling was put in place and aligned carefully. The filter holder was then tightened firmly to avoid leakage;
- The programmable timer was set for the next 24 hrs sampling period;
- The post-sampling filter papers were equilibrated at room temperature and relative humidity < 50% for at least 24 hours before weighing.

TEOM continuous dust monitor (24- hour TSP and 1- hour TSP Monitoring):

- The following parameters of the TEOM model dust meters are regularly checked to ensure proper functionality:
 - Operation Mode;
 - Frequency of the tapered element;
 - Main flow;
 - Bypass flow.

Maintenance & Calibration

- The monitoring equipment and their accessories are maintained in good working conditions.

- Monitoring equipment is calibrated at monthly intervals. Calibration details are shown in [Appendix F](#).

2.6 Results and Observations

All dust monitoring works were conducted on schedule. All monitoring data and graphical presentation of the monitoring results are provided in [Appendix D](#). Key findings and observations are provided below:

1-hour TSP

No exceedance of 1-hour TSP Action/Limit Level was recorded in the month.

24-hour TSP

No exceedance of 24-hour TSP Action/Limit Level was recorded in the month.

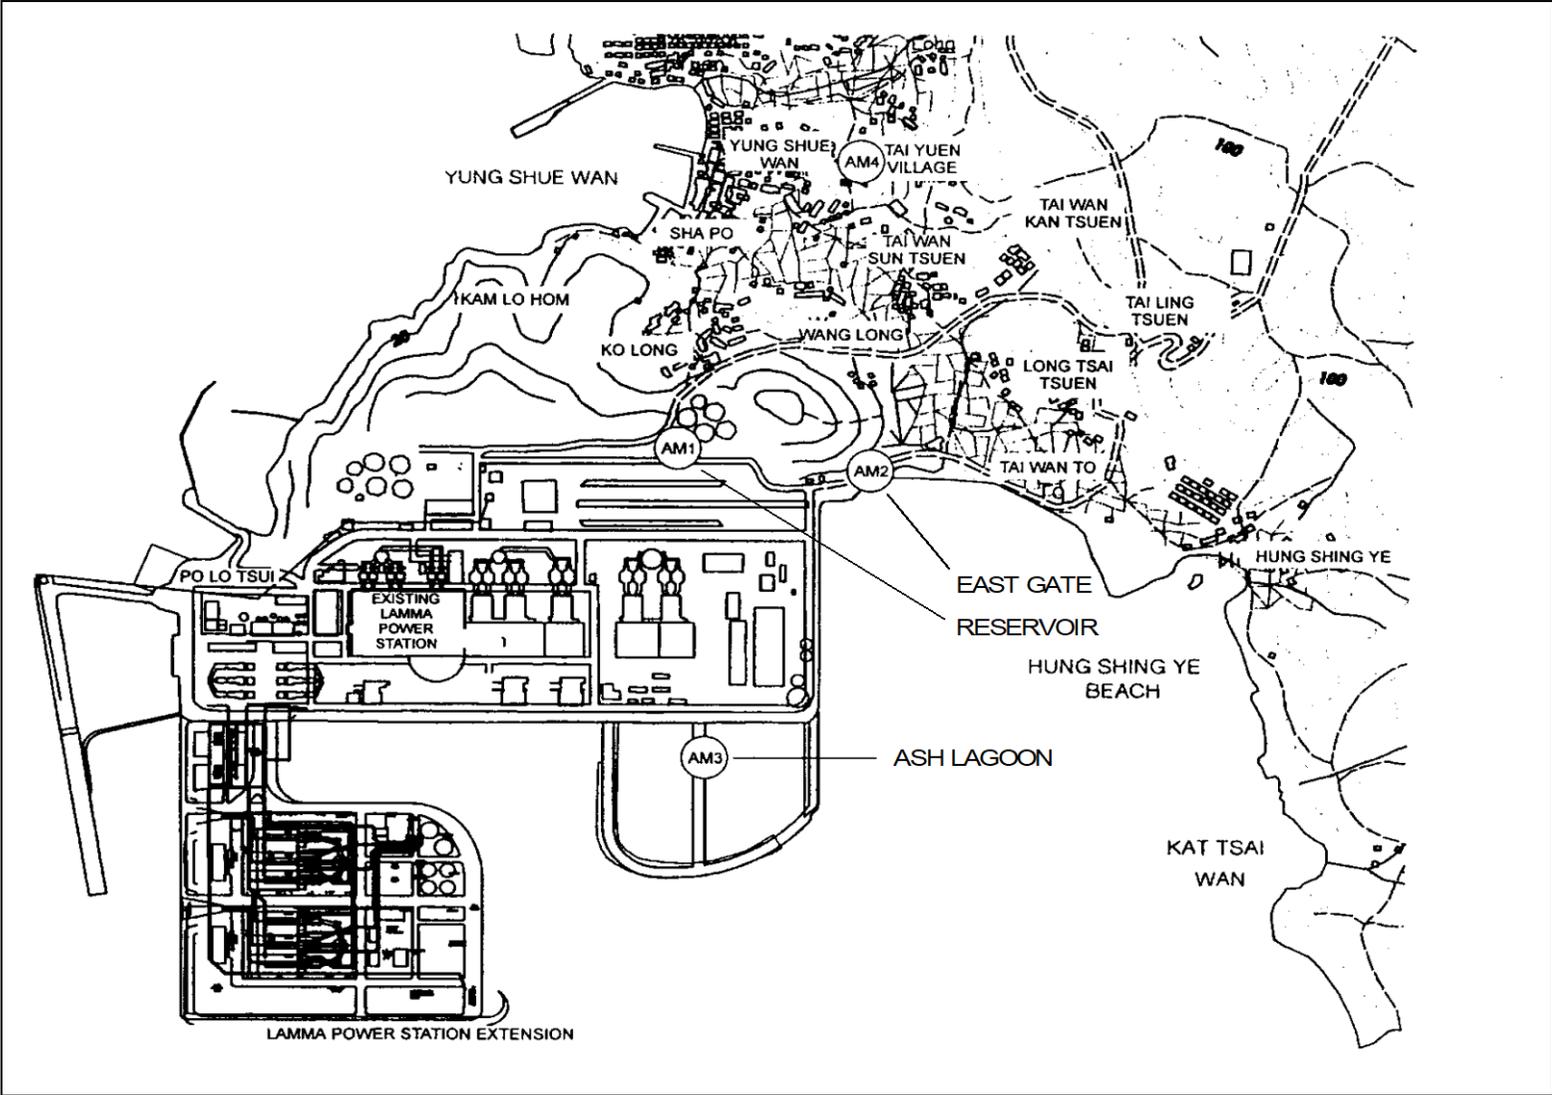


Figure 2.1 Location of Air Quality Monitoring Stations

3. NOISE

3.1 Monitoring Requirements

Continuous noise alarm monitoring at Ash Lagoon/Ching Lam were carried out to calculate the noise contributed by the construction activities at the two critical NSR's, viz. Long Tsai Tsuen/Hung Shing Ye and the school within the village of Tai Wan San Tsuen. The impact monitoring data for construction noise were checked against the limit levels specified in the EM&A Manual. With the availability of the construction noise permits, impact monitoring for the construction work during the restricted hours was also carried out. Section 3 presents the details of the construction noise permits.

The impact noise monitoring data were checked against the limit levels specified in the EM&A Manual. [Appendix B](#) shows the established Action/Limit Levels for noise.

3.2 Monitoring Locations

In accordance with the EM&A manual, the identified noise monitoring locations of Ash Lagoon and Ching Lam are shown in [Figure 3.1](#).

3.3 Monitoring Equipment

The sound level meters used for noise monitoring complied with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). The noise monitoring equipment used is shown in [Table 3.1](#).

Table 3.1 Noise Monitoring Equipment

Equipment	Model
Sound level meters	B&K 2250
Sound level calibrator	B&K 4231

3.4 Monitoring Parameters, Frequency and Duration

Continuous alarm monitoring was carried out at Ash Lagoon and Ching Lam. The measurement duration and parameter of noise monitoring were presented in [Table 3.2](#) as follows:

Table 3.2 Noise Monitoring Duration and Parameter

Location	Time Period	Frequency	Parameter
----------	-------------	-----------	-----------

Ash Lagoon	Day-time: 0700-1900 hrs on normal weekdays	Day-time: 30 minutes	30-min L_{Aeq}
	Evening-time & holidays: 0700-2300 hrs on holidays; and 1900-2300 hrs on all other days	Evening-time & holidays: 5 minutes	5-min L_{Aeq}
Ching Lam	Night-time: 2300-0700 hrs of next day	Night-time: 5 minutes	5-min L_{Aeq}

3.5 Monitoring Procedures and Calibration Details

Monitoring Procedures

Continuous Noise Monitoring for Lamma Extension Construction

The measured noise levels (MNL's) were collected at the noise alarm monitoring stations at Ash Lagoon and Ching Lam. The notional background noise levels (viz. baseline noise data at Ash Lagoon and Ching Lam) were applied to correct the corresponding MNL's in 30-min/5-min L_{Aeq} .

A wind speed sensor was installed at Station Building Rooftop. The wind speed signal was used to determine whether the data from Ash Lagoon and Ching Lam noise alarm monitoring stations were affected. The instantaneous data was discarded in case the instantaneous wind speed exceeded 10 m/s. The 30-min/5-min L_{Aeq} was considered valid only if the amount of valid data was equal to or above 70%.

Equipment Calibration

The sound level meters and calibrators were verified by the manufacturer or accredited laboratory. With the endorsement of the Independent Environmental Checker, the enhancement of calibration of sound level meter at the noise monitoring stations was implemented. The monthly manual on-site calibration using sound level calibrator was replaced by the daily auto charge injection calibration function of the sound level meter. For additional quality assurance, manual on-site calibration would still be conducted for the noise monitoring stations once every 6 months. The manual on-site calibrations for Ash Lagoon and Ching Lam noise monitoring stations were carried out in March and August 2021 respectively. The next calibrations for the two noise monitoring stations were scheduled in September 2021 and February 2022.

3.6 Results and Observations

Continuous noise monitoring was conducted at the two monitoring stations at Ash Lagoon and Ching Lam.

All monitoring results and their graphical presentations are provided in [Appendix E](#). No exceedance of noise Action/Limit Level was recorded in the month.

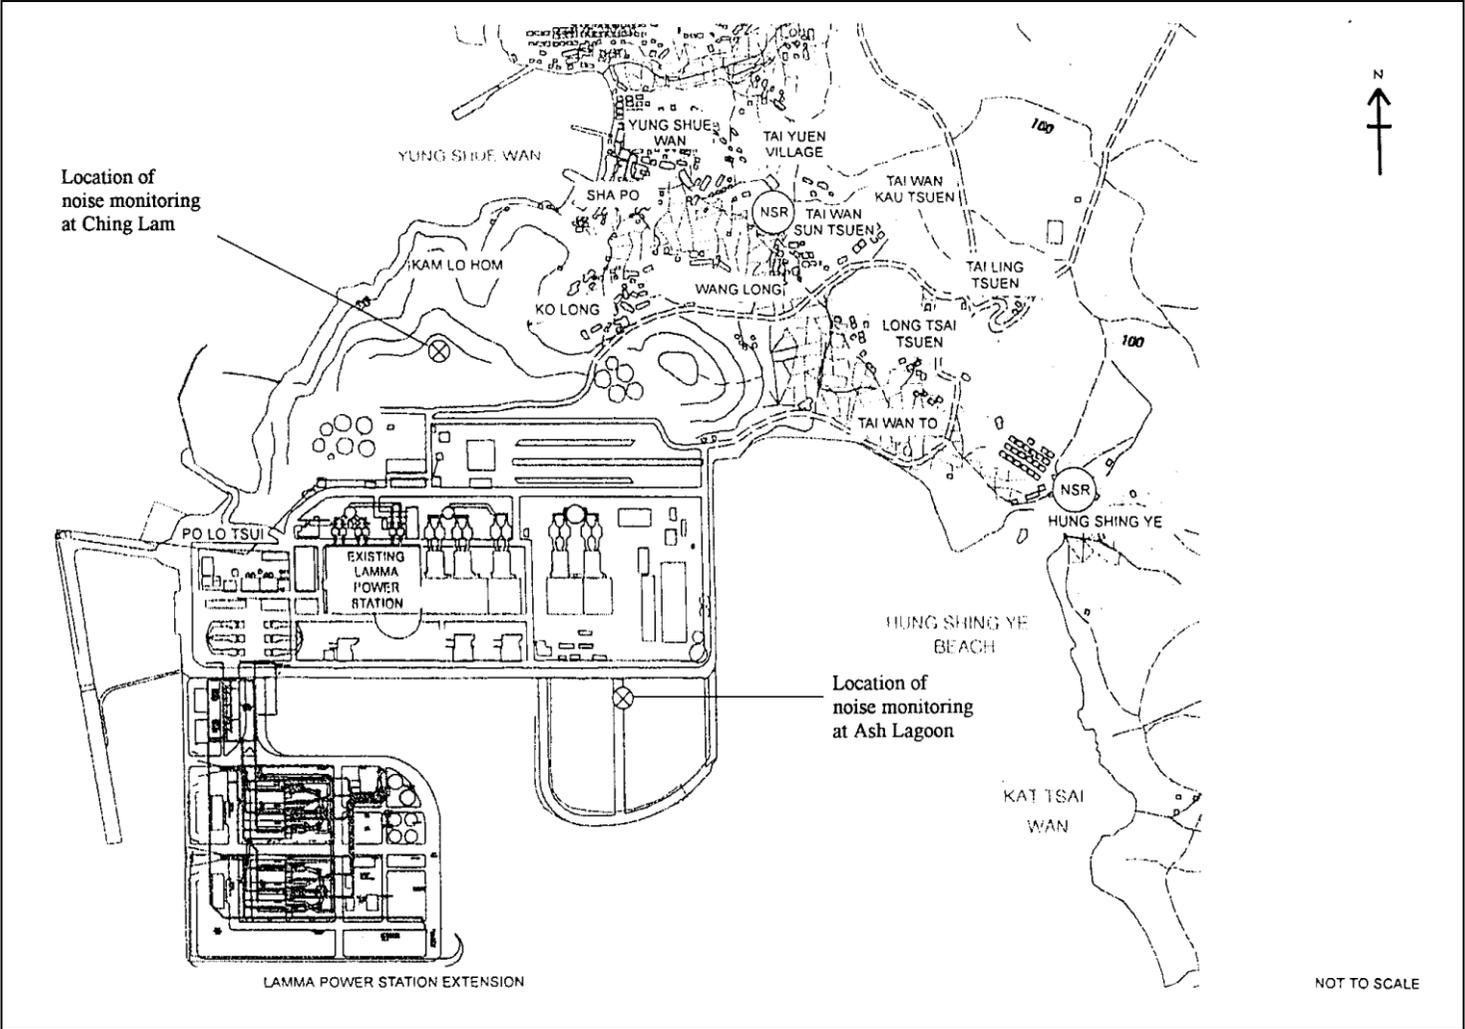


Figure 3.1 Location of Noise Monitoring Stations

4. ENVIRONMENTAL AUDIT

4.1 Review of Environmental Monitoring Procedures

The environmental monitoring procedures were regularly reviewed by the Environmental Team. No modification to the existing monitoring procedures was recommended.

4.2 Assessment of Environmental Monitoring Results

Monitoring results for Air Quality and Noise

The environmental monitoring results for Air Quality and Noise in the reporting month presented in Sections 2 and 3 respectively are summarized in [Table 4.1](#).

Table 4.1 Summary of AL Level Exceedances on Monitoring Parameters

Item	Parameter Monitored	Monitoring Period	No. of Exceedances In		Event/Action Plan Implementation Status and Results
			Action Level	Limit Level	
Air					
1	Ambient TSP (24-hour)	01/08/2021-31/08/2021	0	0	
2	Ambient TSP (1-hour)	01/08/2021-31/08/2021	0	0	
Noise					
1	Noise level at the critical NSR's predicted by the noise alarm monitoring system	01/08/2021-31/08/2021	0	0	

4.3 Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. Inert C&D materials comprise excavated materials and broken concrete. Non-inert C&D materials comprise general refuse, metals and paper/ cardboard packaging, plastics, chemical waste, etc.

Inert C&D material and non-inert C&D material disposed of in August 2021 are shown in [Table 4.2](#).

Table 4.2 Estimated Amounts of Waste in August 2021

Total Inert C&D Waste Materials	Non-inert C&D Materials		
	C&D Materials Recycled	C&D Waste Disposed of at Landfill	Chemical Waste

0 Tonnes	14.55 Tonnes	50.06 Tonnes	0 Litres
----------	--------------	--------------	----------

The monthly waste flow tables prepared by the contractors are attached in [Appendix K](#)

4.4 Site Environmental Audit

EPD officials from Regional Office (South) visited Lamma Power Station on 24/8/2021. There was no adverse comment from EPD regarding the construction site.

Site audits were carried out by ET on a weekly basis to monitor environmental issues at the construction sites to ensure that all mitigation measures were implemented timely and properly. The site audit findings for the reporting month are summarized in [Appendix H](#). The site conditions were generally satisfactory. All required mitigation measures were implemented.

4.5 Status of Environmental Licensing and Permitting

All permits/licenses obtained for the project are summarised in [Table 4.3](#).

Table 4.3 Summary of Environmental Licensing and Permit Status

Description	Permit No.	Valid Period		Highlights	Status
		From	To		
Varied Environmental Permit	EP-071/2000/D	28/09/20	-	The whole construction work site	Valid
Construction Noise Permit	GW-RS0072-21	08/02/21	07/08/21	Civil and Building Works for Unit L12. Operation of PME during restricted hours	Valid
Construction Noise Permit	GW-RS0436-21	01/07/21	31/12/21	Power Block Facilities works for Unit L11. Operation of PME during restricted hours	Valid
Construction Noise Permit	GW-RS0600-21	08/08/21	07/02/22	Civil and Building Works for Unit L12. Operation of PME during restricted hours	Valid
WPCO Discharge Licence#	WT00034006-2019	08/08/19	31/08/24	Civil and Building Works for Unit L11	Valid
WPCO Discharge Licence##	WT00037613-2021	15/04/21	30/04/26	Civil and Building Works for Unit L12 (No.5 C.W. Intake and Cable Bridge)	Valid
Registration of Chemical Waste Producer	WPN5213-912-P2781-22	22/02/16	-	Civil and Building Works	Valid

Description	Permit No.	Valid Period		Highlights	Status
		From	To		
Registration of Chemical Waste Producer	WPN5517-912-T2007-02	17/03/05	-	E&M Equipment Installation and Maintenance	Valid
Waste Disposal Billing Account	Account No.: 7031135	21/06/18	-	Civil and Building Works for Unit L11	Valid
Waste Disposal Billing Account	Account No.: 7027672	24/04/17	-	E&M Erection of Power Block Facilities – L11	Valid
Waste Disposal Billing Account	Account No.: 7038672	27/10/20	-	Civil works for Unit L12 No.5 C.W. intake and cable bridge	Valid
Waste Disposal Billing Account	Account No.: 7039272	08/01/21	-	Civil and building works for Unit L12	Valid

Notes: # - Water quality monitoring was carried out in August 2021 and the results of which had been reported separately by the contractor.
 ## - Water quality monitoring was carried out in August 2021 and the results of which had been reported separately by the contractor.

4.6 Implementation Status of Environmental Mitigation Measures

Mitigation measures detailed in the permits and the EM&A Manual (Construction Phase) are required to be implemented. An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is presented in [Appendix I](#).

4.7 Implementation Status of Event/Action Plans

The Event/Action Plans extracted from the EM&A Manual (Construction Phase) are presented in [Appendix G](#).

4.8 Implementation Status of Environmental Complaint Handling Procedures

In August 2021, no complaint against the construction activities was received.

Table 4.4 Environmental Complaints Received in August 2021

Case Reference / Date, Time Received / Date, Time Concerned	Descriptions / Actions Taken	Conclusion / Status
Nil	N/A	N/A

Table 4.5 Outstanding Environmental Complaints Carried Over

Case Reference / Date, Time Received / Date, Time Concerned	Descriptions / Actions Taken	Conclusion / Status
Nil	N/A	N/A

5. FUTURE KEY ISSUES

5.1 Key Issues for the Coming Month

Key issues to be considered in the coming month include:

Unit L11 Civil and Building Works

Noise Impact

- To continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the noise performance.

Air Impact

- To monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

Water Impact

- To treat wastewater in sedimentation pit and tanks before discharge and to ensure compliance in accordance with the WPCO discharge licence already obtained.

Unit L11 Mechanical Erection

Noise Impact

- To continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained.
- To continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the noise performance.

Air Impact

- To monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

Unit L11 Electrical, Instrumentation & Control Erection

Noise Impact

- To continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained.
- To continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the noise performance.

Air Impact

- To monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

Unit L12 Civil and Building Works

Noise Impact

- To continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained.

Air Impact

- To monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

Water Impact

- To treat wastewater in sedimentation pit and tanks before discharge and to ensure compliance in accordance with the WPCO discharge licence already obtained.
- To provide silt curtain as preventive measures at Northern Cable Bridge area.

5.2 Monitoring Schedules for the Next 3 Months

The tentative environmental monitoring schedules for the next 3 months are shown in [Appendix C](#).

5.3 Construction Program for the Next 3 Months

The tentative construction programs for the next 3 months are shown in [Appendix J](#).

6. CONCLUSION

All monitoring work at designated stations was performed as scheduled satisfactorily. The environmental monitoring works and site inspection were performed as scheduled in the reporting month. All monitoring results were checked and reviewed.

No Action/Limit level exceedance on 1-hour and 24-hour TSP level was recorded in the reporting month.

No Action/Limit level exceedance on noise was recorded in the reporting month.

Environmental mitigation measures recommended in the EM&A manual for the construction activities were implemented in the reporting month. No complaint against the construction activities was received in the reporting month. No prosecution was received for this Project in the reporting period.

The environmental performance of the Project was generally satisfactory.

Appendix A Organization Chart

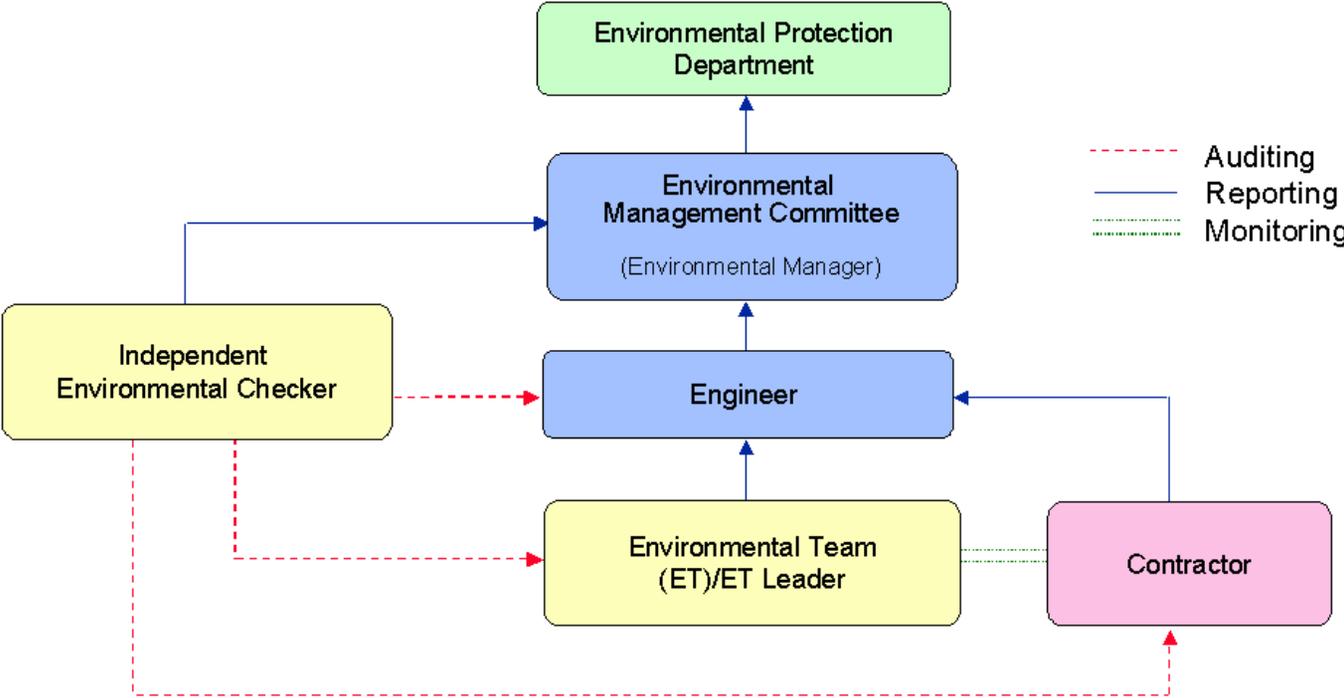


Figure A.1 Organisation of EM&A Programme at Construction Phase

Appendix B Action and Limit Levels for Air Quality and Noise Monitoring

B.1. Air

Table B.1 Action and Limit Levels for 1-hour and 24-hour TSP

	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
1-hour TSP*	340	500
24-hour TSP	190	260

* No Action/Limit Level for 1-hour TSP is applied to AM4 where no real time dust monitor is installed.

B.2. Noise

Table B.2 AL Levels for Construction Noise (Other than Percussive Piling)

Parameters	Action	Limit
Noise Levels at the NSR's at Long Tsai Tsuen/Hung Shing Ye and school within the village of Tai Wan San Tsuen predicted by the noise alarm monitoring system	When one or more documented complaints are received	a. 75 dB(A) in $L_{Aeq,30 \text{ min}}$ (07:00-19:00 hrs on normal weekdays) (Note 1)
Manual noise monitoring at the nearest Pak Kok Tsui residences to cable landing points N4 and N5		b. subject to statutory control under the Noise Control Ordinance (07:00-23:00 hrs on holidays and 19:00-23:00 hrs on all other days). Set to 60 dB(A) in $L_{Aeq,5 \text{ min}}$ c. subject to statutory control under the Noise Control Ordinance (23:00-07:00 hrs of next day). Set to 45 dB(A) in $L_{Aeq,5 \text{ min}}$
Note:		
1. For educational institution, the limit level shall be 70 dB(A), reduced to 65 dB(A) during examination periods.		

Appendix C Environmental Monitoring Schedule

Table C.1 Monitoring schedule for 24hr and 1hr TSP monitoring for Lamma Extension Construction (August 2021 to November 2021)

24hr TSP Monitoring	1hr TSP Monitoring
4/August/2021	4/August/2021 1500hr to 1800hr
10/August/2021	10/August/2021 1500hr to 1800hr
16/August/2021	16/August/2021 1500hr to 1800hr
22/August/2021	22/August/2021 1500hr to 1800hr
28/August/2021	28/August/2021 1500hr to 1800hr
3/September/2021	3/September/2021 1500hr to 1800hr
9/September/2021	9/September/2021 1500hr to 1800hr
15/September/2021	15/September/2021 1500hr to 1800hr
21/September/2021	21/September/2021 1500hr to 1800hr
27/September/2021	27/September/2021 1500hr to 1800hr
3/October/2021	3/October/2021 1500hr to 1800hr
9/October/2021	9/October/2021 1500hr to 1800hr
15/October/2021	15/October/2021 1500hr to 1800hr
21/October/2021	21/October/2021 1500hr to 1800hr
27/October/2021	27/October/2021 1500hr to 1800hr
2/November/2021	2/November/2021 1500hr to 1800hr
8/November/2021	8/November/2021 1500hr to 1800hr
14/November/2021	14/November/2021 1500hr to 1800hr
20/November/2021	20/November/2021 1500hr to 1800hr
26/November/2021	26/November/2021 1500hr to 1800hr

APPENDIX D AIR QUALITY MONITORING RESULTS

Site: Lamma Power Station Extension

Month: August 2021

24 hour TSP Measurement:-

Date	TSP concentration ($\mu\text{g}/\text{m}^3$)				Weather Information (From Hong Kong Observatory)		
	Reservoir (AM1)	East Gate (AM2)	Ash Lagoon (AM3)	Tai Yuen Village (AM4)	Mean Wind Speed (km/hr)	Prevailing Wind Dir. ($^{\circ}$)	Mean R.H. (%)
4/8/2021	17	34	27	13	22.4	360	85
10/8/2021	46	37	28	10	14.8	190	87
16/8/2021	20	26	11	11	7.9	240	83
22/8/2021	22	25	13	7	21.3	230	74
28/8/2021	17	20	16	15	16.2	10	81



1 hour TSP Measurement:-

Date	Time	TSP concentration ($\mu\text{g}/\text{m}^3$)		
		Reservoir (AM1)	East Gate (AM2)	Ash Lagoon (AM3)
4/8/2021	15:00 - 15:59	39	36	34
	16:00 - 16:59	32	36	27
	17:00 - 17:59	19	34	23
10/8/2021	15:00 - 15:59	52	35	27
	16:00 - 16:59	35	36	26
	17:00 - 17:59	45	34	26
16/8/2021	15:00 - 15:59	17	21	12
	16:00 - 16:59	23	22	12
	17:00 - 17:59	37	19	13
22/8/2021	15:00 - 15:59	19	31	12
	16:00 - 16:59	28	33	13
	17:00 - 17:59	21	22	11
28/8/2021	15:00 - 15:59	9	17	13
	16:00 - 16:59	14	16	12
	17:00 - 17:59	18	18	14


	1-hr TSP ($\mu\text{g}/\text{m}^3$)	24-hr TSP ($\mu\text{g}/\text{m}^3$)
Action Level	340	190
Limit Level	500	260
Calibration:	Calibration details are shown in appendix F.	

Equipment used:


Location	1-hr TSP	24-hr TSP
Reservoir, East Gate and Ash Lagoon	TEOM	TEOM
Tai Yuen Village	-	MINIVOL Portable Sampler

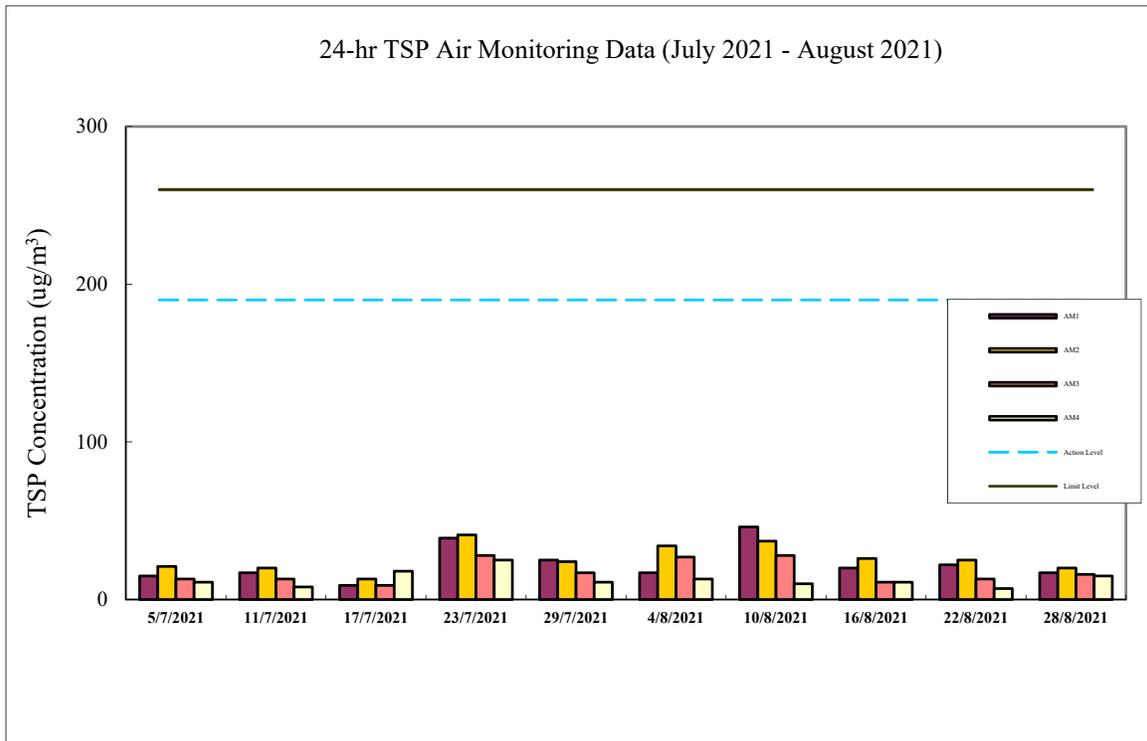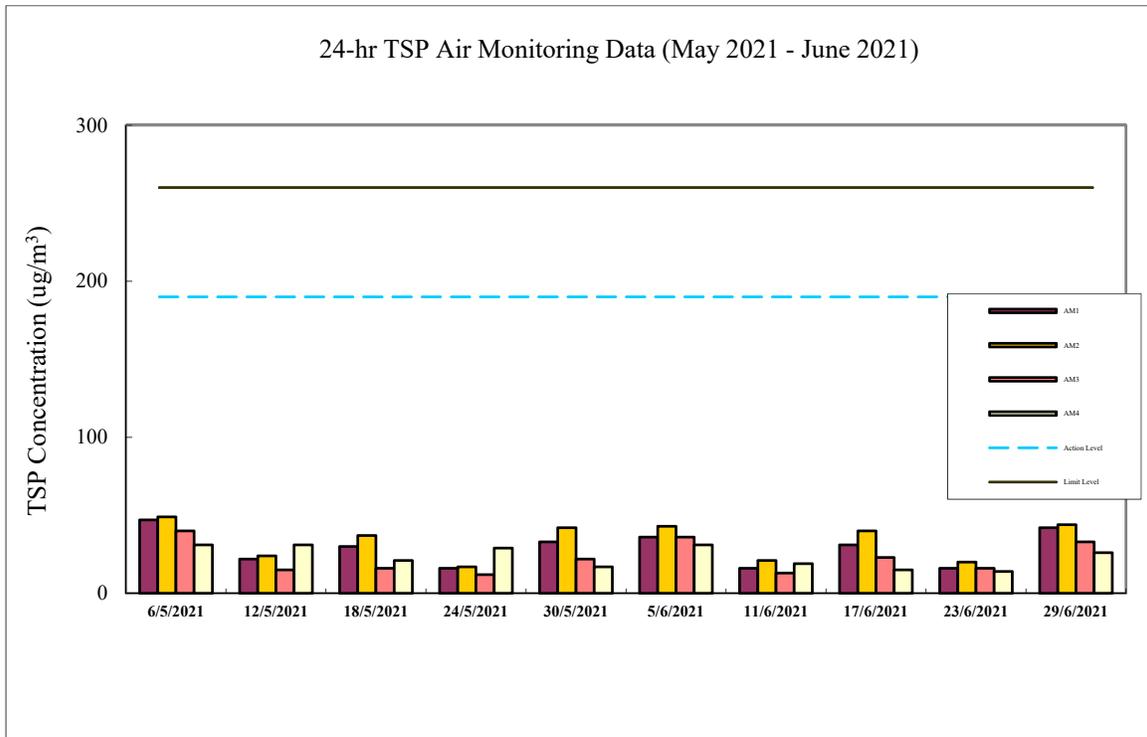

1-hr TSP Air Monitoring Data (May 2021 - June 2021)

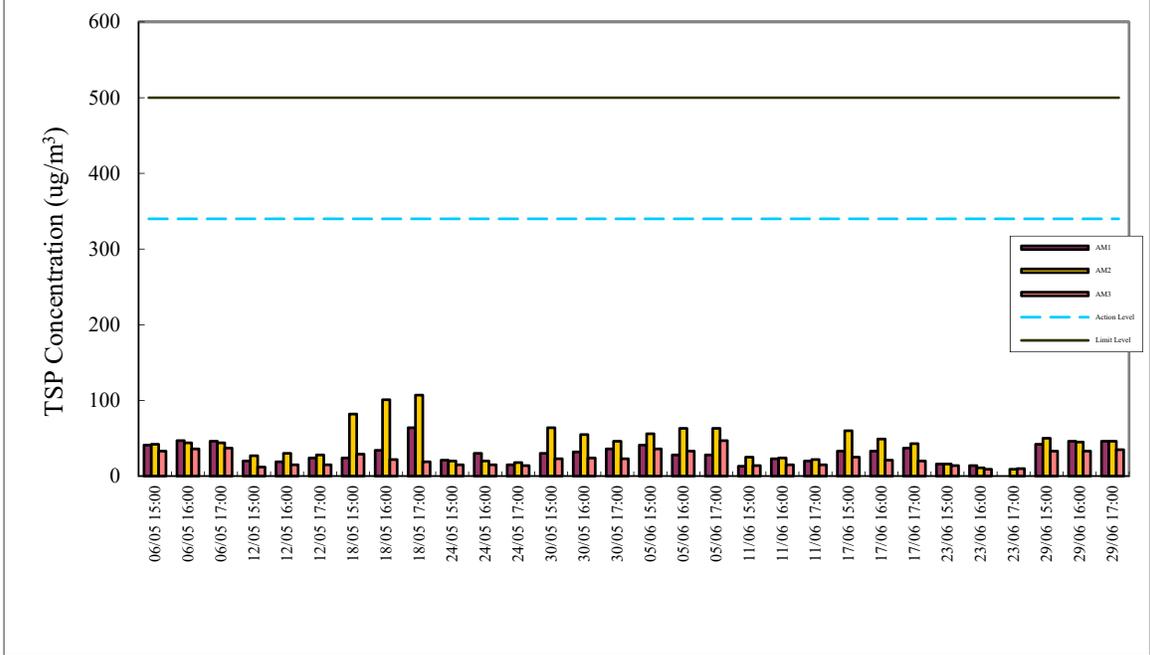

1-hr TSP Air Monitoring Data (July 2021 - August 2021)

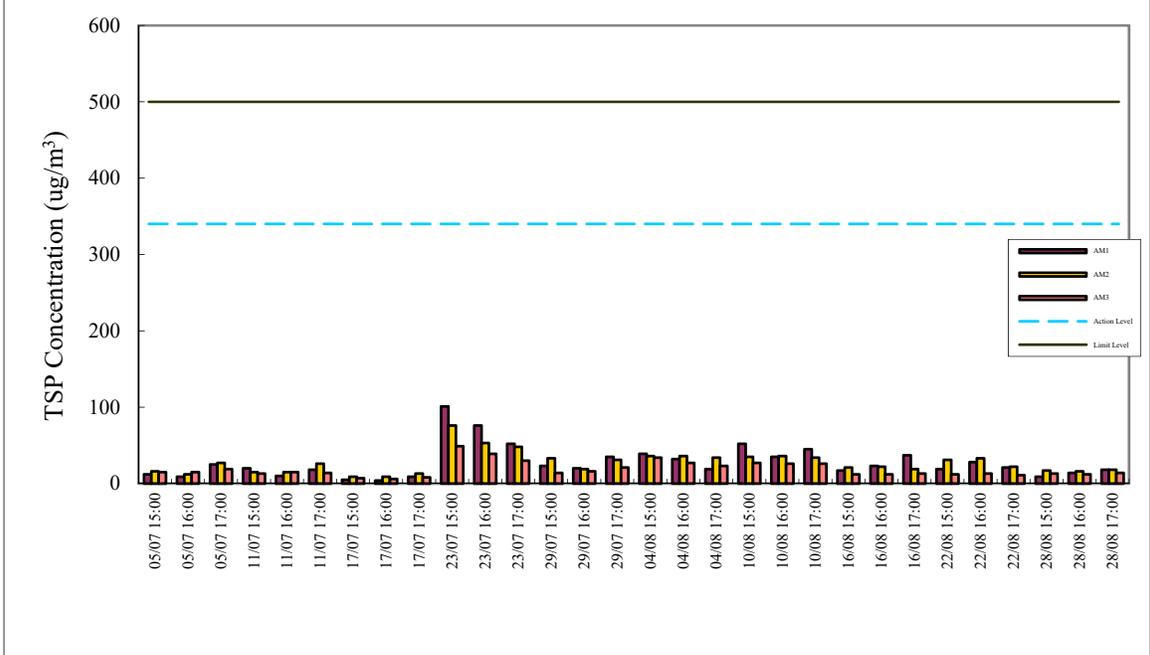

Appendix E

Continuous Noise Monitoring Results for August 2021

Site: Lamma Power Station Extension Construction
 Measurement Location: Ash Lagoon and Ching Lam
 Measurement Parameter: 30-min Leq (07:00-19:00 hrs on normal weekdays)
 5-min Leq (07:00-23:00 hrs on holidays and
 19:00-23:00 hrs on all other days, and 23:00-
 07:00 hrs of next day)
 Noise Equipment: B&K 2250 sound level meters and B&K 4231 sound
 Level calibrator
 Lab. Calibration Date: B&K 2250 sound level meters - 28/06/2020 (Ash Lagoon)
 02/09/2020 (Ching Lam)
 B&K 4231 calibrator - 05/10/2020


Date	Time	Calculated Noise Level at NSR at Long Tsai Tsuen/Hung Shing Ye (dB(A))		Limit Noise Level (dB(A))	Calculated Noise Level at NSR at the school within Tai Wan San Tsuen (dB(A))		Limit Noise Level (dB(A))
		Max	Avg		Max	Avg	
01/08/2021	07:00-23:00	59	46	60	57	41	60
01/08/2021	23:00-07:00	45	42	45	41	34	45
02/08/2021	07:00-19:00	54	54	75	33	30	70
02/08/2021	19:00-23:00	---	---	60	---	---	60
02/08/2021	23:00-07:00	44	41	45	42	32	45
03/08/2021	07:00-19:00	---	---	75	42	35	70
03/08/2021	19:00-23:00	---	---	60	---	---	60
03/08/2021	23:00-07:00	44	41	45	39	36	45
04/08/2021	07:00-19:00	46	41	75	40	36	70
04/08/2021	19:00-23:00	44	39	60	31	31	60
04/08/2021	23:00-07:00	45	39	45	38	33	45
05/08/2021	07:00-19:00	---	---	75	43	43	70
05/08/2021	19:00-23:00	---	---	60	43	42	60
05/08/2021	23:00-07:00	45	39	45	36	32	45
06/08/2021	07:00-19:00	---	---	75	38	35	70
06/08/2021	19:00-23:00	41	41	60	---	---	60
06/08/2021	23:00-07:00	44	39	45	40	33	45
07/08/2021	07:00-19:00	---	---	75	40	40	70
07/08/2021	19:00-23:00	---	---	60	34	31	60
07/08/2021	23:00-07:00	---	---	45	37	30	45
08/08/2021	07:00-23:00	50	42	60	45	34	60
08/08/2021	23:00-07:00	43	37	45	42	31	45
09/08/2021	07:00-19:00	51	51	75	43	37	70
09/08/2021	19:00-23:00	---	---	60	37	35	60
09/08/2021	23:00-07:00	44	36	45	42	33	45
10/08/2021	07:00-19:00	41	41	75	43	36	70
10/08/2021	19:00-23:00	---	---	60	35	35	60
10/08/2021	23:00-07:00	45	39	45	38	30	45
11/08/2021	07:00-19:00	---	---	75	43	30	70
11/08/2021	19:00-23:00	---	---	60	---	---	60
11/08/2021	23:00-07:00	39	32	45	38	32	45
12/08/2021	07:00-19:00	---	---	75	43	36	70
12/08/2021	19:00-23:00	---	---	60	34	32	60
12/08/2021	23:00-07:00	38	31	45	38	31	45
13/08/2021	07:00-19:00	---	---	75	40	36	70
13/08/2021	19:00-23:00	43	38	60	---	---	60

13/08/2021	23:00-07:00	44	38	45	40	33	45
14/08/2021	07:00-19:00	---	---	75	37	33	70
14/08/2021	19:00-23:00	---	---	60	49	40	60
14/08/2021	23:00-07:00	---	---	45	45	34	45
15/08/2021	07:00-23:00	50	46	60	41	33	60
15/08/2021	23:00-07:00	45	39	45	40	32	45
16/08/2021	07:00-19:00	---	---	75	34	34	70
16/08/2021	19:00-23:00	---	---	60	39	34	60
16/08/2021	23:00-07:00	43	41	45	42	35	45
17/08/2021	07:00-19:00	---	---	75	37	34	70
17/08/2021	19:00-23:00	---	---	60	44	37	60
17/08/2021	23:00-07:00	42	38	45	45	36	45
18/08/2021	07:00-19:00	52	52	75	42	38	70
18/08/2021	19:00-23:00	---	---	60	49	43	60
18/08/2021	23:00-07:00	41	36	45	44	38	45
19/08/2021	07:00-19:00	42	41	75	45	34	70
19/08/2021	19:00-23:00	43	34	60	51	38	60
19/08/2021	23:00-07:00	45	36	45	44	36	45
20/08/2021	07:00-19:00	---	---	75	40	34	70
20/08/2021	19:00-23:00	---	---	60	46	36	60
20/08/2021	23:00-07:00	42	40	45	42	36	45
21/08/2021	07:00-19:00	---	---	75	37	29	70
21/08/2021	19:00-23:00	---	---	60	41	34	60
21/08/2021	23:00-07:00	44	38	45	45	38	45
22/08/2021	07:00-23:00	45	40	60	51	36	60
22/08/2021	23:00-07:00	43	33	45	41	37	45
23/08/2021	07:00-19:00	31	31	75	40	33	70
23/08/2021	19:00-23:00	---	---	60	44	37	60
23/08/2021	23:00-07:00	---	---	45	43	38	45
24/08/2021	07:00-19:00	---	---	75	40	34	70
24/08/2021	19:00-23:00	---	---	60	40	34	60
24/08/2021	23:00-07:00	43	39	45	43	37	45
25/08/2021	07:00-19:00	---	---	75	48	41	70
25/08/2021	19:00-23:00	---	---	60	42	38	60
25/08/2021	23:00-07:00	---	---	45	44	40	45
26/08/2021	07:00-19:00	---	---	75	44	39	70
26/08/2021	19:00-23:00	---	---	60	43	37	60
26/08/2021	23:00-07:00	45	45	45	45	37	45
27/08/2021	07:00-19:00	41	41	75	45	41	70
27/08/2021	19:00-23:00	34	34	60	40	36	60
27/08/2021	23:00-07:00	---	---	45	43	36	45
28/08/2021	07:00-19:00	36	36	75	43	38	70
28/08/2021	19:00-23:00	22	22	60	39	30	60
28/08/2021	23:00-07:00	---	---	45	42	35	45
29/08/2021	07:00-23:00	51	44	60	43	37	60
29/08/2021	23:00-07:00	41	38	45	44	39	45
30/08/2021	07:00-19:00	---	---	75	42	39	70
30/08/2021	19:00-23:00	---	---	60	42	37	60
30/08/2021	23:00-07:00	45	39	45	42	38	45
31/08/2021	07:00-19:00	---	---	75	43	38	70
31/08/2021	19:00-23:00	38	38	60	41	33	60
31/08/2021	23:00-07:00	42	31	45	41	36	45


Note:



- a. "----" represents the measured noise monitoring data lower than the established notional background level/discarded under strong wind.
- b. Continuous noise monitoring was also carried out at holidays & evening-time (07:00-23:00 hrs on holidays and 19:00-23:00 hrs on all other days) and night-time (23:00-07:00 hrs of next day).

Construction Noise Monitoring in May - August 2021
 NSR at Long Tsai Tsuen/Hung Shing Ye
 07:00-19:00 hrs on Normal Weekdays

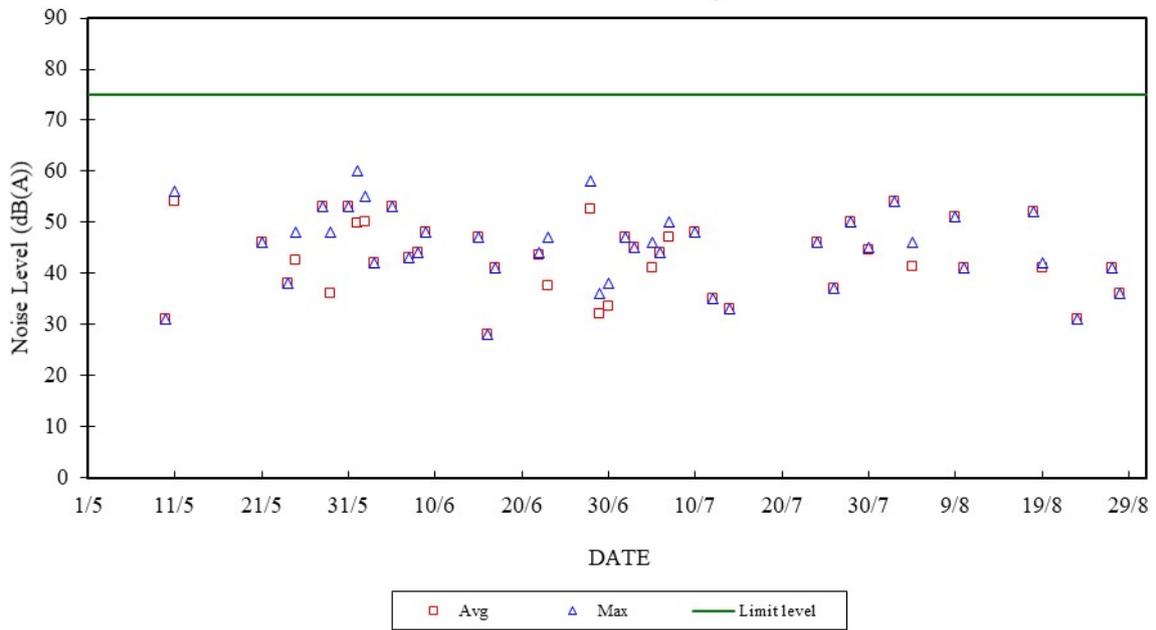


Construction Noise Monitoring in May - August 2021
 NSR at School within Tai Wan San Tsuen
 07:00-19:00 hrs on Normal Weekdays

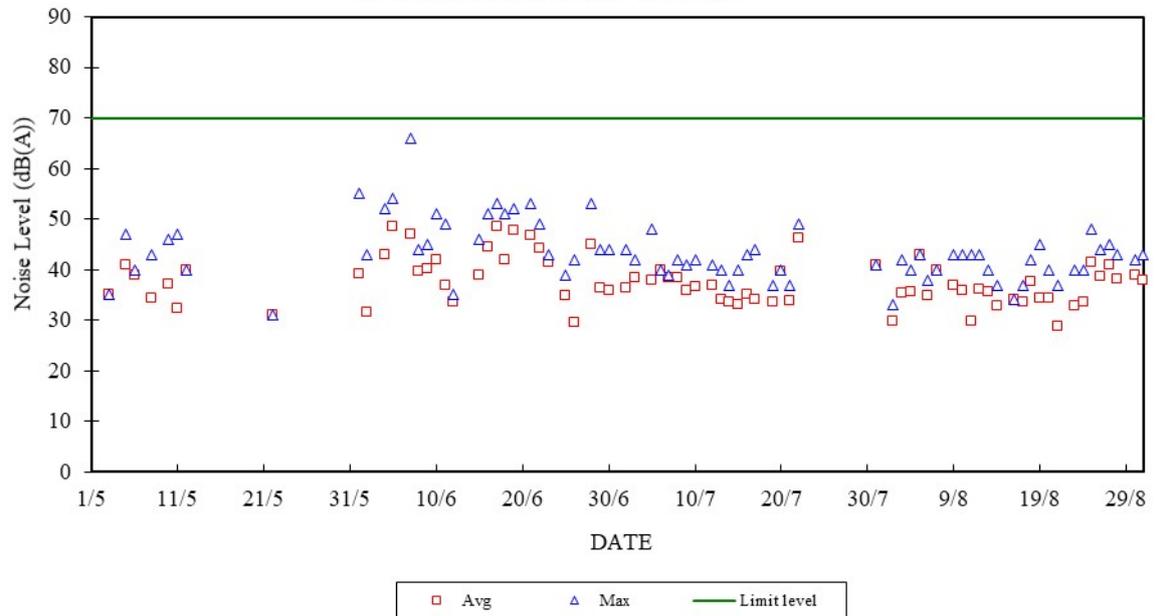


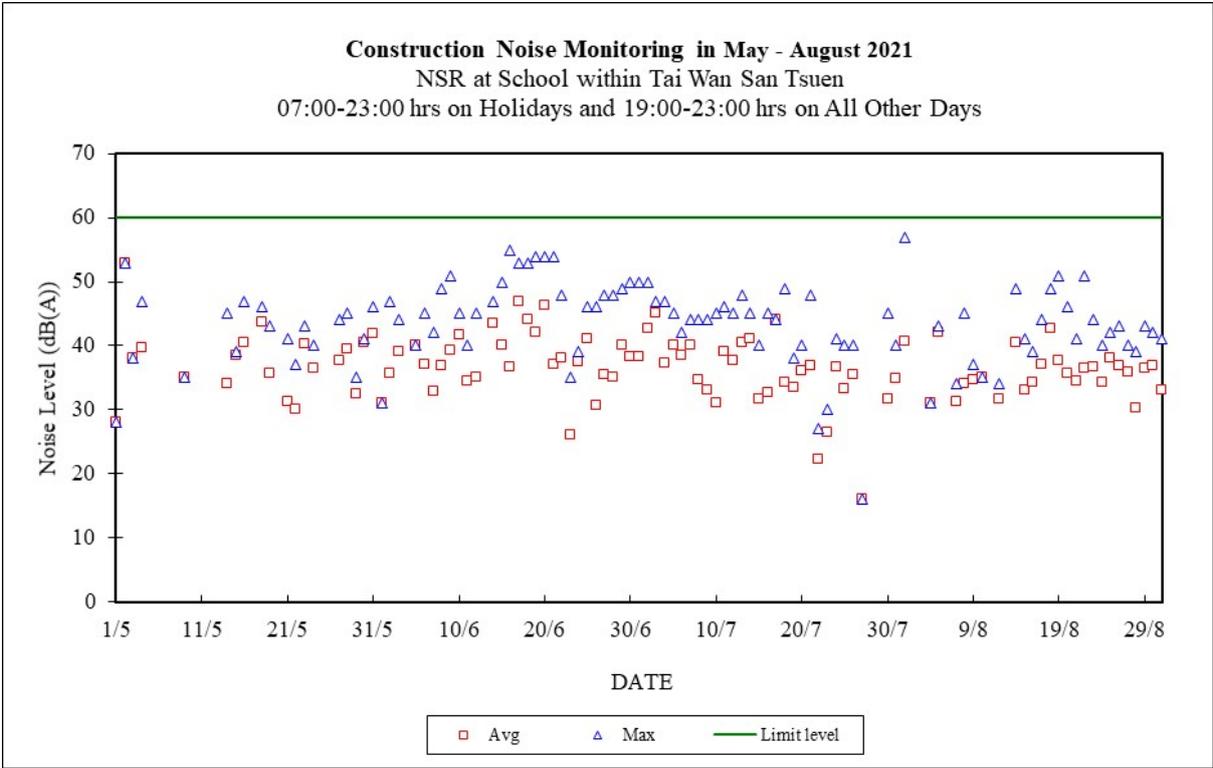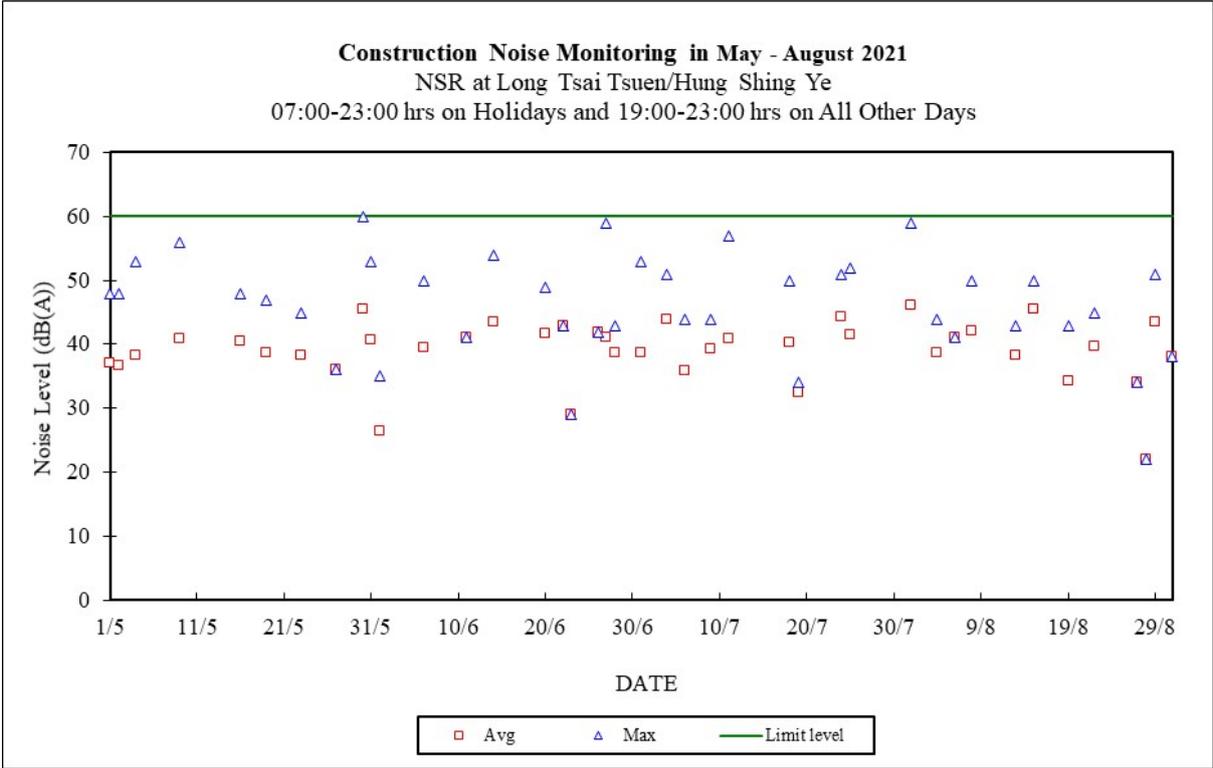

Construction Noise Monitoring in May - August 2021
NSR at Long Tsai Tsuen/Hung Shing Ye
23:00-07:00 hrs of Next Day

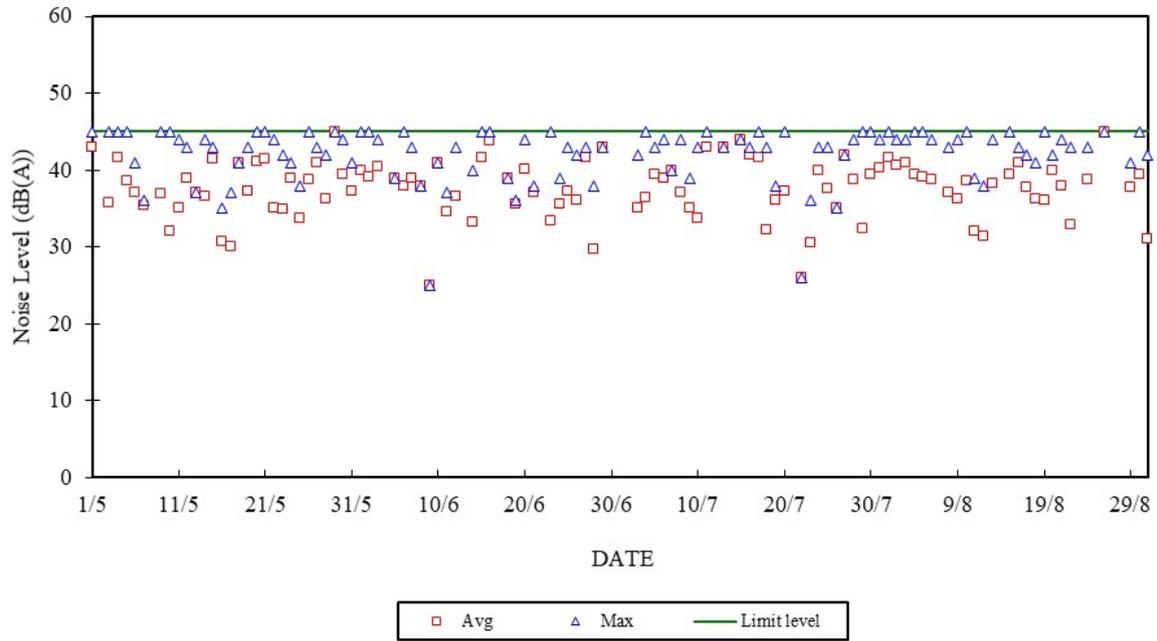

Construction Noise Monitoring in May - August 2021
NSR at School within Tai Wan San Tsuen
23:00-07:00 hrs of Next Day

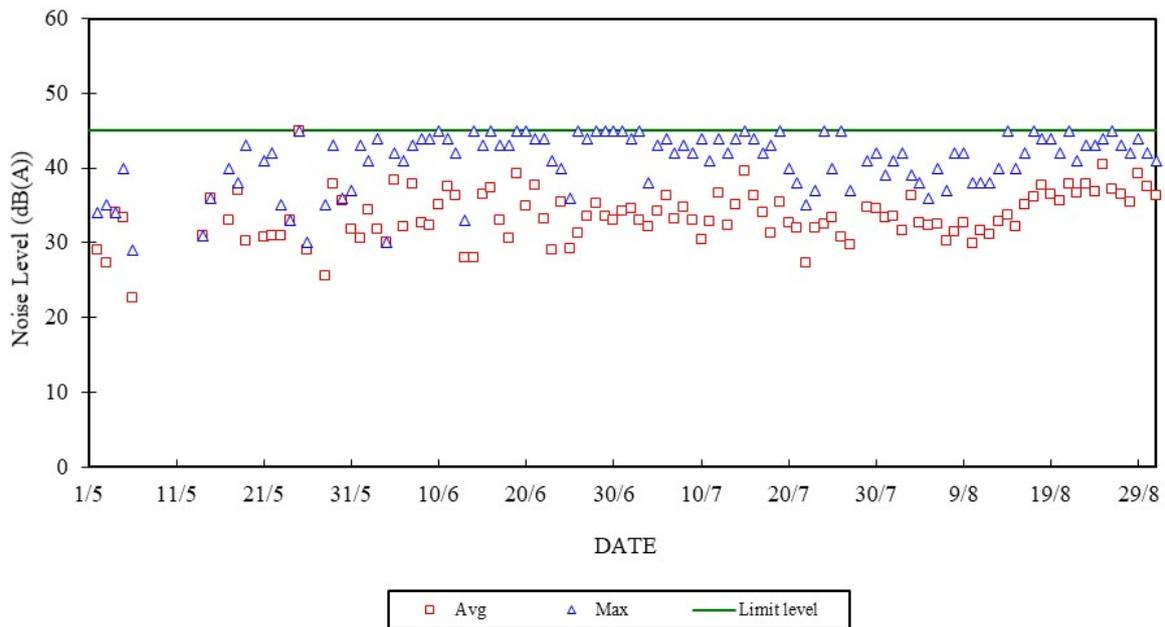

Appendix F

The QA/QC Procedures and Results

The Hongkong Electric Co., Ltd.
Lamma Power Station Extension
TEOM Continuous Dust Monitor
Data Quality Assurance Log Sheet

Month: Aug

Year: 2021

Reservoir (AM1)				
Date	Frequency (Hz) (240 - 275)	Operation Mode (Mode 4)	Main Flow (l/min) (2.70 - 3.30)	Bypass Flow (l/min) (12.30 - 15.04)
4/8/2021	270.035	4	2.93	13.15
10/8/2021	269.508	4	2.95	11.87
16/8/2021	269.177	4	2.97	12.67
22/8/2021	268.876	4	2.93	12.36
28/8/2021	268.675	4	2.96	12.08

East Gate (AM2)				
Date	Frequency (Hz) (240 - 275)	Operation Mode (Mode 4)	Main Flow (l/min) (2.70 - 3.30)	Bypass Flow (l/min) (12.30 - 15.04)
4/8/2021	250.919	4	2.90	13.26
10/8/2021	251.504	4	2.92	13.31
16/8/2021	251.172	4	2.94	13.43
22/8/2021	250.826	4	2.92	13.31
28/8/2021	250.592	4	2.97	13.61

Ash Lagoon (AMB)				
Date	Frequency (Hz) (240 - 275)	Operation Mode (Mode 4)	Main Flow (l/min) (2.70 - 3.30)	Bypass Flow (l/min) (12.30 - 15.04)
4/8/2021	256.192	4	3.00	13.68
10/8/2021	255.868	4	3.00	13.68
16/8/2021	255.668	4	3.00	13.68
22/8/2021	257.045	4	3.00	13.68
28/8/2021	256.904	4	3.00	13.68

Maintenance Record			
	Reservoir	East Gate	Ash Lagoon
TEOM Filter Exchange	✓	✓	✓
Clean TSP Inlet	✓	✓	✓
Replace flow in-line filter	✓	✓	✓
Pump Repair			
Leak Check			
Flow audit			
Flow Controller Calibration			
A/C filter cleaning			

Remarks:

Prepared by: Chris Chan

Checked by: HY Chan

The Hongkong Electric Co., Ltd.
Mini Volume Air Sampler Site Visit Log Sheet

Attendance Log _____

Site Name: Tai Yuen Village (AM4)

Date/Time	Staff Name
17/08/2021 / 14:15	WM Tam

Equipment / Item

Equipment / Item	Serial No. / No.
MINIVOL	5580
Used filter paper no.	MR53
New filter paper no.	MR54

Type of filter: Glass-fibre

- I. Calibration is performed by using Drycal DC-2 Flow Calibrator
5 std. L/min set point is recommended

Before: 5.012
After: 5.012 (No adjustment)

II. General Services

1. Clean Rotameter: Yes
2. Clean / Replace Pump Valves: No
3. Clean / Replace Pump Diaphragms: No
4. Clean Impaction Inlet: Yes
5. Replace Timer Battery Every 6 months: No
6. Replace Inlet Filter: Yes

Remarks

N/A

Conducted by: WM Tam

Checked by: SM Hon

The Hongkong Electric Co., Ltd.
Lamma Power Station Extension
Noise Monitoring Station
Site Visit Log Sheet

Location: Ching Lam

Date/Time	Staff Attended
18/8/2021 / 14:00	WM Tam / Brian So

Equipment	Serial No.
B&K 2250	3009916

1. Calibration

Acoustic calibrator: B&K 4231 (S/N: 3014754)
Noise level measured in calibration: 94.0 (94 ±1.0 dBA)

2. Weather Conditions

- a. Sunny
- b. Calm

3. Remark/Observation

N/A

Prepared by: WM Tam

Checked by: TL Chu

The Hongkong Electric Co., Ltd.
Lamma Power Station Extension
Noise Monitoring Station
Daily Calibration Record

Date	Location: Ash Lagoon	
	Calibration Results	Deviation from Reference (dB)
01/08/2021	Passed	-0.03
02/08/2021	Passed	-0.03
03/08/2021	Passed	-0.04
04/08/2021	Passed	-0.02
05/08/2021	Passed	-0.07
06/08/2021	Passed	-0.05
07/08/2021	Passed	-0.02
08/08/2021	Passed	-0.04
09/08/2021	Passed	-0.03
10/08/2021	Passed	-0.02
11/08/2021	Passed	-0.02
12/08/2021	Passed	-0.03
13/08/2021	Passed	-0.04
14/08/2021	Passed	-0.05
15/08/2021	Passed	-0.03
16/08/2021	Passed	-0.02
17/08/2021	Passed	-0.04
18/08/2021	Passed	-0.02
19/08/2021	Passed	-0.01
20/08/2021	Passed	0.00
21/08/2021	Passed	-0.02
22/08/2021	Passed	-0.01
23/08/2021	Passed	-0.01
24/08/2021	Passed	-0.02
25/08/2021	Passed	-0.01
26/08/2021	Passed	-0.05
27/08/2021	Passed	-0.04
28/08/2021	Passed	-0.02
29/08/2021	Passed	-0.04
30/08/2021	Passed	-0.05
31/08/2021	Passed	-0.06

Remarks:

1. The B&K sound level meter at the noise monitoring station has an advanced feature of internal calibration checking (viz. Charge Injection Calibration (CIC)). CIC is a B&K patented method for in situ verification of the integrity of the entire sound measurement chain (including microphone, preamplifier and cabling).
2. The acceptance criterion of deviation from reference is ± 0.5 dB.

Appendix G Event/Action Plans

Table G.1 Event and Action Plans for Air Quality

Event	Monitoring		Action	
	ET Leader	IEC	Engineer	Contractor
Action Level				
Exceedance of one sample	Identify source Inform Engineer and IEC verbally Repeat measurement to confirm finding	Check monitoring data submitted by ET and advise Engineer.	Notify Contractor Checking monitoring data and contractor's working methods	Rectify any unacceptable practice amend any working methods if appropriate
Exceedance of two or more consecutive samples	Identify source Inform Engineer and IEC verbally Repeat measurement to confirm finding Increase monitoring frequency Discuss with Engineer and Contractor on remedial actions required If exceedance continues, arrange meeting with Engineer If exceedance stops, discontinue additional monitoring	Check monitoring data submitted by ET and advise Engineer. Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Confirm receipt of notification of failure in writing Notify contractor Checking monitoring data and contractor's working methods Discuss proposed remedial actions with the ET and Contractor Ensure remedial actions properly implemented	Submit proposals for remedial actions to Engineer within 3 working days of notifications Implement the agreed proposals Amend proposal if appropriate
Limit level				
Exceedance of one sample	Repeat measurement to confirm finding. Identify the source(s) of the impact. If the exceedance is found to be valid and due to the Construction works, verbally advise the Contractor, Engineer and IEC, and inform the EPD of the exceedance, as soon as practicable. Increase monitoring frequency to daily Assess the effectiveness of the contractor's remedial actions and keep Engineer, IEC and EPD informed of the results	Check monitoring data submitted by ET and advise Engineer Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Confirm receipt of notification of failure in writing Notify Contractor Checking monitoring data and Contractor's working method Discuss with ET and Contractor on remedial actions to be provided Ensure remedial measures properly implemented	Take immediate action to avoid further exceedance Submit proposals for remedial actions to Engineer within 3 working days of notifications Implement the agreed proposals Amend proposal if appropriate
Exceedance of two or more	Identify source	Provide feedback to the Engineer on the remedial actions proposed by the	Confirm receipt of notification of	Take immediate action to

Event	Monitoring			Action		
	ET Leader	IEC	Engineer	Contractor		
consecutive samples	<p>If the exceedance is found to be valid and due to the construction works, verbally advise the Contractor, Engineer and IEC, and inform the EPD of the exceedance as soon as practicable.</p> <p>Repeat measurement to confirm finding</p> <p>Increase monitoring frequency to daily</p> <p>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented</p> <p>Arrange meeting with Engineer and Contractor to discuss the remedial actions to be taken</p> <p>If exceedance stops, discontinue additional monitoring</p>	<p>ET / Contractor</p> <p>Advise Engineer on the effectiveness of the proposed remedial measures</p> <p>Verify the implementation of the remedial measures</p>	<p>failure in writing</p> <p>Checking monitoring data and Contractor's working methods</p> <p>Notify Contractor</p> <p>Discuss proposed remedial actions with ET and Contractor</p> <p>Ensure remedial measures properly implemented</p> <p>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop the portion of work until the exceedance is abated</p>	<p>avoid further exceedance</p> <p>Submit proposals for remedial actions to Engineer within 3 working days of notifications</p> <p>Implement the agreed proposals</p> <p>Resubmit proposals if problem still not under control</p> <p>Stop the relevant portion of works as determined by the Engineer until the exceedance is abated</p>		

Table G.2 Event and Action Plans for Construction Noise

Exceedance	ET Leader	IEC	Engineer	Contractor
Action Level	Undertake noise measurement/check monitoring data to establish validity of complaint.	Review the analysed results submitted by the ET.	Notify Contractor of the complaint if proven.	Submit proposals for remedial actions to Engineer.
	If the complaint is valid, inform Engineer and IEC verbally.	Review the remedial measures proposed by the Contractor and advise the Engineer and ET accordingly.	Check Contractor's working methods and advise IEC and ET accordingly.	Amend proposals if required by the Engineer.
	Identify the source(s) of the noise.	Verify the implementation of the remedial measures.	Remind the Contractor of his contractual obligations and discuss remedial actions.	Implement the remedial actions immediately upon instruction from the Engineer.
	Discuss remedial actions required with Contractor and Engineer.		Keep the Contractor informed of the efficacy of remedial actions.	Liaise with the Engineer to optimise the effectiveness of the agreed mitigation.
	Increase manual monitoring frequency to assess efficacy of remedial measures.			
	If exceedance continues, review implementation of appropriate mitigation measures.			
Limit Level	Repeat manual measurement/check monitoring data to confirm findings.	Agree potential remedial actions with Engineer, ET and Contractor.	Notify Contractor of exceedance.	Take immediate action to avoid further exceedance.
	Identify the source(s) of the impact. If the exceedance is found to be valid and due to the Construction works, verbally advise the Contractor, Engineer and IEC, and inform the EPD of the exceedance, as soon as practicable.	Review Contractor's remedial actions / measures to ensure their effectiveness and advise the Engineer and ET accordingly.	Check Contractor's working methods and advise IEC and ET accordingly. Discuss with Contractor the remedial actions to be implemented.	Submit proposals for remedial actions to Engineer. Amend proposals if required by the Engineer.
	Discuss remedial actions required with Engineer.	Verify the implementation of the remedial measures	Keep the Contractor informed of the efficacy of remedial actions. If the exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop the portion of work until the exceedance is abated	Implement remedial actions immediately upon instruction from the Engineer. If the exceedance continues, consider what portion of the work is responsible and, as instructed by the Engineer, stop the portion of work until the exceedance is abated
	Increase manual monitoring frequency to assess efficacy of remedial measures.			

Table G.3 Event and Action Plans for Water Quality

Exceedance	ET Leader	IEC	Engineer	Contractor
Action level exceeded on one sampling day	Verbally inform the Contractor, and IEC. Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with Engineer and Contractor; Repeat measurement on next day of exceedance.	Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Discuss with Contractor the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures.	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Propose and discuss mitigation measures with Engineer; Implement the agreed mitigation measures.
Action level exceeded on more than one consecutive sampling day	Repeat in-situ measurements to confirm findings; Identify source(s) of impact; Inform Contractor and IEC; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measure with Engineer and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; Repeat measurement on next day of exceedance.	Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Discuss with ET and Contractor on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures.	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Propose mitigation measures to Engineer within 3 working days and discuss with ET and Engineer; Implement the agreed mitigation measures.
Limit level exceeded on one sampling day	Verbally inform the Contractor, IEC and the EPD of the exceedance; Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Check monitoring data, all plant,	Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Discuss with Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Propose mitigation measures to Engineer

Exceedance	ET Leader	IEC	Engineer	Contractor
	<p>equipment and Contractor's working methods;</p> <p>Discuss mitigation measure with Engineer and Contractor;</p> <p>Ensure mitigation measures are implemented;</p> <p>Increase the monitoring frequency to daily until no exceedance of Limit level.</p>		implemented mitigation measures.	<p>within 3 working days and discuss with Engineer;</p> <p>Implement the agreed mitigation measures.</p>
<p>Limit level exceeded by more than one consecutive sampling day</p>	<p>Repeat in-situ measurement to confirm findings;</p> <p>Identify source(s) of impact;</p> <p>Inform Contractor, IEC and EPD;</p> <p>Check monitoring data, all plant, equipment and Contractor's working methods;</p> <p>Discuss mitigation measure with Engineer and Contractor;</p> <p>Ensure mitigation measures are implemented;</p> <p>Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.</p>	<p>Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor</p> <p>Advise Engineer on the effectiveness of the proposed remedial measures</p> <p>Verify the implementation of the remedial measures</p>	<p>Discuss with Contractor on the proposed mitigation measures;</p> <p>Request Contractor to critically review the working methods;</p> <p>Make agreement on the mitigation measures to be implemented;</p> <p>Assess the effectiveness of the implemented mitigation measures;</p> <p>Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine works until no exceedance of the Limit Level.</p>	<p>Inform the Engineer and confirm notification of the non-compliance in writing;</p> <p>Rectify unacceptable practice;</p> <p>Check all plant and equipment; Consider changes of working methods;</p> <p>Propose mitigation measures to Engineer within 3 working days and discuss with Engineer;</p> <p>Implement the agreed mitigation measures..</p> <p>As directed by the Engineer, to slow down or to stop all or part of the marine work</p>

Appendix H Summary of Site Audit Findings

L11 Civil and Building Works

Dates of Inspection: 3/8/2021, 10/8/2021, 17/8/2021, 24/8/2021 and 31/8/2021.

Summary of Findings

General

- No environmental deficiency identified.

Air Quality

- No environmental deficiency identified.

Noise

- No environmental deficiency identified.

Water Quality

- No environmental deficiency identified.

Waste Management

- No environmental deficiency identified.

L11 Mechanical, Electrical, Instrumentation & Control Erection Works

Dates of Inspection: 5/8/2021, 12/8/2021, 19/8/2021 and 26/8/2021.

Summary of Findings

General

- No environmental deficiency identified.

Air Quality

- No environmental deficiency identified.

Noise

- No environmental deficiency identified.

Water Quality

- No environmental deficiency identified.

Waste Management

- No environmental deficiency identified.

L12 Civil and Building Works

Dates of Inspection: 3/8/2021, 10/8/2021, 17/8/2021, 24/8/2021 and 31/8/2021.

Summary of Findings

General

- No environmental deficiency identified.

Air Quality

- No environmental deficiency identified.

Noise

- No environmental deficiency identified.

Water Quality

- No environmental deficiency identified.

Waste Management

- No environmental deficiency identified.

Summary of EMIS

Power Station – (Part B of EIA Report)

Construction Phase Mitigation Measures and their Implementation

EM&A Log Ref.	Mitigation Measures	Implementation Status
	AIR QUALITY	
A1	For general construction works, the dust control measures stipulated under the Air Pollution Control (Construction Dust) Regulation shall be complied with, such as: <ul style="list-style-type: none"> the haul roads shall be sprayed with water to keep the entire road surface wet. the load carried by vehicle shall be covered by impervious sheeting to ensure no leakage of dusty materials from the vehicle. the heights from which fill materials are dropped shall be controlled to a practical level to minimise the fugitive dust arising from unloading. 	C C C
A2	For the concrete batching plant, the following control measures are recommended: <ul style="list-style-type: none"> loading, unloading, handling, transfer or storage of any dusty materials shall be carried out in a totally enclosed system. The materials which may generate airborne dust emissions shall be wetted by water spray system. All receiving hoppers shall be enclosed on three sides up to 3m above unloading point. All conveyor transfer points shall be totally enclosed. 	C C C C
	WATER QUALITY	
B1	Silt curtains shall be installed on the eastern, southern and north western sides of the reclamation site during dredging for the reclamation construction. This is a required mitigation measure for the construction works and shall be implemented prior to the commencement of bulk dredging. **	N/A
B3	As a necessary operational constraint combined bulk dredging and sand filling for site formation shall not be permitted at any time. In addition, sand filling for site platform shall take place behind constructed sea walls which pierce the water surface. **	N/A
B4	HEC shall ensure design to divert all storm drains away from Hung Shing Ye Bay. **	N/A
B5	Sand fill for the rubble mound seawalls shall be placed by controlled pumping down the trailer arm. **	N/A
B6	EM&A shall confirm the acceptability of any impacts during construction and should any unacceptable impacts be found then one or more of the following mitigation measures shall be implemented: ** <ul style="list-style-type: none"> reducing the number of dredgers working at any one time; reducing the rate of working of the dredgers; temporary suspension of operations; phasing of the works so that dredging / filling is only undertaken at certain stages of the tidal cycle. 	N/A

EM&A Log Ref.	Mitigation Measures	Implementation Status
WASTE MANAGEMENT		
E1	HEC to submit a Waste Management Plan for the construction phase to EPD. The Plan shall be verified by the IEC and shall describe the arrangements for avoidance, reuse, recovery and recycling, storage, collection, treatment and disposal of different categories of waste to be generated from the construction activities and shall take into account the recommendations of the EIA report.	C
<i>Dredging Waste</i>		
E2	All vessels for marine transportation of dredged sediment shall be fitted with tight fitting seals to their bottom openings to prevent leakage of materials. In addition, loading of barges and hoppers shall be controlled to prevent splashing of dredged material into the surrounding water, and barges or hoppers should under no circumstances be filled to a level which shall cause the overflowing of materials or polluted water during loading or transportation**	N/A
<i>Storage, Collection and Transport of Waste</i>		
E3	<ul style="list-style-type: none"> • Minimise windblown litter and dust during transportation by either covering trucks or transporting wastes in enclosed containers. 	C
	<ul style="list-style-type: none"> • Obtain the necessary waste disposal permits from the appropriate authorities, if they are required, in accordance with the Waste Disposal Ordinance (Cap.354), Waste Disposal (Chemical Waste) (General) Regulation (Cap.354), the Crown Land Ordinance (Cap 28), Dumping at Sea Ordinance (Cap 466) and Work Branch Technical Circular No. 22/92, Marine Disposal of Dredged Mud. 	C
	<ul style="list-style-type: none"> • Disposal of waste at Licensed sites; 	C
	<ul style="list-style-type: none"> • Develop procedures such as a ticketing system to facilitate tracking of marine mud and chemical waste, and to ensure that illegal disposal does not occur; 	C
	<ul style="list-style-type: none"> • Segregate and sort the waste materials into 3 categories: <ul style="list-style-type: none"> • public fill (e.g. concrete and rubble) for re-use on-site or disposal at a public filling area; • re-use and/or recycling waste (e.g. steel and other metals); • waste which cannot be re-used and/or recycled (e.g. wood, glass and plastic) for landfill disposal. • The sorting process shall be carefully monitored to avoid missing of the 3 categories. Different types of wastes shall be stockpiled and stored in different containers or skips to enhance re-use or recycling of materials and their proper disposal. • Maintain records of the quantities of wastes generated and disposed off-site for each category of waste. 	C
E4	Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes	C
LAND CONTAMINATION		
F1	No land Contamination mitigation measures are required during the construction phase.	N/A
MARINE ECOLOGY		

EM&A Log Ref.	Mitigation Measures	Implementation Status
G1	All percussive piling works shall be conducted on reclaimed land to avoid noise impact to marine mammals**	N/A
G2	All construction related vessels shall approach the extension site from the north and via the East Lamma Channel to avoid disturbance to the finless porpoise**	N/A
G3	Rubble mound seawall to the south and west edges of the reclamation to enhance recolonisation of marine organisms**	N/A
G4	Artificial Reefs of a volume not less than 400 m ³ shall be deployed in a location to be decided upon consultation with the Director of Agriculture and Fisheries to serve the purpose of an Additional Habitat Enhancement Measure.**	N/A
FISHERIES		
H1	No Fisheries-specific mitigation measures are required during the construction phase.	N/A
RISK ASSESSMENT		
I1	No risk mitigation measures are required during the construction phase.	N/A

Remarks:

- ** - No dredging and reclamation work would be involved for L11 & L12 construction
- C - Compliance with mitigation measure
- NC - Non-compliance with mitigation measure
- N/A - Not Applicable

ID	Task Name	Duration	2021			
			Jul	Aug	Sep	
1	Civil and Building Works for Unit 11 and Associated Works	1197 days	▼ 30 Sep '21			
2	Contract Key Dates	1197 days				
3	Contract Commencement Date	0 days				
4	Completion Dates	1044 days	▼ 30 Sep '21			
5	Section A1 - Ground treatment installation works at Zone 1A	0 days				
6	Section A2 - Ground treatment installation works at Zone 1B	0 days				
7	Section A3 - Ground treatment installation works at Zone 2	0 days				
8	Section A4 - Ground treatment installation works at Zone 3	0 days				
9	Section A5 (i) - Ground treatment installation works at Zone 4 - Band drain installation	0 days				
10	Section A5 (ii) - Ground treatment installation works at Zone 4 - Surcharge filling	0 days				
11	Section A6 (i) - A&A Works for No. 4 C.W. Outfall at Area E18	0 days				
12	Section A6 (ii) - External works at Area E15	0 days				
13	Section B1 (i) - Area south of L11 MSB and HRSG from GL11-F eastwards leading to Chimney Road at Area E1 & E2	0 days				
14	Section B1 (ii) - Supporting structures for overhead cranes of L11 MSB including the associated roof structure except the roof deferred works	0 days				
15	Section B1 (iii) - FSRU Civil works at Area E13	0 days				
16	Section B2 - Retractable Cover D at Area E22	0 days				
17	Section B3 - External works at Area B1, D2 and D4	0 days				
18	Section C1 - Area south of L11 MSB from GL11-F westwards leading to Station Road at Area E3(A) & E3(B)	0 days				
19	Section C2 - (i) Southern part of L11 HRSG area and its surrounding at Area E7 except the deferred works for Lube Oil Storage Tank	0 days				
20	Section C2 - (ii) L11 Turbo Block foundation including the L11 MSB ground floor together with the equipment foundations between GL 11-F to 11-H and 11-1 to 11-6 for the installation of power generator, air inlet duct and lube oil reservoir	0 days				
21	Section C2 - (iii) G/F of L11 MSB including the Condenser Pit, Circulating Water Pipe Pit and equipment foundations between GL 11-B to 11-C and 11-1 to 11-6 for the installation of condenser	0 days				
22	Section D - (i) Roads and external grounds surrounding L11 MSB and L11 HRSG in addition to the southern & eastern areas mentioned above in Area E5 and E6	0 days				
23	Section D - (ii) Remaining northern part of L11 HRSG area and its surrounding in Area E6	0 days				
24	Section D - (iii) Whole of L11 MSB including the pipe and cable rack along south façade of L11 MSB with all underground utilities at Area E4 including C.W. Inlet and Outlet Culvert except the deferred works	0 days				
25	Section D - (iv) Link Bridge between L10 and L11 MSB and at the south of L11 MSB including their associated alternations & additions (A&A) Works at L10 MSB	0 days				
26	Section D - (v) Gas Duct Foundation, Pipe and Cable Rack and associated trench in Area E20	0 days				
27	Section E1 - (i) Link Bridge and Pipe and Cable Rack connecting L11 MSB to the western area of L11 MSB at Area E3	0 days				
28	Section E1 - (ii) Gas Receiving Station and L11 Gas Receiving Station Equipment Room (GRS) Area Extension at Area E16	0 days				
29	Section E1 - (iii) External Works at Area E15 (C)	0 days				
30	Section E2 - Pipe and Cable Rack and trench at west of Chimney Road and Pipe and Cable Rack at south of Middle Road at Area E8 and E19	0 days				
31	Section E3 - Gas Pipe Support Foundation and Pipe Trench and associated external works at Area E14, E15 (A) and E15 (B)	0 days				
32	Section E4 - 275kV cable trenching works connecting the 275kV Switching Station Extension and L11 MSB at Area E9 (A)	0 days				
33	Section F - 275kV Station Building Extension and associated works at Area E17	0 days				
34	Section G - A&A Works at No. 4 C.W. Intake at Area E12	0 days				
35	Section H - L11 Steel flue liner at No. 4 Chimney	0 days				

ID	Task Name	Duration	2021		
			Jul	Aug	Sep
36	Section I - (i) 275kV cable trenching works connecting the 275kV Switching Station Extension and L11 MSB at Area E9 (B)	0 days			
37	Section I - (ii) Interconnector 2 Trench Modification Works at Area E10	0 days			
38	Section J - (i) Demolition of Retractable Cover A&B & (ii) Foundation of LMX Light Oil Storage Tank Nos. 3 & 4 and A&A for Existing Bund Wall at	0 days	4 and A&A for Existing Bund Wall at Area E21		
39	Section K1 - External works at Area 15 (E) and 15(F)	0 days			
40	Section K2 - Removal of Southern Bund and External Works at Area D5, D6 and D7	0 days	Works at Area D5, D6 and D7		
41	Section K3 - All remaining works shall be completed for reporting completion to BD and ready for OP inspection	0 days			◆ Section K3 - All remain
42	General & Preliminary	318 days			
43	Set up Temporary Site Office and Utilities	90 days			
44	Permit Applications & Statuary Submissions	120 days			
45	Existing Utilities scanning & Excavation Permit	45 days			
46	Tower Crane erection 2@MSB, 1@ 275	50 days			
47	Submission and Approval	554 days			
48	Method Statement / Temp Work Submission & Approval from HEC for General Works	240 days			
49	BD Approval & Consent (If required)	120 days			
50	BIM Model, CSD & CBWD Submission & Approval from HEC	200 days			
51	Structure Steelwork Connection Design Submission & BD Approval	60 days			
52	Structure Steelwork Shop Drawing & Approval	60 days			
53	Metal Cladding, louvre & windows submission & BD Approval	60 days			
54	Metal Cladding, louvre & windows shop drawing submission	60 days			
55	Order, Off Site Fabrication and Delivery (S. Steel & Cladding & louvres)	180 days			
56	Retractable Cover D BD Submission & Approval	90 days			
57	No. 4 C.W. Outfall A&A BD 1st Submission	90 days			
58	Submission & Approval of Steel Flue Assessment Report and Design Drawings	60 days			
59	Submission and Approval of Steel Flue Design from BD	60 days			
60	Material Fabrication & Delivery for L11 Flue	100 days			
61	Folding Shutters Shop Drawing Submission & Approval	120 days			
62	Fabrication & Delivery of Folding Shutters	150 days			
63	Sewage Pump System Design submission & approval	90 days			
64	Fabrication & Delivery of Sewage Pump	180 days			
65	Other material submission & approval & delivery	300 days			
66	Coordination with the Employer's Specialist Contractors	478 days			
67	Installation of Puddle Pipes at C.W. outlet Culvert	7 days			
68	Installation of Puddle Pipes at C.W. Inlet Culvert	7 days			
69	Template setting at L11 Turbo Block Foundation	60 days			
70	Template setting of holding down bolts at HRSG column base	46 days			
71	I-beam / channel base installation on top of transformer foundations at Transformer Area	30 days			
72	Overhead crane erection at turbine hall using access through a temporary opening at L11 MSB roof between GL11-G to 11-H and 11-2 to 11-6	36 days			
73	Condenser assembly and erection using access through a temporary façade opening at L11 MSB below 1/F along GL 11-6 from GL11-B to 11-C including a clear space below 1/F between GL 11-B to 11-C	127 days			
74	Installation of power train equipment including air inlet duct using access through a temporary façade opening at L11 MSB below 1/F along GL 11-6 from GL11-F to 11-H including a clear space below 1/F of the above area	142 days			
75	Installation of embedded materials such as holding down bolts for equipment foundations - Commencement	30 days			
76	Section A1 & A2 - Ground treatment at Zone 1A & 1B	92 days			
77	Plant establishment for earthworks	7 days			
78	Backfilling and compaction from existing ground +4.5mPD to +5.5mPD	45 days			
79	Delivery of band drain	5 days			
80	Plant establishment for band drain (1st rig)	10 days			
81	Plant establishment for band drain (2nd rig)	7 days			
82	Plant establishment for band drain (3rd rig)	7 days			

ID	Task Name	Duration	2021		
			Jul	Aug	Sep
83	Vert. Band drain installation (1023 nos. x 44m)	45 days			
84	Deposition of surcharge up to +8.3mPD	45 days			
85	Section A3 - Ground treatment installation works at Zone 2	158 days			
86	Backfilling and compaction from existing ground +4.5mPD to +5.5mPD	30 days			
87	Delivery of band drain	6 days			
88	Vert. Band drain installation (1787 nos. x 44m)	50 days			
89	Deposition of surcharge up to +8.3mPD	60 days			
90	Additional Concrete Blocks + Extra Surcharge	60 days			
91	Section A4 - Ground treatment installation works at Zone 3	131 days			
92	Backfilling and compaction from existing ground +4.5mPD to +5.5mPD	12 days			
93	Vert. Band drain installation	60 days			
94	Deposition of surcharge up to +8.3mPD	45 days			
95	Possession of Part 1 Defer portion at Zone 3	0 days			
96	Vert. Band drain installation	10 days			
97	Possession of Part 2 Defer portion at Zone 3	0 days			
98	Vert. Band drain installation	7 days			
99	Surcharge at deferred portion	14 days			
100	Section A5 (i) - Ground treatment installation works at Zone 4	83 days			
101	Site Preparation for Vertical Band Drain	3 days			
102	Band drain installation	21 days			
103	Possession of Defer portion at Zone 4	0 days			
104	Vert. Band drain installation	28 days			
105	Section A5 (ii) - Surcharge works at Zone 4	30 days			
106	Deposition of surcharge up to +8.3mPD	30 days			
107	Section A6 (i) - A&A Works for No. 4 C.W. Outfall at Area E18	493 days			
108	BD Amendment, resubmission & approval for Jacking Pit	170 days			
109	Consent for Jacking Pit ELS	28 days			
110	Mobilization	0 days			
111	Jacking Pit Sheetpile Installation (incl. Stop work notice + CNY)	60 days			
112	Protective screen and preventive measure for U9 gas pipeline (VO)	28 days			
113	Provision of temp support for U10 gas pipeline (VO) upon RMA allow access	28 days			
114	ELS of jacking pit	30 days			
115	Pipe Jacking set up & ground strengthening	18 days			
116	Pipe Jacking	90 days			
117	Receiving Pit BD Approval	170 days			
118	Consent for Pipe & Sheet pile	28 days			
119	Receiving Pit Pipe & Sheet pile installation	30 days			
120	Consent for Receiving Pit ELS	28 days			
121	ELS of Receiving pit	40 days			
122	Allow modify existing outfall manhole for pipe jacking receiving	18 days			
123	Culvert Pipe Intallation & water test	55 days			
124	Inspection Manhole at Jacking Pit + backfill (Area E3(A))	18 days			
125	Manhole extension at Outfall no. 4 + backfill + Reinstate of Outfall Rd	45 days			
126	Sheetpile for L12 Outlet culvert (Connection to Jacking Pit)	45 days			
127	Consent + ELS for remaining jacking pit	75 days			
128	Outlet Culvert pipe installation + Thrust Box (remaining portion at A1 Area)	45 days			
129	Sheet pile for future extension along GRS	60 days			
130	Section A6 (ii) - External works at Area E15(D)	37 days			
131	Area possession & Clearance	6 days			
132	Road & Surface Works	31 days			
133	Section B1 (i) - Area south of L11 MSB and HRSG from GL11-F eastwards leading to Chimney Road at Area E1 & E2	375 days			
134	Area Possession & Clearance	0 days			
135	Excavation for CW Inlet Culvert (South of L11 HRSG)	21 days			
136	Installation CW Inlet Culvert pipe	30 days			
137	Construction of Thrust Box & Manholes,etc	14 days			
138	Backfill	21 days			
139	Install underground utilities	45 days			
140	Backfill and Temporary paving for Condensor Move in (E1)	14 days			
141	Backfill and Temporary paving for Condensor Move in (others)	30 days			
142	Section B1 (ii) - Supporting structures for overhead cranes of L11 MSB including the associated roof structure except the roof deferred works	482 days			
143	Area possession & Clearance	0 days			
144	Erection of turbine hall roof except defer work	0 days			

ID	Task Name	Duration	2021		
			Jul	Aug	Sep
145	Installation of crane grids	21 days			
146	Turbine hall wall claddings	60 days			
147	Section B1 (iii) - FSRU Civil works at Area E13 (GRS)	151 days			
148	Submission and approval for consent to work	0 days			
149	Civil & Building Works	130 days			
150	Ground reinstatement	21 days			
151	Section B2 - Retractable Cover D at Area E22	435 days			
152	Area Possession, Demolition and clearance work	60 days			
153	Revise Structural Form and BD resubmission & approval	150 days			
154	Foundation construction	60 days			
155	Backfill & Ground reinstatement	30 days			
156	Superstructure fabrication & delivery	90 days			
157	Superstructure erection	90 days			
158	E&M Installation and T&C	45 days			
159	Section B3 - External works at Area B1, D2 and D4	416 days			
160	Receive Area from HKE, Area Possession & Clearance	0 days			
161	Removal of existing paving for band drain under Section A5(i)	30 days			
162	Complete Vert. Band drain under Section A5(i)	0 days			
163	Ground preparation for B1, D2 & D4 for handover to Plant contractor	90 days			
164	Section C1 - Area south of L11 MSB from GL11-F westwards leading to Station Road at Area E3(A) & E3(B)	466 days			
165	Area Possession & Clearance	0 days			
166	Excavation for Type C (Area E3A)	21 days			
167	Installation CW Outlet Culvert Pipe connect to Type C1	21 days			
168	Installation CW Inlet Culvert pipe (South of L11 Condensor)	21 days			
169	Construction of Thrust Box	10 days			
170	Construction of Access Manhole	21 days			
171	Backfill	14 days			
172	Construction of Underaround drainage and utilities	60 days			
173	Construct Temp Paving for Condenser move in	45 days			
174	Section C2 - (i) Southern part of L11 HRSG area and its surrounding at Area E7 (No Defer Foundations)	295 days			
175	Area Possession & Clearance	0 days			
176	Excavation & Pile Caps & Tie Beams (HRSG South Area E7)	45 days			
177	Construction RC foundations	45 days			
178	Construction RC plinths	30 days			
179	Construction underground utilities	45 days			
180	Backfill & Construction on-grade slabs	35 days			
181	Backfill and Temporary paving	21 days			
182	Section C2 - (ii) L11 Turbo Block foundation including the L11 MSB ground floor together with the equipment foundations between GL 11-F to 11-H and 11-1 to 11-6 for the installation of power generator, air inlet duct and lube oil reservoir	496 days			
183	Area Possession & Clearance	0 days			
184	Excavation & Pile Caps & Tie Beams (MSBL11 - Turbo Block North)	70 days			
185	Excavation & Pile Caps & Tie Beams (MSBL11 - Turbo Block South)	30 days			
186	Backfill and construction turbine block foundations	21 days			
187	Construction of internal drainage	60 days			
188	Construction RC walls incl. G/F rooms	90 days			
189	Construction turbine block columns and upper portion for plant embed installation	21 days			
190	Concrete Turbine upper part foundation & clear falsework	52 days			
191	Section C2 - (iii) G/F of L11 MSB including the Condenser Pit, Circulating Water Pipe Pit and equipment foundations between GL 11-B to 11-C and 11-1 to 11-6 for the installation of condenser	466 days			
192	Area Possession & Clearance	0 days			
193	Excavation to foundation level at ELS Type A	18 days			
194	Construction of CW Outlet Box + lowest tie beam & caps	40 days			
195	Construction of pile caps & tie beams & hot well sump pit up to +2.5mPD	30 days			
196	Backfill & Construction of CW Inlet Box + tie beams	18 days			
197	Backfill and Construction ground beams & trenches	18 days			

ID	Task Name	Duration	2021		
			Jul	Aug	Sep
198	Construction of indoor underground drainage	12 days			
199	Backfill & construction on-grade slabs	10 days			
200	Construction Column casting and RC walls	30 days			
201	Metal Cladding & Louvres for GLB-C/1-6	60 days			
202	Mis. Works for plant erection	24 days			
203	Section D - (i) Roads and external grounds surrounding L11 MSB and L11 HRSG in addition to the southern & eastern areas mentioned above in Area E5 and E6	414 days			
204	Area Possession & Clearance	14 days			
205	Excavation for Type C1 and open sheet pile	75 days			
206	Install CW Outlet pipe & connect to previous	21 days			
207	Backfill	10 days			
208	Undeground utilities and trenches	60 days			
209	Construction of plant drainage, trenches & RC plinths	45 days			
210	Remaining Undeground utilities & backfill (West of Tx Bay)	75 days			
211	Section D - (ii) Remaining northern part of L11 HRSG area and its surrounding in Area E6	375 days			
212	Area Possession & Clearance	0 days			
213	Excavation & Pits & Pile Caps & Tie Beams (HRSG north Area E6)	45 days			
214	Construction RC foundations	45 days			
215	Construction RC plinths & HRSG Lift Pit & internal drainage	60 days			
216	Backfill Construction on-grade slabs	28 days			
217	Construction underground utilities	45 days			
218	Backfill, Remaining utilities and temporary paving	85 days			
219	Touch up and site clearance	13 days			
220	Section D - (iii) Whole of L11 MSB including the pipe and cable rack along south facade of L11 MSB with all underground utilities at Area E4 including C.W. Inlet and Outlet Culvert except the deferred works	526 days			
221	Area Possession & Clearance	0 days			
222	Construction of pile caps & tie beams at Transformer Area	60 days			
223	Excavation & Construction Blow Down Sum pit (Type B)	45 days			
224	Construction of pile caps & tie beams at SunShadeCover Area	45 days			
225	Preparation for S.Steelwork Erection	14 days			
226	Structural Delivery & Erection (Turbine Hall North fr G.L. 1-3/H->B)	30 days			
227	Structural Delivery & Erection (Equipment Floors)	45 days			
228	Structural Delivery & Erection (Turbine Hall South)	45 days			
229	Fire Coating Application at Joint	120 days			
230	External Scaffolding Erection	150 days			
231	Construction 1/F RC Slab	14 days			
232	Construction M/F RC Slab	7 days			
233	Construction 2/F RC Slab	14 days			
234	Construction 3/F RC Slab	14 days			
235	Construction 4/F RC Slab	14 days			
236	Construction 5/F RC Slab (Roof of turbine hall, except defer portion)	30 days			
237	Construction Roof RC Slab	14 days			
238	Construction Upper Roof RC Slab	12 days			
239	Construction Defer Roof RC Slab (G.L. G-H)	30 days			
240	Construction of Staircase ST-01 & lift shaft & machine room	120 days			
241	Construction of Staircase ST-02 except defer work	76 days			
242	Construction of RC plinth, kerbs & parapet Walls	30 days			
243	Erection of Skylight & Roof Features	45 days			
244	Waterproofing & Flooring at Roof	60 days			
245	ABFW Works from 1/F to 5/F equipment rooms	150 days			
246	Metal Cladding, Windows and Louvres incl. roof feature	100 days			
247	Removal of external scaffolding	60 days			
248	Building Services E&M Access & Installation	150 days			
249	Remaining and Mis. works for Plant erection Full Access	18 days			
250	Section D - (iv) Link Bridge between L10 and L11 MSB and at the south of L11 MSB including their associated alternations & additions (A&A) Works at L10 MSB	526 days			
251	Area Possession & Clearance	0 days			

ID	Task Name	Duration	2021		
			Jul	Aug	Sep
252	A&A works at South of L10 MSB	60 days			
253	Erection of link bridge structural steel	21 days			
254	Casting of bridge deck	7 days			
255	Metal roofing installation	14 days			
256	ABWF work	21 days			
257	Form new opening at MSB for final connection	14 days			
258	E&M Work for completion	21 days			
259	Section D - (v) Gas Duct Foundation, Pipe and Cable Rack and associated trench in Area E20	345 days			
260	Area Possession & Clearance + CNY	0 days			
261	Sheet pile installation & submit as-built	75 days			
262	Consent for excavation	28 days			
263	Excavation & plate load test	45 days			
264	Construction of foundation	45 days			
265	Backfill & Underground utitiies	30 days			
266	Remaining Pipe & cable rack and associated trenches in Area E20	115 days			
267	Section E1 - (i) Link Bridge and Pipe and Cable Rack connecting L11 MSB to the western area of L11 MSB at Area E3	263 days			
268	Area Possession	0 days			
269	Excavation & construction of new foundation	40 days			
270	Backfill	10 days			
271	Erection of Structural steel	30 days			
272	Backfill & Ground works	55 days			
273	Section E1 - (ii) Gas Receiving Station and L11 Gas Receiving Station Equipment Room (GRS) Area Extension at Area E16	173 days			
274	Area Possession	0 days			
275	Removal of Surcharge and excavation	14 days			
276	Modification of Site Drainage	45 days			
277	Construction of new RC for GRS Equipment Room	75 days			
278	ABWF for GRS Equipment room	45 days			
279	E&M Installation	45 days			
280	Construction of new Gas pipe plinths & racks	45 days			
281	Backfill and construction site drainage	21 days			
282	External Paving and install new fencing	60 days			
283	Section E1 - (iii) External Works at Area E15 (C)	273 days			
284	Removal of Surcharge and excavation	45 days			
285	Underground drianage, Utilities and RC plinths	123 days			
286	Backfill and install surface utilities	45 days			
287	Roadwork	60 days			
288	Section E2 - Pipe and Cable Rack and trench at west of Chimney Road and Pipe and Cable Rack at south of Middle Road at Area E8 and E19	495 days			
289	BD consent + Site Possession @ Area E8	0 days			
290	Excavation & Plate load test	60 days			
291	Foundation and Trench constructions	90 days			
292	Backfill & underground utitiles + temp paving	60 days			
293	Excavation & plate load test @ E19	60 days			
294	Construction of foundations & trenches	45 days			
295	Backfill & underground utitiles	60 days			
296	Pipe & cable rack Erection	60 days			
297	Ground reinstatement	60 days			
298	Section E3 - Gas Pipe Support Foundation and Pipe Trench and associated external works at Area E14, E15 (A) and E15 (B)	173 days			
299	Removal of surcharge / site clearance	21 days			
300	Excavation & construction of pipe trench	30 days			
301	Construction of gas pipe support foundation	30 days			
302	Construction of underground drainage and utilities	60 days			
303	Backfill & road work	32 days			
304	Section E4 - 275kV cable trenching works connecting the 275kV Switching Station Extension and L11 MSB at Area E9 (A)	185 days			
305	Site possession	0 days			
306	Obtain Permit to work & Road close permit	10 days			

ID	Task Name	Duration	2021		
			Jul	Aug	Sep
307	Excavation & construction new cable trench to 275kV	45 days			
308	Excavation & construction new cable trench to L11MSB	130 days			
309	Section F - 275kV Station Building Extension and associated works at Area E17	709 days			
310	Installation of ELS for 275kV Switching Station near Staircase ST-3 and ST-6	14 days			
311	Construction of Staircase ST-3	110 days			
312	BD Amendment Approval on A&A	0 days			
313	BD Amendment Approval on A&A ST3 & Drainage	0 days			
314	OP inspection of Staircase ST-3	14 days			
315	Consent of New Foundation Works (Stage 1)	0 days			
316	Consent & BA10 for Demolition of Existing Staircase	0 days			
317	Demolition of Existing Staircase and Submit BA14A	14 days			
318	BD inspection for BA14A & Issue OP	28 days			
319	Consent & BA10 for New Foundation Work (Stage 2)	28 days			
320	Hoarding Modification	7 days			
321	Pile Cap & Tie Beam Construction (Stage 1)	98 days			
322	Erection of Tower Crane	40 days			
323	Pile Cap and Tie Beam (Stage 2)	21 days			
324	RC Construction up to 1/F (Stage 1)	30 days			
325	RC Construction up to 1/F (Stage 2)	75 days			
326	Construction of Staircase ST6	90 days			
327	Shop Drawing Submission & Approval of Structural Steel	45 days			
328	Structural Steel fabrication & Delivery	60 days			
329	Erection of Structural Steel GL 17~18	30 days			
330	Erection of Structural Steel GL 8~17	60 days			
331	Metal Cladding Delivery	60 days			
332	Metal Door, Window & Louvre Delivery	45 days			
333	Erection of Working Platform and Scaffold	150 days			
334	Install Decking	60 days			
335	RC Walls from 1/F @ GIS Hall	40 days			
336	Construction of 2/F RC slab	14 days			
337	Construction of R/F RC slab	21 days			
338	Construction of UR/F RC slab	14 days			
339	Construction of GIS Hall Floor	60 days			
340	Installation of Overhead Crane (By JEC)	60 days			
341	Construction of staircase ST4, ST5, Lift Shaft & Equip Floors	150 days			
342	Lift Installation	90 days			
343	Concrete of RC walls, plinths, kerb & parapet walls & New trench for LV Power	30 days			
344	ABWF Works @ G/F	50 days			
345	ABWF Works @ 1/F	50 days			
346	ABWF Works @ 2/F	75 days			
347	ABWF Works @ R/F	30 days			
348	ABWF Works @ UR/F	21 days			
349	Waterproofing Works at R/F & UR/F	45 days			
350	Building Services E&M Access & Installation & T&C	150 days			
351	Metal Cladding, Windows and Louvres incl. Roof Feature	90 days			
352	Shutter Erection	30 days			
353	Removal of External Scaffolding + Tower Crane	35 days			
354	External Underground Drainage and Utilities	30 days			
355	Road & Paving Reinstatement	30 days			
356	Ready for FSD & OP Inspection	0 days			
357	Section G - A&A Works at No. 4 C.W. Intake at Area E12	143 days			
358	Permit to work	0 days			
359	Erection of temp. platform	14 days			
360	Demolition work	30 days			
361	Modify existing slab openings	75 days			
362	Curing + Removal of platform	24 days			
363	Section H - L11 Steel flue liner at No. 4 Chimney	186 days			
364	Complete erection of L10 Steel flue	0 days			
365	Modification of erection equipment	21 days			
366	Erection temp. platform and demolition work	30 days			
367	Structural steel delivery & Erection	85 days			
368	Removal of temp. work	5 days			
369	Reinstatate G/F louvre wall and access door	45 days			
370	Section I - (i) 275kV cable trenching works connecting the 275kV Switching Station Extension and L11 MSB at Area E9 (B)	232 days			
371	Obtain Permit to work & Road close permit	0 days			
372	Excavation & construction new cable trench	160 days			
373	Re-excavate cable trench for cable laying	72 days			
374	Section I - (ii) Interconnector 2 Trench Modification Works at Area E10	275 days			
375	Obtain Permit to work & Road close permit	0 days			
376	Re-excavate & new cable trench for cable laying	275 days			

ID	Task Name	Duration	2021			
			Jul	Aug	Sep	
377	Section J - (i) Demolition of Retractable Cover A&B & (ii) Construction of new LOT 3 & 4	426 days				
378	Obtain permit to work & Road close permit	0 days				
379	Erection of Hoarding	21 days				
380	Removal of existing cover & structural steel	30 days				
381	Demolish of existing bund wall and staircases	45 days				
382	Demolish of existing slab & foundation	60 days				
383	Consent for new work	30 days				
384	Construction of new bund wall and foundation	100 days				
385	Construction of new oil separator	80 days				
386	Construct underground drainage and surface channel	40 days				
387	Construction on-grade slab	60 days				
388	Removal of hoarding and ground reinstatement	40 days				
389	Section K1 - External works at Area 15 (E) and 15(F)	365 days				
390	Removal of surcharge	30 days				
391	Construct new drainage and utilities work	200 days				
392	Road & Paving	135 days				
393	Section K2 - Removal of Southern Bund and External Works at Area D5, D6 and D7	365 days				
394	Demolition work	30 days				
395	Construct new drainage and utilities work	200 days				
396	Road & Paving	135 days				
397	Section K3 - All remaining works shall be completed for reporting completion to BD and ready for OP inspection (PS1.4.4)	623 days				30 Sep '21
398	Completion of remaining roof after over headcrane move in	30 days				
399	Construction of G/F Lube Oil Tank Room (BY TDK)	61 days				
400	Construction of wall and staircase at G/F after Condensor Move in	90 days				
401	Construction of Durasteel Steel wall panel after IBP installation	30 days				
402	Construction of Transformer fence wall, cladding & associated FS services	122 days				
403	Final restatement of road & paving around MSB & HRSG	122 days				
404	Installation of trench covers and gratings after plant installation	151 days				
405	Backfill and reinstatement after 275kV cable laying	122 days				Backfill and reinstatem

Revised Works Programme for 2no. DN1800 CW Outlet Pipes Installation - Culvert Outfall No. 4 + GRS Works

No.4 Outfall AA+GRS (Rev.13) (21-7-2021)


ID	Task Name	Duration	Start	Finish	Aug				Sep				Oct				Nov			
1	2 no. DN1800 CW Outlet Pipes Installation Overall Duration	905 days	Fri 2/11/18	Sat 6/11/21	2 no. DN1800 CW Outlet Pipes Installation Overall Duration															
2	Completion of pumping test	0 days	Wed 27/1/21	Wed 27/1/21																
3	A&A work for extension of outfall chamber up to +8.506mPD	0 days	Tue 19/1/21	Tue 19/1/21																
4	Complete ELS at jacking pit	0 days	Thu 11/2/21	Thu 11/2/21																
5	Complete ELS at receiving pit	0 days	Thu 5/8/21	Thu 5/8/21																
6	Make opening at JP for pipe jacking works	0 days	Mon 29/3/21	Mon 29/3/21																
7	Completion of ground treatment works at receiving pit	0 days	Thu 15/4/21	Thu 15/4/21																
8	Completion of jack sleeve pipe	0 days	Mon 13/9/21	Mon 13/9/21																
9	Install DN1800 CW outlet pipes from jacking pit to receiving pit	0 days	Fri 1/10/21	Fri 1/10/21																
10	Complete backfill for subsequence underground utilities construction at jacking pit	0 days	Sat 9/10/21	Sat 9/10/21																
11	Jacking Pit and Thrust Block Portion	891 days	Fri 2/11/18	Thu 21/10/21	Jacking Pit and Thrust Block Portion															
12	Submission and approval of ELS plan amendment	30 days	Fri 2/11/18	Sat 1/12/18																
13	Re-submission and approval of ELS plan amendment	60 days	Wed 27/2/19	Sat 27/4/19																
14	Approval of re-submission (dated 2/5/2019; received on 21/5/2019)	0 days	Tue 21/5/19	Tue 21/5/19																
15	Consent application for sheetpile installation	28 days	Wed 22/5/19	Tue 18/6/19																
16	Submit BA14 for completion of Phase 1 & 2 sheetpile	23 days	Wed 19/6/19	Thu 11/7/19																
17	Amendment submission (re-phasing)	30 days	Fri 19/7/19	Sat 17/8/19																
18	Consent application for Phase 1 (new defined) excavation commencement	28 days	Sun 18/8/19	Sat 14/9/19																
19	Consent application for Ground Treatment Works	28 days	Tue 18/6/19	Mon 15/7/19																
20	Consent application for JP sheetpile opening works	28 days	Thu 2/7/20	Wed 29/7/20																
21	Submit BA14 for completion of Phase 1 (new defined) backfilling works	14 days	Sun 2/2/20	Sat 15/2/20																
22	Consent application for Phase 2 (new defined) excavation commencement	28 days	Sun 18/10/20	Sun 15/11/20																
23	Phase 2 (new defined) - Jacking Pit	868 days	Thu 29/11/18	Thu 21/10/21																
24	Mobilization	2 days	Thu 29/11/18	Fri 30/11/18																
25	Phase 1 - Install sheetpile for jacking pit	32 days	Wed 12/12/18	Mon 21/1/19																
26	Trial grouting for ground treatment works, sampling & testing	21 days	Fri 25/10/19	Mon 18/11/19																
27	Submit trial grouting assessment report	35 days	Tue 19/11/19	Tue 31/12/19																
28	Ground treatment works (full scale), sampling & testing	75 days	Thu 12/3/20	Sat 13/6/20																
29	Submit BA14 for completion of ground treatment works (including record plans and assessment report)	14 days	Thu 25/6/20	Wed 8/7/20																
30	Phase 2 (new defined)- Excavate and install struts and walings at jacking pit (including blinding layer)	28 days	Mon 11/1/21	Thu 11/2/21																
31	Water test for CW culvert pipe	14 days	Thu 16/9/21	Fri 1/10/21																
32	Phase 2 (new defined) - Backfilling	10 days	Mon 11/10/21	Thu 21/10/21																
33	Phase 1 (new defined) - Thrust Block Portion	247 days	Mon 6/5/19	Sat 29/2/20																
43	Receiving Pit	884 days	Tue 27/11/18	Sat 6/11/21	Receiving Pit															
44	Submission and approval of ELS plan	60 days	Tue 27/11/18	Fri 25/1/19																
45	Re-Submission and approval of ELS plan	60 days	Fri 15/3/19	Mon 13/5/19																
46	Approval of re-submission (dated 21/5/2019; received on 30/5/2019)	0 days	Thu 30/5/19	Thu 30/5/19																
47	Consent application for pipe pile and sheetpile installation	28 days	Mon 3/6/19	Sun 30/6/19																
48	Consent application for excavation commencement	28 days	Tue 23/2/21	Mon 22/3/21																
49	Advance works - Tree pruning, felling, removing street furniture, trial trench for existing utilities, break existing cable trap concrete support and slab, trial pit to existing outfall structure, protection work to nearby existing cable tray, hoarding	95 days	Mon 24/6/19	Wed 16/10/19																
50	Form platform	69 days	Thu 25/7/19	Wed 16/10/19																
51	Install pipe pile (30no.), sheetpile, pre-grout & curtain grout	150 days	Mon 21/10/19	Wed 22/4/20																
52	Submt BA14 for completion of installation of sheet pile, pipe pile	28 days	Thu 23/4/20	Wed 27/5/20																
53	Install pumping well & observation well	21 days	Thu 23/4/20	Tue 19/5/20																
54	Preparation works for road closure at outfall road (SI no. 45)	36 days	Tue 9/6/20	Wed 22/7/20																
55	Excavate and divert existing DN300&DN200 FS pipes	80 days	Thu 23/7/20	Tue 27/10/20																
56	Open cut excavation down to outfall chamber top	20 days	Wed 28/10/20	Thu 19/11/20																
57	Removal of existing mud inside outfall chamber and inspection for fabrication of penstock	5 days	Wed 9/12/20	Mon 14/12/20																
58	A&A work for extension of outfall chamber up to ~+6.0mPD + backfill	35 days	Fri 20/11/20	Fri 1/1/21																
59	A&A work for extension of outfall chamber up to +8.506mPD	15 days	Sat 2/1/21	Tue 19/1/21																
60	Install penstock	5 days	Tue 4/5/21	Sat 8/5/21																
61	Installation of baffle plate	4 days	Thu 19/8/21	Mon 23/8/21																
62	Metal works for outfall chamber	15 days	Mon 2/8/21	Wed 18/8/21																
63	Installation of top railing for outfall chamber	2 days	Fri 5/11/21	Sat 6/11/21																
64	Pumping test	12 days	Thu 14/1/21	Wed 27/1/21																
65	Consent application for RP excavation work (stage 2A)	28 days	Thu 28/1/21	Mon 1/3/21																
66	Excavate RP, install struts and walings & blinding concrete (stage 2A) (before incident)	54 days	Tue 2/3/21	Mon 3/5/21																
67	Water leakage incident investigation and remedial works & BD submission	67 days	Tue 4/5/21	Tue 20/7/21																
68	Excavate RP & blinding concrete (stage 2A) (after incident)	14 days	Wed 21/7/21	Thu 5/8/21																
69	Demolition of existing outfall structure (1st stage for TBM extraction)	5 days	Fri 6/8/21	Wed 11/8/21																
70	Demolition of existing outfall structure (2nd stage remaining part)	14 days	Thu 12/8/21	Fri 27/8/21																
71	BD amendment for changes from horizontal grout to vertical grout	30 days	Tue 15/12/20	Wed 20/1/21																
72	Consent application for vertical grout block at RP (stage 2B)	28 days	Fri 15/1/21	Tue 16/2/21																
73	Preparation works for vertical grout	30 days	Tue 15/12/20	Wed 20/1/21																
74	Full Scale Ground treatment works (vertical grouting), sampling & testing (stage 2B)	50 days	Wed 17/2/21	Thu 15/4/21																
75	Submit BA14 for completion of ground treatment works (including records plans and assessment report)	14 days	Fri 16/4/21	Thu 29/4/21																
76	Consent application for pipe pile opening works	28 days	Fri 23/4/21	Thu 20/5/21																
77	Pipe pile opening works	7 days	Fri 6/8/21	Fri 13/8/21																
78	Extraction of TBM	4 days	Sat 14/8/21	Wed 18/8/21																

Paul Y Construction Co., Ltd.

Task ■ Split ■ Milestone ◆ Summary Project Summary External Tasks Critical Critical Split Progress


Revised Works Programme for 2no. DN1800 CW Outlet Pipes Installation - Culvert Outfall No. 4 + GRS Works

No.4 Outfall AA+GRS (Rev.13) (21-7-2021)

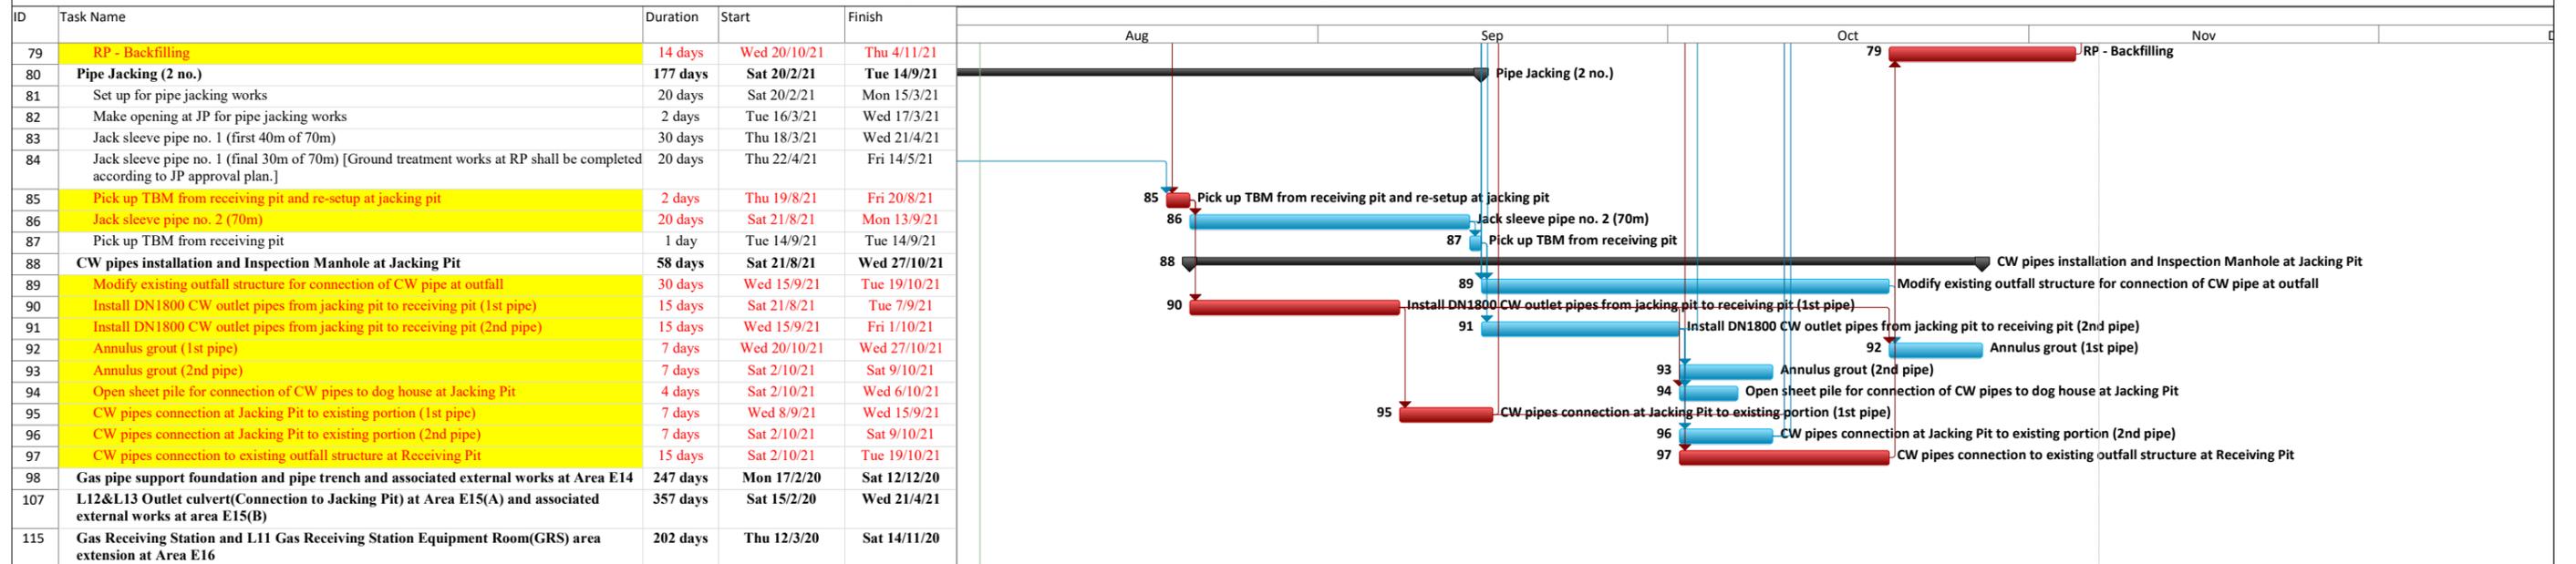

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

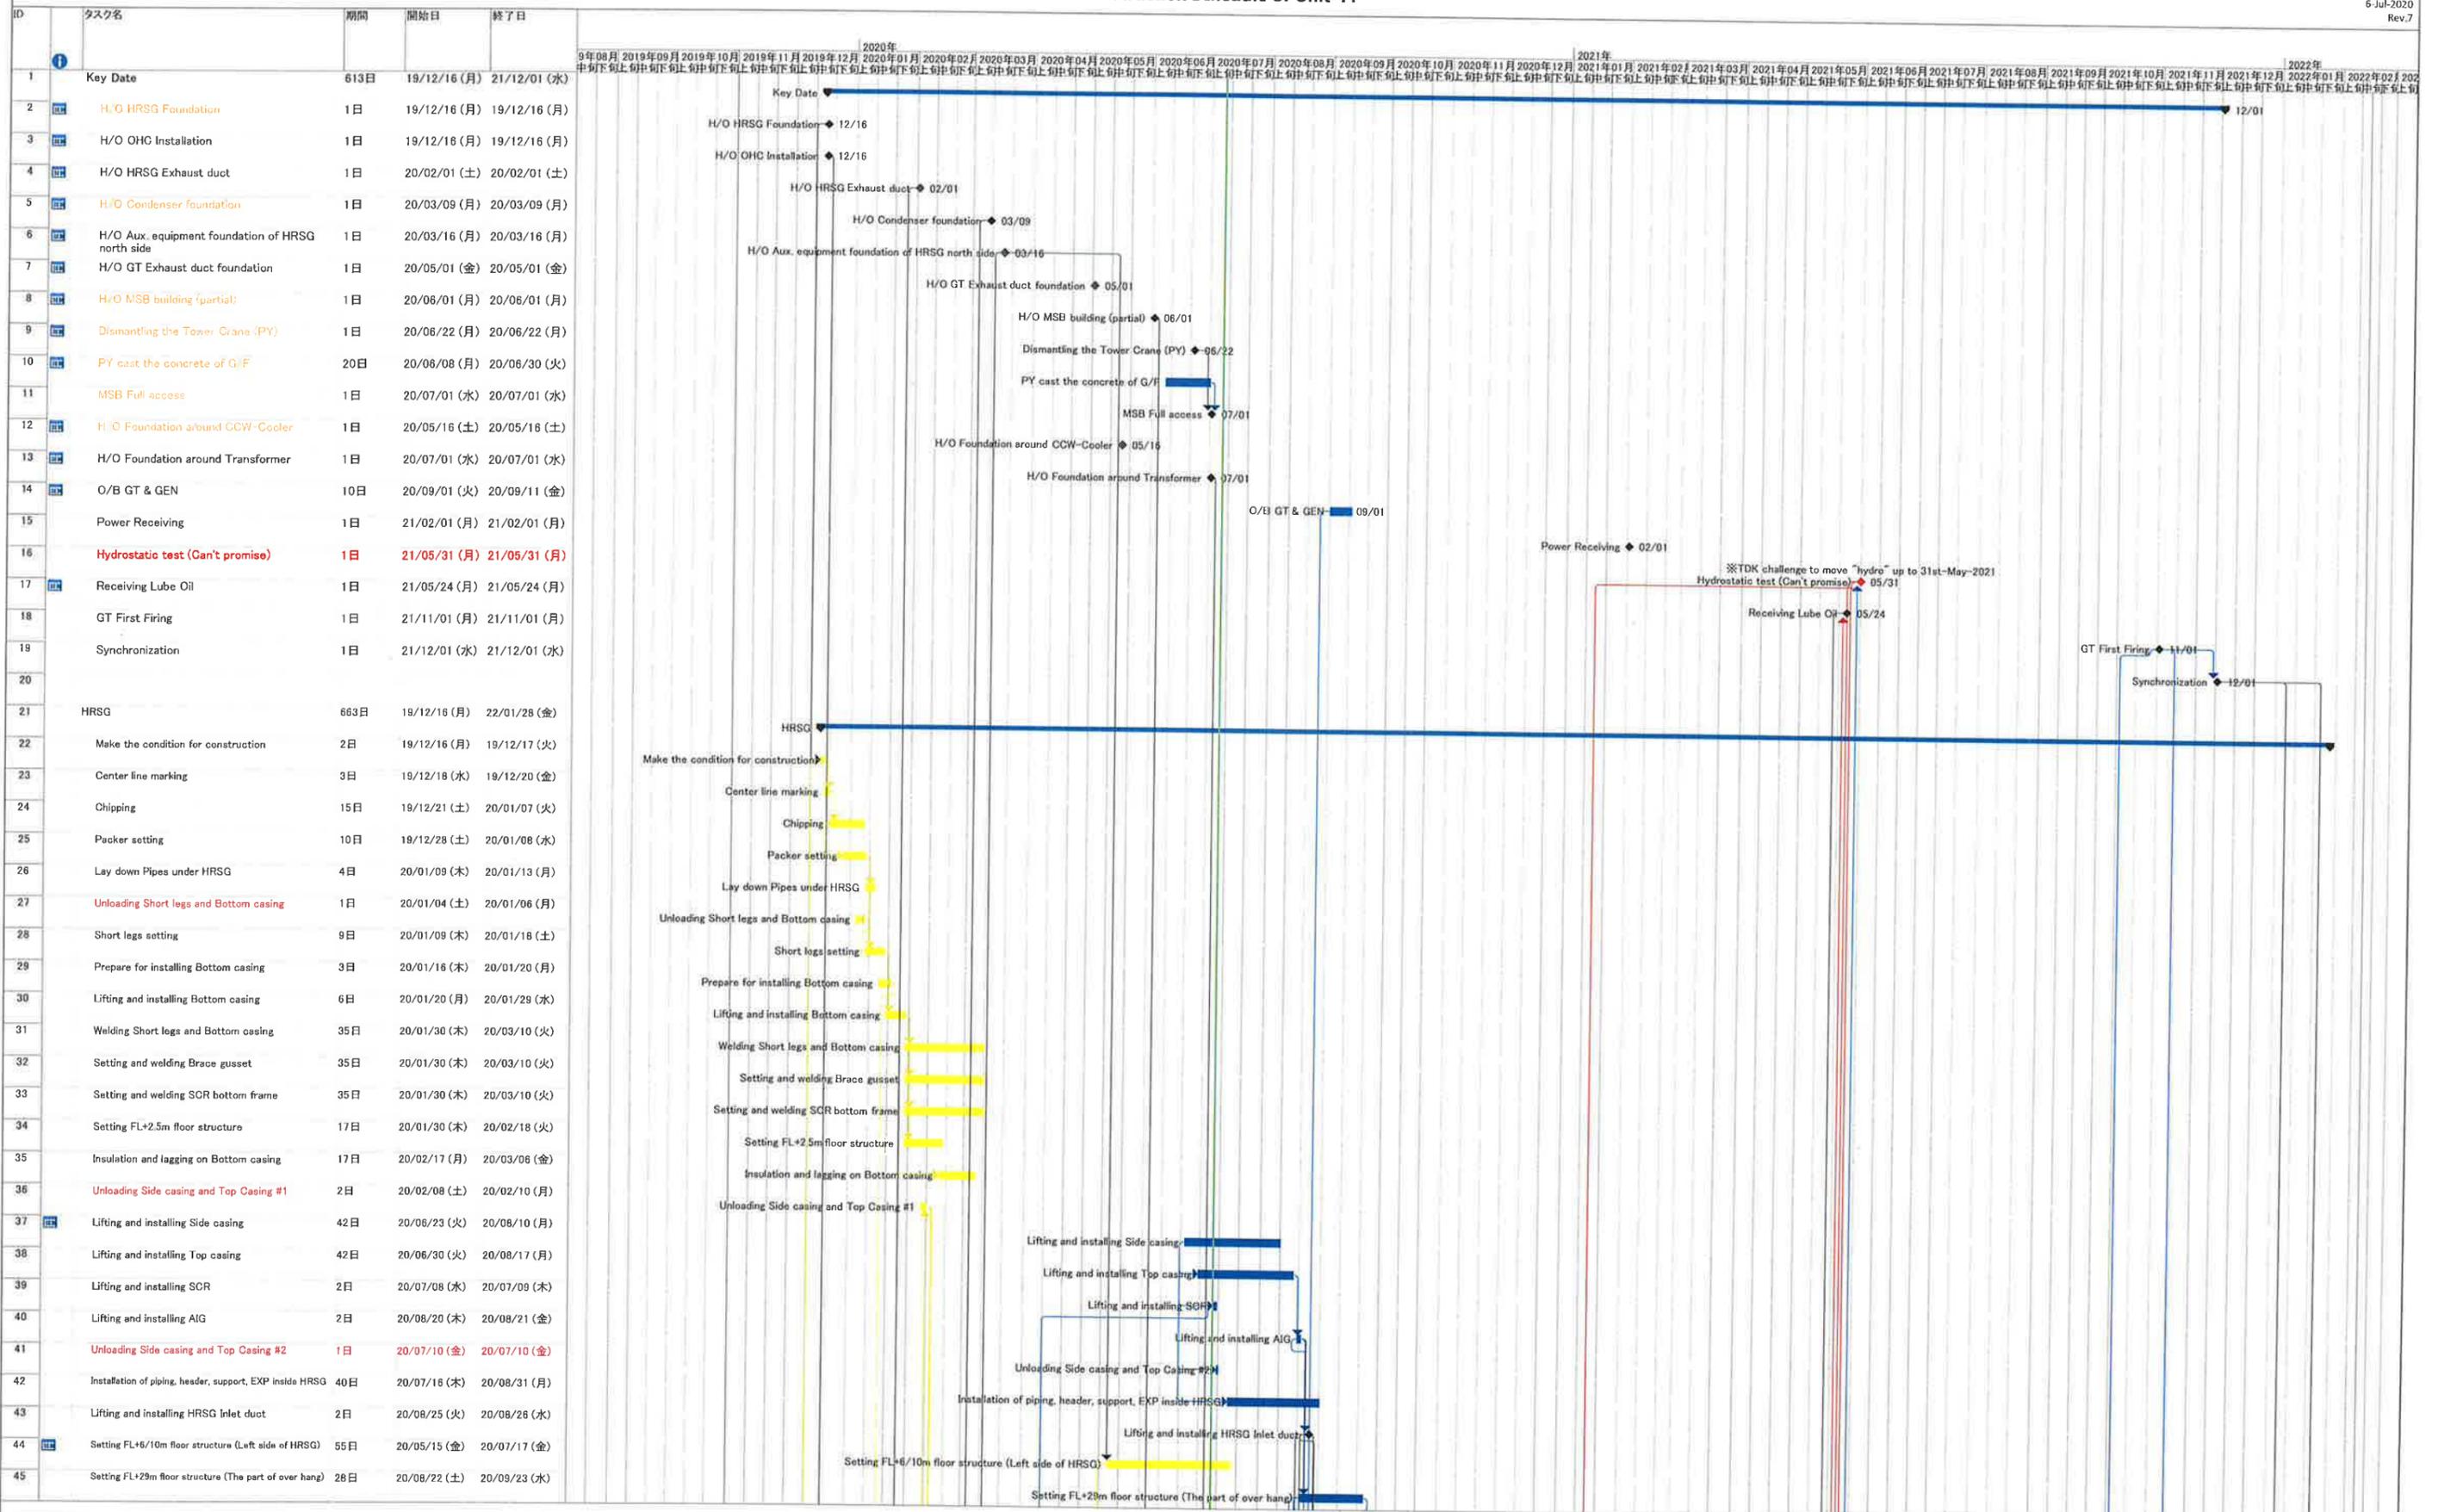


1. Change the starting date of installation below
 - ・ Installation HRSFG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15th-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

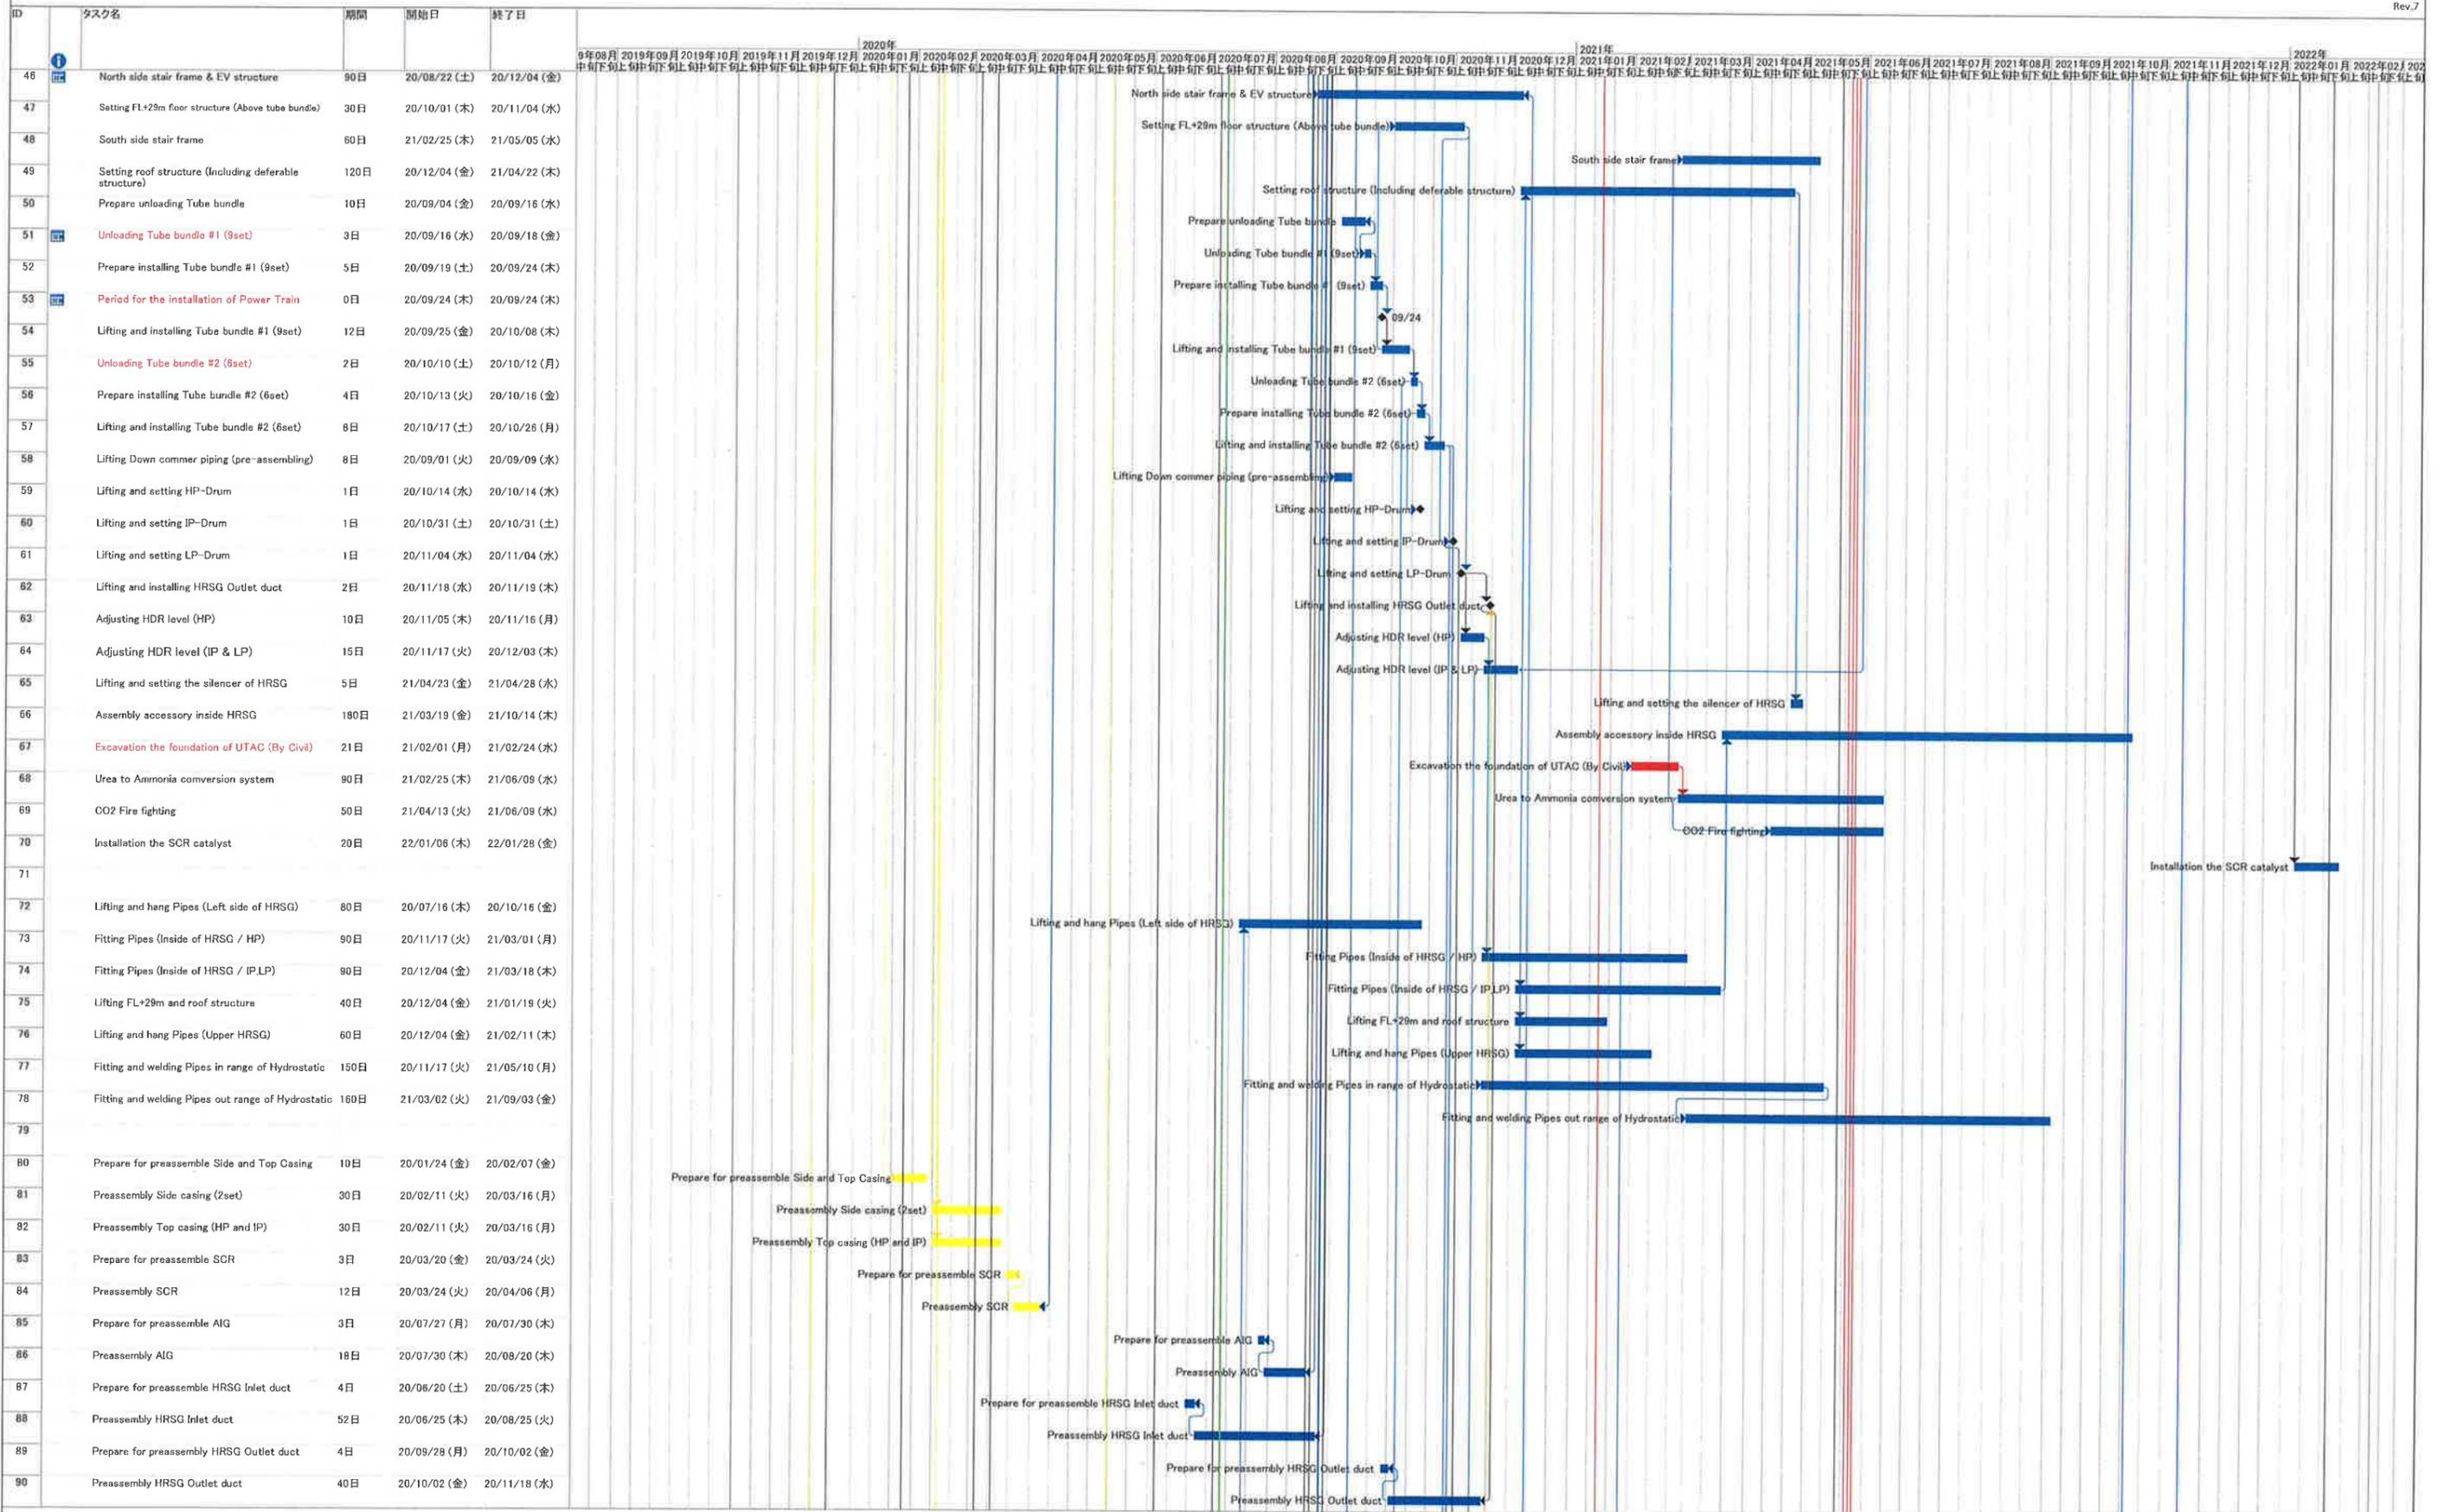


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

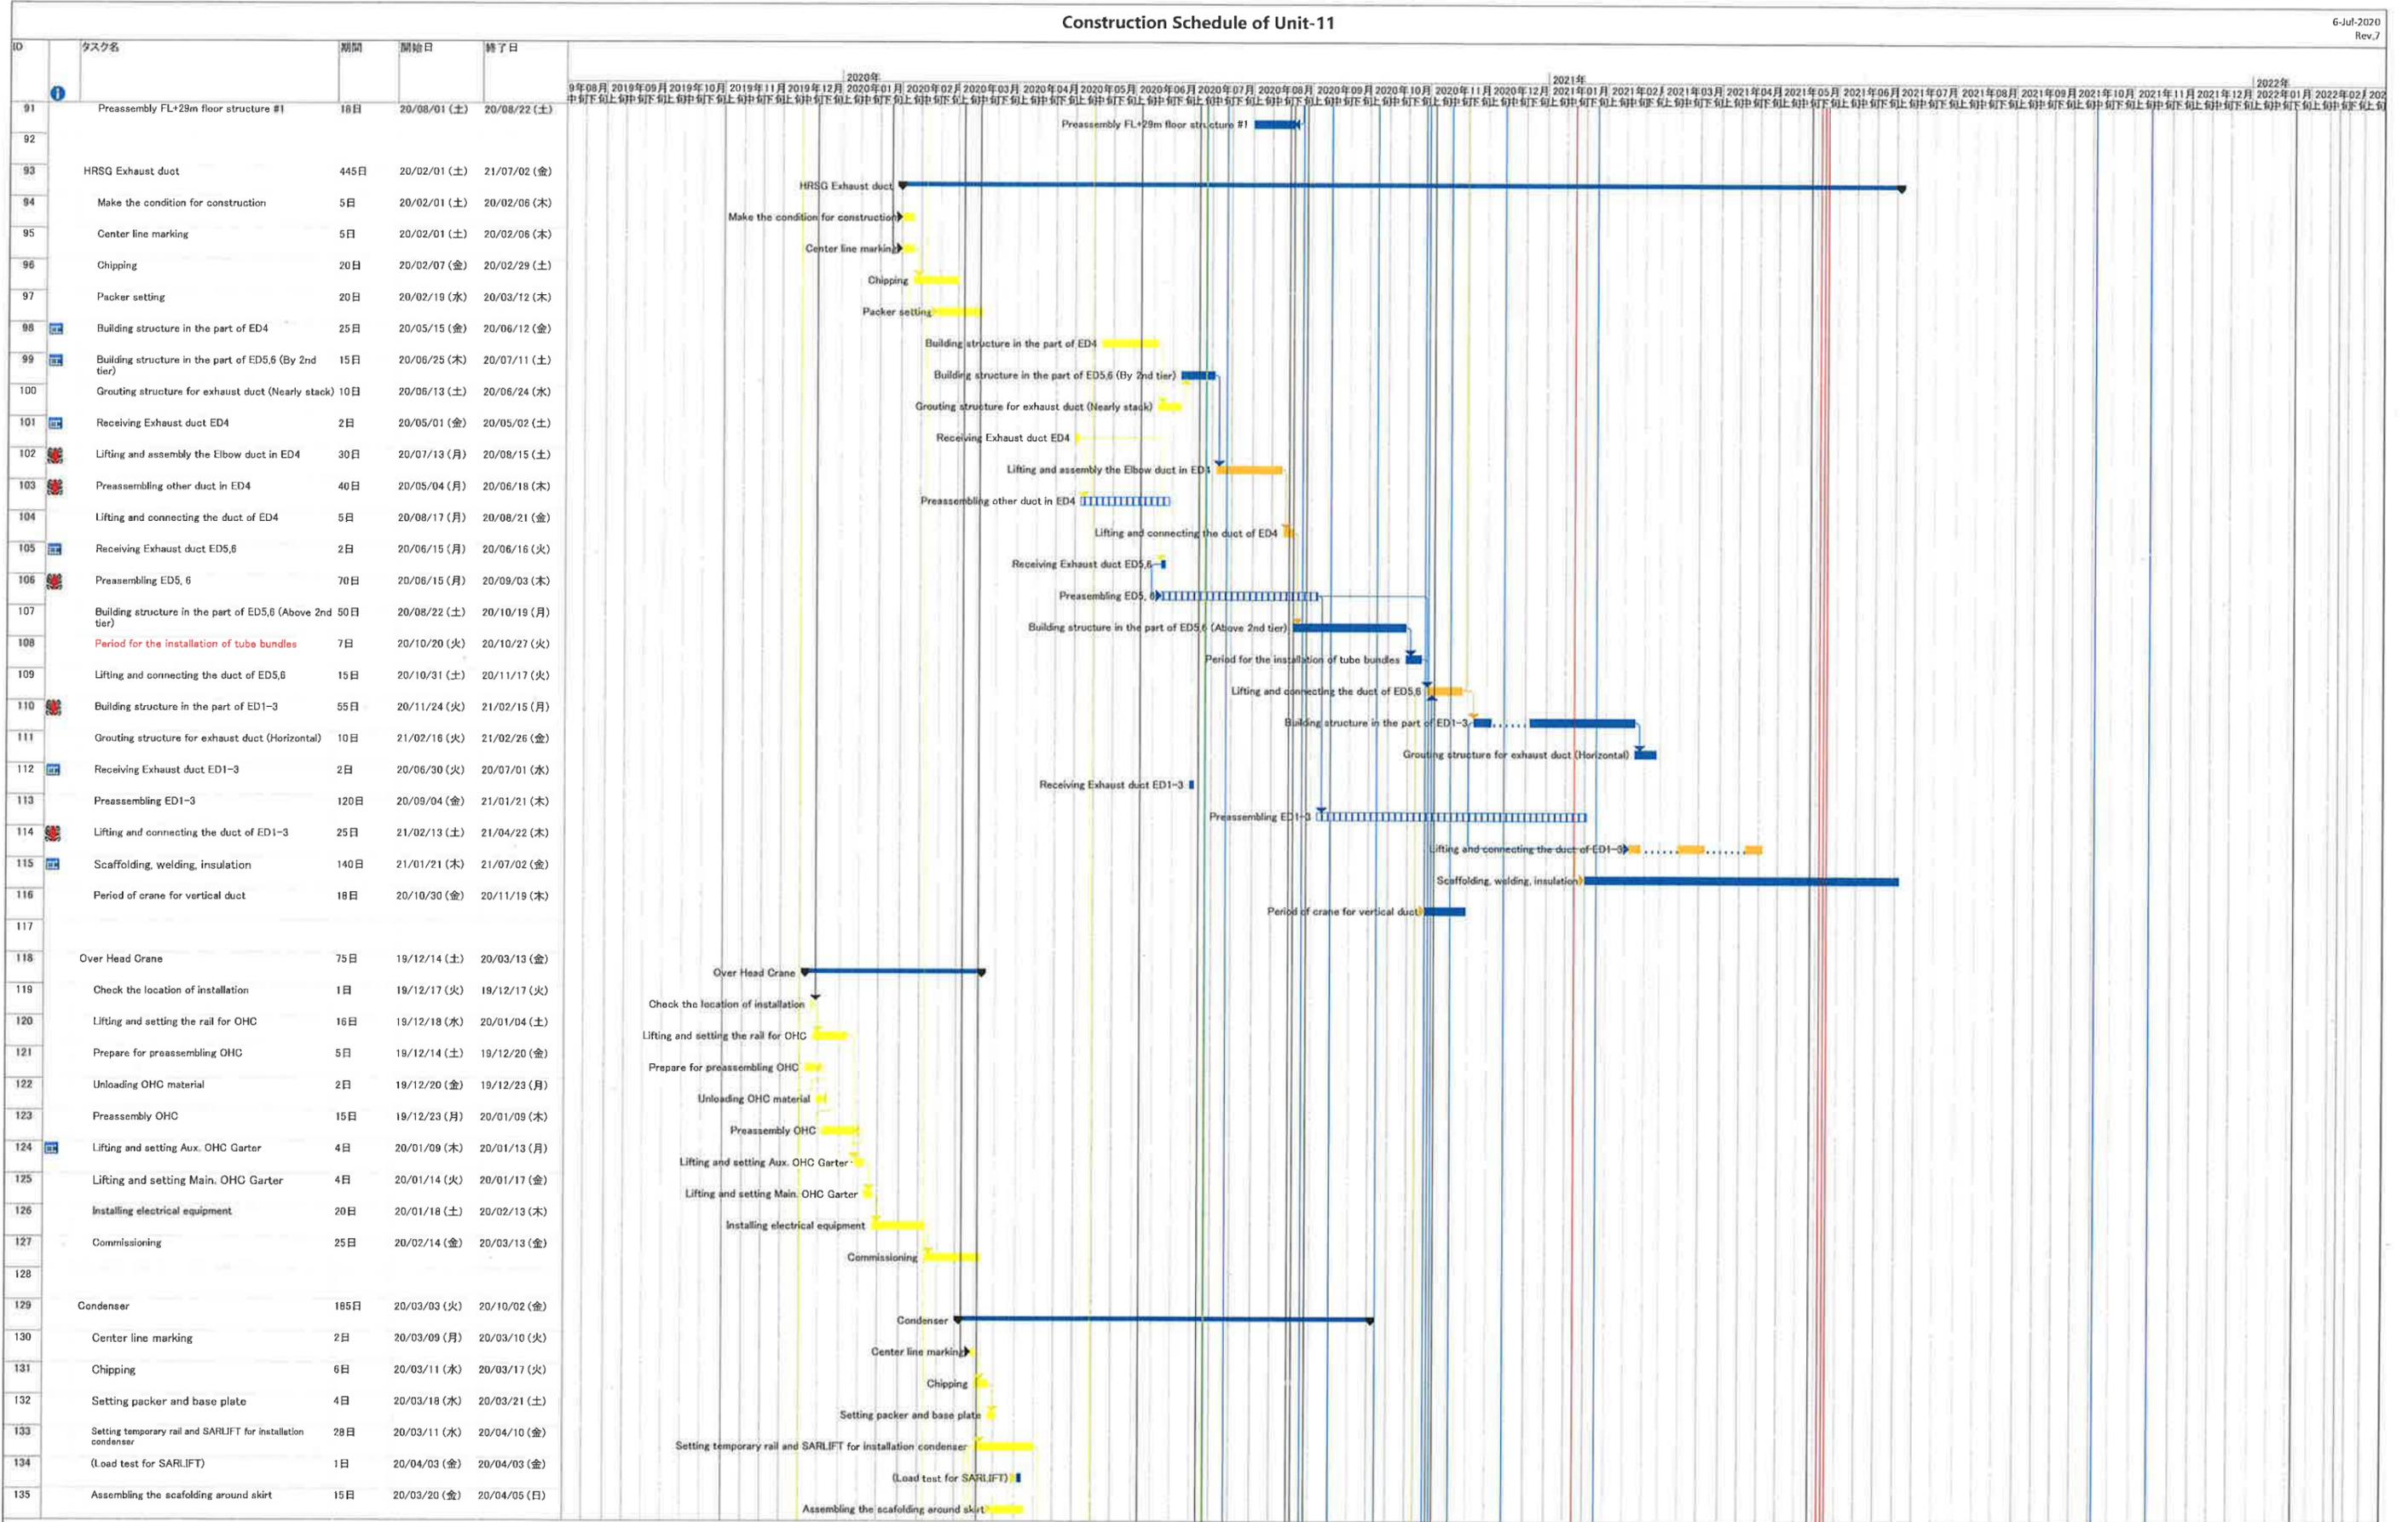


1. Change the starting date of installation below
 - ・ Installation HRSQ was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15th-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

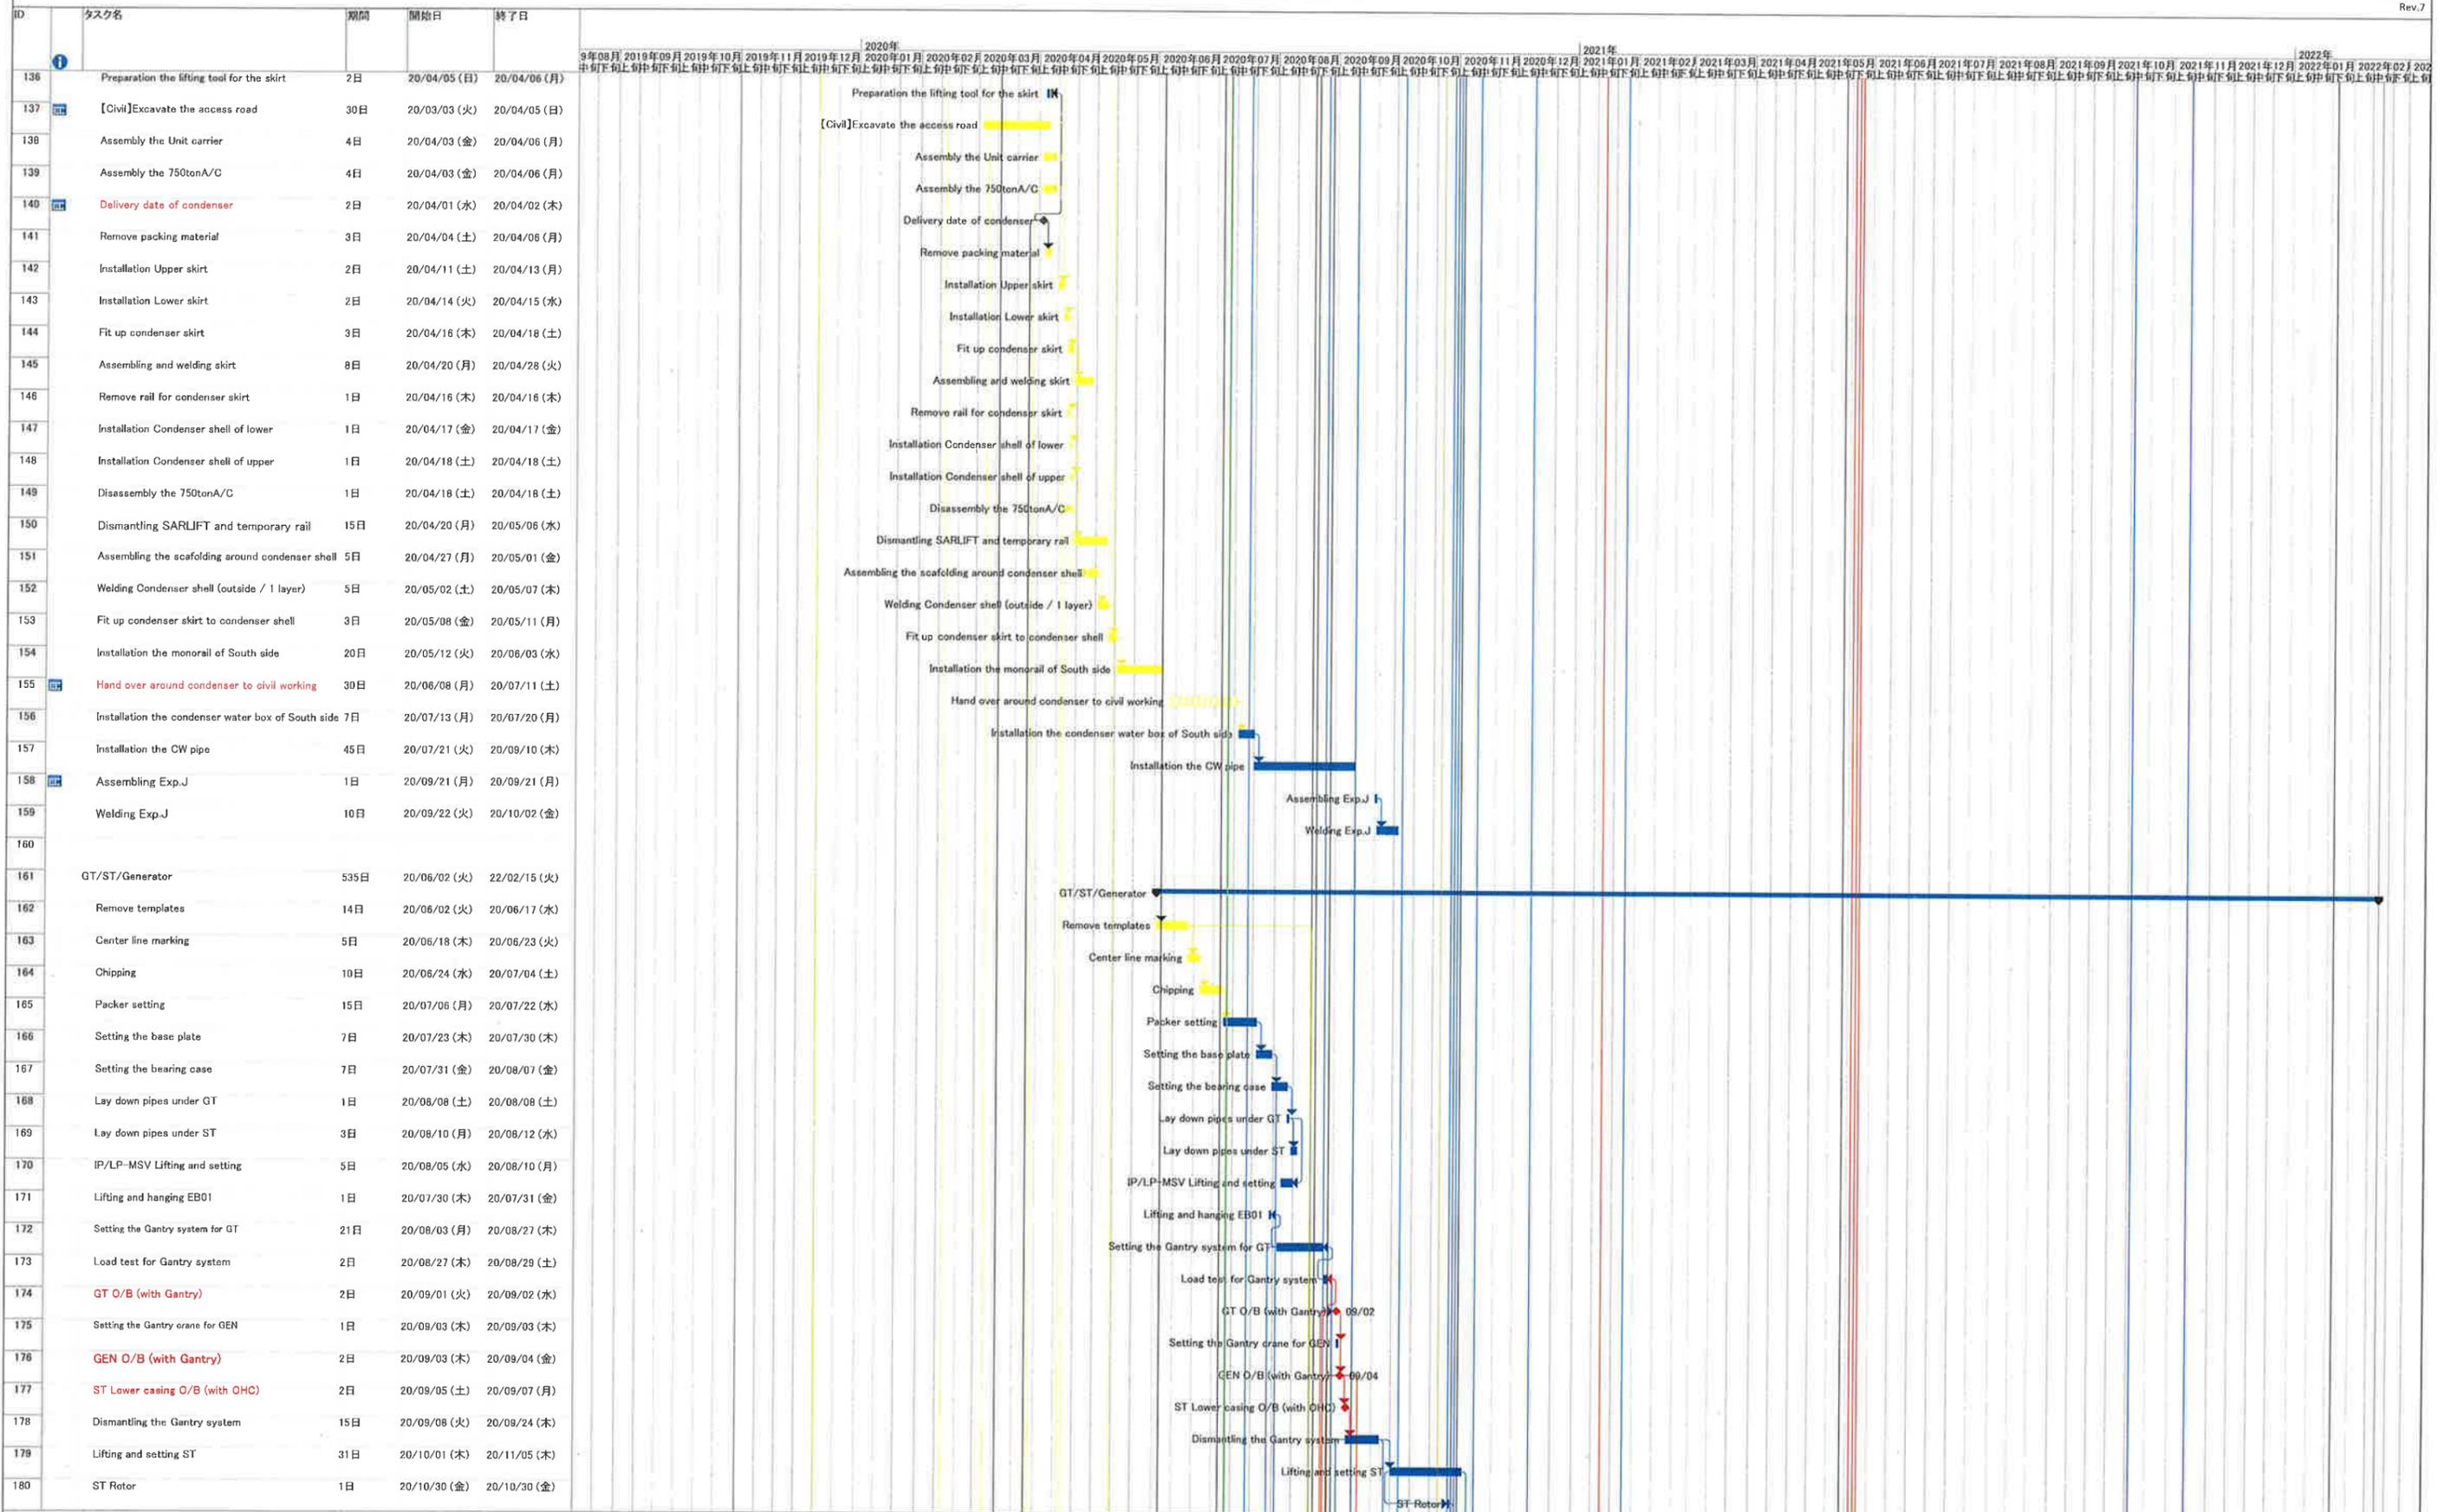


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

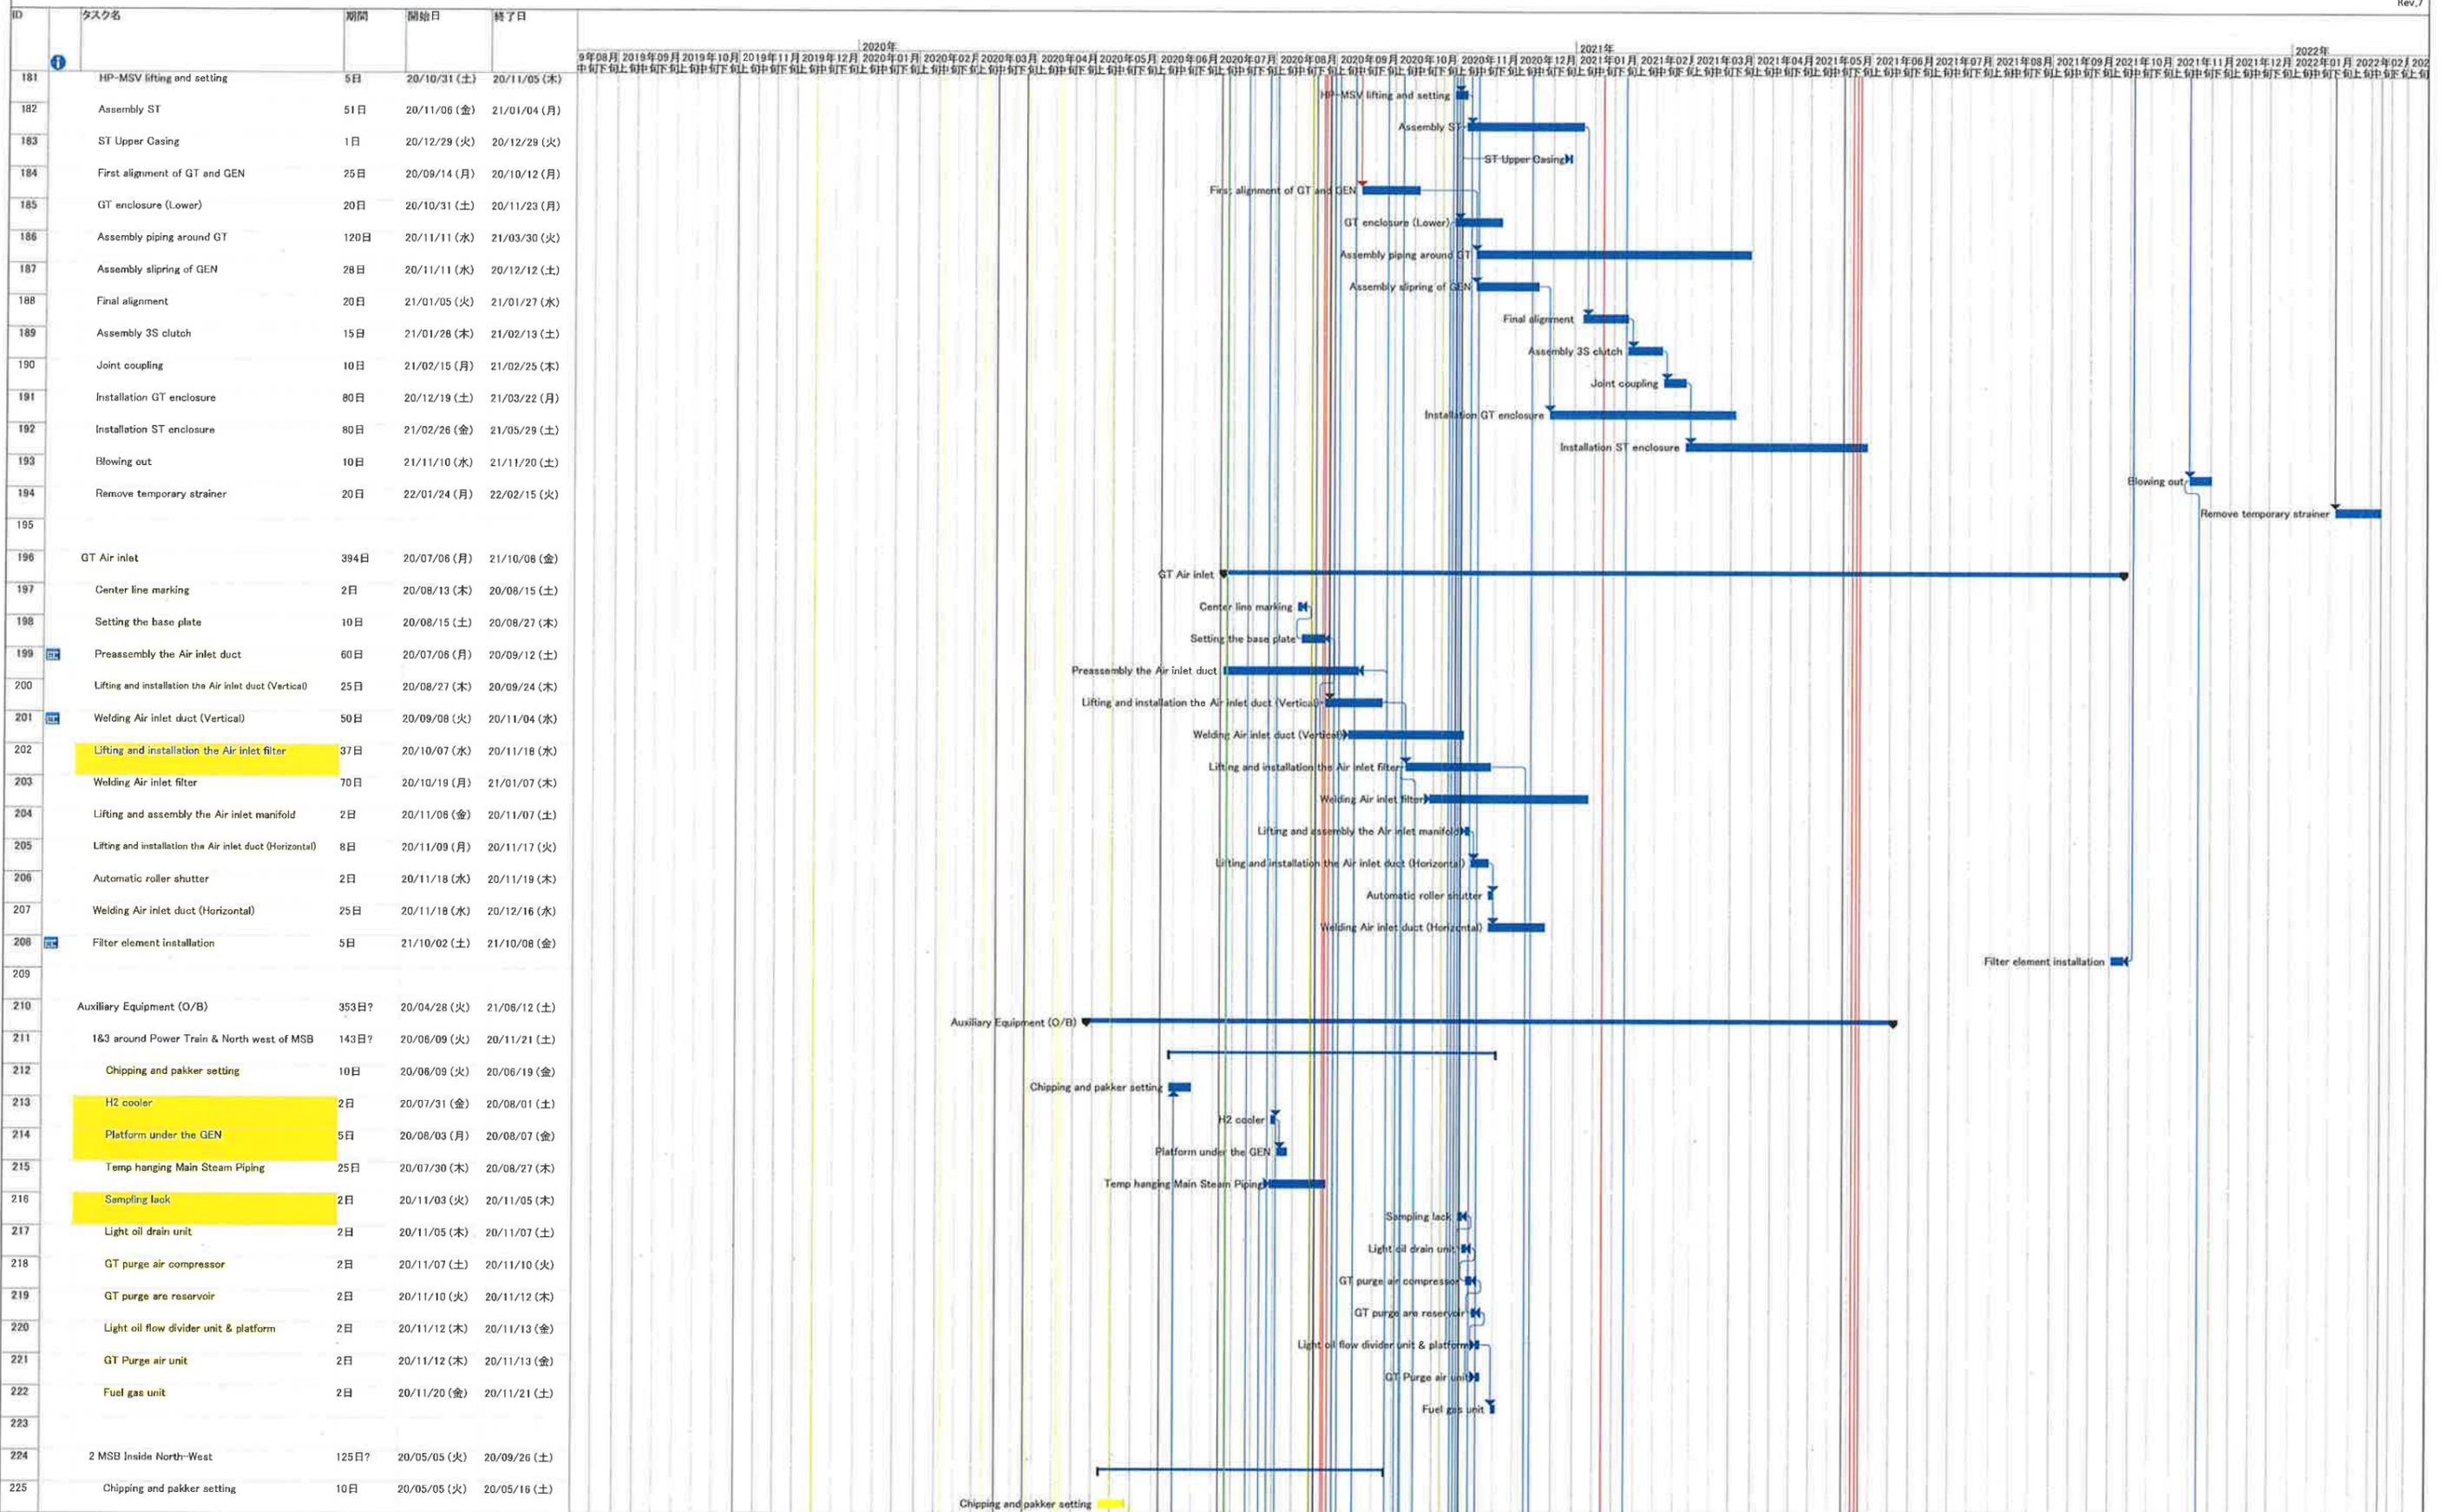


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020 Rev.7

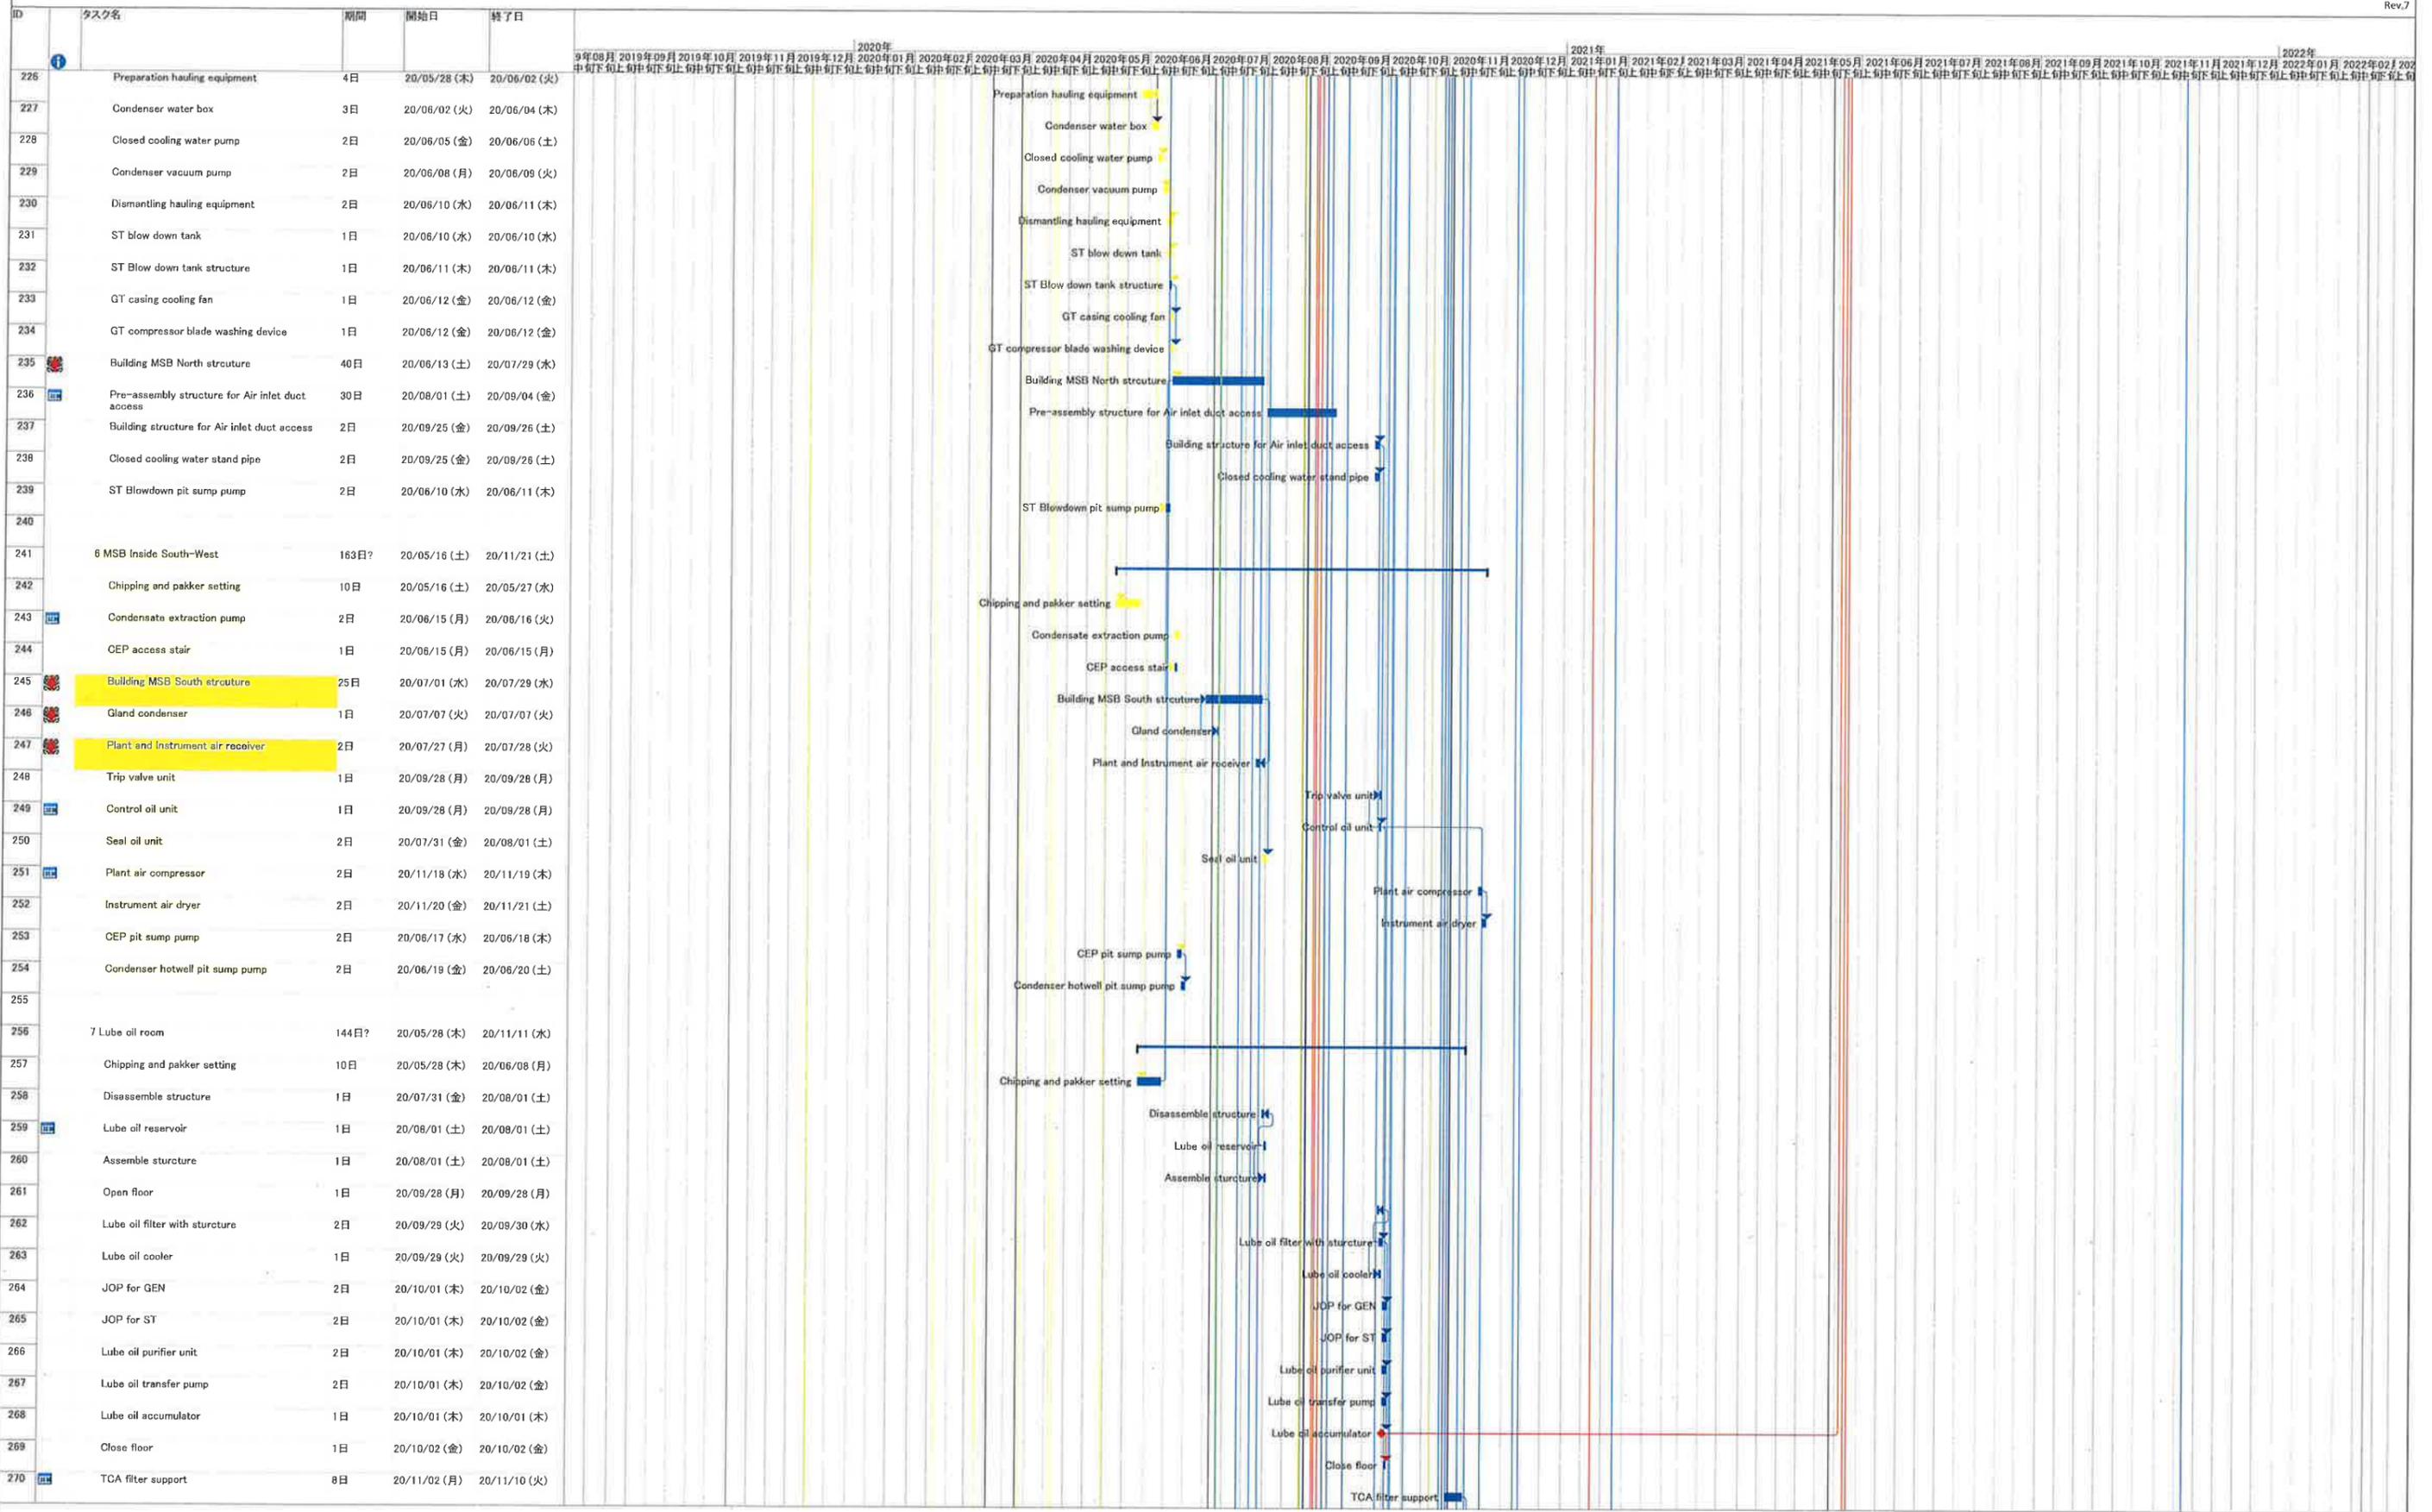


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

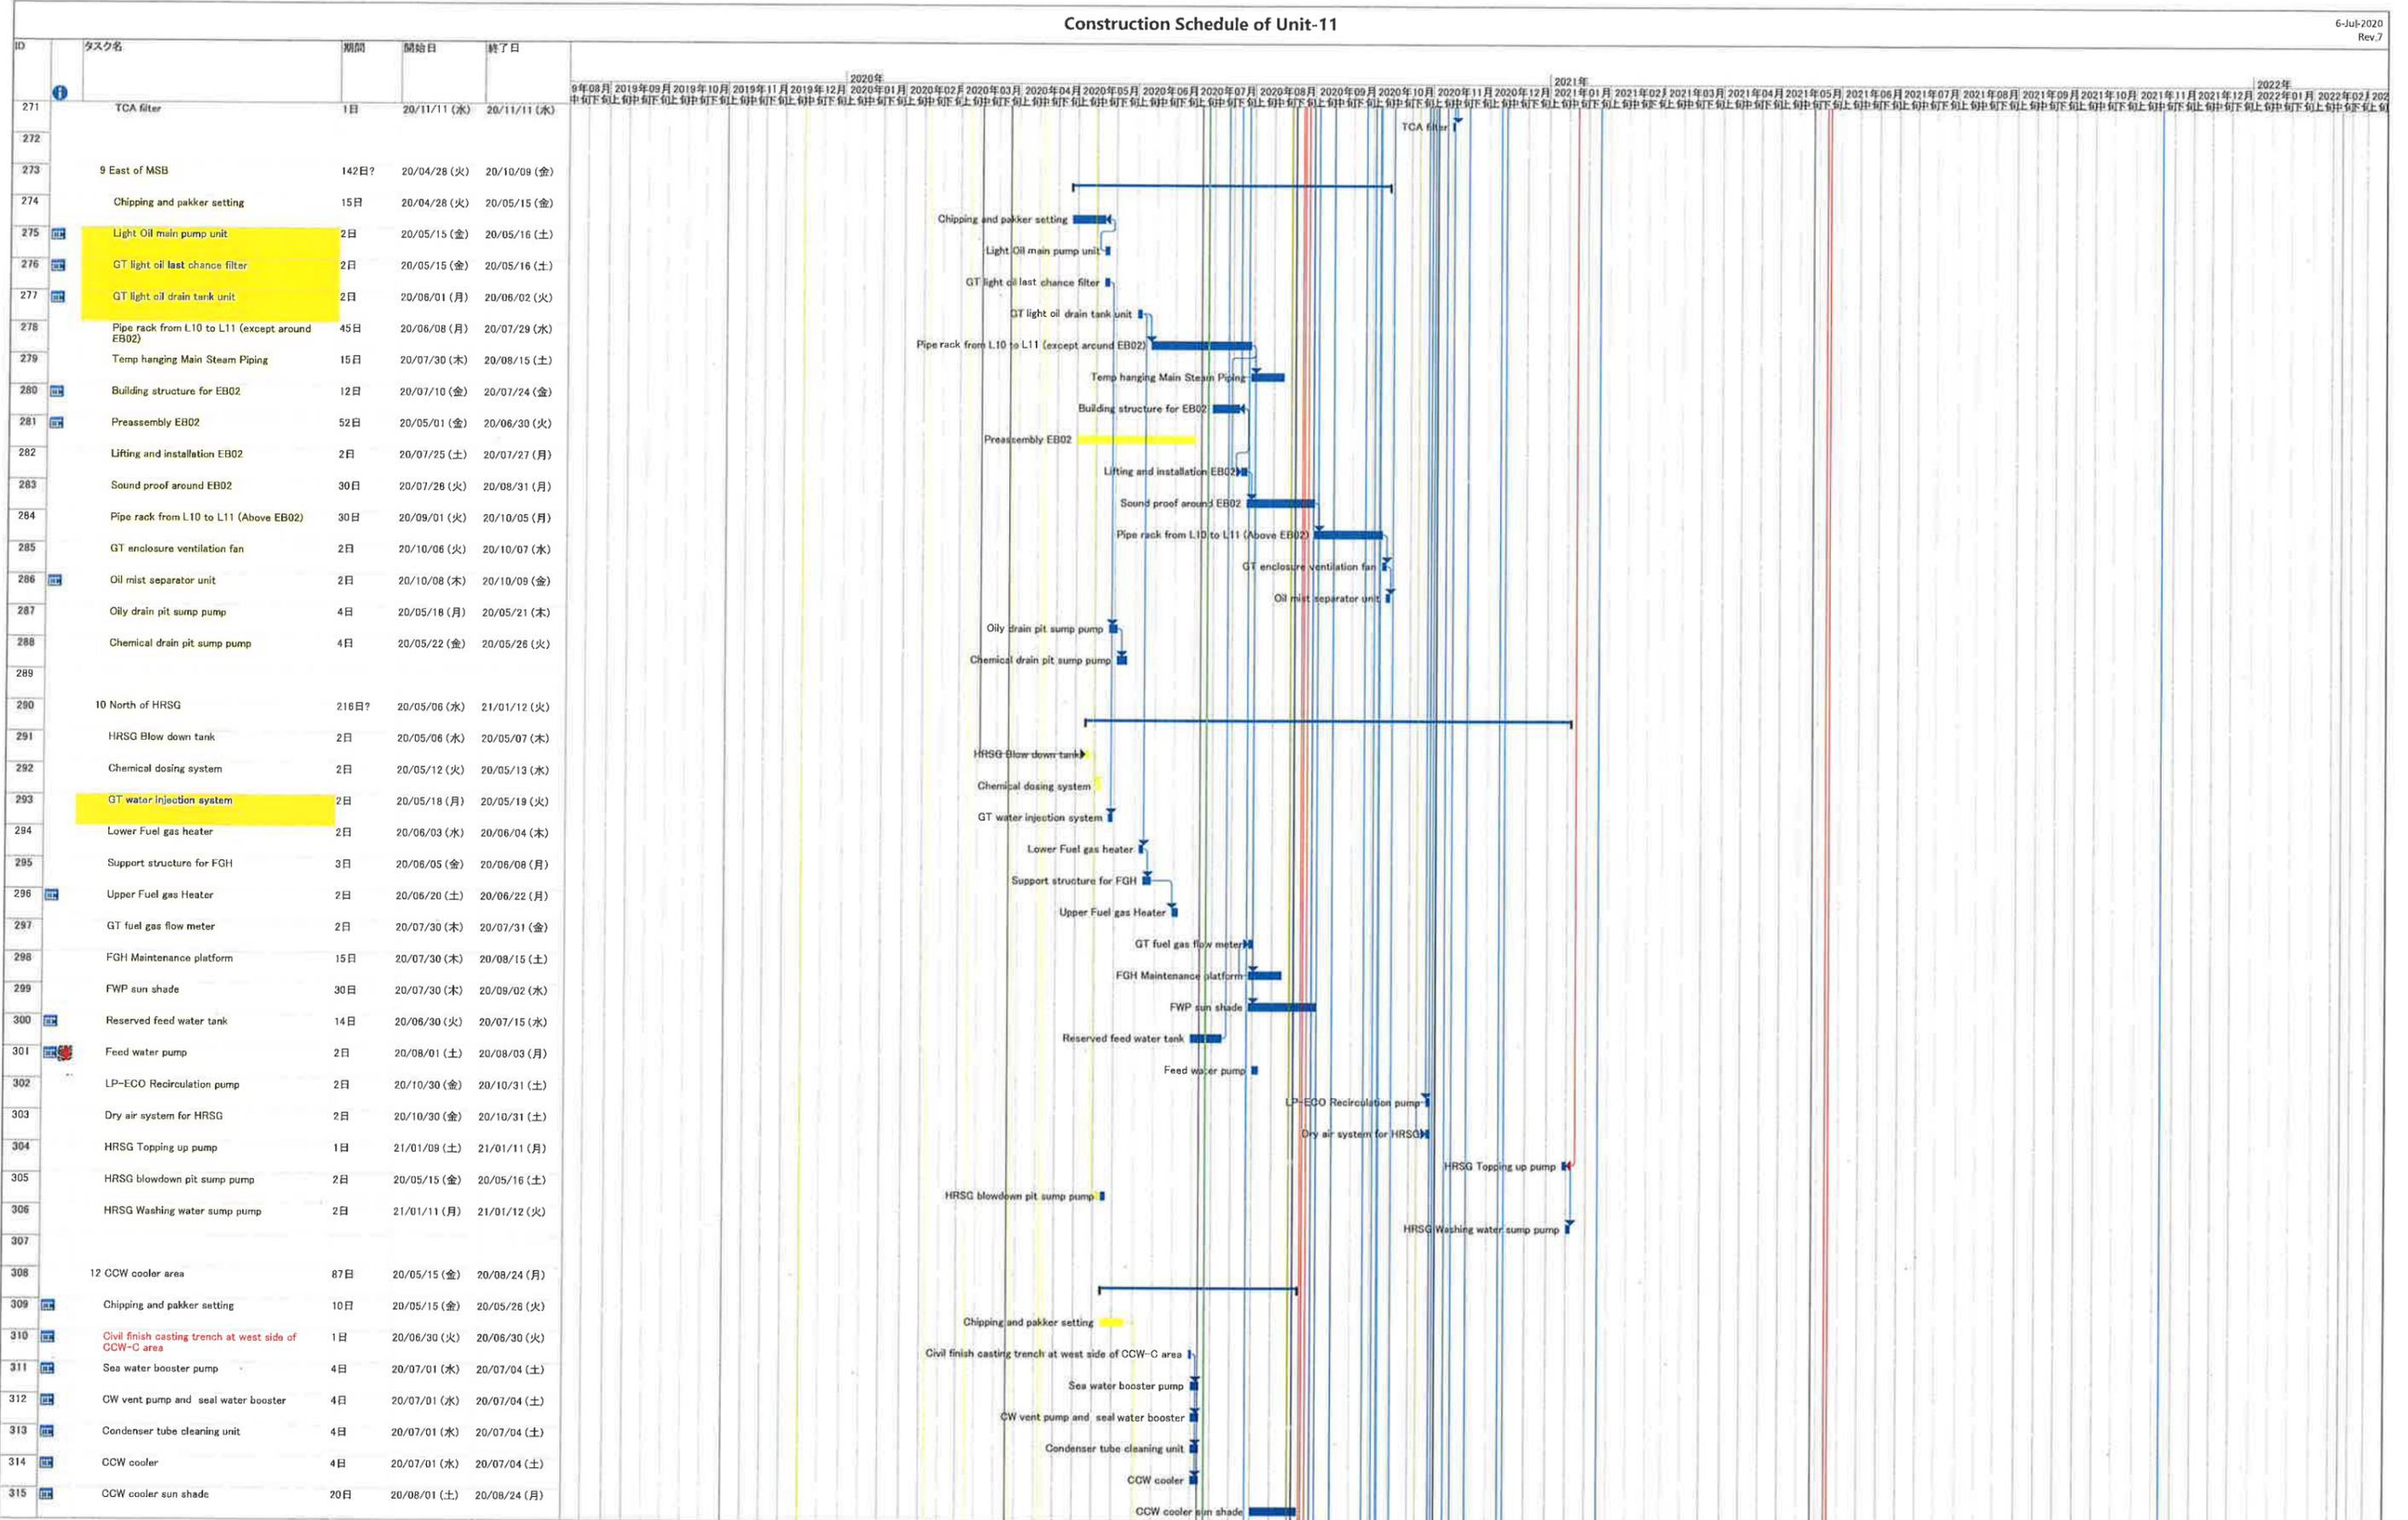


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

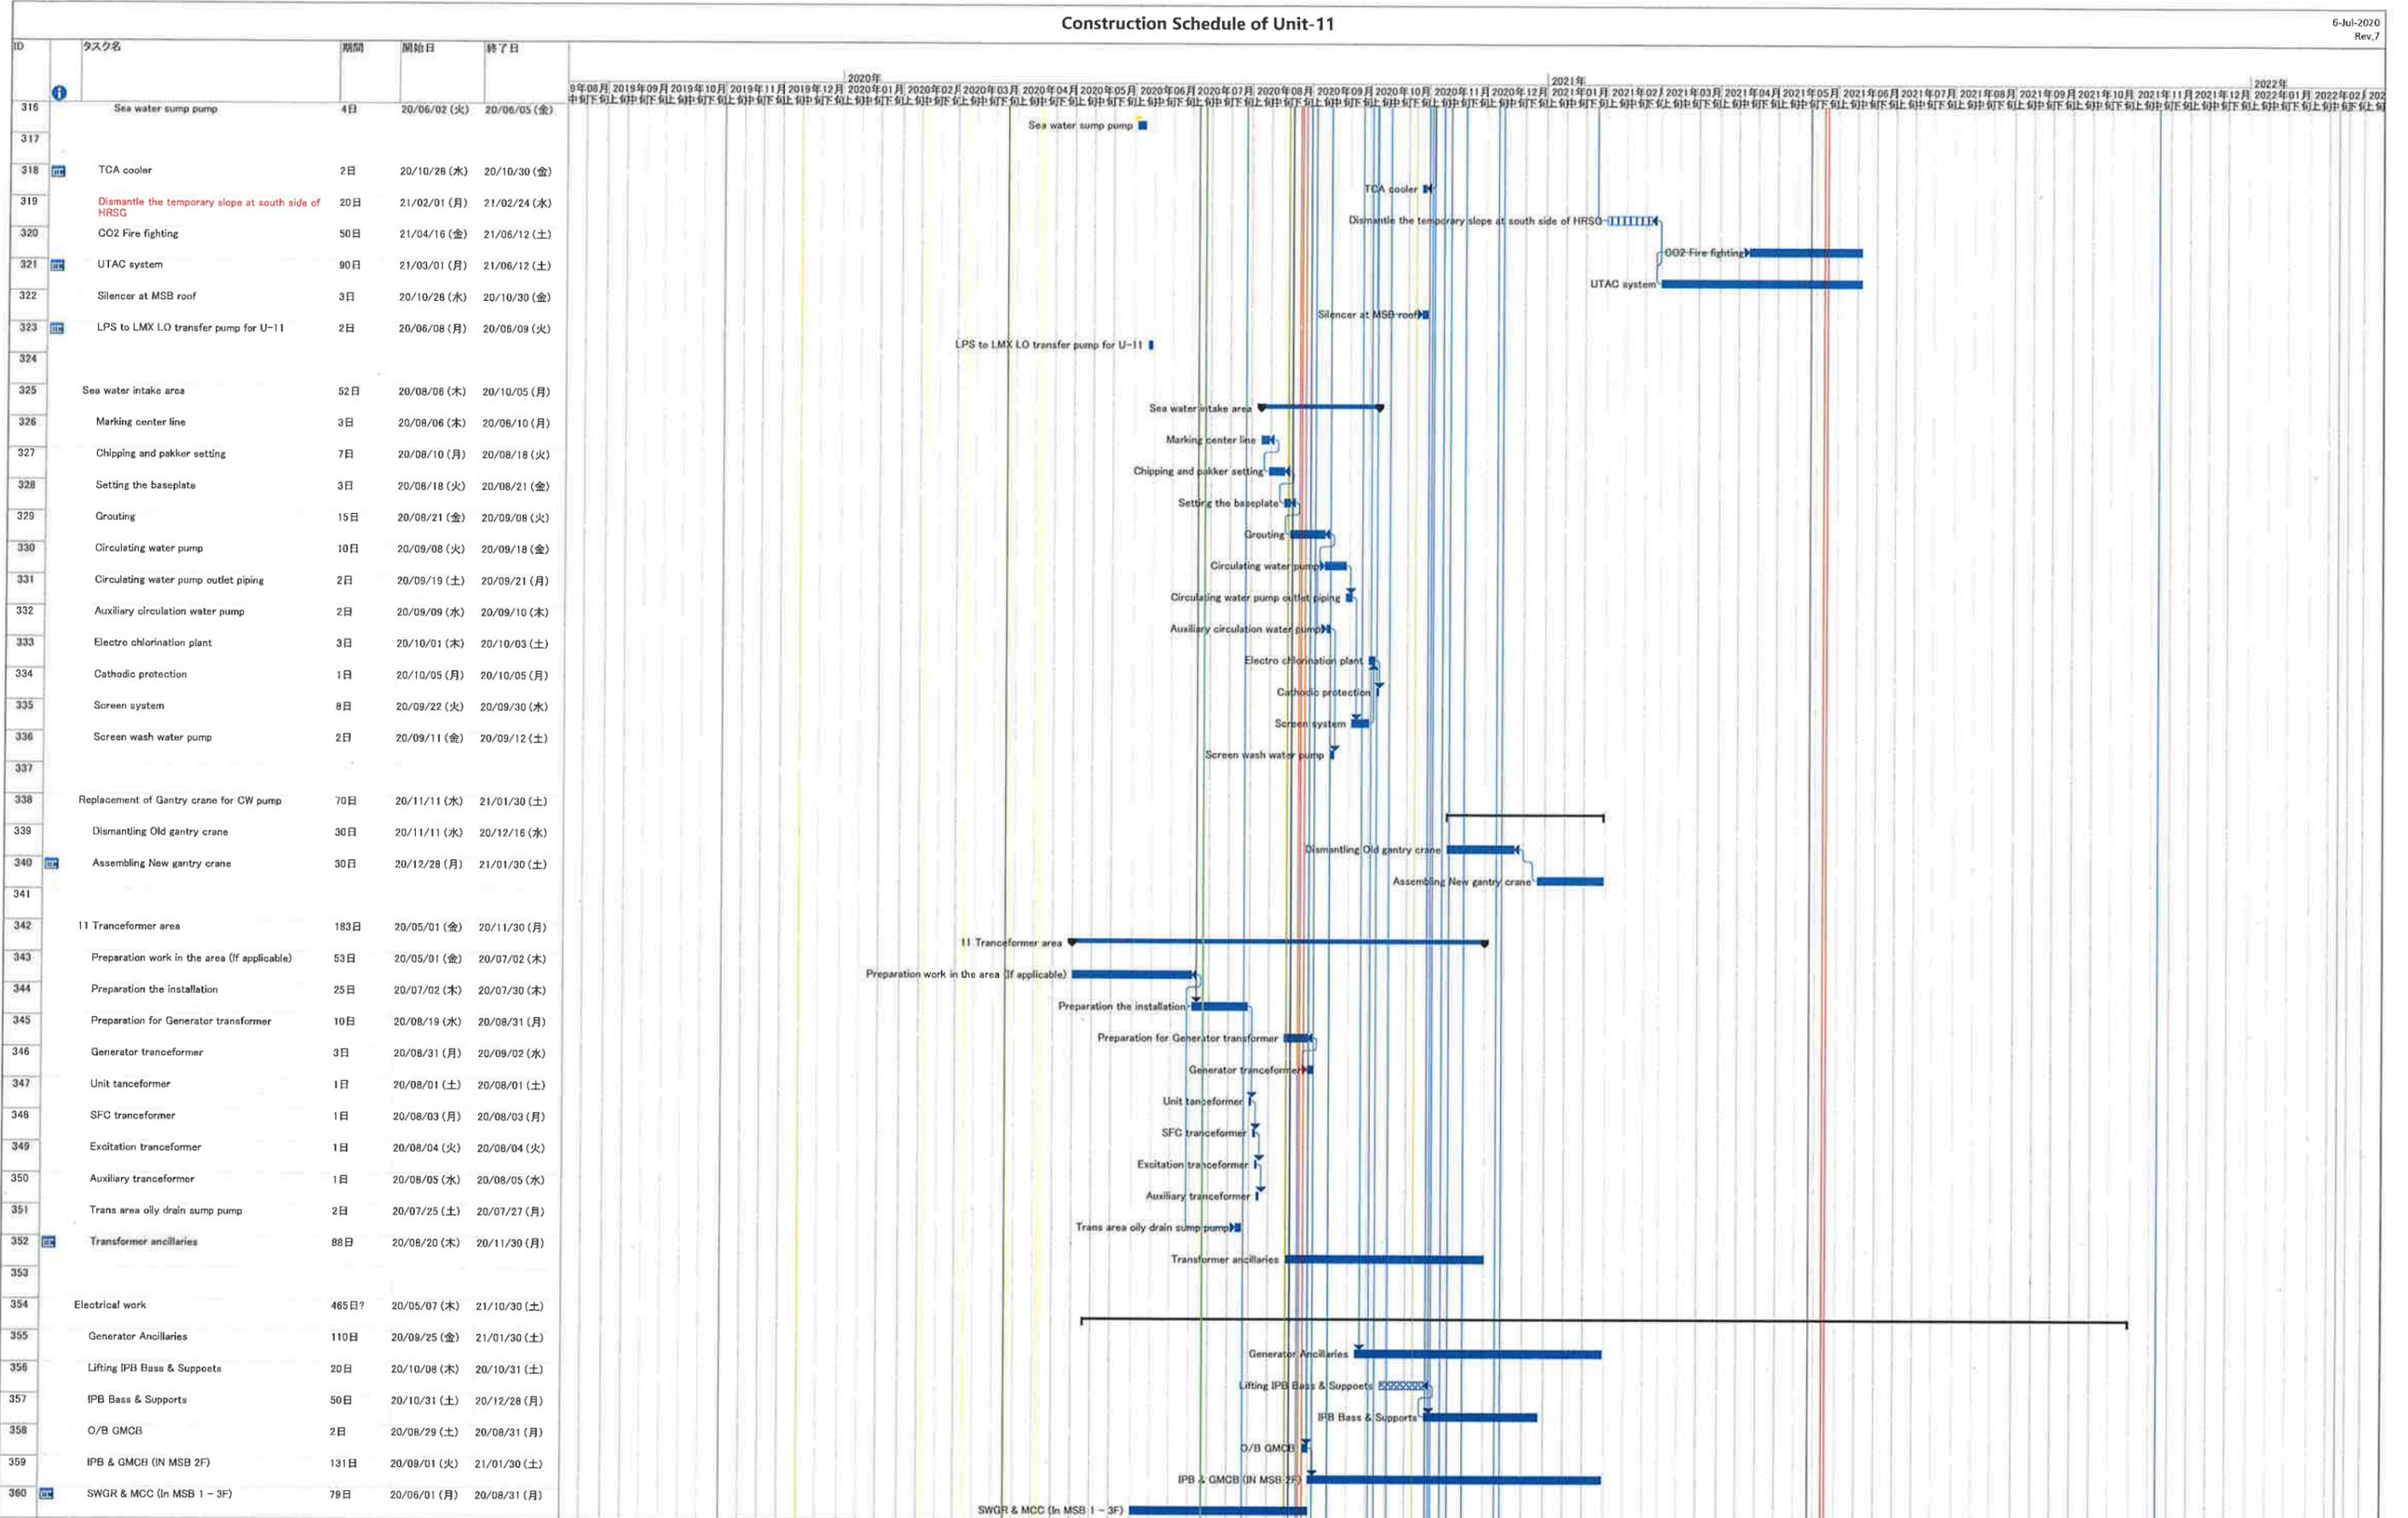


1. Change the starting date of installation below
 ・ Installation HRSG was re-started from 23rd-Jun
 ・ Installation Exhaust duct was re-started from 15st-May
 2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
 5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

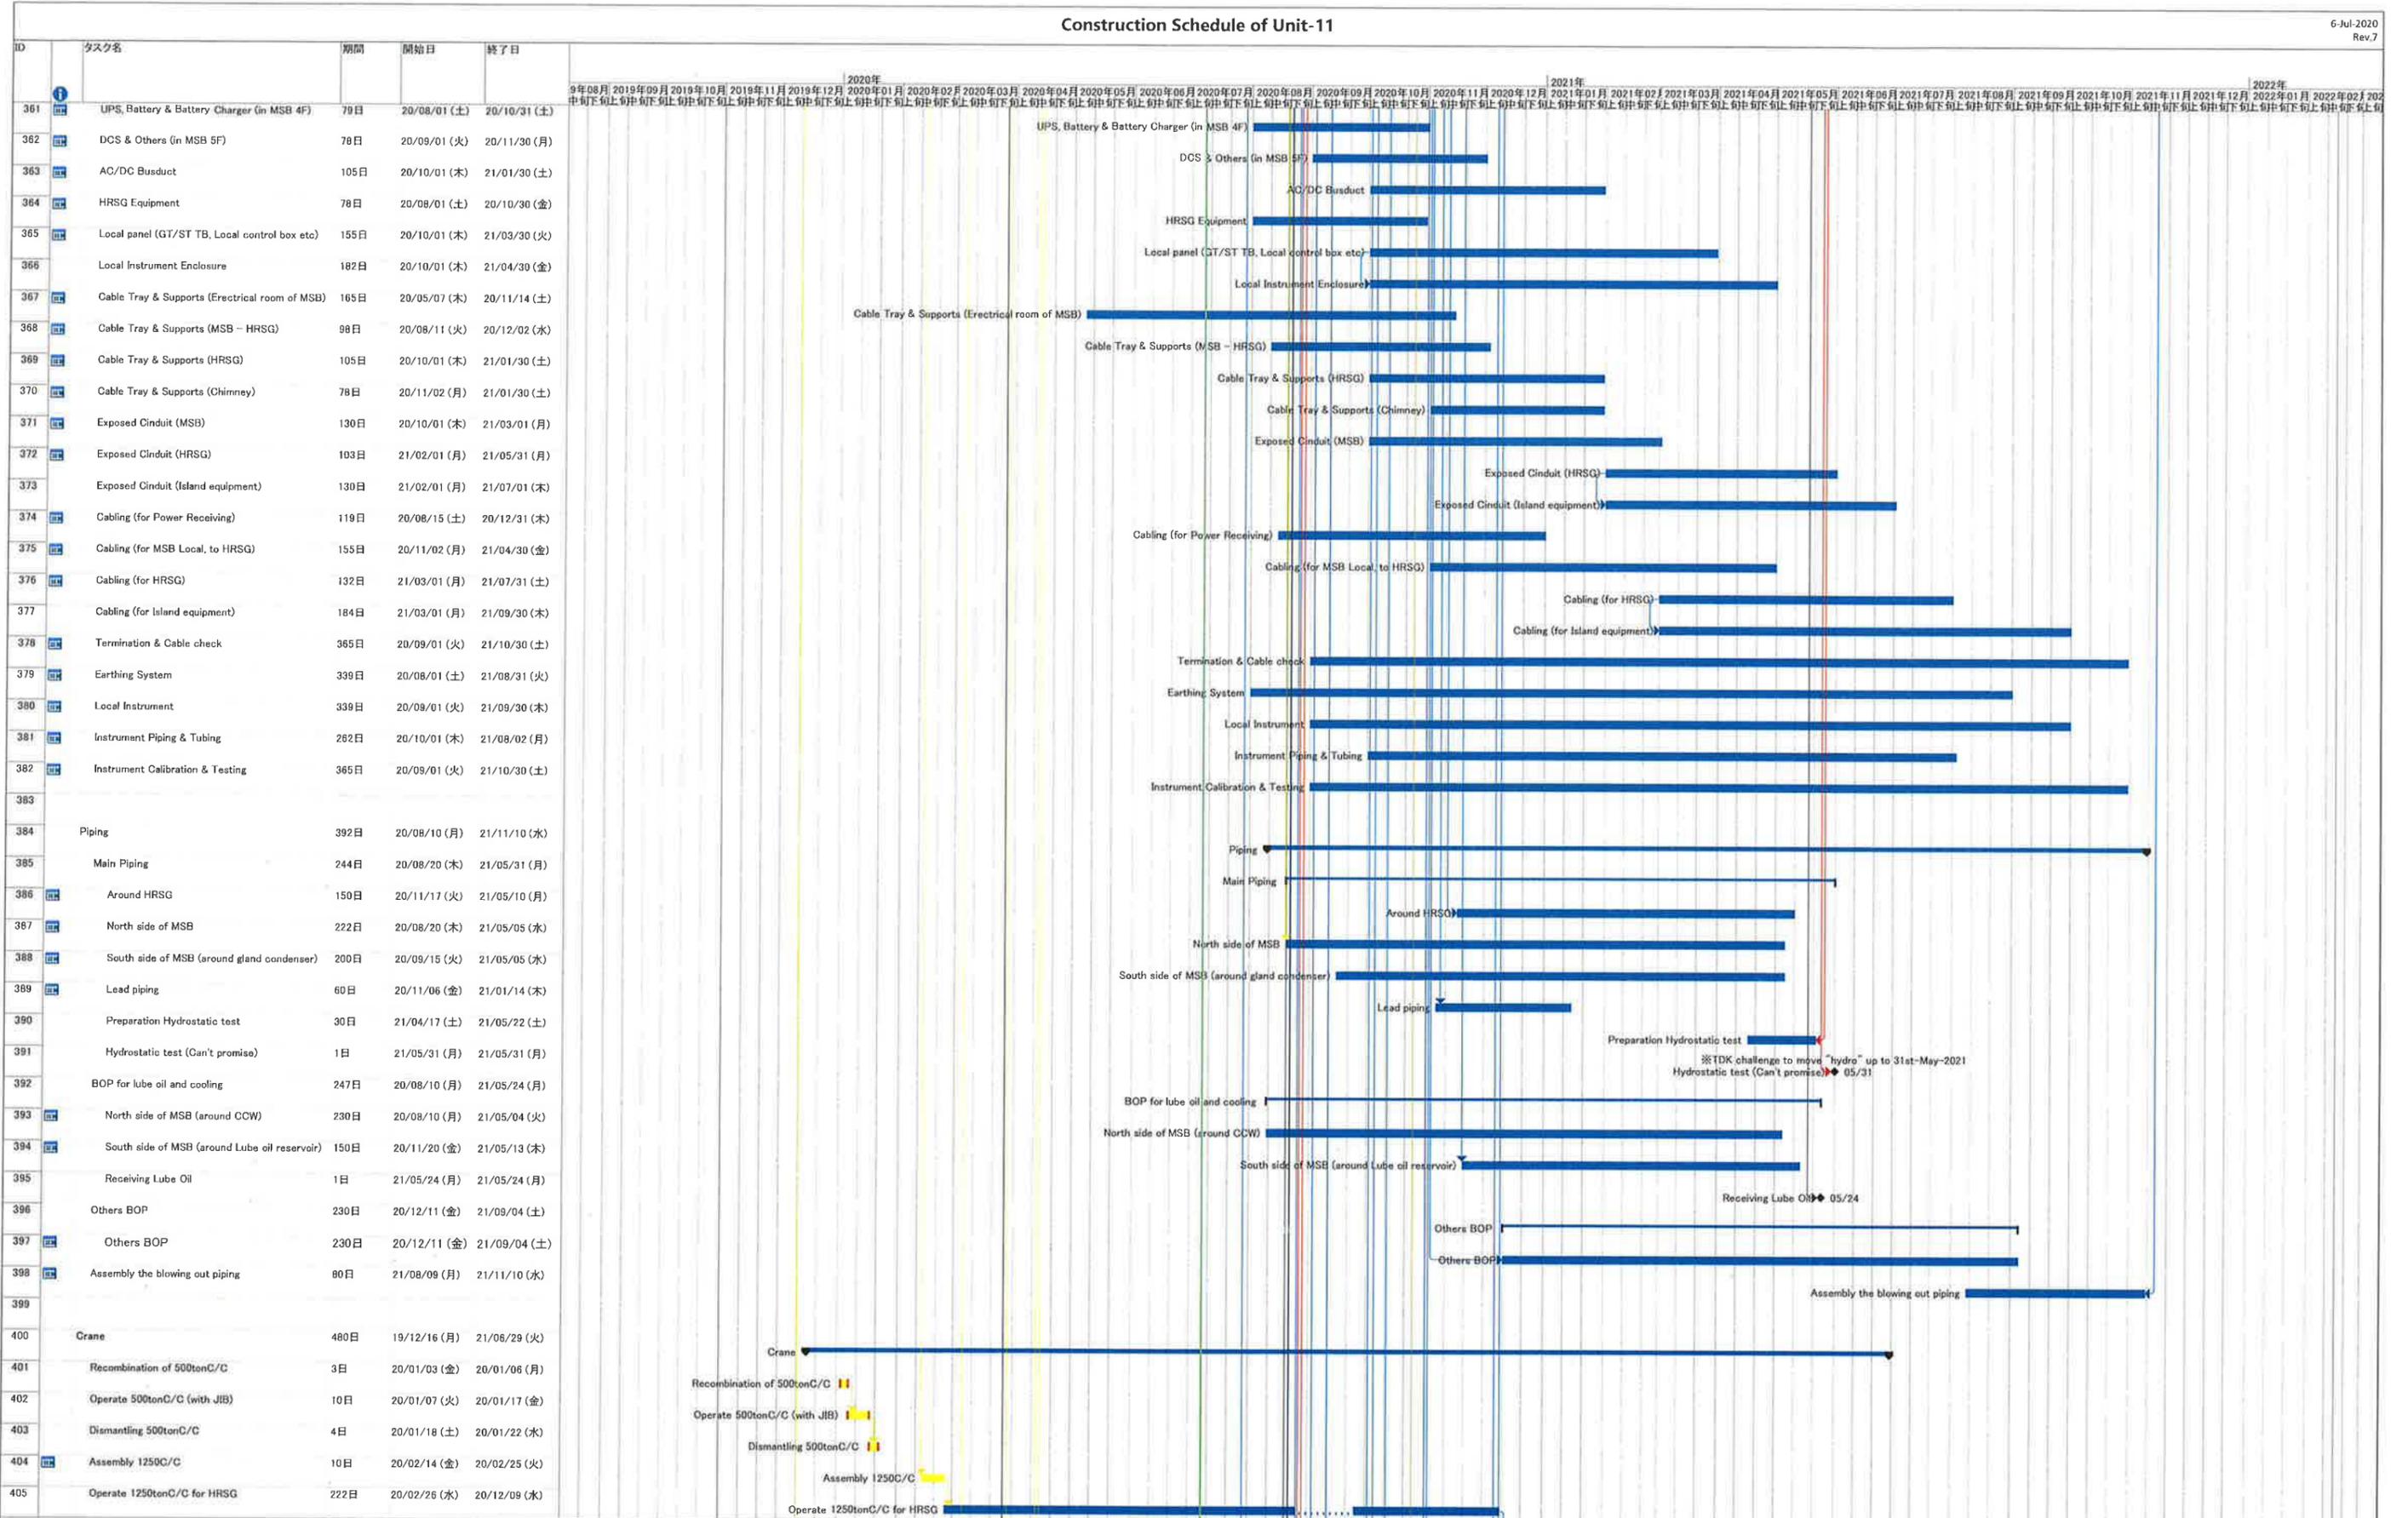


1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15th-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Construction Schedule of Unit-11

6-Jul-2020
Rev.7

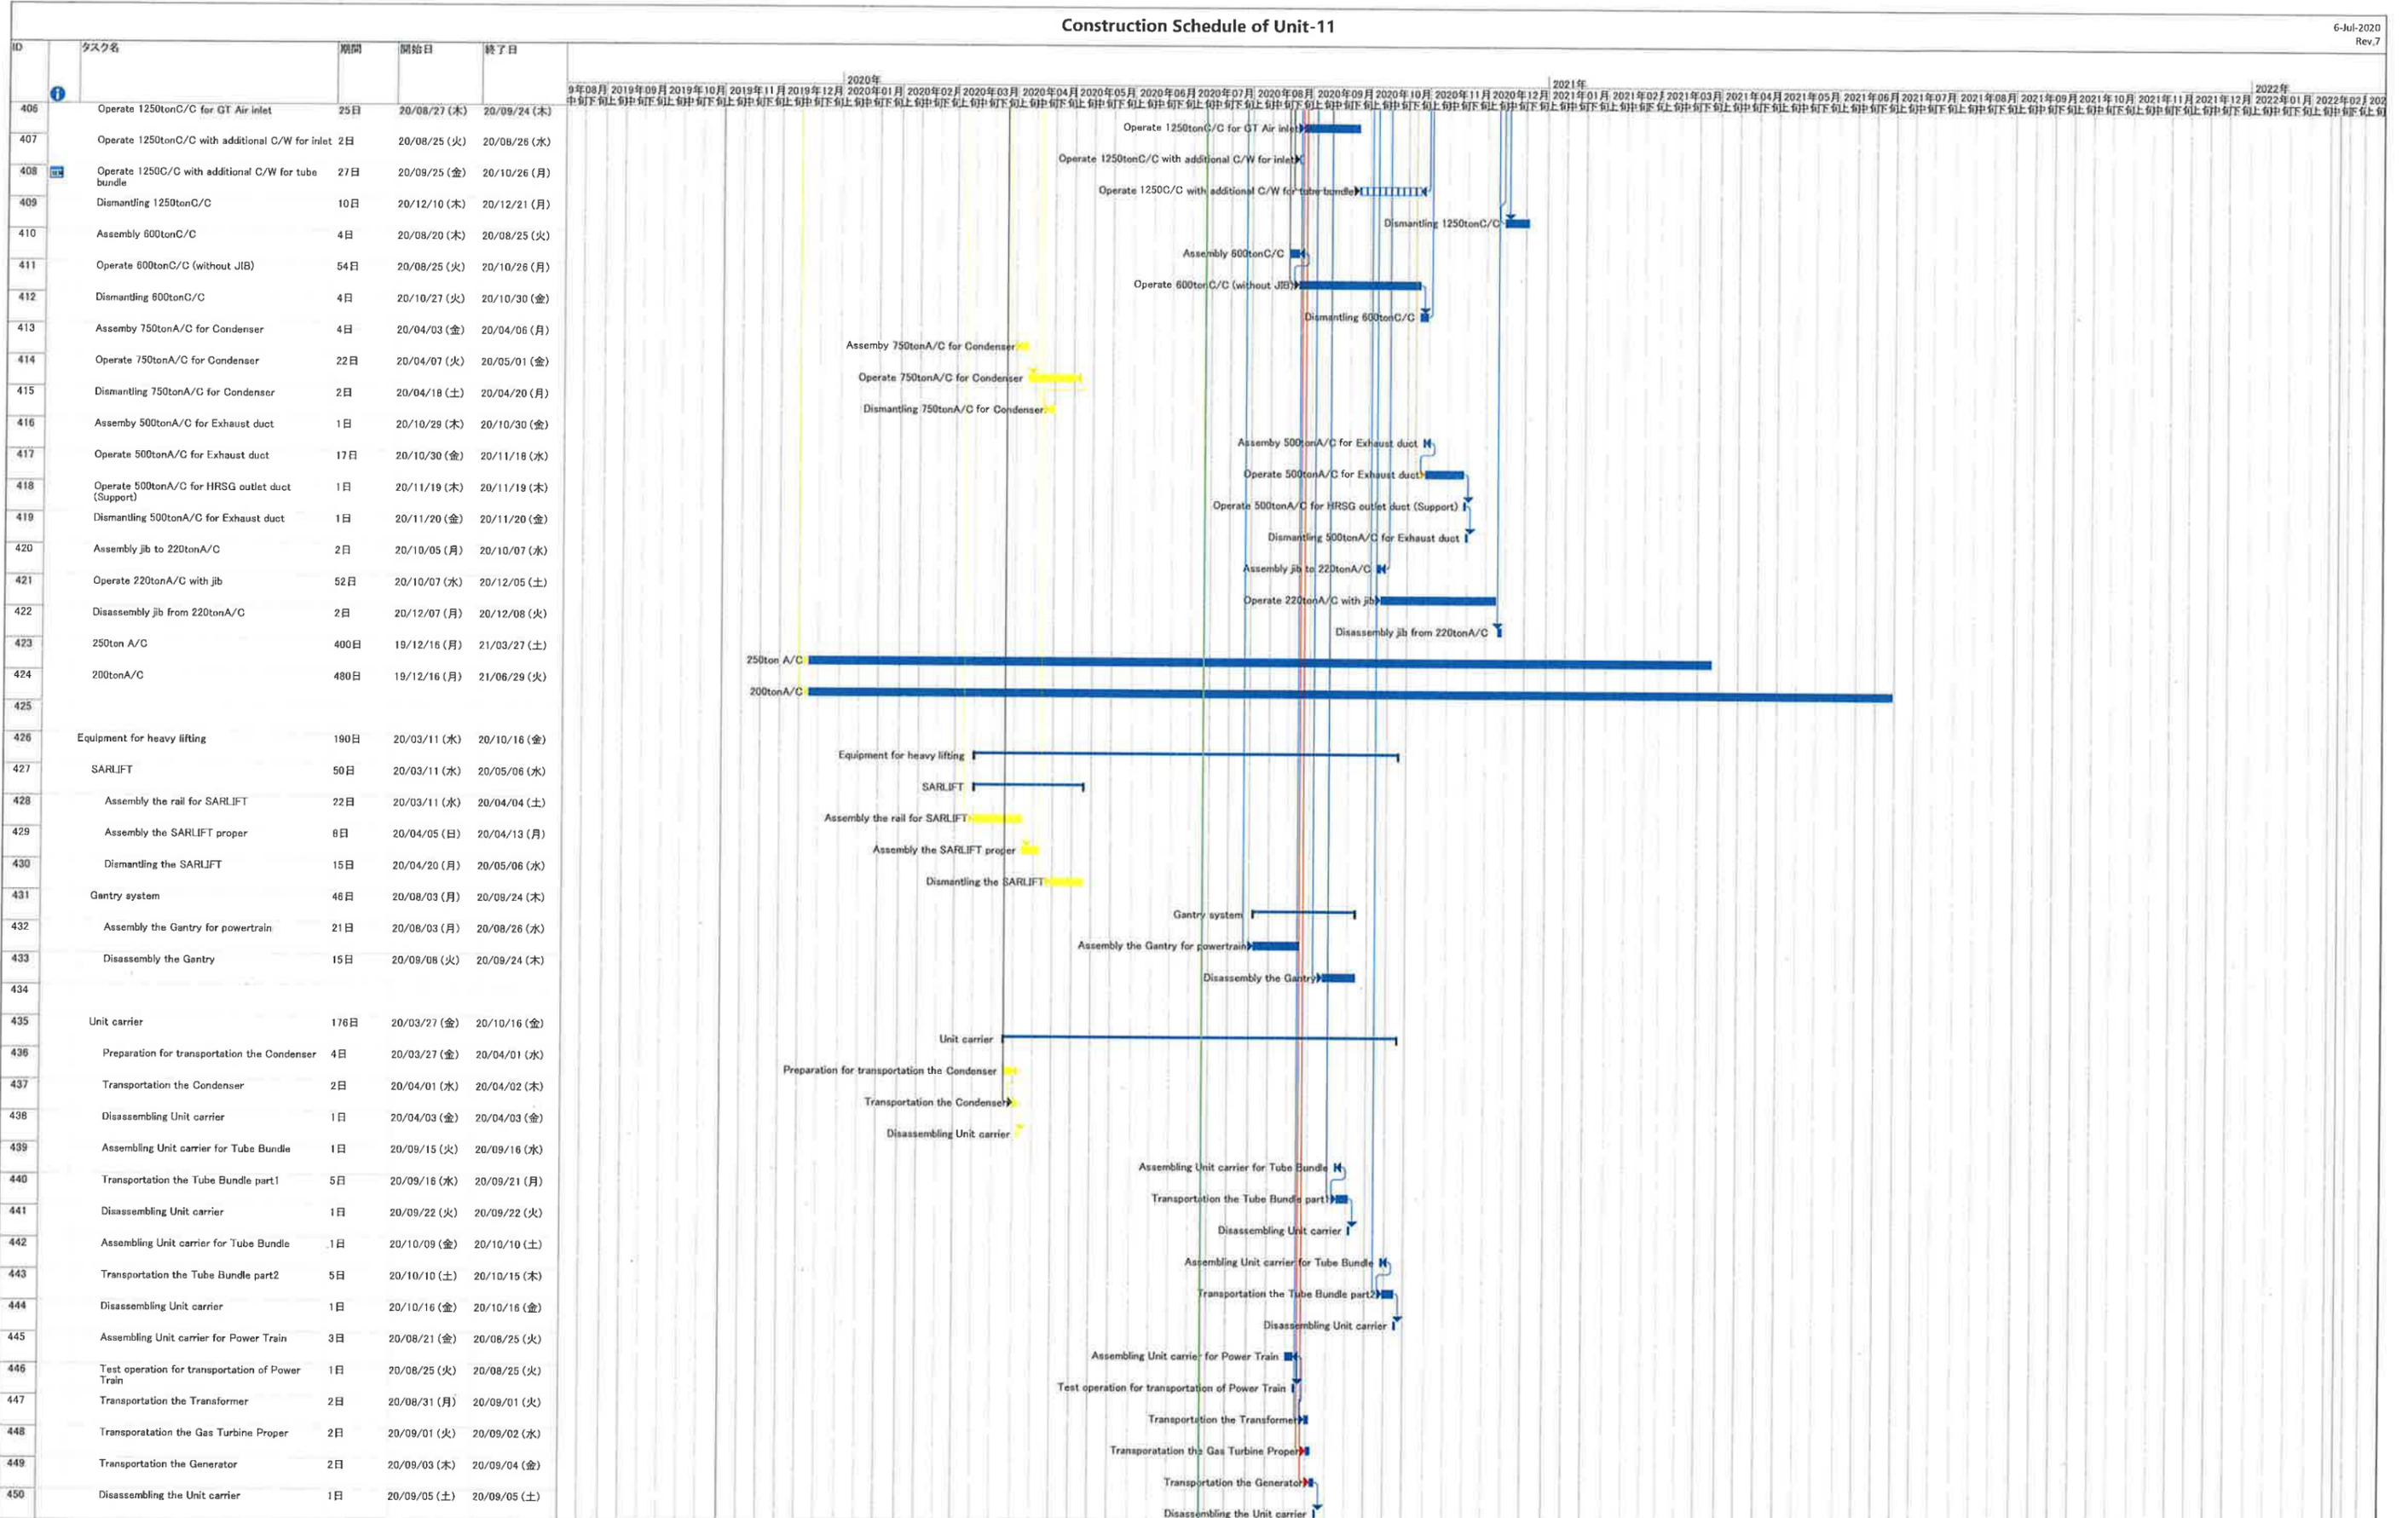

1. Change the starting date of installation below
 - ・ Installation HRSG was re-started from 23rd-Jun
 - ・ Installation Exhaust duct was re-started from 15st-May
2. To consider that structure of Takasago portion is delayed

4. To consider the delay of H/O date from PDC
5. Add the schedule of the electric work and the replacement the gantry crane for CWP

Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12

Master Programme

ID	Task Name	Duration	Start	Finish	Sep	Oct	Nov
1	KEY DATES & MILESTONES	1123 days	Fri 4/12/20	Sun 31/12/23			
2	Contract Period	1123 days	Fri 4/12/20	Sun 31/12/23	[Gantt bar]		
3	Deferred Work Completion Key Dates	784 days	Mon 8/11/21	Sun 31/12/23	[Gantt bar]		
4	Substantial Completion of the Whole Contract Works (1123 Days)	0 days	Sun 31/12/23	Sun 31/12/23	[Milestone]		
5	SITE POSSESSION DATES	513 days	Fri 4/12/20	Sun 1/5/22			
6	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Fri 4/12/20	Fri 4/12/20	[Milestone]		
7	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Fri 1/1/21	Fri 1/1/21	[Milestone]		
8	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Sat 1/5/21	Sat 1/5/21	[Milestone]		
9	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Fri 1/10/21	Fri 1/10/21	[Milestone]		
10	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Fri 1/4/22	Fri 1/4/22	[Milestone]		
11	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Sun 1/5/22	Sun 1/5/22	[Milestone]		
12	COMPLETION DATES as per PS1.4.2 Time for Completion	537 days	Thu 30/9/21	Tue 21/3/23			
13	Section A1 (i) - Area south of L12 MSB and L12 HRSG from GL12-F eastwards leading to Chimney Road at Area F1 & F2	0 days	Thu 30/9/21	Thu 30/9/21	[Milestone]		
14	Section A1 (ii) - Supporting structures for overhead cranes of L12 MSB including the associated roof structure except the roof deferred works	0 days	Mon 1/11/21	Mon 1/11/21	[Milestone]		
15	Section A2 (i) External Works including CW Inlet Culvert at Area F8A	0 days	Mon 10/1/22	Mon 10/1/22	[Milestone]		
16	Section A2 (ii) External Works including CW Inlet Culvert at Area F8B	0 days	Thu 31/3/22	Thu 31/3/22	[Milestone]		
17	Section A2 (iii) External Works including CW Inlet Culvert at Area F8C	0 days	Fri 11/3/22	Fri 11/3/22	[Milestone]		
18	Section B1 - Area south of L12 MSB from GL12-F westwards leading to Station Road at Area F3	0 days	Wed 15/12/21	Wed 15/12/21	[Milestone]		
19	Section B2 (i) - Southern Part of L12 HRSG areas and its surrounding refer to Area F6B as shown in drawing no 553/03/2040 including the foundations for Gas Exhaust Duct	0 days	Thu 30/9/21	Thu 30/9/21	[Milestone]		
20	Section B2 (ii) - Remaining northern part of L12 HRSG area and its surrounding at Area F6A and F6C	0 days	Mon 15/11/21	Mon 15/11/21	[Milestone]		
21	Section B2 - (iii) L12 Turbo Block foundation including the L12 MSB ground floor together with the equipment foundations between GL 12-F to 12-H and 12-1 to 12-6 for the installation of power generator, air inlet duct and lube oil reservoir	0 days	Mon 28/2/22	Mon 28/2/22	[Milestone]		
22	Section B2 - (iv) G/F of L12 MSB including the Condenser Pit, Circulating Water Pipe Pit and equipment foundations between GL 12-B to 12-C and 12-1 to 12-6 for the installation of condenser	0 days	Wed 15/12/21	Wed 15/12/21	[Milestone]		
23	Section C - (i) Roads and external grounds surrounding L12 MSB and L12 HRSG in addition to the southern & eastern areas mentioned above in Area F5	0 days	Sat 15/1/22	Sat 15/1/22	[Milestone]		
24	Section C - (ii) Whole of L12 MSB including the pipe and cable rack along south façade of L12 MSB with all underground utilities at Area F4 including C.W. Inlet and Outlet Culvert except the deferred works	0 days	Thu 31/3/22	Thu 31/3/22	[Milestone]		
25	Section C - (iii) Link Bridge between L11 and L12 MSB including their associated A&A at L11 MSB	0 days	Sun 10/4/22	Sun 10/4/22	[Milestone]		
26	Section D - (i) Microwave Antenna Room and Chimney Windshiled for the installation of microwave equipment and antenna	0 days	Fri 10/6/22	Fri 10/6/22	[Milestone]		
27	Section D (ii) - No. 5 Chimney with L12 Steel Flue liner	0 days	Tue 21/3/23	Tue 21/3/23	[Milestone]		
28	Section E (i) Tx Room of Administration and Control Building	0 days	Sun 31/10/21	Sun 31/10/21	[Milestone]		
29	Section E (ii) - G/F, 1/F, 2/F & Hoisting Well of Admin. & Control Building	0 days	Mon 28/2/22	Mon 28/2/22	[Milestone]		
30	Section E (iii) - Whole of Admin. And Control Building	0 days	Tue 31/5/22	Tue 31/5/22	[Milestone]		
31	Section F (i) - Gas Receiving Station and L12 Gas Receiving Station Equipment Room (GRS) Area Extension at Area F14	0 days	Wed 30/11/22	Wed 30/11/22	[Milestone]		
32	Section F (ii) - Pipe and Cable rack and external work at Area F9A and F9B	0 days	Tue 31/5/22	Tue 31/5/22	[Milestone]		
33	Section F (iii) - No. 5 CW Equipment Room, pipe and cable rack, external works at Area F10	0 days	Wed 31/8/22	Wed 31/8/22	[Milestone]		
34	Section G (i) - External Work surrounding Area F11	0 days	Wed 26/10/22	Wed 26/10/22	[Milestone]		
35	Section G (ii) - External Works at Area F12 & F13	0 days	Fri 30/9/22	Fri 30/9/22	[Milestone]		
36	Section G (iii) - FS Modification works along South Seafront Road at Area F15	0 days	Fri 30/9/22	Fri 30/9/22	[Milestone]		
37	Section G (iv) - 275kV cable trenches and External Works at Area F16	0 days	Fri 30/9/22	Fri 30/9/22	[Milestone]		
38	Section G (v) - Shunt Reactor Compound and External Works at Area F17	0 days	Fri 30/9/22	Fri 30/9/22	[Milestone]		
39	Section G (vi) - 275kV cable trenches and External Works at Area F18	0 days	Wed 1/6/22	Wed 1/6/22	[Milestone]		
40	Section G (vii) - Flood Wall at No. 4 CW Intake Area along HUA at Area F20A	0 days	Sun 8/5/22	Sun 8/5/22	[Milestone]		
41	Section G (viii) - Flood wall at No. 5 CW Intake Area along HUA at Area F20B	0 days	Fri 30/9/22	Fri 30/9/22	[Milestone]		
42	Section G (ix) - Bund wall modification works at South Seafront Road at Area F21	0 days	Fri 15/10/21	Fri 15/10/21	[Milestone]		
43	Section G (x) - DAX Cable Diversion Works (from Part I to Part IV)	0 days	Sat 31/12/22	Sat 31/12/22	[Milestone]		
44	Section H - All remaining works shall be completed for reporting completion to BD and ready for OP inspection	0 days	Tue 28/2/23	Tue 28/2/23	[Milestone]		
45	GENERAL & PRELIMINARY	228 days	Fri 4/12/20	Mon 19/7/21			
46	First Mobilization	18 days	Fri 4/12/20	Mon 21/12/20	[Gantt bar]		
47	Set up Temporary Site Office and Welfare Facilities	90 days	Tue 22/12/20	Sun 21/3/21	[Gantt bar]		
48	Permit Applications & Statuary Submissions	120 days	Mon 22/3/21	Mon 19/7/21	[Gantt bar]		
49	Existing Utilities scanning & Excavation Permit	45 days	Tue 22/12/20	Thu 4/2/21	[Gantt bar]		
50	Tower Crane erections	60 days	Sun 27/12/20	Wed 24/2/21	[Gantt bar]		
51	TECHNICAL SUBMISSION AND APPROVAL	314 days	Thu 10/12/20	Wed 20/10/21			
52	BD Approval & Consent (If required)	0 days	Thu 10/12/20	Thu 10/12/20	[Milestone]		
53	Submission and Approval of Master Programme	14 days	Fri 11/12/20	Thu 24/12/20	[Gantt bar]		
54	Work Execution Overall Plan submission & approval	14 days	Fri 11/12/20	Thu 24/12/20	[Gantt bar]		
55	Material Submissions and approval	300 days	Fri 25/12/20	Wed 20/10/21	[Gantt bar]		
56	Method Statement submission and approval	300 days	Fri 25/12/20	Wed 20/10/21	[Gantt bar]		
57	BIM Model, CSD & CBWD Submission & approval	120 days	Fri 25/12/20	Fri 23/4/21	[Gantt bar]		
58	Structure Steelwork Connection Design Submission & BD approval	45 days	Tue 29/12/20	Thu 11/2/21	[Gantt bar]		
59	Structure Steelwork Shop Drawing & Approval	30 days	Fri 12/2/21	Sat 13/3/21	[Gantt bar]		
60	Metal Cladding, louvre & windows submission & BD approval	45 days	Tue 29/12/20	Thu 11/2/21	[Gantt bar]		
61	Metal Cladding, louvre & windows shop drawing submission	45 days	Fri 12/2/21	Sun 28/3/21	[Gantt bar]		
62	Order, Off Site Fabrication and Delivery (S. Steel & Cladding & Louvres)	120 days	Mon 29/3/21	Mon 26/7/21	[Gantt bar]		
63	ELS Submission and BD approval	90 days	Fri 11/12/20	Wed 10/3/21	[Gantt bar]		
64	No. 5 Chimney windshield temporary work submission, approval & fabrication	60 days	Fri 11/12/20	Mon 8/2/21	[Gantt bar]		
65	Steel Flue Assessment Report and Design Drawings submission & approval	60 days	Tue 9/2/21	Fri 9/4/21	[Gantt bar]		
66	Folding Shutters Shop Drawing Submission & Approval	30 days	Thu 11/2/21	Fri 12/3/21	[Gantt bar]		
67	Fabrication & Delivery of Folding Shutters	180 days	Sat 13/3/21	Wed 8/9/21	[Gantt bar]		
68	Sewage Pump System Design submission & approval	45 days	Tue 23/2/21	Thu 8/4/21	[Gantt bar]		
69	Fabrication & Delivery of Sewage Pump	180 days	Fri 9/4/21	Tue 5/10/21	[Gantt bar]		
70	Other material submission & approval & delivery	180 days	Sat 24/4/21	Wed 20/10/21	[Gantt bar]		
71	Other material submission & approval & delivery	180 days	Sat 24/4/21	Wed 20/10/21	[Gantt bar]		
72	CONSTRUCTION	1123 days	Fri 4/12/20	Sun 31/12/23			
73	Coordination with the Employer's Specialist Contractors	562 days	Fri 15/1/21	Sat 30/7/22			
74	Installation of Puddle Pipes at C.W. outlet Culvert	7 days	Mon 22/3/21	Sun 28/3/21	[Gantt bar]		
75	Installation of Puddle Pipes at C.W. Inlet Culvert	7 days	Thu 27/5/21	Wed 2/6/21	[Gantt bar]		
76	Template setting at L12 Turbo Block Foundation	45 days	Tue 16/11/21	Thu 30/12/21	[Gantt bar]		
77	Template setting of holding down bolts at HRSG column base	45 days	Fri 15/1/21	Sun 28/2/21	[Gantt bar]		
78	I-beam / channel base installation on top of transformer foundations at Transformer Area	45 days	Tue 1/6/21	Thu 15/7/21	[Gantt bar]		
79	Overhead crane erection at turbine hall using access through a temporary opening at L12 MSB roof between GL12-G to 12-H and 12-2 to 12-6	38 days	Mon 1/11/21	Wed 8/12/21	[Gantt bar]		
80	Condenser assembly and erection using access through a temporary façade opening at L12 MSB below 1/F along GL 12-6 from GL12-B to 12-C including a clear space below 1/F between GL 12-B to 12-C	122 days	Thu 16/12/21	Sat 16/4/22	[Gantt bar]		
81	Installation of power train equipment including air inlet duct using access through a temporary façade opening at L12 MSB below 1/F along GL 12-6 from GL12-F to 12-H including a clear space below 1/F of the above area	121 days	Fri 1/4/22	Sat 30/7/22	[Gantt bar]		
82	Installation of embedded materials such as holding down bolts for equipment foundations - Commencement	0 days	Thu 15/4/21	Thu 15/4/21	[Milestone]		
83	Section A1 (i) - Area south of L12 MSB and L12 HRSG from GL12-F eastwards leading to Chimney Road at Area F1 & F2	301 days	Fri 4/12/20	Thu 30/9/21			
84	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21	[Gantt bar]		
85	Subletting / Fabrication / Delivery (both for Area F1 and Area F2)	60 days	Sun 17/1/21	Wed 17/3/21	[Gantt bar]		
86	Excavation for CW Inlet Culvert (Type D Construction Area)	14 days	Tue 1/6/21	Mon 14/6/21	[Gantt bar]		
87	Installation CW Inlet Culvert pipe	70 days	Tue 15/6/21	Mon 23/8/21	[Gantt bar]		
88	Backfill	7 days	Tue 24/8/21	Mon 30/8/21	[Gantt bar]		
89	Construction UG Utilities 2m deep below further surface	21 days	Tue 31/8/21	Mon 27/9/21	[Gantt bar]		
90	Temporary Paving and handover for plant erection	3 days	Tue 28/9/21	Thu 30/9/21	[Gantt bar]		
91	Section A1 (ii) - Supporting structures for overhead cranes of L12 MSB including the associated roof structure except the roof deferred works	333 days	Fri 4/12/20	Mon 1/11/21			
92	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21	[Gantt bar]		
93	Subletting / Fabrication / Delivery	210 days	Tue 23/2/21	Mon 20/9/21	[Gantt bar]		
94	Complete structural steel erection	0 days	Tue 19/10/21	Tue 19/10/21	[Milestone]		
95	Install Crane Girders	11 days	Tue 12/10/21	Fri 29/10/21	[Gantt bar]		
96	Construction of roof slab (except defer work)	14 days	Tue 12/10/21	Mon 1/11/21	[Gantt bar]		
97	Touch up and handover for install overhead cranes	3 days	Sat 30/10/21	Mon 1/11/21	[Gantt bar]		
98	Section A2 (i) External Works including CW Inlet Culvert at Area F8A	403 days	Fri 4/12/20	Mon 10/1/22			
99	BD consent for Sheetpile installation	30 days	Fri 4/12/20	Sat 2/1/21	[Gantt bar]		
100	Subletting / Fabrication / Delivery (both for Area F8A-F8B)	30 days	Fri 18/12/20	Sat 16/1/21	[Gantt bar]		
101	Area Possession & Clearance	14 days	Sat 2/1/21	Fri 15/1/21	[Gantt bar]		
102	Install Sheet pile	55 days	Sat 16/1/21	Thu 11/3/21	[Gantt bar]		
103	Installation of Additional sheet Pile at South of area F8A	7 days	Sat 17/4/21	Fri 23/4/21	[Gantt bar]		
104	BD Consent for ELS	28 days	Sat 24/4/21	Fri 21/5/21	[Gantt bar]		
105	ELS and install CW Inlet Pipe (NW to N direction) (Assume flexible joint deliver in Sep 2021)	100 days	Fri 16/7/21	Sat 23/10/21	[Gantt bar]		
106	Construction of Thrust Box & Manholes,etc	15 days	Thu 16/9/21	Thu 30/9/21	[Gantt bar]		
107	Backfill, UG Utilities and Road Paving	79 days	Sun 24/10/21	Mon 10/1/22	[Gantt bar]		
108	Section A2 (ii) External Works including CW Inlet Culvert at Area F8B	483 days	Fri 4/12/20	Thu 31/3/22			
109	Area Possession & Clearance	30 days	Mon 1/3/21	Tue 30/3/21	[Gantt bar]		
110	BD consent for Sheetpile installation	30 days	Fri 4/12/20	Sat 2/1/21	[Gantt bar]		
111	Install Sheet pile	90 days	Fri 2/4/21	Wed 30/6/21	[Gantt bar]		
112	BD Consent for ELS	28 days	Thu 1/7/21	Wed 28/7/21	[Gantt bar]		
113	ELS and install CW Inlet Pipe	100 days	Thu 29/7/21	Fri 5/11/21	[Gantt bar]		
114	Construction of Thrust Box & Manholes,etc	15 days	Wed 1/9/21	Wed 15/9/21	[Gantt bar]		
115	Backfill, UG Utilities and Road Paving	146 days	Sat 6/11/21	Thu 31/3/22	[Gantt bar]		
116	Section A2 (iii) External Works including CW Inlet Culvert at Area F8C	365 days	Fri 12/3/21	Fri 11/3/22			
117	Area Possession & Clearance	30 days	Fri 12/3/21	Sat 10/4/21	[Gantt bar]		
118	Subletting / Fabrication / Delivery (for Area F8C)	60 days	Fri 12/3/21	Mon 10/5/21	[Gantt bar]		
119	BD consent for Sheetpile installation	30 days	Tue 13/4/21	Wed 12/5/21	[Gantt bar]		
120	Install Sheet pile	62 days	Thu 13/5/21	Tue 13/7/21	[Gantt bar]		
121	BD Consent for ELS	35 days	Wed 14/7/21	Tue 17/8/21	[Gantt bar]		
122	ELS and install CW Inlet Pipe (including soil nail installation under 19/83014)	76 days	Wed 18/8/21	Thu 20/1/22	[Gantt bar]		
123	Construction of Thrust Box & Manholes,etc	30 days	Fri 21/1/22	Sat 19/2/22	[Gantt bar]		
124	Backfill, UG Utilities and Road Paving	20 days	Sun 20/2/22	Fri 11/3/22	[Gantt bar]		
125	Section B1 - Area south of L12 MSB from GL12-F westwards leading to Station Road at Area F3	377 days	Fri 4/12/20	Wed 15/12/21			
126	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21	[Gantt bar]		
127	Subletting / Fabrication / Delivery	120 days	Fri 25/12/20	Fri 23/4/21	[Gantt bar]		
128	Complete CW Pipe Installation & Thrust box	45 days	Tue 25/5/21	Thu 8/7/21	[Gantt bar]		
129	Backfill	30 days	Fri 9/7/21	Sat 7/8/21	[Gantt bar]		
130	Construction of Storm Drain & Manholes	67 days	Mon 20/9/21	Thu 25/11/21	[Gantt bar]		
131	Temp Paving and handover for Condenser Move in	20 days	Fri 26/11/21	Wed 15/12/21	[Gantt bar]		
132	Section B2 - (i) Southern part of L12 HRSG area and its surrounding at Area F6B including the foundations for Gas Exhaust Duct	273 days	Fri 1/1/21	Thu 30/9/21			
133	Area Possession & Clearance	30 days	Fri 1/1/21	Sat 30/1/21	[Gantt bar]		
134	Subletting / Fabrication / Delivery (for F6B Civil and E&M)	120 days	Sat 2/1/21	Sat 1/5/2			

Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12

Master Programme

ID	Task Name	Duration	Start	Finish	Notes
136	Excavation & Construct Pile Caps & Tie Beams & Piers	86 days	Mon 8/3/21	Thu 19/8/21	Construct Pile Caps & Tie Beams & Piers
137	Installation of Pipe Pile for HRSG foundation (VO)	48 days	Thu 25/3/21	Tue 11/5/21	
138	Construction HRSG & Gas Duct foundations	112 days	Fri 7/5/21	Fri 3/9/21	Construction HRSG & Gas Duct foundations
139	Construction of HRSG Equipment Room incl. ABWF & BS (except T&C)	64 days	Tue 4/5/21	Thu 30/9/21	Construction of HRSG Equipment Room incl. ABWF & BS (except T&C)
140	Construction underground utilities within HRSG	55 days	Mon 19/7/21	Sat 11/9/21	Construction underground utilities within HRSG
141	Backfill & Construction on-grade slabs & RC plinths on top	14 days	Fri 30/7/21	Mon 27/9/21	Backfill & Construction on-grade slabs & RC plinths on top
142	Backfill and Temporary paving	21 days	Fri 10/9/21	Thu 30/9/21	Backfill and Temporary paving
143	Section B2 (ii) - Remaining northern part of L12 HRSG area and its surrounding at Area F6A and F6C	319 days	Fri 1/1/21	Mon 15/11/21	
144	Area Possession and Clearance at Area F6A	30 days	Fri 1/1/21	Sat 30/1/21	
145	Subletting / Fabrication / Delivery (for Area F6A and F6C civil)	90 days	Sat 2/1/21	Thu 1/4/21	
146	Construction of Underground pits (HRSG Blowdown sump pit)	110 days	Sat 2/1/21	Wed 21/4/21	
147	Excavation & Construct Pile Caps & Tie Beams & Piers	139 days	Mon 1/2/21	Sat 10/7/21	
148	Construction underground utilities within HRSG	55 days	Mon 19/7/21	Sat 11/9/21	Construction underground utilities within HRSG
149	Construction of Underground pits (GT Oil & Chemical drain pits)	15 days	Thu 5/8/21	Thu 19/8/21	Underground pits (GT Oil & Chemical drain pits)
150	Backfill & Construction on-grade slabs & RC plinths on top	45 days	Sun 12/9/21	Tue 26/10/21	Backfill & Construction on-grade slabs & RC plinths on top
151	Construct RC Walls	90 days	Thu 22/4/21	Tue 20/7/21	
152	Construction of Underground utilities at F6C	21 days	Tue 19/10/21	Mon 8/11/21	Construction of Underground utilities at F6C
153	Backfill and Temporary paving	7 days	Tue 9/11/21	Mon 15/11/21	Backfill and Temporary paving
154	Section B2 - (iii) L12 Turbo Block foundation including the L12 MSB ground floor together with the equipment foundations between GL 12-F to 12-H and 12-1 to 12-6 for the installation of power generator, air inlet duct and lube oil reservoir	452 days	Fri 4/12/20	Mon 28/2/22	
155	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21	
156	Subletting / Fabrication / Delivery (Civil+ABWF+BS for MSBL12)	150 days	Fri 25/12/20	Sun 23/5/21	
157	Complete excavation at Type A&C Construction Area	0 days	Sun 21/3/21	Sun 21/3/21	
158	Excavation & Pile Caps & Tie Beams + Slabs (Turbo Block North)	75 days	Sun 31/1/21	Thu 15/4/21	
159	Backfill and construction turbine block & equipment foundation	85 days	Tue 1/6/21	Tue 24/8/21	Construction turbine block & equipment foundation
160	Excavation & Pile Caps & Tie Beams + Slabs (Turbo Block South)	45 days	Sat 17/4/21	Mon 31/5/21	
161	Construction of internal drainage & on-grade slab	90 days	Wed 1/9/21	Mon 29/11/21	
162	Construction turbine block columns and upper portion for plant embed installation	83 days	Wed 25/8/21	Mon 15/11/21	Construction turbine block columns and upper portion for plant embed installation
163	Concrete Turbine upper part foundation	15 days	Fri 31/12/21	Fri 14/1/22	
164	Construction of Lube Oil Room	14 days	Tue 30/11/21	Fri 28/1/22	
165	Concrete RC walls	115 days	Tue 7/9/21	Thu 30/12/21	
166	ABFW Works	60 days	Thu 4/11/21	Sun 2/1/22	
167	Building Services Works	45 days	Sat 15/1/22	Mon 28/2/22	
168	Remove temporary falsework and scaffolding for installation of power generator	13 days	Mon 7/2/22	Sat 19/2/22	
169	Section B2 - (iv) G/F of L12 MSB including the Condenser Pit, Circulating Water Pipe Pit and equipment foundations between GL 12-B to 12-C and 12-1 to 12-6 for the installation of condenser	377 days	Fri 4/12/20	Wed 15/12/21	
170	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21	
171	Subletting / Fabrication / Delivery (for MSB L12 civil)	150 days	Fri 25/12/20	Sun 23/5/21	
172	Excavation to foundation level at ELS SP Type A & C	80 days	Fri 1/1/21	Sun 21/3/21	
173	Install CW Outlet pipe	85 days	Mon 22/3/21	Mon 14/6/21	
174	Construction of CW Outlet Box + lowest tie beam & caps	40 days	Mon 22/3/21	Fri 30/4/21	
175	Construction of pile caps & tie beams & sump pits up to +2.7mPD	26 days	Sat 1/5/21	Wed 26/5/21	
176	Backfill & Construction of CW Inlet Box + tie beams	71 days	Thu 27/5/21	Thu 5/8/21	
177	Construction of pile caps & tie beams at SunShadeCover Area	45 days	Tue 15/6/21	Thu 29/7/21	
178	Backfill and Construction ground beams & trenches	28 days	Thu 27/5/21	Mon 5/7/21	
179	Construction of indoor underground drainage	14 days	Fri 13/8/21	Thu 26/8/21	Construction of indoor underground drainage
180	Backfill & construction on-grade slabs	60 days	Sun 1/8/21	Wed 29/9/21	Backfill & construction on-grade slabs
181	Construction Column casting and RC walls & equipment foundations	50 days	Thu 30/9/21	Thu 18/11/21	Construction Column casting and RC walls & equipment foundations
182	ABFW Works	15 days	Fri 19/11/21	Fri 3/12/21	
183	Building Services Works	20 days	Fri 26/11/21	Wed 15/12/21	
184	Mis. Works and Ready for condenser move in	25 days	Wed 17/11/21	Wed 15/12/21	
185	Section C - (i) Roads and external grounds surrounding L12 MSB and L12 HRSG in addition to the southern & eastern areas mentioned above in Area F5	408 days	Fri 4/12/20	Sat 15/1/22	
186	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21	
187	Subletting / Fabrication / Delivery	210 days	Fri 25/12/20	Thu 22/7/21	
188	Complete substructure & Steel Erection works for MSB	0 days	Tue 17/8/21	Tue 17/8/21	Steel Erection works for MSB
189	Construction all utilities deeper than 2m from future road level	30 days	Wed 18/8/21	Thu 16/9/21	Construction all utilities deeper than 2m from future road level
190	Construction of cable trenches	30 days	Fri 17/9/21	Sat 16/10/21	Construction of cable trenches
191	Backfill and lay temporary paving	91 days	Sun 17/10/21	Sat 15/1/22	
192	Section C - (ii) Whole of L12 MSB including the pipe and cable rack along south façade of L12 MSB with all underground utilities at Area F4 including C.W. Inlet and Outlet Culvert except the deferred works	483 days	Fri 4/12/20	Thu 31/3/22	
193	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21	
194	Subletting / Fabrication / Delivery	120 days	Fri 25/12/20	Fri 23/4/21	
195	Construction of pile caps & tie beams at Transformer Area	180 days	Sun 31/1/21	Thu 29/7/21	
196	Backfill and on-grade slab at transformer Area	160 days	Sun 11/4/21	Thu 7/10/21	Backfill and on-grade slab at transformer Area
197	Construction of Fire Walls at Transformer Area	45 days	Fri 8/10/21	Sun 21/11/21	
198	Excavation & Construction Blow Down Sump pit (SP Type B)	140 days	Wed 14/4/21	Tue 31/8/21	Excavation & Construction Blow Down Sump pit (SP Type B)
199	Preparation for S.Steelwork Erection	7 days	Sat 5/6/21	Fri 11/6/21	
200	Structural Delivery & Erection (Turbine Hall North fr G.L. 1-3/H->B)	67 days	Sat 12/6/21	Tue 17/8/21	Structural Delivery & Erection (Turbine Hall North fr G.L. 1-3/H->B)
201	Structural Delivery & Erection (Equipment Floors)	33 days	Wed 18/8/21	Sun 19/9/21	Structural Delivery & Erection (Equipment Floors)
202	Structural Delivery & Erection (Turbine Hall South + East Elevation)	47 days	Mon 20/9/21	Mon 15/11/21	Structural Delivery & Erection (Turbine Hall South + East Elevation)
203	Joint Tightening and touch up coating	99 days	Sat 3/7/21	Wed 24/11/21	Joint Tightening and touch up coating
204	External Scaffolding Erection	97 days	Thu 15/7/21	Mon 22/11/21	External Scaffolding Erection
205	Construction 1/F RC Slab	14 days	Mon 20/9/21	Sun 3/10/21	Construction 1/F RC Slab
206	Construction 2/F RC Slab	7 days	Mon 27/9/21	Sun 10/10/21	Construction 2/F RC Slab
207	Construction 3/F RC Slab	18 days	Thu 30/9/21	Sun 17/10/21	Construction 3/F RC Slab
208	Construction 4/F RC Slab	7 days	Thu 7/10/21	Sun 24/10/21	Construction 4/F RC Slab
209	Construction 5/F RC Slab	44 days	Mon 25/10/21	Tue 7/12/21	Construction 5/F RC Slab
210	Construction 6/F RC Slab	14 days	Wed 1/12/21	Tue 14/12/21	Construction 6/F RC Slab
211	Construction Upper Roof RC Slab	10 days	Sun 12/12/21	Fri 24/12/21	Construction Upper Roof RC Slab
212	Construction Main Roof RC Slab	39 days	Tue 12/10/21	Fri 19/11/21	Construction Main Roof RC Slab
213	Construction Defer Roof RC Slab (G.L. G-H)	14 days	Wed 1/12/21	Tue 14/12/21	Construction Defer Roof RC Slab (G.L. G-H)
214	Construction of Staircase ST-01 & lift shaft & machine room	130 days	Fri 27/8/21	Mon 3/1/22	Construction of Staircase ST-01 & lift shaft & machine room
215	Construction M/F RC Slab	14 days	Wed 1/9/21	Tue 14/9/21	Construction M/F RC Slab
216	Lift Installation	60 days	Tue 4/1/22	Fri 4/3/22	
217	Construction of Staircase ST-02 except defer work	68 days	Mon 11/10/21	Fri 24/12/21	
218	Construction of RC plinth, kerbs & parapet Walls	40 days	Sat 20/11/21	Wed 29/12/21	
219	Erection of Skylight & Roof Features	50 days	Fri 26/11/21	Fri 14/1/22	
220	Waterproofing & Flooring at Roof	34 days	Thu 30/12/21	Thu 17/2/22	
221	ABFW Works	100 days	Fri 8/10/21	Sat 15/1/22	
222	Building Services Works	105 days	Tue 16/11/21	Mon 28/2/22	
223	Metal Cladding, Windows and Louvres incl. roof feature	185 days	Mon 23/8/21	Wed 23/2/22	
224	Removal of external scaffolding	90 days	Wed 1/12/21	Mon 28/2/22	
225	Installation of Catwalk at south elevation	26 days	Mon 31/1/22	Tue 1/3/22	
226	Cladding, ABWF & BS Works	30 days	Wed 2/3/22	Thu 3/1/22	
227	Removal of temporary works & clearance for plant erection contractor	30 days	Sun 30/1/22	Mon 28/2/22	
228	Section C - (iii) Link Bridge between L11 and L12 MSB including their associated A&A at L11 MSB	493 days	Fri 4/12/20	Sun 10/4/22	
229	BD Consent	0 days	Fri 4/12/20	Fri 4/12/20	
230	Subletting / Fabrication / Delivery (For BS and ABWF)	250 days	Fri 25/12/20	Tue 31/8/21	Subletting / Fabrication / Delivery (For BS and ABWF)
231	Clearing Works and plant set-up	30 days	Fri 3/12/21	Sat 1/1/22	
232	Dismantle of north scaffold for link bridge erection	0 days	Tue 25/1/22	Tue 25/1/22	
233	A&A works at South of L11 MSB	30 days	Fri 3/12/21	Sat 1/1/22	
234	Erection of link bridge structural steel	30 days	Sun 2/1/22	Mon 31/1/22	
235	Casting of bridge deck	11 days	Tue 1/2/22	Fri 11/2/22	
236	Metal roofing installation	24 days	Sat 12/2/22	Mon 7/3/22	
237	ABWF work	30 days	Sun 20/2/22	Mon 21/3/22	
238	BS Works	20 days	Tue 22/3/22	Sun 10/4/22	
239	Ready for power cable laying work by others	0 days	Sun 10/4/22	Sun 10/4/22	
240	Section D - (ii) No. 5 Chimney with L12 Steel Flue Liner	810 days	Fri 1/1/21	Tue 21/3/23	
241	Area Possession & Clearance	45 days	Fri 1/1/21	Sun 14/2/21	
242	Subletting / Fabrication / Delivery (For Civil and BS for Microwave Antenna and Equipment)	120 days	Fri 8/1/21	Fri 7/5/21	
243	Excavation & Pile Cap & Backfill	90 days	Sat 2/1/21	Thu 1/4/21	
244	Tower Crane erection	30 days	Tue 11/5/21	Wed 9/6/21	
245	Construction of Wind Shiled + clearance for internal floors and flue+Ground slab	308 days	Fri 2/4/21	Mon 4/4/22	
246	Structural steel fabrication & Delivery for floors and staircase	201 days	Mon 3/1/22	Fri 22/7/22	
247	Erection of steel floors	79 days	Tue 19/4/22	Wed 6/7/22	
248	Construction of G/F room incl. Microwave Antenna Rm	45 days	Thu 7/7/22	Sat 20/8/22	
249	Construction of 1/F RC slab	8 days	Sat 13/8/22	Sat 20/8/22	
250	Construction of 2/F RC Slab	8 days	Fri 5/8/22	Fri 12/8/22	
251	Construction of 3/F RC slab	8 days	Thu 28/7/22	Thu 4/8/22	
252	Construction of 4/F RC slab	8 days	Thu 7/7/22	Thu 14/7/22	
253	Construction of Roof RC slab	61 days	Tue 21/6/22	Sat 20/8/22	
254	Removal of tower Crane	7 days	Sun 21/8/22	Sat 27/8/22	
255	Steel Flue fabrication and delivery	145 days	Sat 5/3/22	Wed 27/7/22	
256	Set up for steel flue installation	60 days	Tue 5/7/22	Fri 2/9/22	
257	Lift & install steel flue liner + cladding works	161 days	Thu 28/7/22	Wed 4/1/23	
258	Lift installation	100 days	Mon 12/12/22	Tue 21/3/23	
259	Installation Louvre & Doors	30 days	Thu 5/1/23	Fri 3/2/23	
260	Mis works, Demobilization and ready for gas duct connection	17 days	Thu 5/1/23	Sat 21/1/23	
261	Section D (i) - ABWF and BS Works at Microwave Antenna Room and Chimney Windshield for installation of microwave and antenna	102 days	Tue 1/3/22	Fri 10/6/22	
262	Completion of Microwave Antenna Room	0 days	Tue 1/3/22	Tue 1/3/22	
263	Remaining ABWF & BS Works	100 days	Thu 3/3/22	Fri 10/6/22	
264	Section E - (i) Administration and Control Building (Transformer Room)	332 days	Fri 4/12/20	Sun 31/10/21	
265	Area Possession & Clearance + BD consent	60 days	Fri 4/12/20	Mon 1/2/21	
266	Subletting / Fabrication / Delivery (For Civil+BS+ABWF)	100 days	Tue 2/2/21	Wed 12/5/21	
267	Excavation works	45 days	Fri 4/12/20	Sun 17/1/21	
268	Main Earth Grid Installation	45 days	Sun 3/1/21	Tue 16/2/21	
269	Pile cap and Tie Beam	45 days	Sun 3/1/21	Tue 16/2/21	
270	Tower Crane Erection and modification works	49 days	Wed 10/2/21	Tue 30/3/21	
271	Substructure + Bearing walls + On grade slabs	115 days	Wed 17/2/21	Fri 11/6/21	
272	Construction of RC up to 1/F incl. staircases	69 days	Sat 12/6/21	Thu 19/8/21	
273	ABWF at G/F	52 days	Fri 10/9/21	Sun 31/10/21	
274	Section E (ii) Handover G/F, 1/F, 2/F & Hoisting Well	452 days	Fri 4/12/20	Mon 28/2/22	
275	Clearing Works and plant set-up	21 days	Sun 31/10/21	Sat 20/11/21	
276	Subletting / Fabrication / Delivery (For NSC Lift)	180 days	Sun 3/1/21	Sat 31/7/21	
277	Construction of RC up to 2/F incl. staircases	25 days	Sat 14/8/21	Mon 13/9/21	
278	Construction of RC up to 3/F incl. staircases	20 days	Tue 2/9/21	Mon 21/9/21	
279	Temporary Hoist erection	14 days	Wed 22/9/21	Tue 5/10/21	
280	Construction of RC up to 4/F incl. staircases	20 days	Thu 16/9/21	Tue 5/10/21	



Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12

Master Programme

ID	Task Name	Duration	Start	Finish
281	Construction of RC up to R/F incl. staircases	25 days	Thu 30/9/21	Sun 24/10/21
282	Construction of RC up to lift machine room	21 days	Mon 25/10/21	Sun 14/11/21
283	Construction of RC up to UR/F	21 days	Mon 15/11/21	Sun 5/12/21
284	External Wall Finish, Cladding + Windows and Louvres + Features	138 days	Thu 30/9/21	Mon 14/2/22
285	ABWF at 1/F	95 days	Fri 8/10/21	Mon 10/1/22
286	ABWF at 2/F	96 days	Fri 15/10/21	Tue 18/1/22
287	Building Services Works at G/F, 1/F, 2/F & Hoisting Well	147 days	Tue 5/10/21	Mon 28/2/22
288	Section E (iii) Whole of Administration and Control Building	544 days	Fri 4/12/20	Tue 31/5/22
289	Subletting / Fabrication / Delivery (For BS-ABWF)	127 days	Sat 23/10/21	Sun 20/3/22
290	Construction of New UG Grey Water Tank	60 days	Mon 20/3/23	Thu 18/5/23
291	Submission of WW046 for commencement	60 days	Wed 19/1/22	Sat 19/3/22
292	ABWF at 3/F	120 days	Mon 25/10/21	Mon 21/2/22
293	ABWF at 4/F	90 days	Wed 24/11/21	Mon 21/2/22
294	ABWF at R/F	60 days	Wed 15/12/21	Sat 12/2/22
295	ABWF at UR/F + Lift Machine Room	45 days	Wed 5/1/22	Fri 18/2/22
296	Bridge Erection & Connection	28 days	Mon 7/2/22	Mon 28/3/22
297	Installation of Raised floors	60 days	Fri 7/1/22	Fri 29/4/22
298	Removal of external scaffolding	39 days	Mon 24/1/22	Wed 9/3/22
299	Waterproofing & screeding	60 days	Mon 6/12/21	Thu 3/2/22
300	Removal of Tower Crane	7 days	Thu 10/3/22	Wed 16/3/22
301	External utilities and road work	45 days	Tue 8/2/22	Thu 14/4/22
302	Building Services Works	160 days	Tue 7/12/21	Sun 15/5/22
303	False ceiling after BS works	54 days	Tue 29/3/22	Sat 21/5/22
304	Submission of WW046 for completion	30 days	Wed 9/3/22	Thu 7/4/22
305	Submission of FS inspection	14 days	Fri 13/5/22	Thu 26/5/22
306	Submission for OP Inspection	14 days	Wed 18/5/22	Tue 31/5/22
307	Section F (i) - Gas Receiving Station and L12 Gas Receiving Station Equipment Room (GRS) Area Extension at Area F14	548 days	Tue 1/6/21	Wed 30/11/22
308	Area Possession & Clearance + BD consent	90 days	Tue 1/6/21	Sun 29/8/21
309	Subletting / Fabrication / Delivery	30 days	Tue 22/6/21	Wed 21/7/21
310	Installation of pipe pile at north of GRS (VO)	134 days	Mon 5/7/21	Mon 15/11/21
311	Construction Equipment room extension	145 days	Sun 31/10/21	Thu 24/3/22
312	Modification of existing drainage	45 days	Fri 25/3/22	Sun 8/5/22
313	Excavation & earthing for Skid foundations	21 days	Mon 9/5/22	Sun 29/5/22
314	Construction of Skid foundation	45 days	Mon 30/5/22	Wed 13/7/22
315	Construct underground utilities and drainage	45 days	Thu 14/7/22	Sat 27/8/22
316	Backfill and road works	60 days	Sun 28/8/22	Wed 26/10/22
317	Relocate / install new fencing for completion	21 days	Thu 27/10/22	Wed 16/11/22
318	Mis. Work and ready for OP inspection	14 days	Thu 17/11/22	Wed 30/11/22
319	Section F (ii) - Pipe and Cable rack and external work at Area F9A and F9B	515 days	Sat 2/1/21	Tue 31/5/22
320	BD consent + Site Possession at Area F9A & F9B	90 days	Sat 2/1/21	Thu 1/4/21
321	Excavation & Plate load test	30 days	Mon 1/11/21	Tue 30/11/21
322	Construction new footing for pipe rack	30 days	Wed 1/12/21	Thu 30/12/21
323	Underground utilities and road works for completion	11 days	Thu 31/3/22	Tue 31/5/22
324	Structural Steel fabrication & Delivery	90 days	Sat 2/10/21	Thu 30/12/21
325	Erection of new pipe rack	70 days	Fri 31/12/21	Thu 10/3/22
326	Mis. Work and ready for OP inspection	21 days	Wed 11/5/22	Tue 31/5/22
327	Section F (iii) - No. 5 CW Equipment Room, pipe and cable rack, external works at Area F10	457 days	Tue 1/6/21	Wed 31/8/22
328	Area Possession & Clearance + BD consent	90 days	Tue 1/6/21	Sun 29/8/21
329	Subletting / Fabrication / Delivery For ABWF + BS	150 days	Wed 2/6/21	Fri 29/10/21
330	Installation of Sheet Pile (VO)	85 days	Tue 1/6/21	Tue 24/8/21
331	Consent for ELS Works	28 days	Wed 25/8/21	Tue 21/9/21
332	Excavation & Plate load test	30 days	Wed 22/9/21	Thu 21/10/21
333	Construction new footing for equipment room	68 days	Thu 23/12/21	Mon 28/2/22
334	Superstructure for equipment room	60 days	Tue 1/3/22	Fri 29/4/22
335	ABWF Works	45 days	Sat 30/4/22	Mon 13/6/22
336	BS Works	30 days	Wed 1/6/22	Thu 30/6/22
337	Construction RC Wall & plinths & drainage at Chlorinator area	45 days	Wed 30/3/22	Fri 13/5/22
338	External wall finish & remove scaffolding	30 days	Sat 14/5/22	Sun 12/6/22
339	Excavation & Plate load test for pipe rack extension (For F45-47 & F49)	30 days	Sat 16/10/21	Sun 14/11/21
340	Construction new footing for pipe rack (For F45-47 & F49)	45 days	Mon 15/11/21	Wed 29/12/21
341	Underground utilities and road works for completion	60 days	Thu 30/12/21	Sun 27/2/22
342	Structural Steel fabrication & Delivery	90 days	Sun 12/12/21	Fri 11/3/22
343	Backfilling and prepare for steel erection	12 days	Mon 28/2/22	Fri 11/3/22
344	Excavation & Plate Load test for pipe rack extension (For F48 & F56)	14 days	Wed 30/3/22	Tue 12/4/22
345	Construction of new footing for pipe rak (For F48 & F56)	14 days	Wed 13/4/22	Tue 26/4/22
346	Erection of new pipe rack (For F48 & F56)	65 days	Tue 3/5/22	Wed 6/7/22
347	Erection of new pipe rack (For F45-47 & F49)	70 days	Sat 12/3/22	Fri 20/5/22
348	Mis. Work and ready for OP inspection	56 days	Thu 7/7/22	Wed 31/8/22
349	Section G (i) - External Work surrounding Area F11	145 days	Sat 4/6/22	Wed 26/10/22
350	Area Possession & Clearance after handover from No. 5 Intake Contractor	30 days	Sat 4/6/22	Sun 3/7/22
351	Subletting / Fabrication / Delivery	30 days	Sat 4/6/22	Sun 3/7/22
352	Submission WW0046 for commencement	30 days	Sat 4/6/22	Sun 3/7/22
353	Construct Underground utilities and drainage	30 days	Mon 20/6/22	Tue 19/7/22
354	Install new FS Hydrant	20 days	Mon 20/6/22	Sat 9/7/22
355	Submission WW0046 for completion	30 days	Sat 30/7/22	Sun 28/8/22
356	Construction Road extension	58 days	Sat 30/7/22	Sun 25/9/22
357	Construction road paving and install fencing	30 days	Mon 26/9/22	Tue 25/10/22
358	Ready for OP inspection	14 days	Thu 13/10/22	Wed 26/10/22
359	Section G (ii) - External Works at Area F12 & F13	666 days	Fri 4/12/20	Fri 30/9/22
360	Area Possession & Clearance after handover from other	45 days	Fri 4/12/20	Sun 17/1/21
361	Subletting / Fabrication / Delivery	180 days	Thu 4/3/21	Mon 30/8/21
362	Excavation	21 days	Sat 23/10/21	Fri 12/11/21
363	Submission WW0046 for commencement	30 days	Sat 13/11/21	Sun 12/12/21
364	Construct Underground utilities and drainage	90 days	Mon 13/12/21	Sat 12/3/22
365	Install new FS Hydrant	30 days	Sun 13/3/22	Mon 11/4/22
366	Submission WW0046 for completion	30 days	Tue 12/4/22	Wed 11/5/22
367	Construction Road extension	127 days	Thu 12/5/22	Thu 15/9/22
368	Complete with Mis. Works for completion	15 days	Fri 16/9/22	Fri 30/9/22
369	Section G (iii) - FS Modification works along South Seafront Road at Area F15	183 days	Fri 1/4/22	Fri 30/9/22
370	Area Possession & Clearance after handover from other	45 days	Fri 1/4/22	Sun 15/5/22
371	Subletting / Fabrication / Delivery	21 days	Fri 1/4/22	Thu 21/4/22
372	Temporary Traffic Arrangement approval	14 days	Fri 1/4/22	Thu 14/4/22
373	Utilities scanning and expose existing FS	14 days	Fri 15/4/22	Thu 28/4/22
374	Determine new FS alignment	21 days	Fri 29/4/22	Thu 19/5/22
375	Submission to FSD	14 days	Fri 20/5/22	Thu 2/6/22
376	Modification of FS	60 days	Fri 3/6/22	Mon 1/8/22
377	Backfill and reinstatement + report to FSD	60 days	Tue 2/8/22	Fri 30/9/22
378	Section G (iv) - 275kV cable trenches and External Works at Area F16	518 days	Sat 1/5/21	Fri 30/9/22
379	Area Possession & Clearance	60 days	Sat 1/5/21	Tue 29/6/21
380	Subletting / Fabrication / Delivery	210 days	Wed 17/11/21	Tue 14/6/22
381	Temporary Traffic Arrangement approval	60 days	Sat 1/5/21	Tue 29/6/21
382	Removal of aboveground services	60 days	Wed 30/6/21	Sat 28/8/21
383	Utilities scanning and expose existing UU	30 days	Sun 29/8/21	Mon 27/9/21
384	Arrange of diversion existing UG utilities	90 days	Tue 28/9/21	Sun 26/12/21
385	Construct new cable trenches	173 days	Mon 27/12/21	Fri 17/6/22
386	Realignment / install new UG utilities	60 days	Sat 18/6/22	Tue 16/8/22
387	Backfill and reinstatement + ready for cable laying by others	45 days	Wed 17/8/22	Fri 30/9/22
388	Section G (v) - Shunt Reactor Compound and External Works at Area F17	666 days	Fri 4/12/20	Fri 30/9/22
389	Temporary Traffic Arrangement approval	45 days	Fri 4/12/20	Sun 17/1/21
390	Subletting / Fabrication / Delivery	100 days	Fri 25/12/20	Sat 3/4/21
391	BD approval & consent for pipe pile installation	90 days	Fri 4/12/20	Wed 3/3/21
392	Area Possession & Clearance	14 days	Thu 4/3/21	Wed 17/3/21
393	Removal of aboveground services	21 days	Thu 18/3/21	Wed 7/4/21
394	Utilities scanning and expose existing UU	15 days	Thu 8/4/21	Thu 22/4/21
395	Arrange of diversion existing UG utilities	45 days	Fri 23/4/21	Sun 6/6/21
396	Install pipe piles	61 days	Sun 23/5/21	Thu 22/7/21
397	BA14 for pipepile and BD consent for ELS	28 days	Fri 23/7/21	Thu 19/8/21
398	Excavation & install earthing	35 days	Fri 20/8/21	Thu 23/9/21
399	Construct Pile Caps and Tie Beams	45 days	Fri 24/9/21	Sun 7/11/21
400	Backfill & Erect scaffold	21 days	Mon 8/11/21	Sun 28/11/21
401	Construction of SRC Walls	75 days	Mon 29/11/21	Fri 11/2/22
402	Wall finish and remove scaffolding	24 days	Sat 12/2/22	Mon 7/3/22
403	Construct new cable trenches	60 days	Tue 8/3/22	Fri 6/5/22
404	Install new UG Utilities, Backfill and reinstatement + ready for cable laying by Others for DAX1	55 days	Thu 7/4/22	Tue 31/5/22
405	Realignment / install new UG utilities (for DAX2, APX1 & APX3)	117 days	Sat 7/5/22	Wed 31/8/22
406	Backfill and reinstatement + ready for cable laying by others (for DAX2, APX1, & APX3)	30 days	Thu 1/9/22	Fri 30/9/22
407	Section G (vi) - 275kV cable trenches and External Works at Area F18	397 days	Sat 1/5/21	Wed 1/6/22
408	Temporary Traffic Arrangement approval	45 days	Sat 1/5/21	Mon 14/6/21
409	Subletting / Fabrication / Delivery	60 days	Tue 15/6/21	Fri 13/8/21
410	Area Possession & Clearance	15 days	Sat 1/5/21	Sat 15/5/21
411	Removal of aboveground services	30 days	Sun 16/5/21	Mon 14/6/21
412	Utilities scanning and expose existing UU	45 days	Tue 15/6/21	Thu 29/7/21
413	Arrange of diversion existing UG utilities	60 days	Fri 30/7/21	Mon 27/9/21
414	Construct new cable trenches	172 days	Tue 28/9/21	Fri 18/3/22
415	Realignment / install new UG utilities	45 days	Sat 19/3/22	Mon 2/5/22
416	Backfill and reinstatement + ready for cable laying by others	30 days	Tue 3/5/22	Wed 1/6/22
417	Section G (vii) - Flood wall at No. 5 CW Intake Area along HUA at Area F20A	521 days	Fri 4/12/20	Sun 8/5/22
418	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21
419	Subletting / Fabrication / Delivery	60 days	Fri 25/12/20	Mon 22/2/21
420	Temporary Traffic Arrangement approval	300 days	Fri 4/12/20	Wed 29/9/21
421	ELS BD approval & consent	90 days	Fri 18/12/20	Wed 17/3/21
422	Demolition of existing carriageway	30 days	Thu 11/11/21	Fri 10/12/21
423	Removal of aboveground services	21 days	Thu 30/9/21	Wed 20/10/21
424	Utilities scanning and expose existing UU	21 days	Thu 21/10/21	Wed 10/11/21
425	Arrange of diversion existing UG utilities	30 days	Sat 11/12/21	Sun 9/1/22
426	Excavation and construction of new Flood wall	65 days	Mon 10/1/22	Tue 15/3/22
427	Realignment / install new UG utilities	30 days	Wed 16/3/22	Thu 14/4/22
428	Backfill and construct new carriageway	18 days	Fri 15/4/22	Mon 2/5/22
429	Mis. Work for completion	6 days	Tue 3/5/22	Sun 8/5/22
430	Section G (viii) - Flood wall at No. 5 CW Intake Area along HUA at Area F20B	365 days	Fri 1/10/21	Fri 30/9/22
431	Area Possession & Clearance	45 days	Fri 1/10/21	Sun 14/11/21
432	Subletting / Fabrication / Delivery	90 days	Fri 22/10/21	Wed 19/1/22
433	Temporary Traffic Arrangement approval	14 days	Fri 1/10/21	Thu 14/10/21
434	ELS BD approval & consent	90 days	Fri 15/10/21	Wed 12/1/22



Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12

Master Programme

ID	Task Name	Duration	Start	Finish	
435	Demolition of existing carriageway	60 days	Fri 1/10/21	Mon 29/11/21	
436	Removal of aboveground services	21 days	Tue 30/11/21	Mon 20/12/21	
437	Utilities scanning and expose existing UU	21 days	Tue 21/12/21	Mon 10/1/22	
438	Arrange of diversion existing UG utilities	30 days	Tue 1/1/22	Wed 9/2/22	
439	Install Sheetpiles	55 days	Thu 10/2/22	Tue 5/4/22	
440	BA14 for sheetpile and BD consent for ELS	28 days	Wed 6/4/22	Tue 3/5/22	
441	Excavation and construction of new Flood wall	90 days	Wed 4/5/22	Mon 1/8/22	
442	Realignment / install new UG utilities	30 days	Tue 2/8/22	Wed 31/8/22	
443	Backfill and construct new carriageway	21 days	Thu 1/9/22	Wed 21/9/22	
444	Mis. Work for completion	9 days	Thu 22/9/22	Fri 30/9/22	
445	Section G (ix) - Bund wall modification works at South Seafront Road at Area F21	316 days	Fri 4/12/20	Fri 15/10/21	
446	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21	
447	Subletting / Fabrication / Delivery	90 days	Fri 25/12/20	Wed 24/3/21	
448	Temporary Traffic Arrangement approval	165 days	Fri 4/12/20	Mon 17/5/21	
449	ELS BD approval & consent	0 days	Thu 17/12/20	Thu 17/12/20	
450	Demolition of existing carriageway	14 days	Tue 18/5/21	Mon 31/5/21	
451	Removal of aboveground services	14 days	Tue 1/6/21	Mon 14/6/21	
452	Utilities scanning and expose existing UU	21 days	Tue 15/6/21	Mon 5/7/21	
453	Arrange of diversion existing UG utilities (include FS pipe under 17/8002)	40 days	Tue 6/7/21	Sat 14/8/21	
454	Excavation and expose existing bund wall & demolish	18 days	Wed 28/7/21	Sat 14/8/21	
455	Construction new bund wall for road junction	21 days	Sat 4/9/21	Fri 24/9/21	
456	Realignment / install new UG utilities (include FS pipe under 17/8002)	60 days	Sun 1/8/21	Wed 29/9/21	
457	Backfill and construct new carriageway	16 days	Thu 30/9/21	Fri 15/10/21	
458	Mis. Work for completion	5 days	Mon 11/10/21	Fri 15/10/21	
459	Section G (x) - DAX Cable Diversion Works (from Part I to Part IV)	758 days	Fri 4/12/20	Sat 31/12/22	
460	Temporary Traffic Arrangement approval	14 days	Fri 4/12/20	Thu 17/12/20	
461	Subletting / Fabrication / Delivery	90 days	Fri 25/12/20	Wed 24/3/21	
462	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21	
463	Identification of existing cable trench	7 days	Mon 18/1/21	Sun 24/1/21	
464	Part 1 Re-excavation works incl.construction of joint bay (at Water Reservoir Road)	246 days	Mon 25/1/21	Mon 27/9/21	
465	Part 1 Re-excavation works incl construction of joint bay (other than Reservoir road base on revised routing)	310 days	Mon 25/1/21	Tue 30/11/21	
466	Part 2 Re-excavation works incl. joint bay	120 days	Mon 1/11/21	Mon 28/2/22	
467	Part 3 Re-excavation works incl. joint bay	242 days	Mon 1/11/21	Thu 30/6/22	
468	Part 4 Re-excavation works incl. joint bay & new oil tank pits	92 days	Sat 1/10/22	Sat 31/12/22	
469	Backfill & Reinstatement Part 1	61 days	Mon 1/11/21	Fri 31/12/21	
470	Backfill & Reinstatement Part 2	61 days	Sun 1/5/22	Thu 30/6/22	
471	Backfill & Reinstatement Part 3	61 days	Thu 1/9/22	Mon 31/10/22	
472	Section H - All remaining works shall be completed for reporting completion to BD and ready for OP inspection (PS1.4.4)	775 days	Wed 17/11/21	Sun 31/12/23	
473	Deferred works (MSB & HRS) Listed in PS 1.4.4	272 days	Wed 17/11/21	Mon 15/8/22	
474	Construction of L12 MSB roof between GL12-G to 12-H and 12-2 to 12-6 after the overhead crane installation by the Employer's Specialist Contractors	38 days	Wed 17/11/21	Fri 7/1/22	
475	Construction of walls of L12 MSB below 1/F along GL 12-6 from GL12-B to 12-C and the associated staircases including the enclosure walls between G/F and 1/F. The Contractor shall allow access for the Employer's Specialist Contractors to use the hoisting we	92 days	Mon 16/5/22	Mon 15/8/22	
476	Provision in associated with hoisting well	21 days	Mon 6/6/22	Sun 26/6/22	
477	Construction of internal partition wall at 1/F of L12 MSB along GL 12-C from GL 12-2 to 12-3 AND North Façade at 1/F of L12 MSB along GL 12-1 from GL 12-B to 12-C	30 days	Sat 16/4/22	Sun 15/5/22	
478	Construction of metal fence and the associated Fire Services (F.S.) installations and installation of removable shelter at Transformer Area	92 days	Mon 16/5/22	Mon 15/8/22	
479	Deferred works (DAX1 and DAX2) Listed in PS 1.4.4	334 days	Wed 1/2/23	Sun 31/12/23	
480	Backfilling of whole DAX1 compartment inside existing joint bay "STJ12" and the new oil tank pit A located aside existing joint bay "STJ12".	59 days	Wed 1/2/23	Fri 31/3/23	
481	Re-excavation of whole DAX2 compartment inside existing joint bay "STJ12".	61 days	Tue 1/8/23	Sat 30/9/23	
482	Backfilling of whole DAX2 compartment inside existing joint bay "STJ12" and the new oil tank pit B located aside existing joint bay "STJ12".	61 days	Wed 1/11/23	Sun 31/12/23	
483	Deferred works (External Work) Listed in PS 1.4.4	121 days	Thu 1/12/22	Fri 31/3/23	
484	Final reinstatement of access roads and pavement surrounding and within L12 MSB and L12 HRS area	62 days	Thu 1/12/22	Tue 31/1/23	
485	Installation of trench cover and road reinstatement of gas pipe and cable trenches within Area F5, F14, F16, F17 and F18.	90 days	Sun 1/1/23	Fri 31/3/23	
486	Backfilling and road-reinstatement of 275kV cable trenches	90 days	Sun 1/1/23	Fri 31/3/23	
487	All Remaining work ready for OP inspection	0 days	Tue 28/2/23	Tue 28/2/23	
488	STATUTORY SUBMISSION, INSPECTION & APPROVAL	560 days	Tue 16/11/21	Mon 29/5/23	
489	WSD Statutory Submission, Inspection and Approval WWO Part I to III Submission / Approval	256 days	Tue 16/11/21	Fri 29/7/22	
490	WSD: Submit to WSD Form WWO 046 Part I to II - FOR ACB Building (for Ext Works at later stage)	0 days	Tue 16/11/21	Tue 16/11/21	
491	WSD: Vetting Form WWO 046 Part I and II Submission	90 days	Wed 17/11/21	Mon 14/2/22	
492	WSD: Issued of Form WWO 046 Part III by WSD - FOR ACB Building	0 days	Tue 15/2/22	Tue 15/2/22	
493	WSD: Prepare for 1st Amendment for Plumbing Plan	60 days	Tue 15/2/22	Fri 15/4/22	
494	WSD: Submit to WSD 1st Amendment for Plumbing Plan	0 days	Fri 15/4/22	Fri 15/4/22	
495	WSD: Vetting of Plumbing Plan by WSD	60 days	Sat 16/4/22	Tue 14/6/22	
496	WSD: 1st Approval for Plumbing Plan by WSD	0 days	Tue 14/6/22	Tue 14/6/22	
497	WSD: Prepare and Submit for Final Amendment for Plumbing Plan	45 days	Wed 15/6/22	Fri 29/7/22	
498	WSD: Vetting and Final Approval for Plumbing Plan by WSD	0 days	Fri 29/7/22	Fri 29/7/22	
499	WSD Statutory Submission, Inspection and Approval WWO Part IV to V Fire Services Water Submission / Approval	33 days	Fri 29/7/22	Wed 31/8/22	
500	WSD: Form WWO 046 Part IV Submission (FS)	0 days	Fri 29/7/22	Fri 29/7/22	
501	WSD: WSD Received Form WWO046 Part IV and arrange for inspection (FS)	7 days	Sat 30/7/22	Fri 5/8/22	
502	WSD: WSD Inspection (FS)	7 days	Sat 6/8/22	Fri 12/8/22	
503	WSD: WWO 046 Part V Endorsement by WSD (FS)	12 days	Sat 13/8/22	Wed 24/8/22	
504	WSD: WSD Processing Water Supply Connection Certificate (FS)	7 days	Thu 25/8/22	Wed 31/8/22	
505	WSD: Issue by WSD Water Supply Connection Certificate (FS)	0 days?	Wed 31/8/22	Wed 31/8/22	
506	WSD Statutory Submission, Inspection and Approval WWO Part IV to V Potable /Flush Water Submission / Approval	60 days	Fri 19/8/22	Tue 18/10/22	
507	WSD: Form WWO 046 Part IV Submission (Fresh/Flush)	0 days	Fri 19/8/22	Fri 19/8/22	
508	WSD: WSD Acknowledge Form WWO 046	6 days	Sat 20/8/22	Thu 25/8/22	
509	WSD: WSD Inspection with Testing to lead (Fresh/Fluhs)	12 days	Fri 26/8/22	Tue 6/9/22	
510	WSD: Cleansing/Disinfecting Water Tanks / Piping System (Fresh/Flush)	6 days	Wed 7/9/22	Mon 12/9/22	
511	WSD: Collection of Sample for Testing at Accredited Lab (Fresh/Flush)	12 days	Tue 13/9/22	Sat 24/9/22	
512	WSD: Accredited Lab Testing Report of Sample to WSD	12 days	Sun 25/9/22	Thu 6/10/22	
513	WSD: Vetting of Test Report by WSD	6 days	Fri 7/10/22	Wed 12/10/22	
514	WSD: Issue of WWO 046 Part V (Fresh/Flush)	0 days	Wed 12/10/22	Wed 12/10/22	
515	WSD: WSD Processing WW01005 Water Certification (Fresh/Flush)	6 days	Thu 13/10/22	Tue 18/10/22	
516	WSD: Issue by WSD WW0 1005 Water Certification (Fresh/Flush)	0 days	Tue 18/10/22	Tue 18/10/22	
517	EMSD LIFT Statutory Submission, Inspection and Approval	45 days	Sat 26/3/22	Mon 9/5/22	
518	EMSD: Submission of Lift Form LE5 to EMSD	12 days	Sat 26/3/22	Wed 6/4/22	
519	EMSD: EMSD Makes arrangement for Lift Installation	5 days	Thu 7/4/22	Mon 11/4/22	
520	EMSD: EMSD Inspection to Lift Installation	14 days	Tue 12/4/22	Mon 25/4/22	
521	EMSD: Processing Lift Certificate (Form LE6)	14 days	Tue 26/4/22	Mon 9/5/22	
522	EMSD: Lift Issuance of Form 6 (Lift Certificate)	0 days	Mon 9/5/22	Mon 9/5/22	
523	HKE Transformer Final Inspection	120 days	Thu 30/6/22	Thu 27/10/22	
524	TX Room: Invite HKE For Transformer Room Inspection	7 days	Thu 30/6/22	Wed 6/7/22	
525	TX Room: Give Access to Transformer Room for HKE Contractor	0 days	Wed 6/7/22	Wed 6/7/22	
526	TX Room: Move-IN HKE Transformer Equipments	5 days	Thu 7/7/22	Mon 11/7/22	
527	TX Room: Install HKE Transformer, MEP Works & Testing	90 days	Tue 12/7/22	Sun 9/10/22	
528	TX Room: HKE Power Energization / Inspection	6 days	Mon 10/10/22	Sat 15/10/22	
529	TX Room: Metering Installation	12 days	Sun 16/10/22	Thu 27/10/22	
530	TX Room: HKE Power-ON Date	0 days	Thu 27/10/22	Thu 27/10/22	
531	DSD Drainage Completion Memo	65 days	Sun 2/10/22	Mon 5/12/22	
532	DSD: CCTV Survey Report on Completed Drainage	30 days	Sun 2/10/22	Mon 31/10/22	
533	DSD: Submitted CCTV Report & Form HPB1 of Completed Drainage to DSD For Technical Audit	7 days	Tue 1/11/22	Mon 7/11/22	
534	DSD: Completed Drainage System including TMC Inspection/Technical Audit by DSD	14 days	Tue 8/11/22	Mon 21/11/22	
535	DSD: Preparation of Drainage Connection Completion Memo by DSD	14 days	Tue 22/11/22	Mon 5/12/22	
536	DSD: Issue of Drainage Connection Completion Memo by DSD	0 days	Mon 5/12/22	Mon 5/12/22	
537	EPD Submission, Inspection and Approval	60 days	Thu 30/6/22	Mon 29/8/22	
538	EPD: License Application to EPD under APCO (Cap 311) for Generator Sets	0 days	Thu 30/6/22	Thu 30/6/22	
539	EPD: Vetting of Application by EPD under APCO (Cap 311) for Generator Sets	60 days	Fri 1/7/22	Mon 29/8/22	
540	EPD: Approval from EPD under APCO (Cap 311) for Generator Sets Installation	0 days	Mon 29/8/22	Mon 29/8/22	
541	FSD VAC Statutory Submission, Inspection and Approval	150 days	Wed 20/7/22	Fri 16/12/22	
542	Preparation of FSD VAC Drawings and Submission to HEC	60 days	Wed 20/7/22	Sat 17/9/22	
543	HEC: Review and Approval	30 days	Sun 18/9/22	Mon 17/10/22	
544	Preparation of VAC Drawings and Submission to FSD	30 days	Tue 18/10/22	Wed 16/11/22	
545	FSD: Review and Approval	30 days	Thu 17/11/22	Fri 16/12/22	
546	FSD Statutory Submission, Inspection and Approval	91 days	Tue 28/2/23	Mon 29/5/23	
547	Testing and Commissioning (Individual System - FSI Related)	45 days	Tue 28/2/23	Thu 13/4/23	
548	FSD: All Sections FS Ingration Test by NSC BS	15 days	Fri 14/4/23	Fri 28/4/23	
549	FSD: Completion of FS Integration Test by NSC BS for FS314/501	0 days	Fri 28/4/23	Fri 28/4/23	
550	FSD: Submit Form 213/314 & Form 501 Request for Inspection	0 days	Fri 28/4/23	Fri 28/4/23	
551	FSD: FSD Makes Arrangement for Inspection	7 days	Sat 29/4/23	Fri 5/5/23	
552	FSD: FSD Inspection	12 days	Sat 6/5/23	Wed 17/5/23	
553	FSD: Completion of FS Inspection	0 days	Wed 17/5/23	Wed 17/5/23	
554	FSD: FSD Processing FS Certificate Form 172	12 days	Thu 18/5/23	Mon 29/5/23	
555	FSD: Issue of Fire Services FS Certificate Form 172	0 days	Mon 29/5/23	Mon 29/5/23	
556	PRACTICAL COMPLETION	216 days	Tue 30/5/23	Sun 31/12/23	
557	BD Inspection	97 days	Tue 30/5/23	Sun 3/9/23	
558	BD: Application Form BA13 for OP Application	21 days	Tue 30/5/23	Mon 19/6/23	
559	BD: BD Inspection Date	15 days	Tue 20/6/23	Tue 4/7/23	
560	BD: Reinspection date with defects and rectification works	60 days	Wed 5/7/23	Sat 2/9/23	
561	BD: Obtain Occupation Permit (OP) from BD	1 day	Sun 3/9/23	Sun 3/9/23	
562	As-Built Drawings & Handover Documentation	120 days	Wed 14/6/23	Wed 11/10/23	
563	Prepare and Submit As-Built Drawings & Handover Documentation	45 days	Wed 14/6/23	Fri 28/7/23	
564	Review and Approval	45 days	Sat 29/7/23	Mon 11/9/23	
565	As-Built Drawings & Handover Documentation - Revision by MC	30 days	Tue 12/9/23	Wed 11/10/23	
566	Revised As-Built Drawings & Handover Documentation - Final Submission	0 days	Wed 11/10/23	Wed 11/10/23	
567	Completion of the Whole Contract Works	119 days	Mon 4/9/23	Sun 31/12/23	
568	1st Client Inspection for Review and Comments	30 days	Mon 4/9/23	Tue 3/10/23	
569	Defects and Rectification works	60 days	Wed 4/10/23	Sat 2/12/23	
570	2nd Client Inspection	14 days	Sun 3/12/23	Sat 16/12/23	
571	Minor Defects Rectification Works and Final Inspection	15 days	Sun 17/12/23	Sun 31/12/23	
572	PRACTICAL COMPLETION	0 days	Sun 31/12/23	Sun 31/12/23	



ID	Task Name	Duration	Start	Finish	September 2021							October 2021							November 2021												
					01	04	07	10	13	16	19	22	25	28	01	04	07	10	13	16	19	22	25	28	31	03	06	09	12	15	18
1	19-83014 - Civil Works for No. 5 C.W. Intake and Cable Bridge at Lamma Power Station Extension	664 days	Mon 10/05/20	Fri 12/23/22																											
2	Contract Details	518 days	Mon 10/05/20	Thu 07/07/22																											
15	Submission	308 days	Wed 10/28/20	Wed 11/10/21																											
36	Procurement	166 days	Mon 10/19/20	Thu 05/13/21																											
45	No.5 C.W. Intake	589 days	Mon 10/05/20	Tue 09/27/22																											
46	Erect of Hoarding and Door Gate	12 days	Mon 10/05/20	Sat 10/17/20																											
47	Install Monitoring Instrumentation	16 days	Sat 10/17/20	Fri 11/06/20																											
54	ELS works for No. C.W. Intake	323 days	Tue 12/29/20	Sat 01/29/22																											
55	Installation of pipe pile wall	147 days	Tue 12/29/20	Wed 06/30/21																											
64	Excavate upto +4.50mPD	6 days	Fri 07/02/21	Thu 07/08/21																											
65	Installation the 1st row of waling (WT1) and strut (CS1)	12 days	Fri 07/09/21	Thu 07/22/21																											
66	Installation of 1st row of Tie Back	65 days	Tue 07/13/21	Mon 09/27/21																											
67	RW01 (01-22)	8 days	Fri 08/13/21	Sat 08/21/21																											
68	RW01 (23-70)	16 days	Mon 08/23/21	Thu 09/09/21																											
69	RW01F (01-28)	10 days	Tue 07/13/21	Fri 07/23/21																											
70	RW01F (29-77)	17 days	Sat 08/21/21	Thu 09/09/21																											
71	RW01F (78-98)	7 days	Fri 08/13/21	Fri 08/20/21																											
72	Pull Out Test for Tie Back	2 days	Sat 09/25/21	Mon 09/27/21																											
73	Excavate upto +2.70mPD	6 days	Tue 09/28/21	Tue 10/05/21																											
74	Installation the 2nd row of waling (WT2) and strut (CS2)	12 days	Wed 10/06/21	Wed 10/20/21																											
75	Installation of 2nd row of Tie Back	85 days	Tue 08/10/21	Fri 11/19/21																											
76	RW02 (01-22)	8 days	Wed 10/06/21	Fri 10/15/21																											
77	RW02 (23-70)	16 days	Sat 10/16/21	Wed 11/03/21																											
78	RW02F (01-28)	10 days	Tue 08/10/21	Fri 08/20/21																											
79	RW02F (29-77)	17 days	Fri 10/15/21	Wed 11/03/21																											
80	RW02F (78-98)	7 days	Wed 10/06/21	Wed 10/13/21																											
81	Pull Out Test for Tie Back	2 days	Thu 11/18/21	Fri 11/19/21																											
82	Excavate upto +1.00mPD	6 days	Sat 11/20/21	Fri 11/26/21																											
83	Excavate upto -7.50mPD	52 days	Sat 11/27/21	Sat 01/29/22																											
84	Temporary removal of sea wall	236 days	Fri 05/21/21	Fri 03/04/22																											
85	Application of Marine Permit	78 days	Fri 05/21/21	Mon 08/23/21																											
86	Install silt curtain wall	2 days	Thu 11/25/21	Sat 11/27/21																											
87	Temporary removal of sea wall (USS)	26 days	Sat 11/27/21	Wed 12/29/21																											
88	Removal of existing culvert off-site (USS)	26 days	Thu 12/30/21	Sat 01/29/22																											
89	Prepare formation level for intake chamber	26 days	Mon 01/31/22	Fri 03/04/22																											
90	Construction of No. 5 C.W. Intake Chamber	266 days	Sat 09/25/21	Thu 08/18/22																											
91	Off-site fabrication for Bottom Part of Intake Chamber (From -7.20mPD to +3.20mPD)	107 days	Sat 09/25/21	Sat 02/05/22																											
92	Semisubmersible Barge Return to Casting Yard	0 days	Sat 09/25/21	Sat 09/25/21																											
93	Setup work on Semisubmersible Barge	26 days	Sat 09/25/21	Wed 10/27/21																											
94	Bottom Slab (from -7.20mPD to -5.50mPD, 1596m3)	31 days	Thu 10/28/21	Thu 12/02/21																											
95	External Wall (from -6.35mPD to -5.50mPD, 701m3)	11 days	Fri 12/03/21	Wed 12/15/21																											
96	External Wall (from -5.00mPD to -1.50mPD, 380m3)	13 days	Thu 12/16/21	Mon 01/03/22																											
97	External Wall (from -1.50mPD to +3.00mPD, 571m3)	18 days	Tue 01/04/22	Mon 01/24/22																											
98	Temporary metal gate and support frame	8 days	Tue 01/25/22	Sat 02/05/22																											
99	Delivery of Precast Intake Chamber	3 days	Wed 03/02/22	Fri 03/04/22																											
100	Installation of Precast Intake Chamber	12 days	Sat 03/05/22	Fri 03/18/22																											
101	In-situ casting for Top Part of Intake Chamber (From +3.00mPD to +7.20mPD)	118 days	Sat 03/26/22	Thu 08/18/22																											
115	Reinstatement of sea wall	104 days	Sat 03/26/22	Tue 08/02/22																											
119	Backfilling Works and Strut removal	122 days	Sat 03/19/22	Tue 08/16/22																											
126	Steel Gantry Frame at No. 5 C.W. Intake Chamber	36 days	Wed 08/17/22	Tue 09/27/22																											
129	E&M Works	240 days	Sat 11/27/21	Sat 09/17/22																											
130	Temporary diversion of existing drainage system (from MH807 to MH804)	12 days	Sat 11/27/21	Fri 12/10/21																											
131	Earthing System	26 days	Fri 08/19/22	Sat 09/17/22																											
132	Sump Pump for Drainage System	26 days	Fri 08/19/22	Sat 09/17/22																											
133	Drainage Improvement Works	26 days	Wed 08/03/22	Thu 09/01/22																											
134	External works including CW Inlet Culvert at Area F8C	210 days	Fri 03/12/21	Wed 11/24/21																											
147	No 5 CW Equipment Room, pipe and cable rack, external works at Area F10	426 days	Wed 04/14/21	Thu 09/15/22																											
168	External Work Surrounding Area F11	115 days	Fri 08/12/22	Fri 12/23/22																											
175	Cable Bridge	444 days	Wed 11/11/20	Mon 05/16/22																											

Project: 19-83014 - No. 5 Intake and Cable Br
 Date: 23 Jan 2021
 Rev. 2(a) - Combined L12 Area (Draft)

Task		Summary		External Milestone		Inactive Summary		Manual Task		Manual Summary Rollup		Finish-only	
Split		Project Summary		Inactive Task		Duration-only		Start-only			Progress		
Milestone		External Tasks		Inactive Milestone							Deadline		

ID	Task Name	Duration	Start	Finish	September 2021							October 2021							November 2021													
					29	01	04	07	10	13	16	19	22	25	28	01	04	07	10	13	16	19	22	25	28	31	03	06	09	12	15	18
1	19-83014 - Civil Works for No. 5 C.W. Intake and Cable Bridge at Lamma Power Station Extension	518 days	Mon 10/05/20	Thu 07/07/22																												
2	Contract Details	518 days	Mon 10/05/20	Thu 07/07/22																												
15	Submission	308 days	Wed 10/28/20	Wed 11/10/21																												
36	Procurement	166 days	Mon 10/19/20	Thu 05/13/21																												
45	Cable Bridge	442 days	Wed 11/11/20	Fri 05/13/22																												
46	Erect of Hoarding and Door Gate	12 days	Wed 11/11/20	Tue 11/24/20																												
47	Install Monitoring Instrumentation	2 days	Wed 11/25/20	Thu 11/26/20																												
54	Pile Cap Construction	196 days	Wed 12/30/20	Sat 08/28/21																												
55	LPS Pile Cap (PC5)	80 days	Thu 01/21/21	Mon 05/03/21																												
60	LMX Pile Cap (PC6)	196 days	Wed 12/30/20	Sat 08/28/21																												
61	Expose existing 275kV cable trench by hand dig method	12 days	Wed 12/30/20	Wed 01/13/21																												
62	Install pipe pile (P1-P47)	24 days	Thu 01/28/21	Sat 02/27/21																												
63	Submission of BA14, as-built plan and record	14 days	Mon 03/01/21	Tue 03/16/21																												
64	BD Excavation Consent	0 days	Tue 04/20/21	Tue 04/20/21																												
65	Excavate to 500mm below strut level	6 days	Wed 04/21/21	Tue 04/27/21																												
66	Install waling system (W1)	6 days	Wed 04/28/21	Wed 05/05/21																												
67	Excavate to F.E.L.	12 days	Thu 05/06/21	Thu 05/20/21																												
68	Trimming to COL for Dia 2180mm Bored Pile (8nos)	26 days	Fri 05/21/21	Mon 06/21/21																												
69	Construction of Pile Cap PC6	52 days	Tue 06/22/21	Sat 08/21/21																												
70	Backfilling to pile cap level	6 days	Mon 08/23/21	Sat 08/28/21																												
71	Existing Seawall modification works (USS)	26 days	Mon 08/23/21	Tue 09/21/21																												
72	Construction of Cable Bridge	326 days	Wed 04/07/21	Fri 05/13/22																												
73	Off-site precast beam construction (PCB1-PCB12)	142 days	Wed 04/07/21	Fri 09/24/21																												
74	Type 2 (PCB6 - PCB12)	88 days	Wed 04/07/21	Thu 07/22/21																												
82	Type 1 (PCB1 - PCB5)	60 days	Fri 07/16/21	Fri 09/24/21																												
83	PCB5	16 days	Fri 07/16/21	Tue 08/03/21																												
84	PCB4	16 days	Wed 07/28/21	Sat 08/14/21																												
85	PCB3	16 days	Mon 08/09/21	Thu 08/26/21																												
86	PCB2	16 days	Fri 08/20/21	Tue 09/07/21																												
87	PCB1	20 days	Wed 09/01/21	Fri 09/24/21																												
88	Application of Marine Permit	78 days	Tue 06/22/21	Thu 09/23/21																												
89	Erect precast beam (PCB1-PCB12)	16 days	Thu 09/23/21	Tue 10/12/21																												
90	Construction of Diaphragm Beams (DB7-DB11)	36 days	Wed 10/13/21	Wed 11/24/21																												
91	Stage 2 PT Stressing	6 days	Thu 12/02/21	Wed 12/08/21																												
92	Construction of 200mm thk R.C. Middle Slab	36 days	Thu 12/09/21	Sat 01/22/22																												
93	Installation of Precast Panel (for planter and kerb)	52 days	Mon 01/24/22	Mon 03/28/22																												
94	Casting of 250mm thk R.C. Top Slab	18 days	Tue 03/08/22	Mon 03/28/22																												
95	Road paving work	24 days	Mon 04/11/22	Fri 05/13/22																												
96	Installation of steel parapet	24 days	Mon 04/11/22	Fri 05/13/22																												
97	Construction of Abutment at LPS	114 days	Thu 12/09/21	Tue 05/03/22																												
104	Construction of Abutment at LMX	110 days	Thu 12/09/21	Wed 04/27/22																												
111	Stormwater Drainage	32 days	Tue 03/29/22	Wed 05/11/22																												
113	E&M works	32 days	Tue 03/29/22	Wed 05/11/22																												

Project: 19-83014 - No. 5 Intake and Cable Br Date: 23 Jan 2021 Rev. 2(a) - Combined L12 Area (Draft)	Task		Summary		External Milestone		Inactive Summary		Manual Task		Manual Summary Rollup		Finish-only		Deadline
	Split		Project Summary		Inactive Task		Duration-only			Manual Summary		Progress			
	Milestone		External Tasks		Inactive Milestone					Start-only		Deadline			

Monthly Waste Flow Table for Aug 2021

Project: Lamma Power Station Extension - Civil and Building Works for Unit L11

Contractor: Paul Y. Construction Company, Limited

Record by: Ben Lam

Year of Record: 2018, 2019, 2020 & 2021

MM.YYYY	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of Non-inert C&D Materials Generated Monthly					
	Excavated Materials				Non-excavated Materials				Metals (steel bar / metal strip) ⁽¹⁾	Metals (aluminum can) ⁽¹⁾	Paper / cardboard packaging ⁽¹⁾	Plastics ^{(1) & (4)}	Chemical waste (wasted lubricant / oil / container)	Other, e.g. general refuse
	Disposed in Public Fill	Disposed in Sorting Facilities	Others (e.g. Reused in the Contract / Other Projects)	Broken Concrete or Construction Waste Collected by Recycled Company	Reused in the Contract	Reused in other Projects	Disposed in Public Fill	Disposed in Sorting Facilities						
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000L)	(in '000kg)	
Jul 2018	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Aug 2018	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Sep 2018	3160.23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Oct 2018	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Nov 2018	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.87	
Dec 2018	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	10.67	
Jan 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Feb 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.66	0.00	0.00	0.00	0.60	
Mar 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	19.05	0.00	0.00	0.00	0.00	
Apr 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.08	0.00	0.00	0.00	19.09	
May 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	3.63	0.00	0.00	0.00	59.75	
Jun 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	14.64	
Jul 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	2.66	
Aug 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Sep 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	27.31	
Oct 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.109	0.00	4.76	
Nov 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.60	4.87	
Dec 2019	0.00	0.00	0.00	0.00	0.00	10226.24	0.00	0.00	0.00	0.00	0.00	0.00	18.19	
Jan 2020	0.00	0.00	0.00	0.00	0.00	7981.09	0.00	0.00	0.00	0.00	0.157	0.00	26.89	
Feb 2020	0.00	0.00	0.00	0.00	0.00	8782.98	0.00	0.00	0.00	0.00	0.000	0.00	0.00	
Mar 2020	0.00	0.00	0.00	0.00	0.00	20252.12	0.00	0.00	0.00	0.00	0.000	0.00	76.96	
Apr 2020	0.00	0.00	0.00	0.00	0.00	12976.86	0.00	0.00	8.30	0.00	0.000	0.00	68.75	
May 2020	0.00	0.00	0.00	0.00	0.00	20203.01	0.00	0.00	0.00	0.00	0.000	0.00	0.00	
Jun 2020	0.00	0.00	0.00	0.00	0.00	28030.33	0.00	0.00	0.00	0.00	0.000	0.00	58.49	
Jul 2020	0.00	0.00	0.00	0.00	0.00	12481.37	0.00	0.00	0.00	0.00	0.000	0.00	33.88	
Aug 2020	0.00	0.00	0.00	0.00	0.00	11179.56	0.00	0.00	0.00	0.00	0.000	0.60	73.73	
Sep 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	7.53	0.00	0.296	0.00	64.93	
Oct 2020	0.00	0.00	0.00	0.00	0.00	10762.20	0.00	0.00	7.12	0.00	0.297	0.00	83.34	
Nov 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.46	0.00	0.000	0.20	61.21	
Dec 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	59.98	
Jan 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	51.37	
Feb 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	44.94	
Mar 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	34.57	
Apr 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	30.92	
May 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	18.65	
Jun 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	10.76	
Jul 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	
Aug 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	24.19	
Total	3160.23	0.00	0.00	0.00	0.00	142875.75	0.00	0.00	74.83	0.00	0.849	0.00	996.37	

Total Inert C&D Waste Materials Generated	Non-inert C&D Materials		
	C&D Materials Recycled	C&D Waste Disposed of at Landfill	Chemical Waste
146035.98 tonnes	75.68 tonnes	996.37 tonnes	2000 Liters

Where (A) Inert C&D materials include bricks, concrete, building debris, rubble and excavated spoil. In total, 146035.98 tonnes of inert C&D material were generated from the Project, of which 142875.75 tonnes were reused in this and other contracts, and the remaining 3160.23 tonnes were disposed as public fill to Fill Banks / Sorting Facilities.

(b) Non-inert C&D materials (construction wastes) include metals, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Metals generated from the Project were grouped into construction wastes as the materials were not disposed of with others at the public fill.

(c) 0 kg of metals, 0 kg of papers/ cardboard packing and 0 kg of plastics were sent to recyclers for recycling during the reporting period.

(d) Construction wastes other than metals, paper/cardboard packaging, plastics and chemicals were disposed of at Landfill.

- Notes:
- (1) metal, paper & plastic were collected by recycler
 - (2) The performance target of waste recycling are specified in the Contract.
 - (3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 - (4) Plastics refer to plastic bottles/ containers, plastic/ foam from packaging material.
 - (5) Broken concrete for recycling into aggregates.
 - (6) Disposal of inert waste to public fill or sorting facilities will NOT be considered as recycled waste.

Monthly Waste Flow Table for August 2021

Project: LAMMA POWER STATION EXTENSION – Unit 11 Complete Erection, Inspection, Testing & Commissioning of Power Block Facilities
 Contractor: Taihei Dengyo Kaisha, Ltd.
 Record by: Stephen Sin
 Year of Record: 2019, 2020, 2021

MM.YYYY	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of Non-inert C&D Materials Generated Monthly					
	Excavated Materials				Non-excavated Materials				Metals (steel bar / metal strip) ⁽¹⁾	Metals (aluminum can) ⁽¹⁾	Paper / cardboard packaging ⁽¹⁾	Plastics ^{(1) & (4)}	Chemical waste (wasted lubricant oil/oil container)	Other, e.g. general refuse
	Disposed in Public Fill	Disposed in Sorting Facilities	Others (e.g. Reused in the Contract / Other Projects)	Broken Concrete or Construction Waste Collected by Recycled Company	Reused in the Contract	Reused in other Projects	Disposed in Public Fill	Disposed in Sorting Facilities						
(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in L)	(in '000kg)	
Nov 2019	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	
Dec 2019	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Jan 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Feb 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Mar 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	3.35	
Apr 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.61	
May 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	12.39	
Jun 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.03	
Jul 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.32	
Aug 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	2600	10.38	
Sep 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	10.20	
Oct 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	12.02	
Nov 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	2400	26.18	
Dec 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.38	
Jan 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.65	
Feb 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	10.40	
Mar 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.43	
Apr 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	2400	20.24	
May 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0	14.08	
Jun 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0	17.43	
Jul 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0	20.38	
Aug 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0	22.38	
Total	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	7400	274.85	

Total Inert C&D Waste Materials Generated	Non-inert C&D Materials		
	C&D Materials Recycled	C&D Waste Disposed of at Landfill	Chemical Waste
0.00 tonnes	0.00 tonnes	274.85 tonnes	7400 Liters

- Where (A) Inert C&D materials include bricks, concrete, building debris, rubble and excavated spoil. In total, 0.00 tonnes of inert C&D material were generated from the Project, of which 0 tonnes were reused in this and other contracts, and the remaining 0.00 tonnes were disposed in Public Fill and Sorting Facilities.
- (b) Non-inert C&D materials (construction wastes) include metals, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Metals generated from the Project were grouped into construction wastes as the materials were not disposed of with others at the public fill.
- (c) 0 kg of metals, 0 kg of papers/ cardboard packing and 0 kg of plastics were sent to recyclers for recycling during the reporting period.
- (d) Construction wastes other than metals, paper/cardboard packaging, plastics and chemicals were disposed of at Landfill.

- Notes:
- (1) metal, paper & plastic were collected by recycler
 - (2) The performance target of waste recycling are specified in the Contract.
 - (3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 - (4) Plastics refer to plastic bottles/ containers, plastic/ foam from packaging material.
 - (5) Broken concrete for recycling into aggregates.
 - (6) Disposal of inert waste to public fill or sorting facilities will **NOT** be considered as recycled waste.

