

香港電燈有限公司  
The Hongkong Electric Co., Ltd.



**Lamma Power Station Extension  
Construction Phase  
Monthly Environmental Monitoring & Audit Report**

**March 2023**

香港電燈有限公司  
The Hongkong Electric Co., Ltd.



**ENVIRONMENTAL IMPACT ASSESSMENT (EIA) ORDINANCE, CAP. 499**

**ENVIRONMENTAL PERMIT NO. EP-071/2000/D**

**LAMMA POWER STATION EXTENSION  
ENVIRONMENTAL MONITORING & AUDIT PROGRAMME  
AT CONSTRUCTION PHASE**

Report Title	Lamma Power Station Extension – Unit L12 Monthly EM&A Report (March 2023)
Date	14 April 2023
Certified by	 (Mr. CHAN Hon Yeung, Environmental Team Leader)
Verified by	 Mr. Y. W. Fung (AECOM Asia Company Limited, Independent Environmental Checker)

## TABLE OF CONTENT

### EXECUTIVE SUMMARY

<b>1.</b>	<b>INTRODUCTION.....</b>	<b>1</b>
1.1	Background	1
1.2	Project Organisation	1
1.3	Construction Works undertaken during the Reporting Month	1
1.4	Summary of EM&A Requirements	4
<b>2.</b>	<b>AIR QUALITY.....</b>	<b>6</b>
2.1	Monitoring Requirements	6
2.2	Monitoring Locations	6
2.3	Monitoring Equipment	6
2.4	Monitoring Parameters, Frequency and Duration	6
2.5	Monitoring Procedures and Calibration Details	7
2.6	Results and Observations	8
<b>3.</b>	<b>NOISE .....</b>	<b>10</b>
3.1	Monitoring Requirements	10
3.2	Monitoring Locations	10
3.3	Monitoring Equipment	10
3.4	Monitoring Parameters, Frequency and Duration	10
3.5	Monitoring Procedures and Calibration Details	11
3.6	Results and Observations	11
<b>4.</b>	<b>ENVIRONMENTAL AUDIT .....</b>	<b>13</b>
4.1	Review of Environmental Monitoring Procedures	13
4.2	Assessment of Environmental Monitoring Results	13
4.3	Waste Management	13
4.4	Site Environmental Audit	14
4.5	Status of Environmental Licensing and Permitting	14
4.6	Implementation Status of Environmental Mitigation Measures	15
4.7	Implementation Status of Event/Action Plans	15
4.8	Implementation Status of Environmental Complaint Handling Procedures	15
<b>5.</b>	<b>FUTURE KEY ISSUES.....</b>	<b>16</b>
5.1	Key Issues for the Coming Month	16
5.2	Monitoring Schedules for the Next 3 Months	16
5.3	Construction Program for the Next 3 Months	17
<b>6.</b>	<b>CONCLUSION.....</b>	<b>18</b>

## **LIST OF TABLES**

Table 1.1	Construction Activities and Their Corresponding Environmental Mitigation Measures
Table 2.1	Air Quality Monitoring Locations
Table 2.2	Air Quality Monitoring Equipment
Table 2.3	Air Quality Monitoring Parameter, Duration and Frequency
Table 3.1	Noise Monitoring Equipment
Table 3.2	Noise Monitoring Duration and Parameter
Table 4.1	Summary of AL Level Exceedances on Monitoring Parameters
Table 4.2	Estimated Amounts of Waste in March 2023
Table 4.3	Summary of Environmental Licensing and Permit Status
Table 4.4	Environmental Complaints Received in March 2023
Table 4.5	Outstanding Environmental Complaints Carried Over

## **LIST OF FIGURES**

Figure 1.1	Layout of Work Site
Figure 2.1	Location of Air Quality Monitoring Stations
Figure 3.1	Location of Noise Monitoring Stations

## **APPENDICES**

Appendix A	Organization Chart
Appendix B	Action and Limit Levels for Air Quality and Noise
Appendix C	Environmental Monitoring Schedule
Appendix D	Air Quality Monitoring Results for March 2023
Appendix E	Noise Monitoring Results for March 2023
Appendix F	The QA/QC Procedures and Results
Appendix G	Event/Action Plans
Appendix H	Site Audit Summary
Appendix I	Summary of EMIS
Appendix J	Tentative Construction Programme
Appendix K	Monthly Waste Flow Table for March 2023

## EXECUTIVE SUMMARY

This is the 155<sup>th</sup> monthly Environmental Monitoring and Audit (EM&A) report for the Project “Construction of Lamma Power Station Extension” prepared by the Environmental Team (ET). This report presents the results of impact monitoring on air quality and noise for the said project in March 2023.

The reclamation and submarine pipeline works were completed with the first gas-fired combined cycle unit (viz. Unit L9) commissioned in October 2006, working currently on base load operation. To cope with the scheduled retirement of the existing units at Lamma Power Station, the second gas-fired combined cycle unit (viz. Unit L10) L10 was commissioned for reliable operation in February 2020.

In September 2016, the Government approved HK Electric to construct the third combined cycle gas-fired generating unit (Unit L11) to implement the 2020 Fuel Mix Target. L11 was commissioned for reliable operation effective in May 2022. The operational EM&A work for L9, L10 and L11 is recorded in the separate monthly EM&A report for the Project “Operation of Lamma Power Station Extension”.

With the Government’s approval to build the fourth combined cycle gas-fired generating unit (L12) in July 2018, the associated construction work commenced in April 2019. When L12 is commissioned in 2023, the total gas-fired electricity generation will further rise to reach about 70% of our total output.

Air and noise monitoring were performed. The results were checked against the established Action/Limit (AL) levels. An on-site audit was conducted once per week. The implementation status of the environmental mitigation measures, Event/Action Plan and environmental complaint handling procedures were also checked.

### Construction Activities Undertaken

Construction activities for Lamma Extension during the reporting month are tabulated as follows:

Item	Construction Activities
Unit L12 Civil and Building Works	External works of Main Station Building, construction of staircase at No. 5 chimney, construction of L12 GRS, fitting out and external works, cable trench works for ACB, construction of cable trench for Cable Bridge (North & South), construction of superstructure for shunt reactor compound extension and external works for No. 5 C.W. Intake.
Unit L12 Mechanical Erection	Condenser installation, HRSG installation and turbine block installation
Unit L12 Electrical, Instrumentation & Control Erection	Cable installation

### Environmental Monitoring Works

All monitoring work at designated stations was performed as scheduled satisfactorily.

#### *Air Quality*

No exceedance of Action/Limit levels on 1-hour TSP and 24-hour TSP for air quality was recorded in the month.

## Noise

No exceedance of Action and Limit levels for noise arising from the construction of Lamma Extension was recorded in the month.

## Site Environmental Audit

EPD officials from Regional Office (South) visited Lamma Power Station on 3 and 10/3/2023. There was no adverse comment from EPD regarding the construction site.

Site audits were carried out on a weekly basis to monitor environmental issues on the construction site. The site conditions were generally satisfactory.

## Environmental Licensing and Permitting

Description	Permit No.	Valid Period		Issued To	Date of Issuance
		From	To		
Varied Environmental Permit	EP-071/2000/D	28/09/20	-	HK Electric	28/09/20
Construction Noise Permit	GW-RS1163-22	08/01/23	06/07/23	Contractor	04/01/23
Construction Noise Permit	GW-RS0027-23	28/01/23	27/07/23	Contractor	20/01/23
Construction Noise Permit	GW-RS0126-23	01/03/23	31/08/23	Contractor	21/02/23
WPCO Discharge Licence	WT00037613-2021	15/04/21	30/04/26	Contractor	15/04/21
WPCO Discharge Licence	WT00037665-2021	06/05/21	31/05/26	Contractor	06/05/21
Registration of Chemical Waste Producer	WPN5213-912-P2781-22	22/02/16	-	Contractor	22/02/16
Registration of Chemical Waste Producer	WPN5517-912-T2007-02	17/03/05	-	Contractor	17/03/05
Waste Disposal Billing Account	Account No.: 7038672	27/10/20	-	Contractor	27/10/20
Waste Disposal Billing Account	Account No.: 7039272	08/01/21	-	Contractor	08/01/21
Waste Disposal Billing Account	Account No.: 7041942	21/10/21	-	Contractor	21/10/21

## Implementation Status of Environmental Mitigation Measures

Environmental mitigation measures for the construction activities as recommended in the EM&A manual were implemented in the reporting month.

## Environmental Complaints

No complaint in relation to the environmental impact of the construction activities was received in the reporting month.

## Future Key Issues

The future key issues to be considered in the coming month are as follows:

### Unit L12 Civil and Building Works

- to continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained;
- to monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary;
- to treat wastewater in sedimentation pit and tanks before discharge and to ensure compliance with the WPCO discharge licence already obtained;

### Unit L12 Mechanical Erection

- to continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained;
- to continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the performance;
- to monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

### Unit L12 Electrical, Instrumentation & Control Erection

- to continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained;
- to continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the performance;
- to monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

### **Concluding Remarks**

The environmental performance of the project was generally satisfactory.

## 1. INTRODUCTION

### 1.1 Background

The Environmental Team (hereinafter called the “ET”) was formed within the Hongkong Electric Co. Ltd (HEC) to undertake Environmental Monitoring and Audit for “Construction of Lamma Power Station Extension” (hereinafter called the “Project”). Under the requirements of Section 6 of Environmental Permit EP-071/2000/D, an EM&A programme for impact environmental monitoring set out in the EM&A Manual (Construction Phase) is required to be implemented. In accordance with the EM&A Manual, environmental monitoring of air quality, noise and water quality and regular environmental audits are required for the Project. With the completion of reclamation and submarine pipeline works, no further marine water quality monitoring would be required.

The Project involves the construction of a gas-fired power station employing combined cycled gas turbine technology, forming an extension to the existing Lamma Power Station. The key elements of the Project including the construction activities associated with the transmission system and submarine gas pipeline are outlined as follows.

- dredging and reclamation to form approximately 22 hectares of usable area;
- construction of six 300MW class gas-fired combined cycle units;
- construction of a gas receiving station;
- construction of a transmission system linking the Lamma Extension to load centres on Hong Kong Island;
- laying of a gas pipeline for the supply of natural gas to the new power station

This report summarizes the environmental monitoring and audit work for the Project for the month of March 2023.

### 1.2 Project Organisation

An Environmental Management Committee (EMC) has been set up in HEC to oversee the Project. The management structure includes the following:

- Environmental Protection Department (The Authority);
- Environmental Manager (The Chairman of the Environmental Management Committee);
- Engineer;
- Independent Environmental Checker (IEC);
- Environmental Team (ET);
- Contractor.

The project organisation chart for the construction EM&A programme is shown in [Appendix A](#).

### 1.3 Construction Works undertaken during the Reporting Month

Construction activities for Unit L12 civil and building works were, external works of Main Station Building, construction of staircase at No.5 chimney, construction of L12 GRS, fitting out and external works, cable trench works for ACB, and construction of cable trench for Cable Bridge (North & South), construction of superstructure for shunt reactor compound extension, external works for No. 5 C.W. Intake. Construction activities for Unit L12 mechanical erection were condenser installation, HRSG installation and turbine block installation. Construction

activity for Unit L12 electrical, instrumentation & control erection was cable installation. Layout plan for construction site is shown in [Figure 1.1](#).

The main construction activities carried out during the reporting month and the corresponding environmental mitigation measures are summarized in [Table 1.1](#). The implementation of major mitigation measures in the month is provided in [Appendix I](#).

Table 1.1 Construction Activities and Their Corresponding Environmental Mitigation Measures

Item	Construction Activities	Environmental Mitigation Measures
Unit L12 Civil and Building Works		
1.	External works of Main Station Building  Construction of staircase at No.5 Chimney  Construction of L12 GRS  <u>ACB</u> Fitting out and external works  Cable trench works	<p><b>Air</b></p> <ul style="list-style-type: none"> <li>– All regulated machine attached with valid exception/approval NRMM labels.</li> <li>– Water truck and water sprinkler system would be used.</li> <li>– Water spraying for concrete breaking works.</li> <li>– Soil stock would be covered with cement or tarpaulin or keep the entire surface wet. Wheel washing facility was provided.</li> </ul> <p><b>Noise</b></p> <ul style="list-style-type: none"> <li>– Works conducted during restricted hours should comply with the valid CNP.</li> <li>– Noise emission label was provided for air compressor.</li> </ul> <p><b>Wastewater</b></p> <ul style="list-style-type: none"> <li>– Wastewater should be treated in desilting pit and tanks before discharge. Solution should be added to speed up the sedimentation process. Sediment in pit and tanks must be removed regularly. The frequency would be in weekly basis depends on the volume of sediment accumulated in order to maintain sufficient volume for wastewater treatment.</li> <li>–</li> </ul> <p><b>Waste Management</b></p> <ul style="list-style-type: none"> <li>– Excavated soil was temporary stored for backfilling and reuse in other projects.</li> <li>– Scrape metal would be recycled.</li> <li>– Chemical waste should be collected by licensed collector.</li> </ul>
2.	<u>Cable Bridge (North &amp; South):</u> Construction of	<p><b>Air</b></p> <ul style="list-style-type: none"> <li>– All regulated machine attached with valid exception/approval NRMM labels.</li> </ul>

Item	Construction Activities	Environmental Mitigation Measures
	cable trench  <u>Shunt Reactor Compound Extension</u> Construction of superstructure  <u>No. 5 C.W. Intake</u> External works	<ul style="list-style-type: none"> <li>- Water truck, water sprinkler system and mist cannon were used.</li> <li>- Excavated soil slop covered with tarpaulin.</li> <li>- Wheel washing facilities was provided.</li> <li>- Water spraying on haul road and during concrete breaking.</li> </ul> <p><b>Noise</b></p> <ul style="list-style-type: none"> <li>- Noise emission label was provided for air compressor.</li> <li>- Works conducted during restricted hours should comply with the valid CNP.</li> </ul> <p><b>Waste Management</b></p> <ul style="list-style-type: none"> <li>- Excavated soil would be transferred to other projects for reuse.</li> <li>- Scrape metal will be recycled.</li> </ul> <p><b>Wastewater</b></p> <ul style="list-style-type: none"> <li>- Wastewater would be treated in desilting tanks or wastewater treatment facility before discharge.</li> </ul>
Unit L12 Mechanical Erection		
3.	Condenser installation  HRSG installation  Turbine block installation	<p><b>Air</b></p> <ul style="list-style-type: none"> <li>- Dust suppression measures implemented according to the EMP.</li> </ul> <p><b>Noise</b></p> <ul style="list-style-type: none"> <li>- General noise mitigation measures employed at all work sites throughout the construction phase.</li> </ul> <p><b>Waste Management</b></p> <ul style="list-style-type: none"> <li>- Waste Management Plan submitted and implemented</li> </ul>
Unit L12 Electrical, Instrumentation & Control Erection		
4.	Cable installation	<p><b>Air</b></p> <ul style="list-style-type: none"> <li>- Dust suppression measures implemented according to the EMP.</li> </ul> <p><b>Noise</b></p> <ul style="list-style-type: none"> <li>- General noise mitigation measures employed at all work sites throughout the construction phase.</li> </ul>

<b>Item</b>	<b>Construction Activities</b>	<b>Environmental Mitigation Measures</b>
		<b>Waste Management</b> – Waste Management Plan submitted and implemented.

#### **1.4 Summary of EM&A Requirements**

The detailed EM&A monitoring work for air quality and noise are described in Sections 2 and 3 respectively. Regular environmental site audits for air quality, noise, water quality and waste management were carried out.

The following environmental audits are summarized in Section 4 of this report:

- Environmental monitoring results;
- Waste Management Records;
- Weekly site audit results;
- The status of environmental licensing and permits for the Project;
- The implementation status of environmental protection and pollution control/ mitigation measures.

Future key issues will be reported in Section 5 of this report.

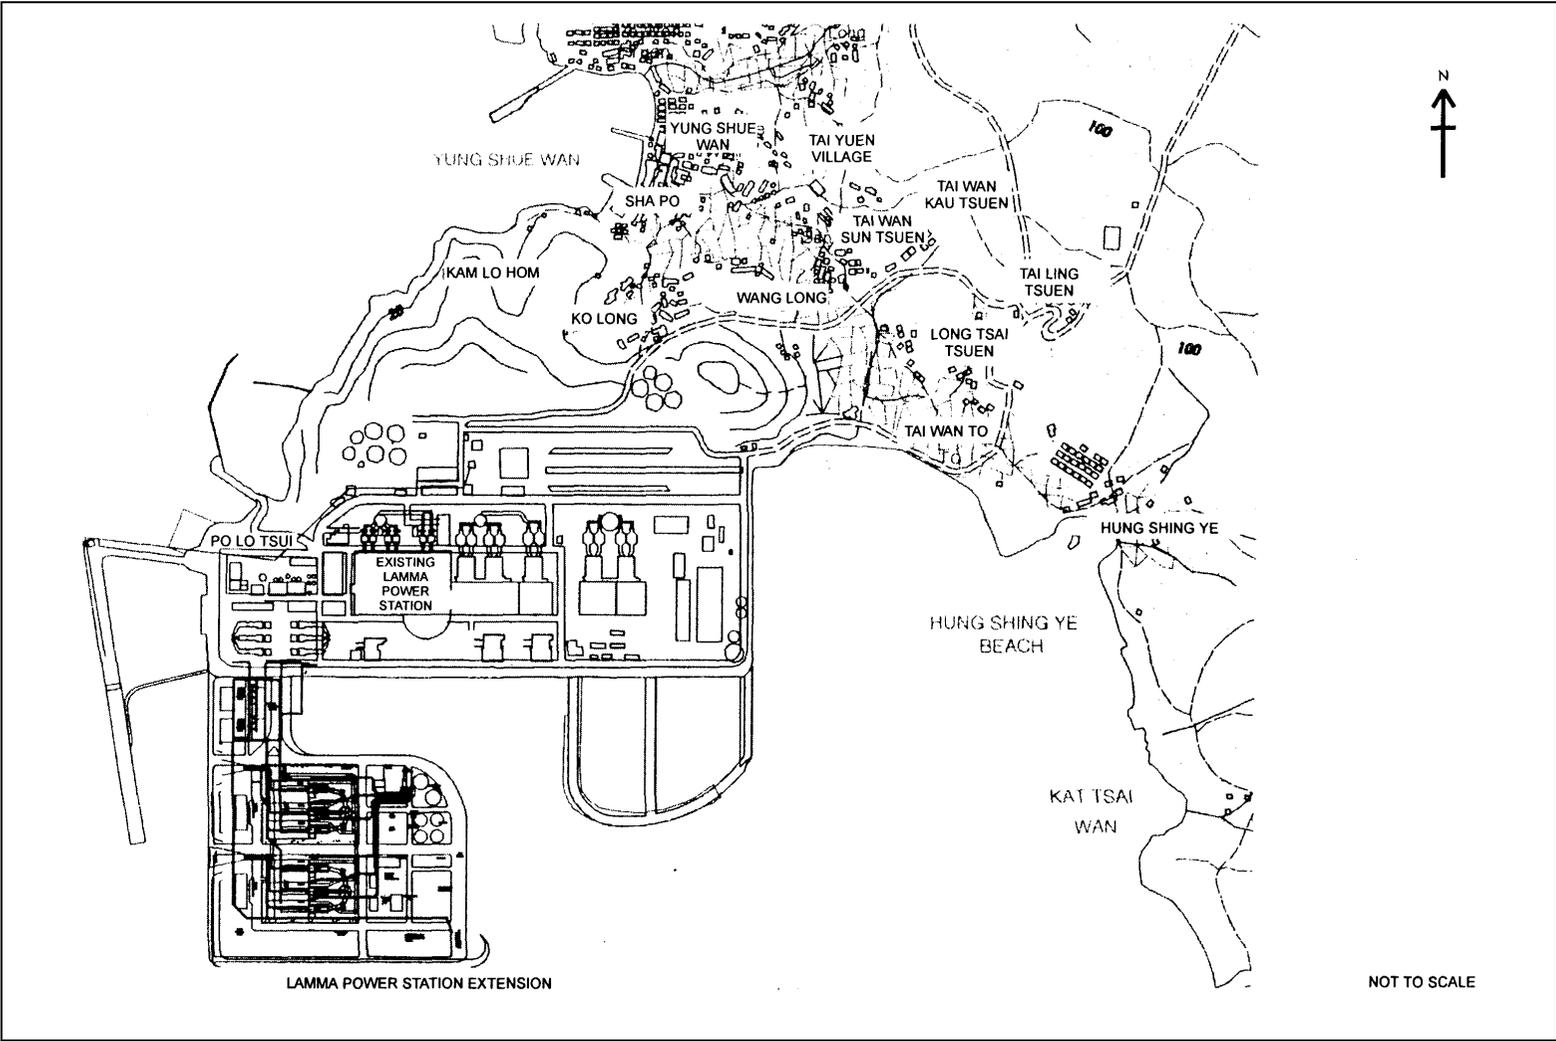


Figure 1.1 Layout of Work Site

## 2. AIR QUALITY

### 2.1 Monitoring Requirements

1-hour and 24-hour TSP monitoring at agreed frequencies were conducted to monitor air quality. The impact monitoring data were checked against the Action/Limit Levels as determined in the Baseline Monitoring Report (Construction Phase). [Appendix B](#) shows the established Action/Limit Levels for Air Quality.

### 2.2 Monitoring Locations

Three dust monitoring locations were selected for 1-hour TSP sampling (AM1, AM2 & AM3) while four monitoring locations were selected for 24-hour TSP sampling (AM1, AM2, AM3 and AM4). [Table 2.1](#) tabulates the monitoring stations. The locations of the monitoring stations are shown in [Figure 2.1](#).

Table 2.1 Air Quality Monitoring Locations

Location I.D.	Description
AM1	Reservoir
AM2	East Gate
AM3	Ash Lagoon
AM4	Tai Yuen Village

### 2.3 Monitoring Equipment

It is agreed with EPD that continuous 24-hour TSP air quality monitoring would be performed using TEOM continuous dust monitor and the MINIVOL Portable Sampler at AM1,2&3 and AM4 respectively. TEOM continuous dust monitors were used to carry out 1-hour TSP monitoring at AM1, AM2 and AM3. [Table 2.2](#) summarises the equipment used in dust monitoring.

Table 2.2 Air Quality Monitoring Equipment

Equipment	Model and Make
<i>24-hour sampling:</i>	
Continuous TSP Dust Meter	TEOM continuous dust monitor Thermo Scientific
MINIVOL Portable Sampler	AIRMETRICS
<i>1-hour sampling:</i>	
Continuous TSP Dust Meter	TEOM continuous dust monitor Thermo Scientific

### 2.4 Monitoring Parameters, Frequency and Duration

[Table 2.3](#) summarises the monitoring parameters, duration and frequency of air quality monitoring. The monitoring schedule for the reporting month is shown in [Appendix C](#).

Table 2.3 Air Quality Monitoring Parameter, Duration and Frequency

Monitoring Stations	Parameter	Duration	Frequency
AM1	1-hour TSP	1	3 hourly samples every 6 days
	24-hour TSP	24	Once every 6 days
AM2	1-hour TSP	1	3 hourly samples every 6 days
	24-hour TSP	24	Once every 6 days
AM3	1-hour TSP	1	3 hourly samples every 6 days
	24-hour TSP	24	Once every 6 days
AM4	24-hour TSP	24	Once every 6 days

## 2.5 Monitoring Procedures and Calibration Details

MINIVOL (24- hour TSP Monitoring):

### *Preparation of Filter Papers*

- Visual inspection of filter papers was carried out to ensure that there were no pinholes, tears and creases;
- The filter papers were then labeled before sampling.
- The filter papers were equilibrated at room temperature and relative humidity < 50% for at least 24 hours before weighing.

### *Field Monitoring*

- During collection of the sampled filter paper, the information on the elapse timer was logged. Site observations around the monitoring stations, which might have affected the monitoring results, were also recorded. Major pollution sources, if any, would be identified and reported.
- The post-sampling filter papers were removed carefully from the filter holder and folded to avoid loss of fibres or dust particles from the filter papers;
- The filter holder and its surrounding were cleaned;
- A pre-weighed blank filter paper for the next sampling was put in place and aligned carefully. The filter holder was then tightened firmly to avoid leakage;
- The programmable timer was set for the next 24 hrs sampling period;
- The post-sampling filter papers were equilibrated at room temperature and relative humidity < 50% for at least 24 hours before weighing.

TEOM continuous dust monitor (24- hour TSP and 1- hour TSP Monitoring):

- The following parameters of the TEOM model dust meters are regularly checked to ensure proper functionality:
  - Operation Mode;
  - Frequency of the tapered element;
  - Main flow;
  - Bypass flow.

### *Maintenance & Calibration*

- The monitoring equipment and their accessories are maintained in good working conditions.

- Monitoring equipment is calibrated at monthly intervals. Calibration details are shown in [Appendix F](#).

## 2.6 Results and Observations

All dust monitoring works were conducted on schedule. All monitoring data and graphical presentation of the monitoring results are provided in [Appendix D](#). Key findings and observations are provided below:

### *1-hour TSP*

No exceedance of 1-hour TSP Action/Limit Level was recorded in the month.

### *24-hour TSP*

No exceedance of 24-hour TSP Action/Limit Level was recorded in the month.

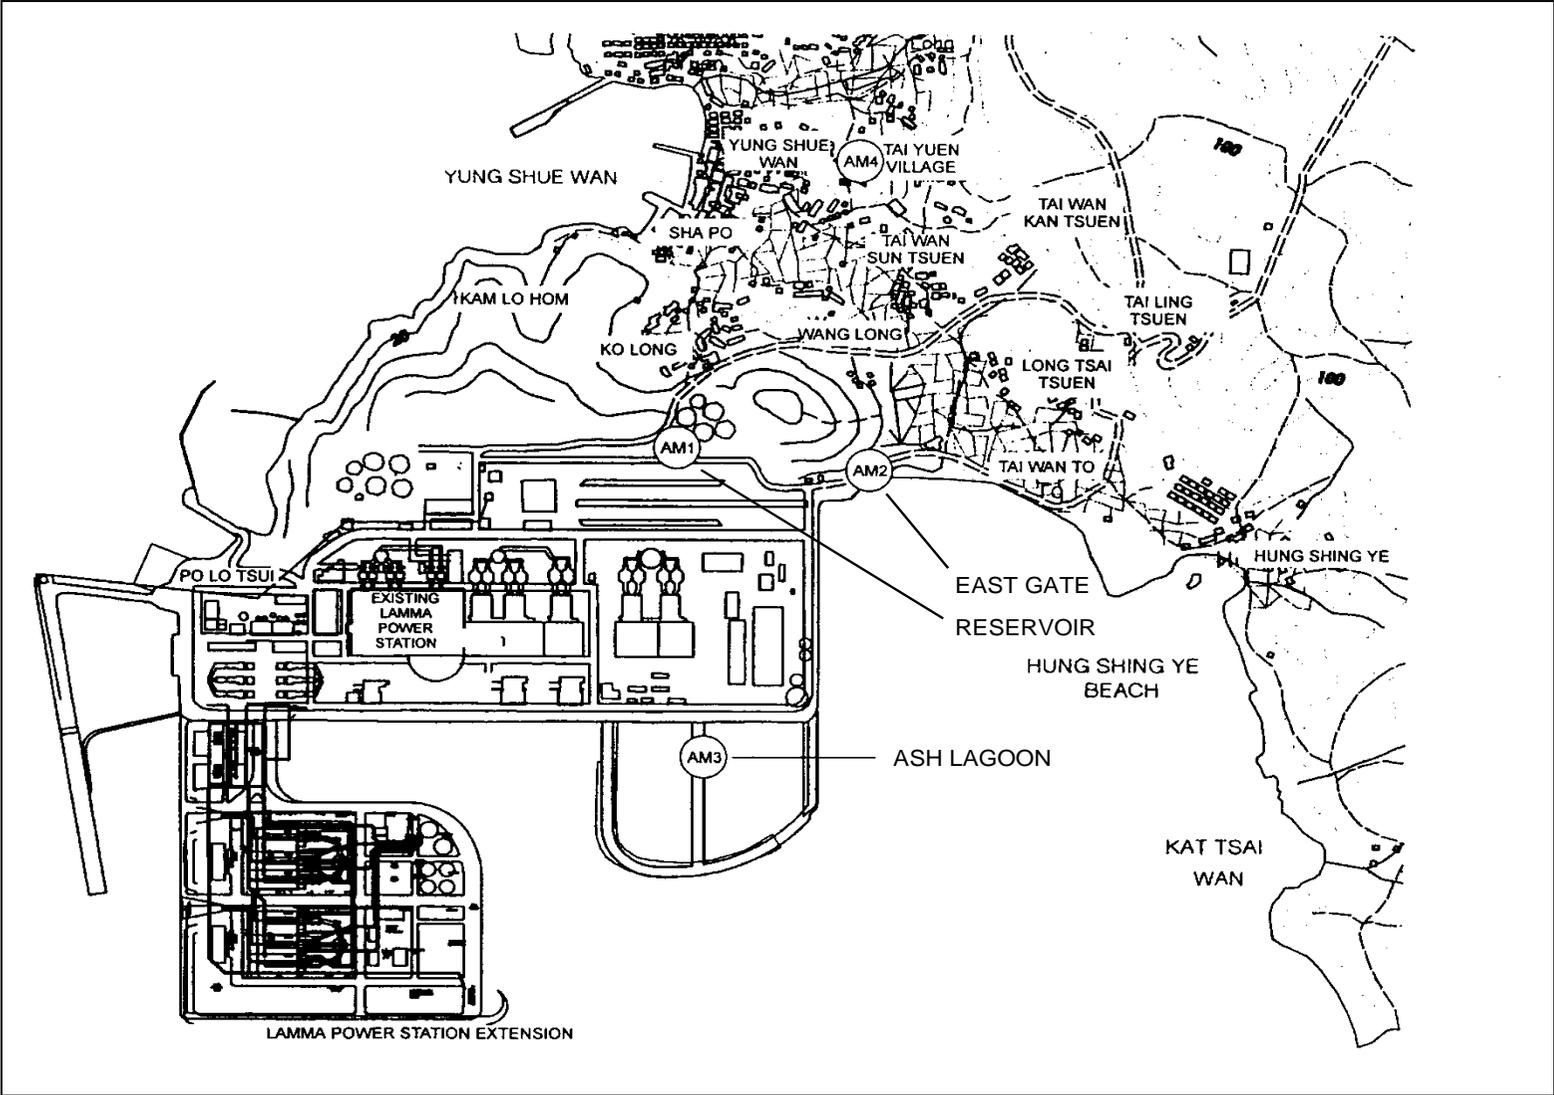


Figure 2.1 Location of Air Quality Monitoring Stations

### 3. NOISE

#### 3.1 Monitoring Requirements

Continuous noise alarm monitoring at Ash Lagoon/Ching Lam were carried out to calculate the noise contributed by the construction activities at the two critical NSR's, viz. Long Tsai Tsuen/Hung Shing Ye and the school within the village of Tai Wan San Tsuen. The impact monitoring data for construction noise were checked against the limit levels specified in the EM&A Manual. With the availability of the construction noise permits, impact monitoring for the construction work during the restricted hours was also carried out. Section 3 presents the details of the construction noise permits.

The impact noise monitoring data were checked against the limit levels specified in the EM&A Manual. [Appendix B](#) shows the established Action/Limit Levels for noise.

#### 3.2 Monitoring Locations

In accordance with the EM&A manual, the identified noise monitoring locations of Ash Lagoon and Ching Lam are shown in [Figure 3.1](#).

#### 3.3 Monitoring Equipment

The sound level meters used for noise monitoring complied with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). The noise monitoring equipment used is shown in [Table 3.1](#).

Table 3.1 Noise Monitoring Equipment

Equipment	Model
Sound level meters	B&K 2250
Sound level calibrator	B&K 4231

#### 3.4 Monitoring Parameters, Frequency and Duration

Continuous alarm monitoring was carried out at Ash Lagoon and Ching Lam. The measurement duration and parameter of noise monitoring were presented in [Table 3.2](#) as follows:

Table 3.2 Noise Monitoring Duration and Parameter

Location	Time Period	Frequency	Parameter
----------	-------------	-----------	-----------

Ash Lagoon	Day-time: 0700-1900 hrs on normal weekdays	Day-time: 30 minutes	30-min $L_{Aeq}$
	Evening-time & holidays: 0700-2300 hrs on holidays; and 1900-2300 hrs on all other days	Evening-time & holidays: 5 minutes	5-min $L_{Aeq}$
Ching Lam	Night-time: 2300-0700 hrs of next day	Night-time: 5 minutes	5-min $L_{Aeq}$

### 3.5 Monitoring Procedures and Calibration Details

#### *Monitoring Procedures*

##### *Continuous Noise Monitoring for Lamma Extension Construction*

The measured noise levels (MNL's) were collected at the noise alarm monitoring stations at Ash Lagoon and Ching Lam. The notional background noise levels (viz. baseline noise data at Ash Lagoon and Ching Lam) were applied to correct the corresponding MNL's in 30-min/5-min  $L_{Aeq}$ .

A wind speed sensor was installed at Station Building Rooftop. The wind speed signal was used to determine whether the data from Ash Lagoon and Ching Lam noise alarm monitoring stations were affected. The instantaneous data was discarded in case the instantaneous wind speed exceeded 10 m/s. The 30-min/5-min  $L_{Aeq}$  was considered valid only if the amount of valid data was equal to or above 70%.

#### *Equipment Calibration*

The sound level meters and calibrators were verified by the manufacturer or accredited laboratory. With the endorsement of the Independent Environmental Checker, the enhancement of calibration of sound level meter at the noise monitoring stations was implemented. The monthly manual on-site calibration using sound level calibrator was replaced by the daily auto charge injection calibration function of the sound level meter. For additional quality assurance, manual on-site calibration would still be conducted for the noise monitoring stations once every 6 months. The manual on-site calibrations for Ash Lagoon and Ching Lam noise monitoring stations were carried out in November 2022 and March 2023 respectively. The next calibrations for the two corresponding noise monitoring stations were scheduled in May and September 2023 respectively.

### 3.6 Results and Observations

Continuous noise monitoring was conducted at the two monitoring stations at Ash Lagoon and Ching Lam.

All monitoring results and their graphical presentations are provided in [Appendix E](#). No exceedance of noise Action/Limit Level was recorded in the month.

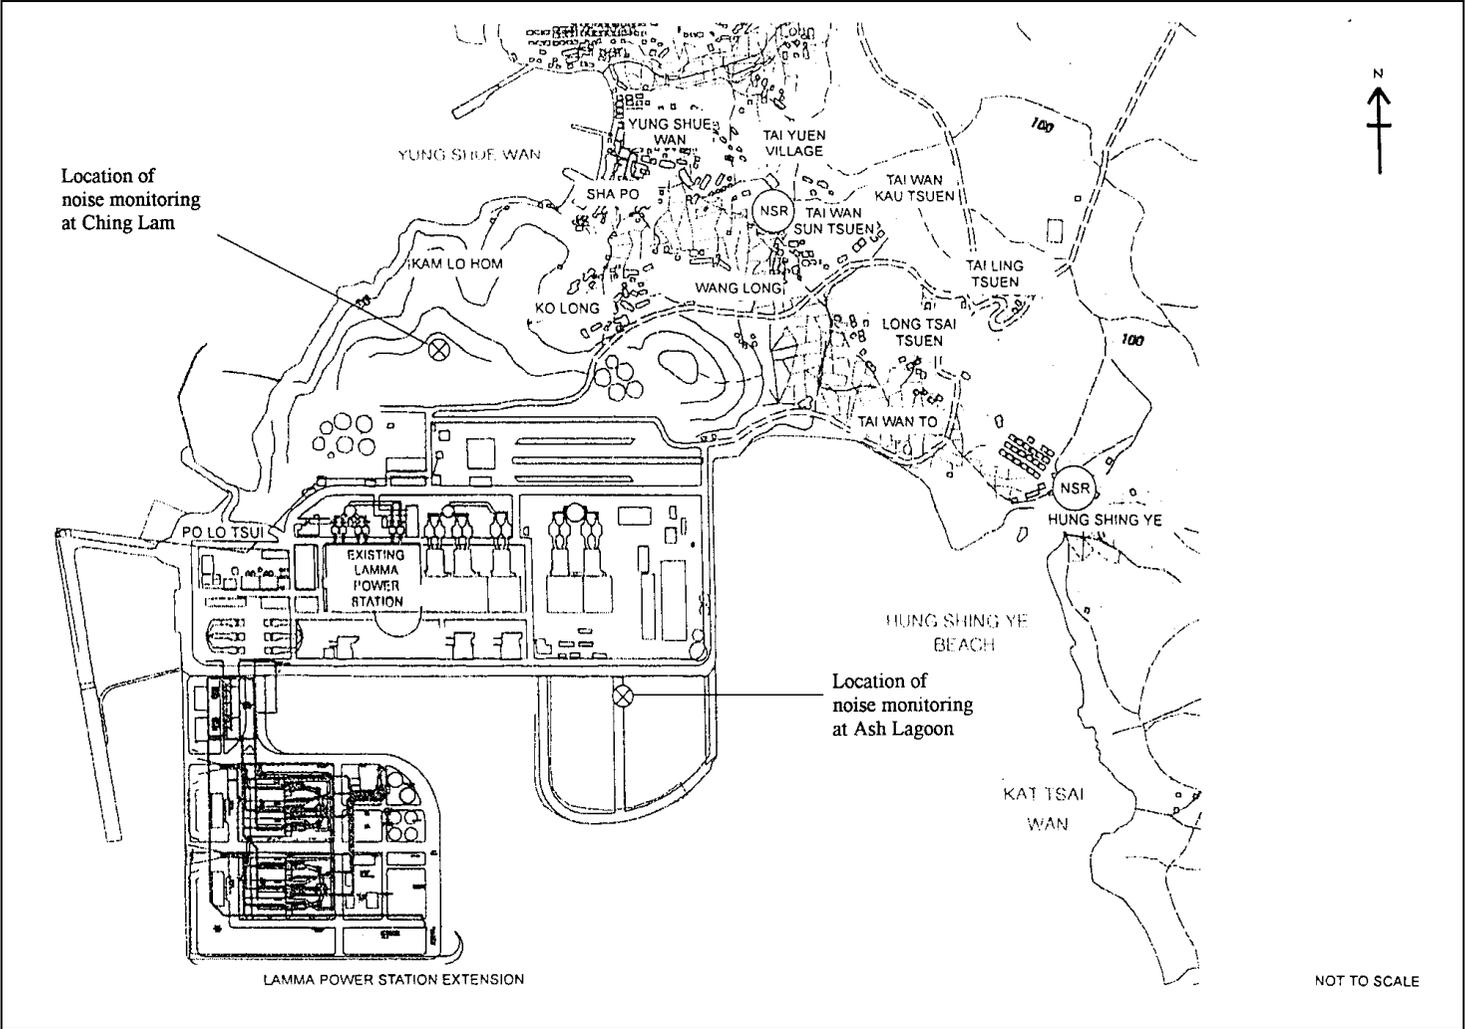


Figure 3.1 Location of Noise Monitoring Stations

## 4. ENVIRONMENTAL AUDIT

### 4.1 Review of Environmental Monitoring Procedures

The environmental monitoring procedures were regularly reviewed by the Environmental Team. No modification to the existing monitoring procedures was recommended.

### 4.2 Assessment of Environmental Monitoring Results

#### *Monitoring results for Air Quality and Noise*

The environmental monitoring results for Air Quality and Noise in the reporting month presented in Sections 2 and 3 respectively are summarized in [Table 4.1](#).

Table 4.1 Summary of AL Level Exceedances on Monitoring Parameters

Item	Parameter Monitored	Monitoring Period	No. of Exceedances In		Event/Action Plan Implementation Status and Results
			Action Level	Limit Level	
Air					
1	Ambient TSP (24-hour)	01/03/2023-31/03/2023	0	0	
2	Ambient TSP (1-hour)	01/03/2023-31/03/2023	0	0	
Noise					
1	Noise level at the critical NSR's predicted by the noise alarm monitoring system	01/03/2023-31/03/2023	0	0	

### 4.3 Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. Inert C&D materials comprise excavated materials and broken concrete. Non-inert C&D materials comprise general refuse, metals and paper/ cardboard packaging, plastics, chemical waste, etc.

Inert C&D material and non-inert C&D material disposed of in March 2023 are shown in [Table 4.2](#).

Table 4.2 Estimated Amounts of Waste in March 2023

Total Inert C&D Waste Materials	Non-inert C&D Materials		
	C&D Materials Recycled	C&D Waste Disposed of at Landfill	Chemical Waste

0 Tonnes	33.68 Tonnes	86.58 Tonnes	0 Litres
----------	--------------	--------------	----------

The monthly waste flow tables prepared by the contractors are attached in [Appendix K](#)

#### 4.4 Site Environmental Audit

EPD officials from Regional Office (South) visited Lamma Power Station on 3 and 10/3/2023. There was no adverse comment from EPD regarding the construction site.

Site audits were carried out by ET on a weekly basis to monitor environmental issues at the construction sites to ensure that all mitigation measures were implemented timely and properly. The site audit findings for the reporting month are summarized in [Appendix H](#). The site conditions were generally satisfactory. All required mitigation measures were implemented.

#### 4.5 Status of Environmental Licensing and Permitting

All permits/licenses obtained for the project are summarised in [Table 4.3](#).

Table 4.3 Summary of Environmental Licensing and Permit Status

Description	Permit No.	Valid Period		Highlights	Status
		From	To		
Varied Environmental Permit	EP-071/2000/D	28/09/20	-	The whole construction work site	Valid
Construction Noise Permit	GW-RS1163-22	08/01/23	06/07/23	Construction site of Unit L12. Operation of PME during restricted hours	Valid
Construction Noise Permit	GW-RS0027-23	28/01/23	27/07/23	Civil and Building Works for Unit L12. Operation of PME during restricted hours	Valid
Construction Noise Permit	GW-RS0126-23	01/03/23	31/08/23	Power Block Facilities works for Unit L12. Operation of PME during restricted hours	Valid
WPCO Discharge Licence#	WT00037613-2021	15/04/21	30/04/26	Civil and Building Works for No.5 C.W. Intake and Cable Bridge	Valid
WPCO Discharge Licence##	WT00037665-2021	06/05/21	31/05/26	Civil and Building Works for Unit L12	Valid
Registration of Chemical Waste Producer	WPN5213-912-P2781-22	22/02/16	-	Civil and Building Works	Valid

Description	Permit No.	Valid Period		Highlights	Status
		From	To		
Registration of Chemical Waste Producer	WPN5517-912-T2007-02	17/03/05	-	E&M Equipment Installation and Maintenance	Valid
Waste Disposal Billing Account	Account No.: 7038672	27/10/20	-	Civil works for Unit L12 No.5 C.W. intake and cable bridge	Valid
Waste Disposal Billing Account	Account No.: 7039272	08/01/21	-	Civil and building works for Unit L12	Valid
Waste Disposal Billing Account	Account No.: 7041942	21/10/21	-	E&M Erection of Power Block Facilities – L12	Valid

Notes: # and ## - Water quality monitoring was carried out in February 2023 and the results of which would be reported separately by the contractor.

#### 4.6 Implementation Status of Environmental Mitigation Measures

Mitigation measures detailed in the permits and the EM&A Manual (Construction Phase) are required to be implemented. An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is presented in [Appendix I](#).

#### 4.7 Implementation Status of Event/Action Plans

The Event/Action Plans extracted from the EM&A Manual (Construction Phase) are presented in [Appendix G](#).

#### 4.8 Implementation Status of Environmental Complaint Handling Procedures

In March 2023, no complaint in relation to the environmental impact of the construction activities was received.

Table 4.4 Environmental Complaints Received in March 2023

Case Reference / Date, Time Received / Date, Time Concerned	Descriptions / Actions Taken	Conclusion / Status
Nil	N/A	N/A

Table 4.5 Outstanding Environmental Complaints Carried Over

Case Reference / Date, Time Received / Date, Time Concerned	Descriptions / Actions Taken	Conclusion / Status
Nil	N/A	N/A

## **5. FUTURE KEY ISSUES**

### **5.1 Key Issues for the Coming Month**

Key issues to be considered in the coming month include:

#### Unit L12 Civil and Building Works

##### *Noise Impact*

- To continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained.

##### *Air Impact*

- To monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

##### *Water Impact*

- To treat wastewater in sedimentation pit and tanks before discharge and to ensure compliance in accordance with the WPCO discharge licence already obtained.

#### Unit L12 Mechanical Erection

##### *Noise Impact*

- To continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained.
- To continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the noise performance.

##### *Air Impact*

- To monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

#### Unit L12 Electrical, Instrumentation & Control Erection

##### *Noise Impact*

- To continue monitoring the noise level during construction and to ensure compliance with the CNP's already obtained.
- To continue executing the preventive measures for avoiding noise exceedance and keep monitoring/ reviewing the noise performance.

##### *Air Impact*

- To monitor and review the sufficiency of the dust suppression measures provided and increase the resources accordingly if necessary.

### **5.2 Monitoring Schedules for the Next 3 Months**

The tentative environmental monitoring schedules for the next 3 months are shown in [Appendix C](#).

### **5.3 Construction Program for the Next 3 Months**

The tentative construction programs for the next 3 months are shown in [Appendix J](#).

## **6. CONCLUSION**

All monitoring work at designated stations was performed as scheduled satisfactorily. The environmental monitoring works and site inspection were performed as scheduled in the reporting month. All monitoring results were checked and reviewed.

No Action/Limit level exceedance on 1-hour and 24-hour TSP level was recorded in the reporting month.

No Action/Limit level exceedance on noise was recorded in the reporting month.

Environmental mitigation measures recommended in the EM&A manual for the construction activities were implemented in the reporting month. No complaint in relation to the environmental impact of the construction activities was received in the reporting month. No prosecution was received for this Project in the reporting period.

The environmental performance of the Project was generally satisfactory.

Appendix A Organization Chart

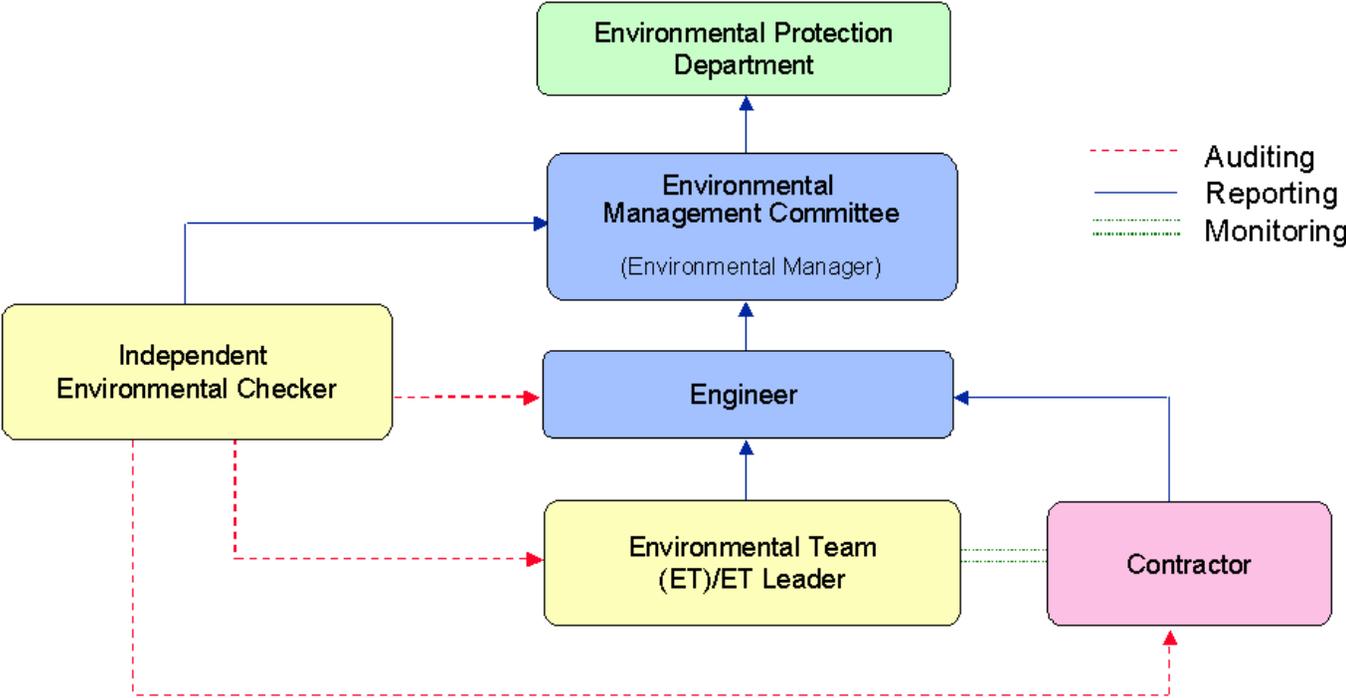


Figure A.1 Organisation of EM&A Programme at Construction Phase

## Appendix B Action and Limit Levels for Air Quality and Noise Monitoring

### B.1. Air

Table B.1 Action and Limit Levels for 1-hour and 24-hour TSP

	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
1-hour TSP*	340	500
24-hour TSP	190	260

\* No Action/Limit Level for 1-hour TSP is applied to AM4 where no real time dust monitor is installed.

### B.2. Noise

Table B.2 AL Levels for Construction Noise (Other than Percussive Piling)

Parameters	Action	Limit
Noise Levels at the NSR's at Long Tsai Tsuen/Hung Shing Ye and school within the village of Tai Wan San Tsuen predicted by the noise alarm monitoring system	When one or more documented complaints are received	a. 75 dB(A) in $L_{Aeq,30 \text{ min}}$ (07:00-19:00 hrs on normal weekdays) (Note 1)
Manual noise monitoring at the nearest Pak Kok Tsui residences to cable landing points N4 and N5		b. subject to statutory control under the Noise Control Ordinance (07:00-23:00 hrs on holidays and 19:00-23:00 hrs on all other days). Set to 60 dB(A) in $L_{Aeq,5 \text{ min}}$ c. subject to statutory control under the Noise Control Ordinance (23:00-07:00 hrs of next day). Set to 45 dB(A) in $L_{Aeq,5 \text{ min}}$
Note:		
1. For educational institution, the limit level shall be 70 dB(A), reduced to 65 dB(A) during examination periods.		

## Appendix C Environmental Monitoring Schedule

Table C.1 Monitoring schedule for 24hr and 1hr TSP monitoring for Lamma Extension Construction (March 2023 to June 2023)

24hr TSP Monitoring	1hr TSP Monitoring
3/March/2023	3/March/2023 1500hr to 1800hr
9/March/2023	9/March/2023 1500hr to 1800hr
15/March/2023	15/March/2023 1500hr to 1800hr
21/March/2023	21/March/2023 1500hr to 1800hr
27/March/2023	27/March/2023 1500hr to 1800hr
2/April/2023	2/April/2023 1500hr to 1800hr
8/April/2023	8/April/2023 1500hr to 1800hr
14/April/2023	14/April/2023 1500hr to 1800hr
20/April/2023	20/April/2023 1500hr to 1800hr
26/April/2023	26/April/2023 1500hr to 1800hr
2/May/2023	2/May/2023 1500hr to 1800hr
8/May/2023	8/May/2023 1500hr to 1800hr
14/May/2023	14/May/2023 1500hr to 1800hr
20/May/2023	20/May/2023 1500hr to 1800hr
26/May/2023	26/May/2023 1500hr to 1800hr
1/June/2023	1/June/2023 1500hr to 1800hr
7/June/2023	7/June/2023 1500hr to 1800hr
13/June/2023	13/June/2023 1500hr to 1800hr
19/June/2023	19/June/2023 1500hr to 1800hr
25/June/2023	25/June/2023 1500hr to 1800hr

## APPENDIX D AIR QUALITY MONITORING RESULTS

Site: Lamma Power Station Extension

Month: March 2023

### 24 hour TSP Measurement:-

Date	TSP concentration ( $\mu\text{g}/\text{m}^3$ )				Weather Information (From Hong Kong Observatory)		
	Reservoir (AM1)	East Gate (AM2)	Ash Lagoon (AM3)	Tai Yuen Village (AM4)	Mean Wind Speed (km/hr)	Prevailing Wind Dir. ( $^{\circ}$ )	Mean R.H. (%)
3/3/2023	68	68	48	75	30.8	80	56
9/3/2023	66	51	31	18	5.0	230	75
15/3/2023	48	49	34	64	13.2	80	77
21/3/2023	26	27	15	19	14.8	170	85
27/3/2023	19	18	22	21	42.3	80	86



### 1 hour TSP Measurement:-

Date	Time	TSP concentration ( $\mu\text{g}/\text{m}^3$ )		
		Reservoir (AM1)	East Gate (AM2)	Ash Lagoon (AM3)
3/3/2023	15:00 - 15:59	66	119	50
	16:00 - 16:59	69	76	58
	17:00 - 17:59	84	76	56
9/3/2023	15:00 - 15:59	96	87	38
	16:00 - 16:59	70	86	37
	17:00 - 17:59	57	59	33
15/3/2023	15:00 - 15:59	70	47	38
	16:00 - 16:59	50	49	36
	17:00 - 17:59	47	49	39
21/3/2023	15:00 - 15:59	29	20	10
	16:00 - 16:59	24	21	13
	17:00 - 17:59	25	22	13
27/3/2023	15:00 - 15:59	20	21	24
	16:00 - 16:59	22	21	32
	17:00 - 17:59	12	17	30


	1-hr TSP ( $\mu\text{g}/\text{m}^3$ )	24-hr TSP ( $\mu\text{g}/\text{m}^3$ )
Action Level	340	190
Limit Level	500	260
Calibration:	Calibration details are shown in appendix F.	

Equipment used:


Location	1-hr TSP	24-hr TSP
Reservoir, East Gate and Ash Lagoon	TEOM	TEOM
Tai Yuen Village	-	MINIVOL Portable Sampler

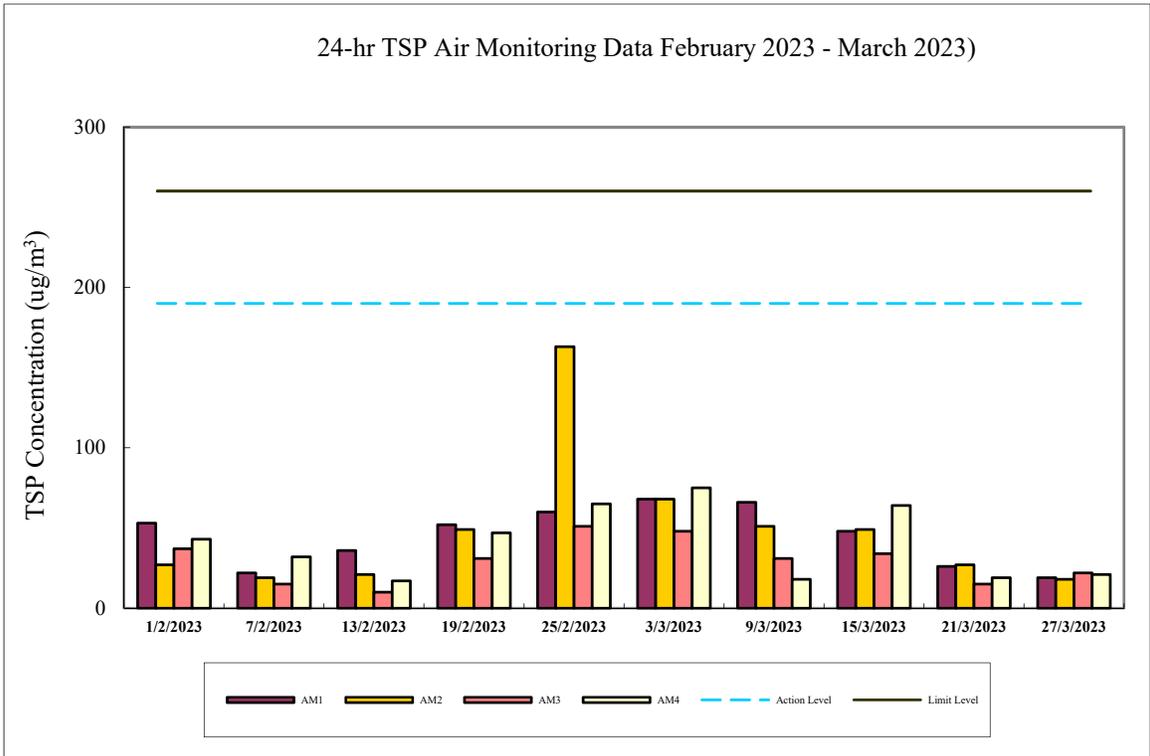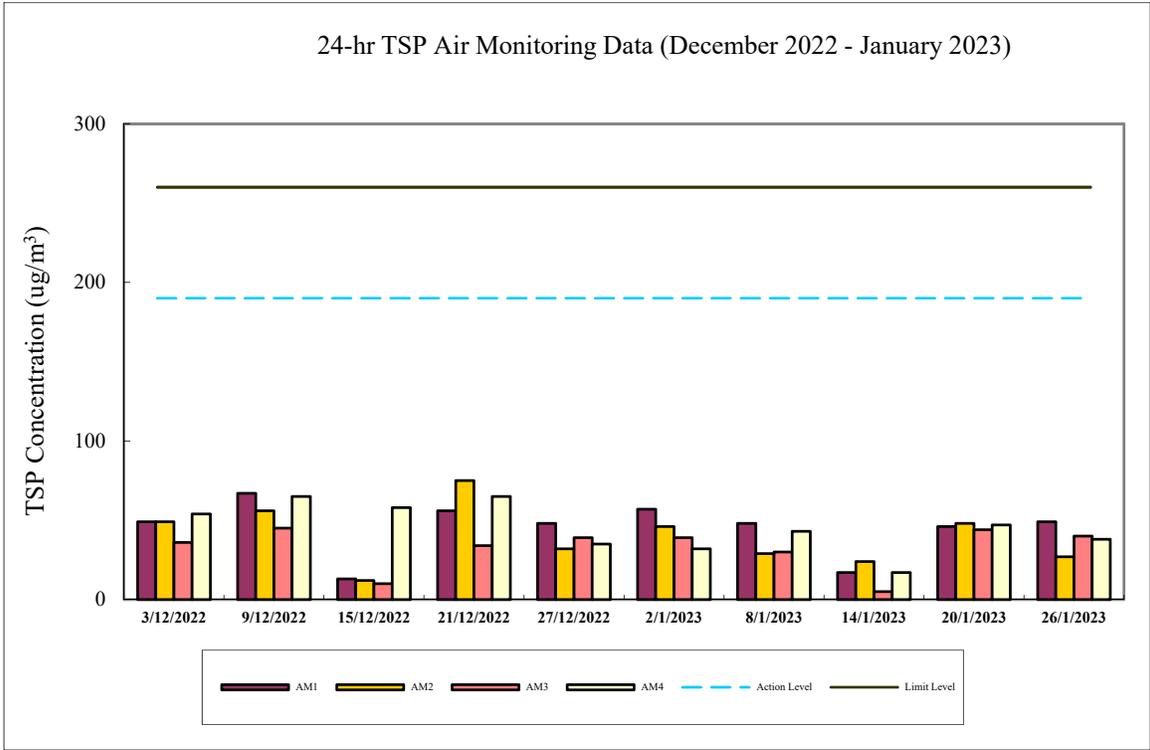

1-hr TSP Air Monitoring Data (December 2022 - January 2023)

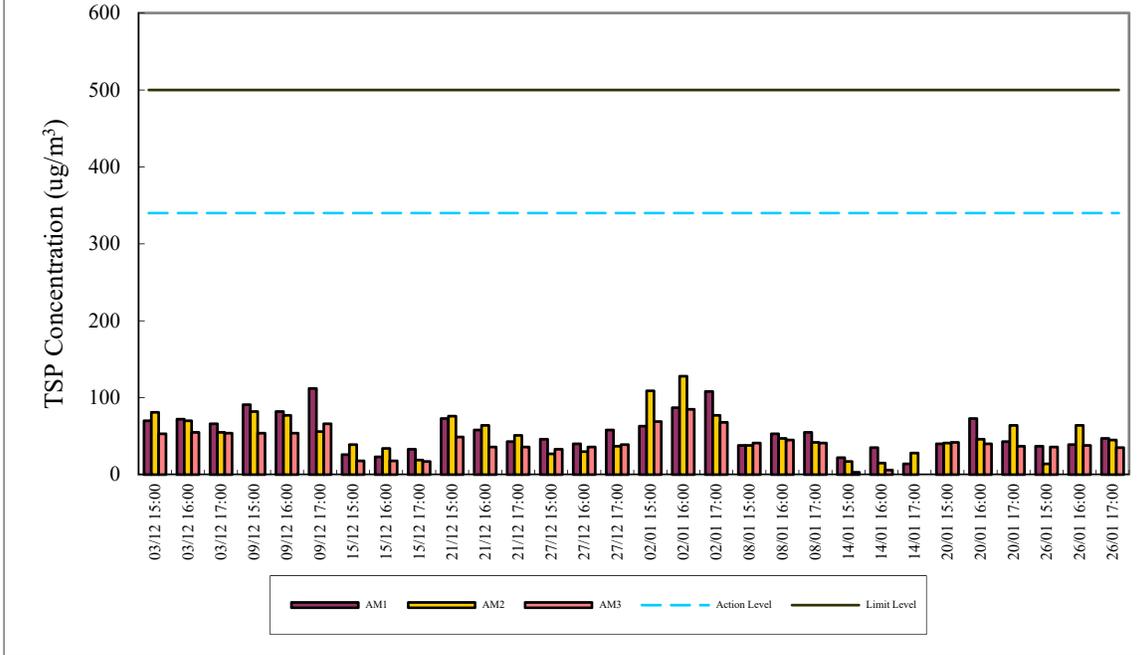

1-hr TSP Air Monitoring Data (Februray 2023 - March 2023)

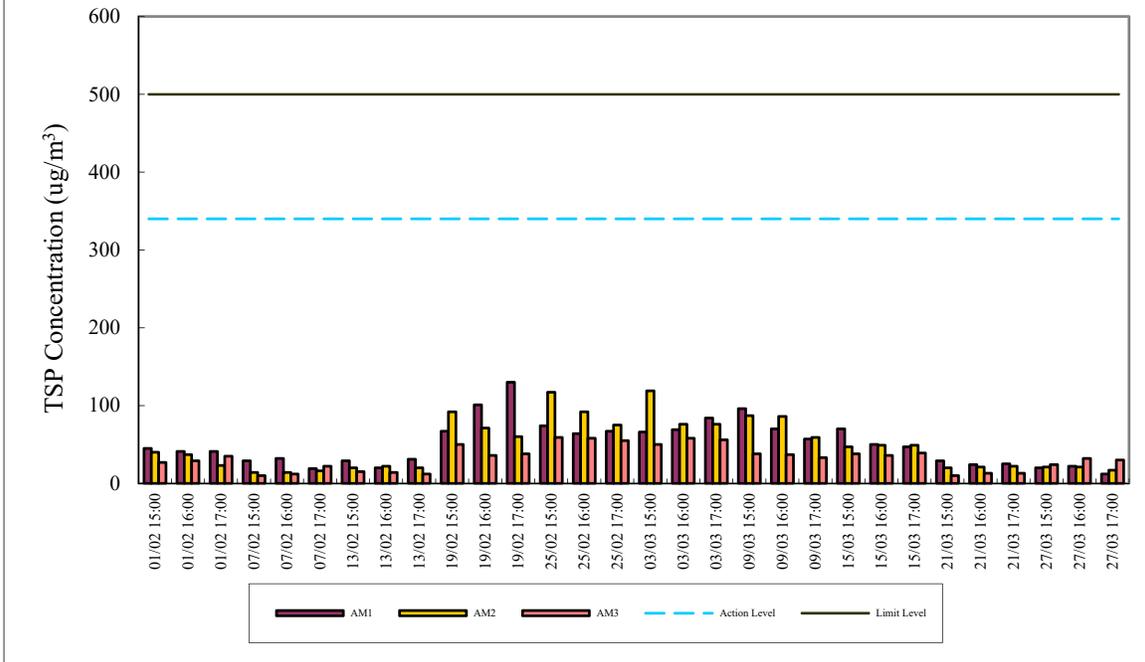

## Appendix E Continuous Noise Monitoring Results for March 2023



Site: Lamma Power Station Extension Construction  
 Measurement Location: Ash Lagoon and Ching Lam  
 Measurement Parameter: 30-min Leq (07:00-19:00 hrs on normal weekdays)  
 5-min Leq (07:00-23:00 hrs on holidays and  
 19:00-23:00 hrs on all other days, and 23:00-  
 07:00 hrs of next day)  
 Noise Equipment: B&K 2250 sound level meters and B&K 4231 sound  
 Level calibrator  
 Lab. Calibration Date: B&K 2250 sound level meters - 21/10/2021 (Ash Lagoon)  
 03/09/2021 (Ching Lam)  
 B&K 4231 calibrator (17/10/2022)

Date	Time	Calculated Noise Level at NSR at Long Tsai Tsuen/Hung Shing Ye (dB(A))		Limit Noise Level (dB(A))	Calculated Noise Level at NSR at the school within Tai Wan San Tsuen (dB(A))		Limit Noise Level (dB(A))
		Max	Avg		Max	Avg	
01/03/2023	07:00-19:00	---	---	75	---	---	70
01/03/2023	19:00-23:00	30	30	60	47	42	60
01/03/2023	23:00-07:00	40	37	45	30	30	45
02/03/2023	07:00-19:00	---	---	75	27	27	70
02/03/2023	19:00-23:00	---	---	60	---	---	60
02/03/2023	23:00-07:00	40	34	45	37	29	45
03/03/2023	07:00-19:00	---	---	75	---	---	70
03/03/2023	19:00-23:00	32	32	60	42	35	60
03/03/2023	23:00-07:00	37	37	45	41	34	45
04/03/2023	07:00-19:00	40	40	75	30	30	70
04/03/2023	19:00-23:00	---	---	60	42	39	60
04/03/2023	23:00-07:00	31	30	45	40	30	45
05/03/2023	07:00-23:00	47	37	60	41	35	60
05/03/2023	23:00-07:00	36	36	45	37	32	45
06/03/2023	07:00-19:00	---	---	75	32	32	70
06/03/2023	19:00-23:00	---	---	60	35	32	60
06/03/2023	23:00-07:00	44	34	45	42	36	45
07/03/2023	07:00-19:00	54	50	75	42	34	70
07/03/2023	19:00-23:00	50	41	60	41	37	60
07/03/2023	23:00-07:00	44	34	45	38	29	45
08/03/2023	07:00-19:00	51	45	75	---	---	70
08/03/2023	19:00-23:00	---	---	60	47	43	60
08/03/2023	23:00-07:00	44	37	45	36	29	45
09/03/2023	07:00-19:00	56	56	75	36	36	70
09/03/2023	19:00-23:00	---	---	60	46	42	60
09/03/2023	23:00-07:00	41	35	45	41	31	45
10/03/2023	07:00-19:00	---	---	75	---	---	70
10/03/2023	19:00-23:00	---	---	60	45	42	60
10/03/2023	23:00-07:00	45	33	45	41	33	45
11/03/2023	07:00-19:00	50	49	75	---	---	70
11/03/2023	19:00-23:00	---	---	60	27	27	60
11/03/2023	23:00-07:00	41	32	45	39	32	45
12/03/2023	07:00-23:00	60	44	60	48	40	60
12/03/2023	23:00-07:00	41	37	45	37	32	45
13/03/2023	07:00-19:00	---	---	75	---	---	70
13/03/2023	19:00-23:00	---	---	60	43	41	60
13/03/2023	23:00-07:00	41	34	45	39	30	45


14/03/2023	07:00-19:00	45	45	75	---	---	70
14/03/2023	19:00-23:00	40	40	60	---	---	60
14/03/2023	23:00-07:00	42	37	45	41	33	45
15/03/2023	07:00-19:00	50	46	75	---	---	70
15/03/2023	19:00-23:00	52	48	60	34	30	60
15/03/2023	23:00-07:00	45	40	45	37	31	45
16/03/2023	07:00-19:00	---	---	75	---	---	70
16/03/2023	19:00-23:00	---	---	60	45	43	60
16/03/2023	23:00-07:00	41	37	45	41	36	45
17/03/2023	07:00-19:00	---	---	75	38	37	70
17/03/2023	19:00-23:00	---	---	60	39	32	60
17/03/2023	23:00-07:00	43	36	45	40	31	45
18/03/2023	07:00-19:00	40	40	75	---	---	70
18/03/2023	19:00-23:00	36	36	60	49	38	60
18/03/2023	23:00-07:00	37	35	45	44	39	45
19/03/2023	07:00-23:00	48	35	60	49	33	60
19/03/2023	23:00-07:00	38	34	45	41	38	45
20/03/2023	07:00-19:00	---	---	75	---	---	70
20/03/2023	19:00-23:00	---	---	60	48	40	60
20/03/2023	23:00-07:00	39	38	45	42	37	45
21/03/2023	07:00-19:00	52	51	75	34	34	70
21/03/2023	19:00-23:00	---	---	60	31	28	60
21/03/2023	23:00-07:00	42	36	45	44	34	45
22/03/2023	07:00-19:00	---	---	75	54	54	70
22/03/2023	19:00-23:00	---	---	60	---	---	60
22/03/2023	23:00-07:00	43	37	45	40	32	45
23/03/2023	07:00-19:00	34	34	75	33	33	70
23/03/2023	19:00-23:00	---	---	60	29	27	60
23/03/2023	23:00-07:00	45	43	45	42	36	45
24/03/2023	07:00-19:00	52	52	75	31	29	70
24/03/2023	19:00-23:00	---	---	60	40	31	60
24/03/2023	23:00-07:00	44	39	45	44	40	45
25/03/2023	07:00-19:00	37	37	75	42	42	70
25/03/2023	19:00-23:00	49	34	60	44	35	60
25/03/2023	23:00-07:00	42	36	45	45	38	45
26/03/2023	07:00-23:00	51	41	60	53	44	60
26/03/2023	23:00-07:00	45	37	45	43	38	45
27/03/2023	07:00-19:00	---	---	75	---	---	70
27/03/2023	19:00-23:00	---	---	60	---	---	60
27/03/2023	23:00-07:00	---	---	45	---	---	45
28/03/2023	07:00-19:00	62	54	75	39	39	65
28/03/2023	19:00-23:00	---	---	60	48	46	60
28/03/2023	23:00-07:00	45	39	45	45	38	45
29/03/2023	07:00-19:00	46	42	75	42	42	65
29/03/2023	19:00-23:00	50	43	60	38	34	60
29/03/2023	23:00-07:00	39	36	45	39	33	45
30/03/2023	07:00-19:00	39	34	75	35	28	65
30/03/2023	19:00-23:00	---	---	60	39	37	60
30/03/2023	23:00-07:00	40	38	45	41	33	45
31/03/2023	07:00-19:00	48	42	75	40	35	65
31/03/2023	19:00-23:00	33	33	60	39	30	60
31/03/2023	23:00-07:00	45	40	45	44	37	45

Note:


- a. "---" represents the measured noise monitoring data lower than the established notional background level/discarded under strong wind.
- b. Continuous noise monitoring was also carried out at holidays & evening-time (07:00-23:00 hrs on holidays and 19:00-23:00 hrs on all other days) and night-time (23:00-07:00 hrs of next day).

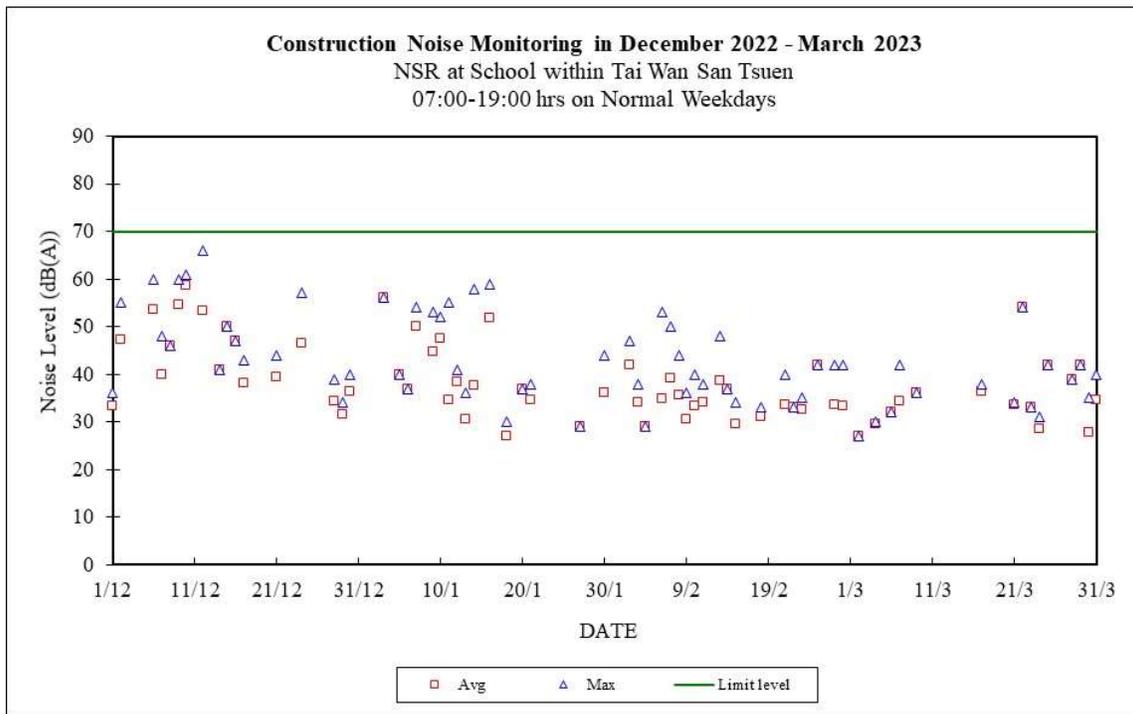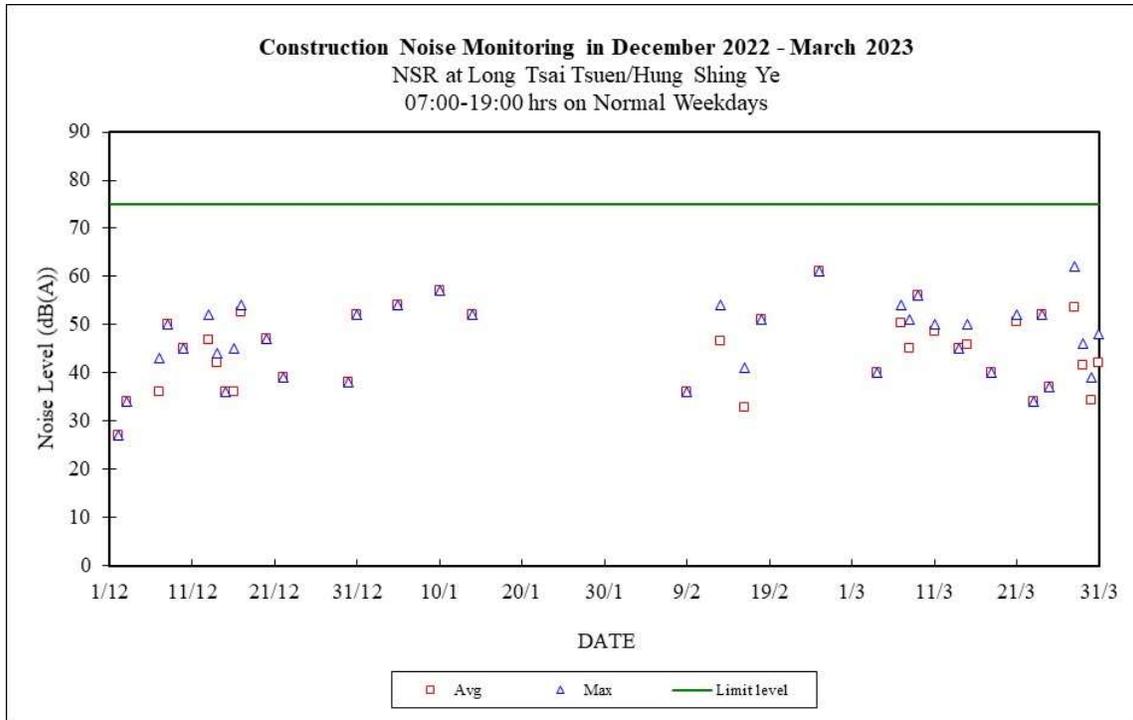


**Construction Noise Monitoring in December 2022 - March 2023**  
 NSR at Long Tsai Tsuen/Hung Shing Ye  
 07:00-23:00 hrs on Holidays and 19:00-23:00 hrs on All Other Days

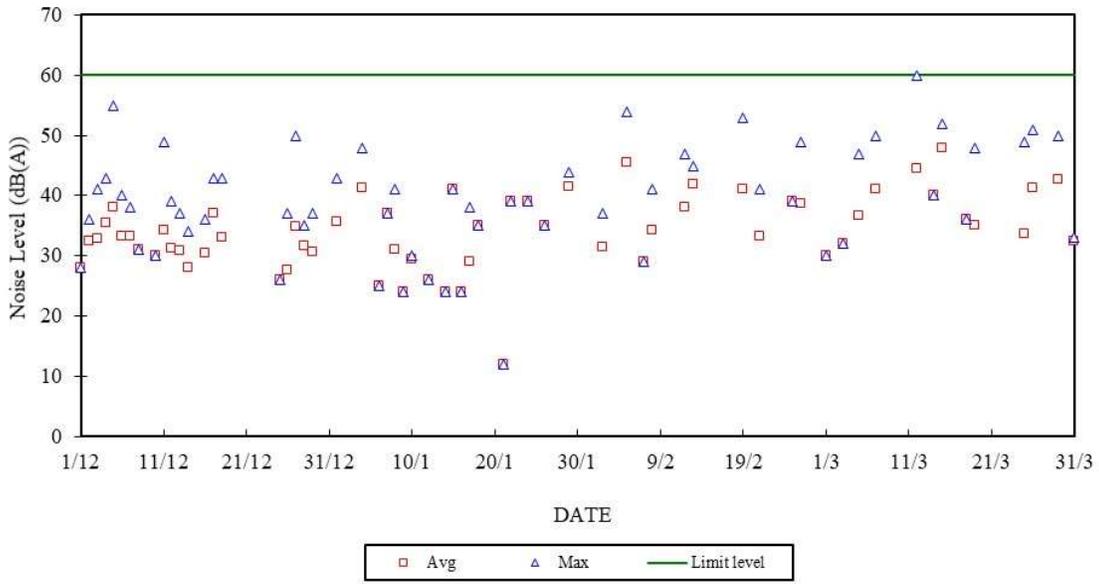


**Construction Noise Monitoring in December 2022 - March 2023**  
 NSR at School within Tai Wan San Tsuen  
 07:00-23:00 hrs on Holidays and 19:00-23:00 hrs on All Other Days

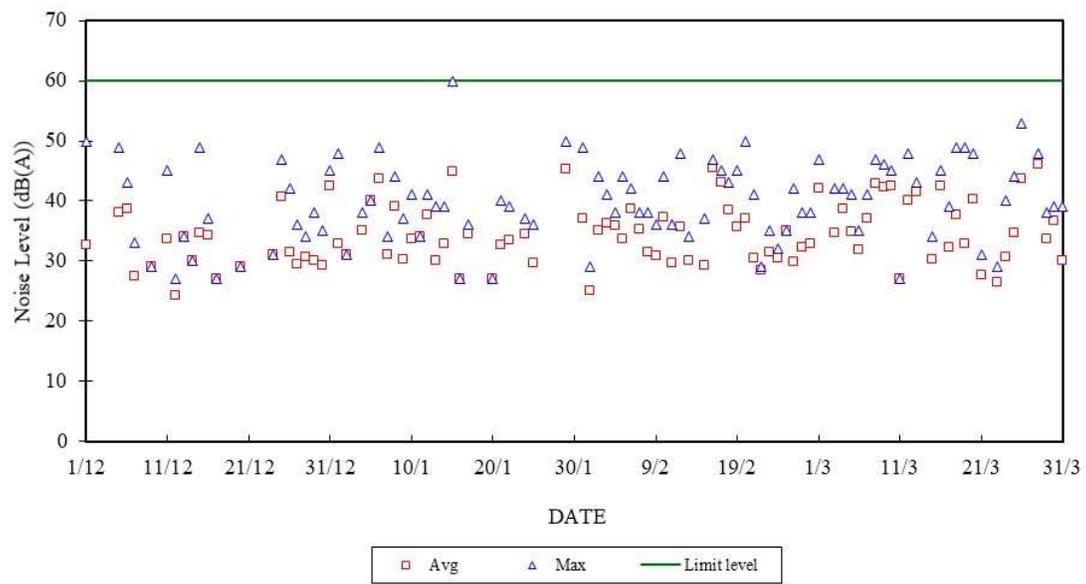

**Construction Noise Monitoring in December 2022 - March 2023**  
NSR at Long Tsai Tsuen/Hung Shing Ye  
23:00-07:00 hrs of Next Day

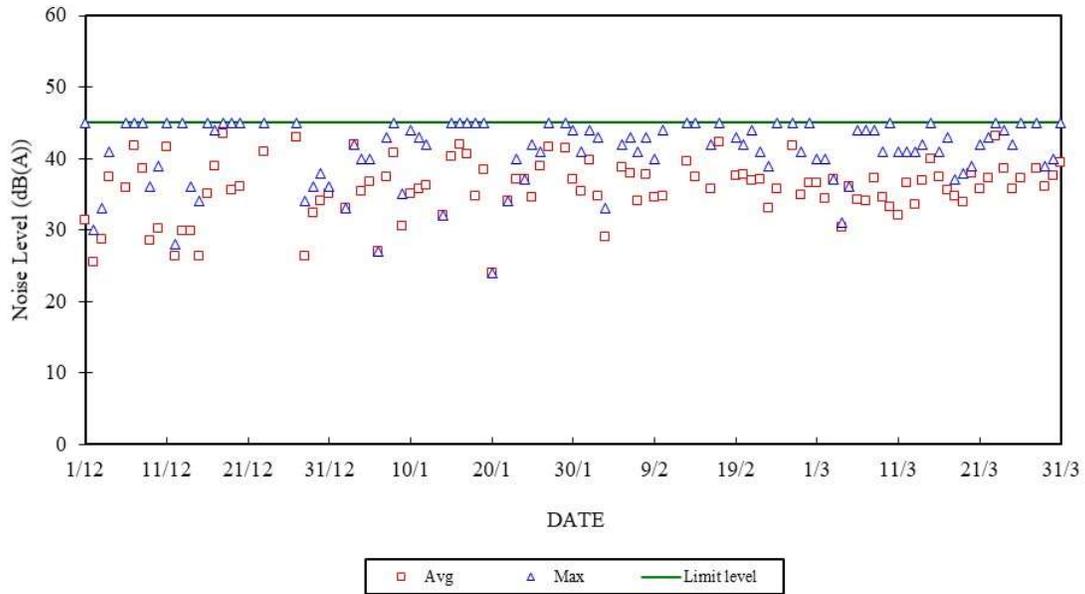

**Construction Noise Monitoring in December 2022 - March 2023**  
NSR at School within Tai Wan San Tsuen  
23:00-07:00 hrs of Next Day

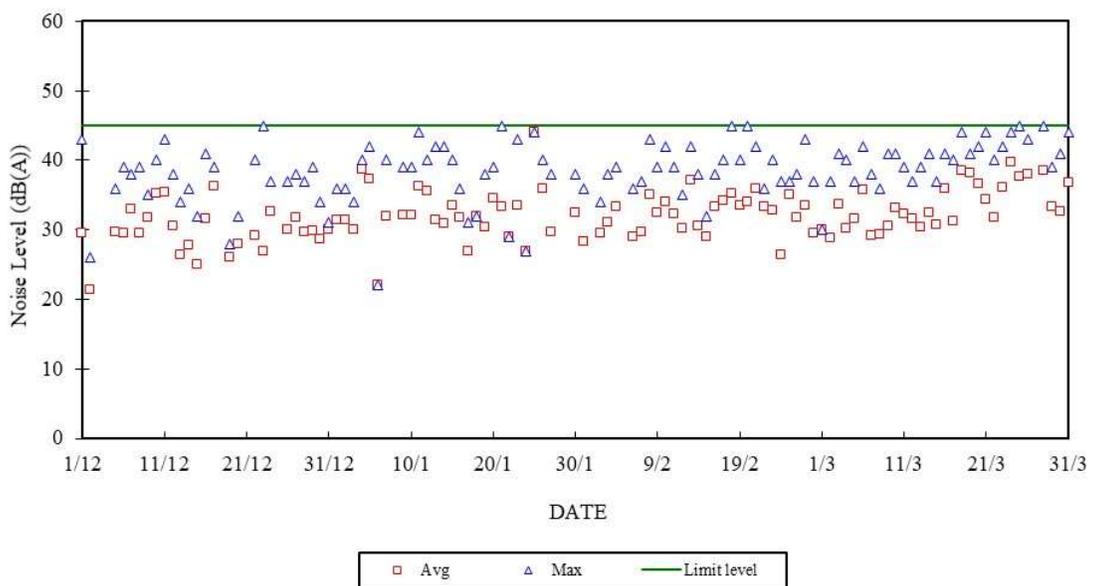

# Appendix F

The QA/QC Procedures and Results

**The Hongkong Electric Co., Ltd.**  
**Lamma Power Station Extension**  
**TEOM Continuous Dust Monitor**  
**Data Quality Assurance Log Sheet**

Month: March

Year: 2023

Reservoir (AM1)				
Date	Frequency (Hz) (240 - 275)	Operation Mode (Mode 4)	Main Flow (l/min) (2.70 - 3.30)	Bypass Flow (l/min) (12.30 - 15.04)
3/3/2023	267.534	4	2.99	10.31
9/3/2023	271.142	4	2.92	10.31
15/3/2023	270.132	4	2.94	10.31
21/3/2023	269.590	4	2.91	10.31
27/3/2023	269.242	4	2.98	10.31

East Gate (AM2)				
Date	Frequency (Hz) (240 - 275)	Operation Mode (Mode 4)	Main Flow (l/min) (2.70 - 3.30)	Bypass Flow (l/min) (12.30 - 15.04)
3/3/2023	264.844	4	3.00	13.66
9/3/2023	264.104	4	3.00	13.67
15/3/2023	263.221	4	3.00	13.67
21/3/2023	267.786	4	3.00	13.67
27/3/2023	267.432	4	3.00	13.66

Ash Lagoon (AM3)				
Date	Frequency (Hz) (240 - 275)	Operation Mode (Mode 4)	Main Flow (l/min) (2.70 - 3.30)	Bypass Flow (l/min) (12.30 - 15.04)
3/3/2023	256.908	4	2.36	13.68
9/3/2023	256.385	4	2.14	13.68
15/3/2023	255.817	4	1.94	13.68
21/3/2023	255.530	4	1.90	13.68
27/3/2023	257.546	4	2.52	13.69

Maintenance Record			
	Reservoir	East Gate	Ash Lagoon
TEOM Filter Exchange	✓	✓	✓
Clean TSP Inlet	✓	✓	✓
Replace flow in-line filter	✓	✓	✓
Pump Repair			
Leak Check			
Flow audit			
Flow Controller Calibration			
A/C filter cleaning			

Remarks:

Prepared by: Chris Chan

Checked by: HY Chan

The Hongkong Electric Co., Ltd.  
Mini Volume Air Sampler Site Visit Log Sheet

Attendance Log \_\_\_\_\_

Site Name: Tai Yuen Village (AM4)

Date/Time	Staff Name
10/03/2023 / 14:00	WM Tam / Brian So

Equipment / Item

Equipment / Item	Serial No. / No.
MINIVOL	5580
Used filter paper no.	MS49
New filter paper no.	MS50

Type of filter: Glass-fibre

- I. Calibration is performed by using Drycal DC-2 Flow Calibrator  
5 std. L/min set point is recommended

Before: 5.021  
After: 5.021 (No adjustment)

II. General Services

1. Clean Rotameter: Yes
2. Clean / Replace Pump Valves: No
3. Clean / Replace Pump Diaphragms: No
4. Clean Impaction Inlet: Yes
5. Replace Timer Battery Every 6 months: No
6. Replace Inlet Filter: Yes

Remarks

N/A

Conducted by: WM Tam / Brian So

Checked by: SM Hon

The Hongkong Electric Co., Ltd.  
Lamma Power Station Extension  
Noise Monitoring Station  
Site Visit Log Sheet

Location: Ching Lam

Date/Time	Staff Attended
17/3/2023 / 11:00	WM Tam/Pako Yu

Equipment	Serial No.
B&K 2250	3008903

1. Calibration

Acoustic calibrator: B&K 4231 (S/N: 3014754)

Noise level measured in calibration: 93.8 (94 ±1.0 dBA)

2. Weather Conditions

- a. Fine
- b. Calm

3. Remark/Observation

N/A

Prepared by: WM Tam

Checked by: TL Chu

**The Hongkong Electric Co., Ltd.**  
**Lamma Power Station Extension**  
**Noise Monitoring Station**  
**Daily Calibration Record**

Date	Location: Ash Lagoon	
	Calibration Results	Deviation from Reference (dB)
01/03/2023	Passed	-0.04
02/03/2023	Passed	-0.07
03/03/2023	Passed	-0.05
04/03/2023	Passed	-0.05
05/03/2023	Passed	-0.04
06/03/2023	Passed	-0.04
07/03/2023	Passed	-0.03
08/03/2023	Passed	-0.04
09/03/2023	Passed	-0.02
10/03/2023	Passed	-0.03
11/03/2023	Passed	-0.02
12/03/2023	Passed	-0.06
13/03/2023	Passed	-0.05
14/03/2023	Passed	-0.03
15/03/2023	Passed	-0.05
16/03/2023	Passed	-0.03
17/03/2023	Passed	-0.01
18/03/2023	Passed	-0.03
19/03/2023	Passed	-0.02
20/03/2023	Passed	0.01
21/03/2023	Passed	0.01
22/03/2023	Passed	-0.01
23/03/2023	Passed	-0.01
24/03/2023	Passed	-0.02
25/03/2023	Passed	-0.05
26/03/2023	Passed	-0.07
27/03/2023	Passed	-0.05
28/03/2023	Passed	-0.02
29/03/2023	Passed	-0.06
30/03/2023	Passed	-0.04
31/03/2023	Passed	-0.03

Remarks:

1. The B&K sound level meter at the noise monitoring station has an advanced feature of internal calibration checking (viz. Charge Injection Calibration (CIC)). CIC is a B&K patented method for in situ verification of the integrity of the entire sound measurement chain (including microphone, preamplifier and cabling).
2. The acceptance criterion of deviation from reference is  $\pm 0.5$  dB.

## Appendix G Event/Action Plans

Table G.1 Event and Action Plans for Air Quality

Event	Monitoring		Action	
	ET Leader	IEC	Engineer	Contractor
<b>Action Level</b>				
Exceedance of one sample	Identify source Inform Engineer and IEC verbally Repeat measurement to confirm finding	Check monitoring data submitted by ET and advise Engineer.	Notify Contractor Checking monitoring data and contractor's working methods	Rectify any unacceptable practice amend any working methods if appropriate
Exceedance of two or more consecutive samples	Identify source Inform Engineer and IEC verbally Repeat measurement to confirm finding Increase monitoring frequency Discuss with Engineer and Contractor on remedial actions required If exceedance continues, arrange meeting with Engineer If exceedance stops, discontinue additional monitoring	Check monitoring data submitted by ET and advise Engineer. Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Confirm receipt of notification of failure in writing Notify contractor Checking monitoring data and contractor's working methods Discuss proposed remedial actions with the ET and Contractor Ensure remedial actions properly implemented	Submit proposals for remedial actions to Engineer within 3 working days of notifications Implement the agreed proposals Amend proposal if appropriate
<b>Limit level</b>				
Exceedance of one sample	Repeat measurement to confirm finding. Identify the source(s) of the impact. If the exceedance is found to be valid and due to the Construction works, verbally advise the Contractor, Engineer and IEC, and inform the EPD of the exceedance, as soon as practicable. Increase monitoring frequency to daily Assess the effectiveness of the contractor's remedial actions and keep Engineer, IEC and EPD informed of the results	Check monitoring data submitted by ET and advise Engineer Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Confirm receipt of notification of failure in writing Notify Contractor Checking monitoring data and Contractor's working method Discuss with ET and Contractor on remedial actions to be provided Ensure remedial measures properly implemented	Take immediate action to avoid further exceedance Submit proposals for remedial actions to Engineer within 3 working days of notifications Implement the agreed proposals Amend proposal if appropriate
Exceedance of two or more	Identify source	Provide feedback to the Engineer on the remedial actions proposed by the	Confirm receipt of notification of	Take immediate action to

Event	Monitoring			Action		
	ET Leader	IEC	Engineer	Contractor		
consecutive samples	<p>If the exceedance is found to be valid and due to the construction works, verbally advise the Contractor, Engineer and IEC, and inform the EPD of the exceedance as soon as practicable.</p> <p>Repeat measurement to confirm finding</p> <p>Increase monitoring frequency to daily</p> <p>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented</p> <p>Arrange meeting with Engineer and Contractor to discuss the remedial actions to be taken</p> <p>If exceedance stops, discontinue additional monitoring</p>	<p>ET / Contractor</p> <p>Advise Engineer on the effectiveness of the proposed remedial measures</p> <p>Verify the implementation of the remedial measures</p>	<p>failure in writing</p> <p>Checking monitoring data and Contractor's working methods</p> <p>Notify Contractor</p> <p>Discuss proposed remedial actions with ET and Contractor</p> <p>Ensure remedial measures properly implemented</p> <p>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop the portion of work until the exceedance is abated</p>	<p>avoid further exceedance</p> <p>Submit proposals for remedial actions to Engineer within 3 working days of notifications</p> <p>Implement the agreed proposals</p> <p>Resubmit proposals if problem still not under control</p> <p>Stop the relevant portion of works as determined by the Engineer until the exceedance is abated</p>		

Table G.2 Event and Action Plans for Construction Noise

Exceedance	ET Leader	IEC	Engineer	Contractor
<b>Action Level</b>	Undertake noise measurement/check monitoring data to establish validity of complaint.	Review the analysed results submitted by the ET.	Notify Contractor of the complaint if proven.	Submit proposals for remedial actions to Engineer.
	If the complaint is valid, inform Engineer and IEC verbally.	Review the remedial measures proposed by the Contractor and advise the Engineer and ET accordingly.	Check Contractor's working methods and advise IEC and ET accordingly.	Amend proposals if required by the Engineer.
	Identify the source(s) of the noise.	Verify the implementation of the remedial measures.	Remind the Contractor of his contractual obligations and discuss remedial actions.	Implement the remedial actions immediately upon instruction from the Engineer.
	Discuss remedial actions required with Contractor and Engineer.		Keep the Contractor informed of the efficacy of remedial actions.	Liaise with the Engineer to optimise the effectiveness of the agreed mitigation.
	Increase manual monitoring frequency to assess efficacy of remedial measures.			
	If exceedance continues, review implementation of appropriate mitigation measures.			
<b>Limit Level</b>	Repeat manual measurement/check monitoring data to confirm findings.	Agree potential remedial actions with Engineer, ET and Contractor.	Notify Contractor of exceedance.	Take immediate action to avoid further exceedance.
	Identify the source(s) of the impact. If the exceedance is found to be valid and due to the Construction works, verbally advise the Contractor, Engineer and IEC, and inform the EPD of the exceedance, as soon as practicable.	Review Contractor's remedial actions / measures to ensure their effectiveness and advise the Engineer and ET accordingly.	Check Contractor's working methods and advise IEC and ET accordingly.  Discuss with Contractor the remedial actions to be implemented.	Submit proposals for remedial actions to Engineer.  Amend proposals if required by the Engineer.
	Discuss remedial actions required with Engineer.	Verify the implementation of the remedial measures	Keep the Contractor informed of the efficacy of remedial actions. If the exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop the portion of work until the exceedance is abated	Implement remedial actions immediately upon instruction from the Engineer. If the exceedance continues, consider what portion of the work is responsible and, as instructed by the Engineer, stop the portion of work until the exceedance is abated
	Increase manual monitoring frequency to assess efficacy of remedial measures.			

Table G.3 Event and Action Plans for Water Quality

<b>Exceedance</b>	<b>ET Leader</b>	<b>IEC</b>	<b>Engineer</b>	<b>Contractor</b>
Action level exceeded on one sampling day	Verbally inform the Contractor, and IEC. Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with Engineer and Contractor; Repeat measurement on next day of exceedance.	Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Discuss with Contractor the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures.	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Propose and discuss mitigation measures with Engineer; Implement the agreed mitigation measures.
Action level exceeded on more than one consecutive sampling day	Repeat in-situ measurements to confirm findings; Identify source(s) of impact; Inform Contractor and IEC; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measure with Engineer and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; Repeat measurement on next day of exceedance.	Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Discuss with ET and Contractor on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures.	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Propose mitigation measures to Engineer within 3 working days and discuss with ET and Engineer; Implement the agreed mitigation measures.
Limit level exceeded on one sampling day	Verbally inform the Contractor, IEC and the EPD of the exceedance; Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Check monitoring data, all plant,	Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor Advise Engineer on the effectiveness of the proposed remedial measures Verify the implementation of the remedial measures	Discuss with Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Propose mitigation measures to Engineer

<b>Exceedance</b>	<b>ET Leader</b>	<b>IEC</b>	<b>Engineer</b>	<b>Contractor</b>
	<p>equipment and Contractor's working methods;</p> <p>Discuss mitigation measure with Engineer and Contractor;</p> <p>Ensure mitigation measures are implemented;</p> <p>Increase the monitoring frequency to daily until no exceedance of Limit level.</p>		<p>implemented mitigation measures.</p>	<p>within 3 working days and discuss with Engineer;</p> <p>Implement the agreed mitigation measures.</p>
<p>Limit level exceeded by more than one consecutive sampling day</p>	<p>Repeat in-situ measurement to confirm findings;</p> <p>Identify source(s) of impact;</p> <p>Inform Contractor, IEC and EPD;</p> <p>Check monitoring data, all plant, equipment and Contractor's working methods;</p> <p>Discuss mitigation measure with Engineer and Contractor;</p> <p>Ensure mitigation measures are implemented;</p> <p>Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.</p>	<p>Provide feedback to the Engineer on the remedial actions proposed by the ET / Contractor</p> <p>Advise Engineer on the effectiveness of the proposed remedial measures</p> <p>Verify the implementation of the remedial measures</p>	<p>Discuss with Contractor on the proposed mitigation measures;</p> <p>Request Contractor to critically review the working methods;</p> <p>Make agreement on the mitigation measures to be implemented;</p> <p>Assess the effectiveness of the implemented mitigation measures;</p> <p>Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine works until no exceedance of the Limit Level.</p>	<p>Inform the Engineer and confirm notification of the non-compliance in writing;</p> <p>Rectify unacceptable practice;</p> <p>Check all plant and equipment; Consider changes of working methods;</p> <p>Propose mitigation measures to Engineer within 3 working days and discuss with Engineer;</p> <p>Implement the agreed mitigation measures..</p> <p>As directed by the Engineer, to slow down or to stop all or part of the marine work</p>

## **Appendix H Summary of Site Audit Findings**

### L12 Civil and Building Works

Dates of Inspection: 7/3/2023, 14/3/2023, 21/3/2023 and 28/3/2023.

#### Summary of Findings

##### *General*

- No environmental deficiency identified.

##### *Air Quality*

- No environmental deficiency identified.

##### *Noise*

- No environmental deficiency identified.

##### *Water Quality*

- No environmental deficiency identified.

##### *Waste Management*

- No environmental deficiency identified.

L12 Mechanical, Electrical, Instrumentation & Control Erection Works

Dates of Inspection: 2/3/2023, 9/3/2023, 16/3/2023, 23/3/2023 and 30/3/2023

Summary of Findings

*General*

- No environmental deficiency identified.

*Air Quality*

- No environmental deficiency identified.

*Noise*

- No environmental deficiency identified.

*Water Quality*

- No environmental deficiency identified.

*Waste Management*

- No environmental deficiency identified.

## Summary of EMIS

### Power Station – (Part B of EIA Report)

#### Construction Phase Mitigation Measures and their Implementation

EM&A Log Ref.	Mitigation Measures	Implementation Status
	<b>AIR QUALITY</b>	
A1	For general construction works, the dust control measures stipulated under the Air Pollution Control (Construction Dust) Regulation shall be complied with, such as: <ul style="list-style-type: none"> <li>the haul roads shall be sprayed with water to keep the entire road surface wet.</li> <li>the load carried by vehicle shall be covered by impervious sheeting to ensure no leakage of dusty materials from the vehicle.</li> <li>the heights from which fill materials are dropped shall be controlled to a practical level to minimise the fugitive dust arising from unloading.</li> </ul>	C C C
A2	For the concrete batching plant, the following control measures are recommended: <ul style="list-style-type: none"> <li>loading, unloading, handling, transfer or storage of any dusty materials shall be carried out in a totally enclosed system.</li> <li>The materials which may generate airborne dust emissions shall be wetted by water spray system.</li> <li>All receiving hoppers shall be enclosed on three sides up to 3m above unloading point.</li> <li>All conveyor transfer points shall be totally enclosed.</li> </ul>	N/A N/A N/A N/A
	<b>WATER QUALITY</b>	
B1	Silt curtains shall be installed on the eastern, southern and north western sides of the reclamation site during dredging for the reclamation construction. This is a required mitigation measure for the construction works and shall be implemented prior to the commencement of bulk dredging. **	N/A
B3	As a necessary operational constraint combined bulk dredging and sand filling for site formation shall not be permitted at any time. In addition, sand filling for site platform shall take place behind constructed sea walls which pierce the water surface. **	N/A
B4	HEC shall ensure design to divert all storm drains away from Hung Shing Ye Bay. **	N/A
B5	Sand fill for the rubble mound seawalls shall be placed by controlled pumping down the trailer arm. **	N/A
B6	EM&A shall confirm the acceptability of any impacts during construction and should any unacceptable impacts be found then one or more of the following mitigation measures shall be implemented: ** <ul style="list-style-type: none"> <li>reducing the number of dredgers working at any one time;</li> <li>reducing the rate of working of the dredgers;</li> <li>temporary suspension of operations;</li> <li>phasing of the works so that dredging / filling is only undertaken at certain stages of the tidal cycle.</li> </ul>	N/A



EM&A Log Ref.	Mitigation Measures	Implementation Status
<b>WASTE MANAGEMENT</b>		
E1	HEC to submit a Waste Management Plan for the construction phase to EPD. The Plan shall be verified by the IEC and shall describe the arrangements for avoidance, reuse, recovery and recycling, storage, collection, treatment and disposal of different categories of waste to be generated from the construction activities and shall take into account the recommendations of the EIA report.	C
<i>Dredging Waste</i>		
E2	All vessels for marine transportation of dredged sediment shall be fitted with tight fitting seals to their bottom openings to prevent leakage of materials. In addition, loading of barges and hoppers shall be controlled to prevent splashing of dredged material into the surrounding water, and barges or hoppers should under no circumstances be filled to a level which shall cause the overflowing of materials or polluted water during loading or transportation**	N/A
<i>Storage, Collection and Transport of Waste</i>		
E3	<ul style="list-style-type: none"> <li>Minimise windblown litter and dust during transportation by either covering trucks or transporting wastes in enclosed containers.</li> </ul>	C
	<ul style="list-style-type: none"> <li>Obtain the necessary waste disposal permits from the appropriate authorities, if they are required, in accordance with the Waste Disposal Ordinance (Cap.354), Waste Disposal (Chemical Waste) (General) Regulation (Cap.354), the Crown Land Ordinance (Cap 28), Dumping at Sea Ordinance (Cap 466) and Work Branch Technical Circular No. 22/92, Marine Disposal of Dredged Mud.</li> </ul>	C
	<ul style="list-style-type: none"> <li>Disposal of waste at Licensed sites;</li> </ul>	C
	<ul style="list-style-type: none"> <li>Develop procedures such as a ticketing system to facilitate tracking of marine mud and chemical waste, and to ensure that illegal disposal does not occur;</li> </ul>	C
	<ul style="list-style-type: none"> <li>Segregate and sort the waste materials into 3 categories:               <ul style="list-style-type: none"> <li>public fill (e.g. concrete and rubble) for re-use on-site or disposal at a public filling area;</li> <li>re-use and/or recycling waste (e.g. steel and other metals);</li> <li>waste which cannot be re-used and/or recycled (e.g. wood, glass and plastic) for landfill disposal.</li> <li>The sorting process shall be carefully monitored to avoid missing of the 3 categories. Different types of wastes shall be stockpiled and stored in different containers or skips to enhance re-use or recycling of materials and their proper disposal.</li> </ul> </li> <li>Maintain records of the quantities of wastes generated and disposed off-site for each category of waste.</li> </ul>	C
E4	Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes	C
<b>LAND CONTAMINATION</b>		
F1	No land Contamination mitigation measures are required during the construction phase.	N/A
<b>MARINE ECOLOGY</b>		

<b>EM&amp;A Log Ref.</b>	<b>Mitigation Measures</b>	<b>Implementation Status</b>
G1	All percussive piling works shall be conducted on reclaimed land to avoid noise impact to marine mammals**	N/A
G2	All construction related vessels shall approach the extension site from the north and via the East Lamma Channel to avoid disturbance to the finless porpoise**	N/A
G3	Rubble mound seawall to the south and west edges of the reclamation to enhance recolonisation of marine organisms**	N/A
G4	Artificial Reefs of a volume not less than 400 m <sup>3</sup> shall be deployed in a location to be decided upon consultation with the Director of Agriculture and Fisheries to serve the purpose of an Additional Habitat Enhancement Measure.**	N/A
<b>FISHERIES</b>		
H1	No Fisheries-specific mitigation measures are required during the construction phase.	N/A
<b>RISK ASSESSMENT</b>		
I1	No risk mitigation measures are required during the construction phase.	N/A

## Remarks:

- \*\* - No dredging and reclamation work would be involved for L12 construction  
C - Compliance with mitigation measure  
NC - Non-compliance with mitigation measure  
N/A - Not Applicable

**Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12** **Master Programme**

ID	Task Name	Duration	Start	Finish	Mar	1st Quarter	Apr	May	Jun
<b>1</b>	<b>KEY DATES &amp; MILESTONES</b>	<b>1123 days</b>	<b>Fri 4/12/20</b>	<b>Sun 31/12/23</b>					
2	Contract Period	1123 days	Fri 4/12/20	Sun 31/12/23					
3	Deferred Work Completion Key Dates	784 days	Mon 8/11/21	Sun 31/12/23					
4	Substantial Completion of the Whole Contract Works (1123 Days)	0 days	Sun 31/12/23	Sun 31/12/23					
<b>5</b>	<b>SITE POSSESSION DATES</b>	<b>513 days</b>	<b>Fri 4/12/20</b>	<b>Sun 1/5/22</b>					
6	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Fri 4/12/20	Fri 4/12/20					
7	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Fri 1/1/21	Fri 1/1/21					
8	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Sat 1/5/21	Sat 1/5/21					
9	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Fri 1/10/21	Fri 1/10/21					
10	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Fri 1/4/22	Fri 1/4/22					
11	Site Possession Date as phased site possession plan and PS1.4.2	0 days	Sun 1/5/22	Sun 1/5/22					
<b>12</b>	<b>COMPLETION DATES as per PS1.4.2 Time for Completion</b>	<b>838 days</b>	<b>Thu 30/9/21</b>	<b>Tue 16/1/24</b>					
13	Section A1 (i) - Area south of L12 MSB and L12 HRSG from GL12-F eastwards leading to Chimney Road Area F1	0 days	Thu 30/9/21	Thu 30/9/21					
14	Section A1 (ii) - Supporting structures for overhead cranes of L12 MSB including the associated roof structures except the roof deferred works	0 days	Mon 1/11/21	Mon 1/11/21					
15	Section A2 (i) External Works including CW Inlet Culvert at Area F8A	0 days	Fri 28/7/23	Fri 28/7/23					
16	Section A2 (ii) External Works including CW Inlet Culvert at Area F8B	0 days	Tue 16/1/24	Tue 16/1/24					
17	Section A2 (iii) External Works including CW Inlet Culvert at Area F8C	0 days	Sat 28/10/23	Sat 28/10/23					
18	Section B1 - Area south of L12 MSB from GL12-F westwards leading to Station Road at Area F3	0 days	Wed 15/12/21	Wed 15/12/21					
19	Section B2 (i) - Southern Part of L12 HRSG areas and its surrounding refer to Area F6B as shown in drawing no 553/03/2040 including the foundations for Gas Exhaust Duct	0 days	Thu 30/9/21	Thu 30/9/21					
20	Section B2 (ii) - Remaining northern part of L12 HRSG area and its surrounding at Area F6A and F6C	0 days	Mon 15/11/21	Mon 15/11/21					
21	Section B2 - (iii) L12 Turbo Block foundation including the L12 MSB ground floor together with the equipment foundations between GL 12-F to 12-H and 12-1 to 12-6 for the installation of power generator, air inlet duct and lube oil reservoir	0 days	Mon 28/2/22	Mon 28/2/22					
22	Section B2 - (iv) G/F of L12 MSB including the Condenser Pit, Circulating Water Pipe Pit and equipment foundations between GL 12-B to 12-C and 12-1 to 12-6 for the installation of condenser	0 days	Wed 15/12/21	Wed 15/12/21					
23	Section C - (i) Roads and external grounds surrounding L12 MSB and L12 HRSG in addition to the southern & eastern areas mentioned above in Area F5	0 days	Sat 15/1/22	Sat 15/1/22					
24	Section C - (ii) Whole of L12 MSB including the pipe and cable rack along south facade of L12 MSB with all underground utilities at Area F4 including C.W. Inlet and Outlet Culvert except the deferred works	0 days	Tue 30/5/23	Tue 30/5/23					Section C - (ii) Whole of L12 MSB Incl
25	Section C - (iii) Link Bridge between L11 and L12 MSB including their associated A&A at L11 MSB	0 days	Sun 7/5/23	Sun 7/5/23					Section C - (iii) Link Bridge between L11 and L12 MSB including the
26	Section D - (i) Microwave Antenna Room and Chimney Windshiled for the installation of microwave equipment and antenna	0 days	Fri 10/6/22	Fri 10/6/22					Section D
27	Section D (ii) - No. 5 Chimney with L12 Steel Flue liner	0 days	Wed 21/6/23	Wed 21/6/23					
28	Section E (i) - Tx Room of Administration and Control Building	0 days	Sun 31/10/21	Sun 31/10/21					
29	Section E (ii) - G/F, 1/F, 2/F & Hoisting Well of Admin. & Control Building	0 days	Mon 28/2/22	Mon 28/2/22					
30	Section E (iii) - Whole of Admin. And Control Building	0 days	Tue 31/5/22	Tue 31/5/22					
31	Section F (i) - Gas Receiving Station and L12 Gas Receiving Station Equipment Room (GRS) Area Extension at Area F14	0 days	Sun 9/4/23	Sun 9/4/23					Section F (i) - Gas Receiving Station and L12 Gas Receiving Station Equipment Room (GRS) Area Extension
32	Section F (ii) - Pipe and Cable rack and external work at Area F9A and F9B	0 days	Mon 31/7/23	Mon 31/7/23					
33	Section F (iii) - No. 5 CW Equipment Room, pipe and cable rack, external works at Area F10	0 days	Wed 5/7/23	Wed 5/7/23					
34	Section G (i) - External Work surrounding Area F11	0 days	Tue 31/10/23	Tue 31/10/23					
35	Section G (ii) - External Works at Area F12 & F13	0 days	Fri 20/10/23	Fri 20/10/23					
36	Section G (iii) - FS Modification works along South Seafront Road at Area F15	0 days	Fri 30/9/22	Fri 30/9/22					
37	Section G (iv) - 275kV cable trenches and External Works at Area F16	0 days	Mon 14/8/23	Mon 14/8/23					
38	Section G (v) - Shunt Reactor Compound and External Works at Area F17	0 days	Sat 3/6/23	Sat 3/6/23					Section G (v) - Shunt Reactor Co
39	Section G (vi) - 275kV cable trenches and External Works at Area F18	0 days	Wed 1/6/22	Wed 1/6/22					
40	Section G (vii) - Flood Wall at No. 4 CW Intake Area along HUA at Area F20A	0 days	Tue 14/2/23	Tue 14/2/23					Flood Wall at No. 4 CW Intake Area along HUA at Area F20A
41	Section G (viii) - Flood wall at No. 5 CW Intake Area along HUA at Area F20B	0 days	Sat 30/9/23	Sat 30/9/23					
42	Section G (ix) - Bund wall modification works at South Seafront Road at Area F21	0 days	Fri 15/10/21	Fri 15/10/21					
43	Section G (x) - DAX Cable Diversion Works (from Part I to Part IV)	0 days	Sun 16/7/23	Sun 16/7/23					
44	Section H - All remaining works shall be completed for reporting completion to BD and ready for OP inspection	0 days	Sat 1/7/23	Sat 1/7/23					
<b>45</b>	<b>GENERAL &amp; PRELIMINARY</b>	<b>228 days</b>	<b>Fri 4/12/20</b>	<b>Mon 19/7/21</b>					
46	First Mobilization	18 days	Fri 4/12/20	Mon 21/12/20					
47	Set up Temporary Site Office and Welfare Facilities	90 days	Tue 22/12/20	Sun 21/3/21					
48	Permit Applications & Statuary Submissions	120 days	Mon 22/3/21	Mon 19/7/21					
49	Existing Utilities scanning & Excavation Permit	45 days	Tue 22/12/20	Thu 4/2/21					
50	Tower Crane erections	60 days	Sun 27/12/20	Wed 24/2/21					
<b>51</b>	<b>TECHNICAL SUBMISSION AND APPROVAL</b>	<b>1021 days</b>	<b>Thu 10/12/20</b>	<b>Wed 27/9/23</b>					
52	BD Approval & Consent (If required)	0 days	Thu 10/12/20	Thu 10/12/20					
53	Submission and Approval of Master Programme	14 days	Fri 11/12/20	Thu 24/12/20					
54	Work Execution Overall Plan submission & approval	14 days	Fri 11/12/20	Thu 24/12/20					
55	Material Submissions and approval	300 days	Fri 25/12/20	Wed 20/10/21					
56	Method Statement submission and approval	300 days	Fri 25/12/20	Wed 20/10/21					
57	BIM Model, CSD & CBWD Submission & approval	120 days	Fri 25/12/20	Fri 23/4/21					
58	Structure Steelwork Connection Design Submission & BD approval	45 days	Tue 29/12/20	Thu 11/2/21					
59	Structure Steelwork Shop Drawing & Approval	30 days	Fri 12/2/21	Sat 13/3/21					
60	Metal Cladding, louvre & windows submission & BD approval	45 days	Tue 29/12/20	Thu 11/2/21					
61	Metal Cladding, louvre & windows shop drawing submission	45 days	Fri 12/2/21	Sun 28/3/21					
62	Order, Off Site Fabrication and Delivery (S. Steel & Cladding & louvres)	120 days	Mon 29/3/21	Mon 26/7/21					
63	ELS Submission and BD approval	90 days	Fri 11/12/20	Wed 10/3/21					
64	No. 5 Chimney windshield temporary work submission, approval & fabrication	60 days	Fri 11/12/20	Mon 8/2/21					
65	Steel Flue Assessment Report and Design Drawings submission & approval	60 days	Tue 9/2/21	Fri 9/4/21					
66	Folding Shutters Shop Drawing Submission & Approval	30 days	Thu 11/2/21	Fri 12/3/21					
67	Fabrication & Delivery of Folding Shutters	180 days	Sat 13/3/21	Wed 8/9/21					
68	Sewage Pump System Design submission & approval	45 days	Wed 15/2/23	Fri 31/3/23					Sewage Pump System Design submission & approval
69	Fabrication & Delivery of Sewage Pump	180 days	Sat 1/4/23	Wed 27/9/23					
70	Other material submission & approval & delivery	180 days	Sat 24/4/21	Wed 20/10/21					
71	Other material submission & approval & delivery	180 days	Sat 24/4/21	Wed 20/10/21					
<b>72</b>	<b>CONSTRUCTION</b>	<b>1139 days</b>	<b>Fri 4/12/20</b>	<b>Tue 16/1/24</b>					
73	Coordination with the Employer's Specialist Contractors	562 days	Fri 15/1/21	Sat 30/7/22					
74	Installation of Puddle Pipes at C.W. outlet Culvert	7 days	Mon 22/3/21	Sun 28/3/21					
75	Installation of Puddle Pipes at C.W. Inlet Culvert	7 days	Thu 27/5/21	Wed 2/6/21					
76	Template setting at L12 Turbo Block Foundation	45 days	Tue 16/11/21	Thu 30/12/21					
77	Template setting of holding down bolts at HRSG column base	45 days	Fri 15/1/21	Sun 28/2/21					
78	I-beam / channel base installation on top of transformer foundations at Transformer Area	45 days	Tue 1/6/21	Thu 15/7/21					
79	Overhead crane erection at turbine hall using access through a temporary opening at L12 MSB roof between GL12-G to 12-H and 12-2 to 12-6	38 days	Mon 1/11/21	Wed 8/12/21					
80	Condenser assembly and erection using access through a temporary facade opening at L12 MSB below 1/F along GL 12-6 from GL12-B to 12-C including a clear space below 1/F between GL 12-B to 12-C	122 days	Thu 16/12/21	Sat 16/4/22					

MASTER PROGRAMME  
Rev 1-B 23 Aug 2021



Task █ Split █ Milestone ◆ Summary █

**Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12** **Master Programme**

ID	Task Name	Duration	Start	Finish	Mar	1st Quarter	Apr	May	Jun
81	Installation of power train equipment including air inlet duct using access through a temporary façade opening at L12 MSB below 1/F along GL 12-6 from GL12-F to 12-H including a clear space below 1/F of the above area	121 days	Fri 1/4/22	Sat 30/7/22					
82	Installation of embedded materials such as holding down bolts for equipment foundations - Commencement	0 days	Thu 15/4/21	Thu 15/4/21					
83	<b>Section A1 (i) - Area south of L12 MSB and L12 HRSBG from GL12-F eastwards leading to Chimney Road at Area F1 &amp; F2</b>	<b>301 days</b>	<b>Fri 4/12/20</b>	<b>Thu 30/9/21</b>					
84	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21					
85	Subletting / Fabrication / Delivery (both for Area F1 and Area F2)	60 days	Sun 17/1/21	Wed 17/3/21					
86	Excavation for CW Inlet Culvert (Type D Construction Area)	14 days	Tue 1/6/21	Mon 14/6/21					
87	Installation CW Inlet Culvert pipe	70 days	Tue 15/6/21	Mon 23/8/21					
88	Backfill	7 days	Tue 24/8/21	Mon 30/8/21					
89	Construction UG Utilities 2m deep below further surface	28 days	Tue 31/8/21	Mon 27/9/21					
90	Temporary Paving and handover for plant erection	3 days	Tue 28/9/21	Thu 30/9/21					
91	<b>Section A1 (ii) - Supporting structures for overhead cranes of L12 MSB including the associated roof structure except the roof deferred works</b>	<b>333 days</b>	<b>Fri 4/12/20</b>	<b>Mon 1/11/21</b>					
92	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21					
93	Subletting / Fabrication / Delivery	210 days	Tue 23/2/21	Mon 20/9/21					
94	Complete structural steel erection	0 days	Tue 19/10/21	Tue 19/10/21					
95	Install Crane Girders	11 days	Tue 12/10/21	Fri 29/10/21					
96	Construction of roof slab (except defer work)	14 days	Tue 19/10/21	Mon 1/11/21					
97	Touch up and handover for install overhead cranes	3 days	Sat 30/10/21	Mon 1/11/21					
98	<b>Section A2 (i) External Works including CW Inlet Culvert at Area F8A</b>	<b>967 days</b>	<b>Fri 4/12/20</b>	<b>Fri 28/7/23</b>					
99	BD consent for Sheetpile installation	30 days	Fri 4/12/20	Sat 2/1/21					
100	Subletting / Fabrication / Delivery (both for Area F8A-F8B)	30 days	Fri 18/12/20	Sat 16/1/21					
101	Area Possession & Clearance	14 days	Sat 2/1/21	Fri 15/1/21					
102	Install Sheet pile	55 days	Sat 16/1/21	Thu 11/3/21					
103	Installation of Additional sheet Pile at South of area F8A	7 days	Sat 17/4/21	Fri 23/4/21					
104	BD Consent for ELS	28 days	Sat 24/4/21	Fri 21/5/21					
105	ELS and install CW Inlet Pipe (NW to N direction) (Assume flexible joint deliver in Sep 2021)	100 days	Fri 16/7/21	Sat 23/10/21					
106	Construction of Thrust Box & Manholes,etc	15 days	Thu 16/9/21	Thu 30/9/21					
107	Backfill, UG Utilities and Road Paving	150 days	Wed 1/3/23	Fri 28/7/23					
108	<b>Section A2 (ii) External Works including CW Inlet Culvert at Area F8B</b>	<b>1139 days</b>	<b>Fri 4/12/20</b>	<b>Tue 16/1/24</b>					
109	Area Possession & Clearance	30 days	Mon 1/3/21	Tue 30/3/21					
110	BD consent for Sheetpile installation	30 days	Fri 4/12/20	Sat 2/1/21					
111	Install Sheet pile	90 days	Fri 2/4/21	Wed 30/6/21					
112	BD Consent for ELS	28 days	Thu 1/7/21	Wed 28/7/21					
113	ELS and install CW Inlet Pipe	100 days	Thu 29/7/21	Fri 5/11/21					
114	Construction of Thrust Box & Manholes,etc	15 days	Wed 1/9/21	Wed 15/9/21					
115	Backfill, UG Utilities and Road Paving	200 days	Sat 1/7/23	Tue 16/1/24					
116	<b>Section A2 (iii) External Works including CW Inlet Culvert at Area F8C</b>	<b>961 days</b>	<b>Fri 12/3/21</b>	<b>Sat 28/10/23</b>					
117	Area Possession & Clearance	30 days	Fri 12/3/21	Sat 10/4/21					
118	Subletting / Fabrication / Delivery (for Area F8C)	60 days	Fri 12/3/21	Mon 10/5/21					
119	BD consent for Sheetpile installation	30 days	Tue 13/4/21	Wed 12/5/21					
120	Install Sheet pile	62 days	Tue 13/5/21	Tue 13/7/21					
121	BD Consent for ELS	35 days	Wed 14/7/21	Tue 17/8/21					
122	ELS and install CW Inlet Pipe (including soil nail installation under 19/83014)	76 days	Wed 18/8/21	Thu 20/1/22					
123	Construction of Thrust Box & Manholes,etc	30 days	Fri 21/1/22	Sat 19/2/22					
124	Backfill, UG Utilities and Road Paving	150 days	Thu 1/6/23	Sat 28/10/23					
125	<b>Section B1 - Area south of L12 MSB from GL12-F westwards leading to Station Road at Area F3</b>	<b>377 days</b>	<b>Fri 4/12/20</b>	<b>Wed 15/12/21</b>					
126	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21					
127	Subletting / Fabrication / Delivery	120 days	Fri 25/12/20	Fri 23/4/21					
128	Complete CW Pipe Installation & Thrust box	45 days	Tue 25/5/21	Thu 8/7/21					
129	Backfill	30 days	Fri 9/7/21	Sat 7/8/21					
130	Construction of Storm Drain & Manholes	67 days	Mon 20/9/21	Thu 25/11/21					
131	Temp Paving and handover for Condenser Move in	20 days	Fri 26/11/21	Wed 15/12/21					
132	<b>Section B2 - (i) Southern part of L12 HRSBG area and its surrounding at Area F6B including the foundations for Gas Exhaust Duct</b>	<b>273 days</b>	<b>Fri 1/1/21</b>	<b>Thu 30/9/21</b>					
133	Area Possession & Clearance	30 days	Fri 1/1/21	Sat 30/1/21					
134	Subletting / Fabrication / Delivery (for F6B Civil and E&M)	120 days	Sat 2/1/21	Sat 1/5/21					
135	Construction of Underground pits	35 days	Tue 8/6/21	Mon 12/7/21					
136	Excavation & Construct Pile Caps & Tie Beams & Piers	86 days	Mon 8/3/21	Thu 19/8/21					
137	Installation of Pipe Pile for HRSBG foundation (VO)	48 days	Thu 25/3/21	Tue 11/5/21					
138	Construction HRSBG & Gas Duct foundations	112 days	Fri 7/5/21	Fri 3/9/21					
139	Construction of HRSBG Equipment Room incl. ABWF & BS (except T&C)	64 days	Tue 4/5/21	Thu 30/9/21					
140	Construction underground utilities within HRSBG	55 days	Mon 19/7/21	Sat 11/9/21					
141	Backfill & Construction on-grade slabs & RC plinths on top	14 days	Fri 30/7/21	Mon 27/9/21					
142	Backfill and Temporary paving	21 days	Fri 10/9/21	Thu 30/9/21					
143	<b>Section B2 (ii) - Remaining northern part of L12 HRSBG area and its surrounding at Area F6A and F6C</b>	<b>319 days</b>	<b>Fri 1/1/21</b>	<b>Mon 15/11/21</b>					
144	Area Possession and Clearance at Area F6A	30 days	Fri 1/1/21	Sat 30/1/21					
145	Subletting / Fabrication / Delivery (for Area F6A and F6C civil)	90 days	Sat 2/1/21	Thu 1/4/21					
146	Construction of Underground pits (HRSBG Blowdown sump pit)	110 days	Sat 2/1/21	Wed 21/4/21					
147	Excavation & Construct Pile Caps & Tie Beams & Piers	139 days	Mon 1/2/21	Sat 10/7/21					
148	Construction underground utilities within HRSBG	55 days	Mon 19/7/21	Sat 11/9/21					
149	Construction of Underground pits (GT Oil & Chemical drain pits)	15 days	Thu 5/8/21	Thu 19/8/21					
150	Backfill & Construction on-grade slabs & RC plinths on top	45 days	Sun 12/9/21	Tue 26/10/21					
151	Construct RC Walls	90 days	Thu 22/4/21	Tue 20/7/21					
152	Construction of Underground utilities at F6C	21 days	Tue 19/10/21	Mon 8/11/21					
153	Backfill and Temporary paving	7 days	Tue 9/11/21	Mon 15/11/21					
154	<b>Section B2 - (iii) L12 Turbo Block foundation including the L12 MSB ground floor together with the equipment foundations between GL 12-F to 12-H and 12-1 to 12-6 for the installation of power generator, air inlet duct and lube oil reservoir</b>	<b>452 days</b>	<b>Fri 4/12/20</b>	<b>Mon 28/2/22</b>					
155	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21					
156	Subletting / Fabrication / Delivery (Civil+ABWF+BS for MSBL12)	150 days	Fri 25/12/20	Sun 23/5/21					
157	Complete excavation at Type A&C Construction Area	0 days	Sun 21/3/21	Sun 21/3/21					
158	Excavation & Pile Caps & Tie Beams + Slabs (Turbo Block North)	75 days	Sun 31/1/21	Thu 15/4/21					
159	Backfill and construction turbine block & equipment foundation	85 days	Tue 1/6/21	Tue 24/8/21					
160	Excavation & Pile Caps & Tie Beams + Slabs (Turbo Block South)	45 days	Sat 17/4/21	Mon 31/5/21					
161	Construction of internal drainage & on-grade slab	90 days	Wed 1/9/21	Mon 29/11/21					
162	Construction turbine block columns and upper portion for plant embed installation	83 days	Wed 25/8/21	Mon 15/11/21					
163	Concrete Turbine upper part foundation	15 days	Fri 31/12/21	Fri 14/1/22					
164	Construction of Lube Oil Room	60 days	Tue 30/11/21	Fri 28/1/22					
165	Concrete RC walls	115 days	Tue 7/9/21	Thu 30/12/21					
166	ABFW Works	60 days	Thu 4/11/21	Sun 2/1/22					
167	Building Services Works	45 days	Sat 15/1/22	Mon 28/2/22					
168	Remove temporary falsework and scaffolding for installation of power generator	13 days	Mon 7/2/22	Sat 19/2/22					



**Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12** **Master Programme**

ID	Task Name	Duration	Start	Finish	1st Quarter	2nd Quarter	3rd Quarter	4th Quarter
169	<b>Section B2 - (iv) G/F of L12 MSB including the Condenser Pit, Circulating Water Pipe Pit and equipment foundations between GL 12-B to 12-C and 12-1 to 12-6 for the installation of condenser</b>	<b>377 days</b>	<b>Fri 4/12/20</b>	<b>Wed 15/12/21</b>				
170	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21				
171	Subletting / Fabrication / Delivery (for MSB L12 civil)	150 days	Fri 25/12/20	Sun 23/5/21				
172	Excavation to foundation level at ELS SP Type A & C	80 days	Fri 1/1/21	Sun 21/3/21				
173	Install CW Outlet pipe	85 days	Mon 22/3/21	Mon 14/6/21				
174	Construction of CW Outlet Box + lowest tie beam & caps	40 days	Mon 22/3/21	Fri 30/4/21				
175	Construction of pile caps & tie beams & sump pits up to +2.7mPD	26 days	Sat 1/5/21	Wed 26/5/21				
176	Backfill & Construction of CW Inlet Box + tie beams	71 days	Thu 27/5/21	Thu 5/8/21				
177	Construction of pile caps & tie beams at SunShadeCover Area	45 days	Tue 15/6/21	Thu 29/7/21				
178	Backfill and Construction ground beams & trenches	28 days	Thu 27/5/21	Mon 5/7/21				
179	Construction of indoor underground drainage	14 days	Fri 13/8/21	Thu 26/8/21				
180	Backfill & construction on-grade slabs	60 days	Sun 1/8/21	Wed 29/9/21				
181	Construction Column casting and RC walls & equipment foundations	50 days	Thu 30/9/21	Thu 18/11/21				
182	ABFW Works	15 days	Fri 19/11/21	Fri 3/12/21				
183	Building Services Works	20 days	Fri 26/11/21	Wed 15/12/21				
184	Mis. Works and Ready for condenser move in	25 days	Wed 17/11/21	Wed 15/12/21				
185	<b>Section C - (i) Roads and external grounds surrounding L12 MSB and L12 HRSG in addition to the southern &amp; eastern areas mentioned above in Area F5</b>	<b>408 days</b>	<b>Fri 4/12/20</b>	<b>Sat 15/1/22</b>				
186	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21				
187	Subletting / Fabrication / Delivery	210 days	Fri 25/12/20	Thu 22/7/21				
188	Complete substructure & Steel Erection works for MSB	0 days	Tue 17/8/21	Tue 17/8/21				
189	Construction all utilities deeper than 2m from future road level	30 days	Wed 18/8/21	Thu 16/9/21				
190	Construction of cable trenches	30 days	Fri 17/9/21	Sat 16/10/21				
191	Backfill and lay temporary paving	91 days	Sun 17/10/21	Sat 15/1/22				
192	<b>Section C - (ii) Whole of L12 MSB including the pipe and cable rack along south façade of L12 MSB with all underground utilities at Area F4 including C.W. Inlet and Outlet Culvert except the deferred works</b>	<b>908 days</b>	<b>Fri 4/12/20</b>	<b>Tue 30/5/23</b>				
193	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21				
194	Subletting / Fabrication / Delivery	120 days	Fri 25/12/20	Fri 23/4/21				
195	Construction of pile caps & tie beams at Transformer Area	180 days	Sun 31/1/21	Thu 29/7/21				
196	Backfill and on-grade slab at transformer Area	160 days	Sun 11/4/21	Thu 7/10/21				
197	Construction of Fire Walls at Transformer Area	45 days	Fri 8/10/21	Mon 29/11/21				
198	Excavation & Construction Blow Down Sump pit (SP Type B)	140 days	Wed 14/4/21	Tue 31/8/21				
199	Preparation for S.Steelwork Erection	7 days	Sat 5/6/21	Fri 11/6/21				
200	Structural Delivery & Erection (Turbine Hall North fr G.L. 1-3/H->B)	67 days	Sat 12/6/21	Tue 17/8/21				
201	Structural Delivery & Erection (Equipment Floors)	33 days	Wed 18/8/21	Sun 19/9/21				
202	Structural Delivery & Erection (Turbine Hall South + East Elevation)	47 days	Mon 20/9/21	Fri 5/11/21				
203	Joint Tightening and touch up coating	99 days	Sat 3/7/21	Wed 24/11/21				
204	External Scaffolding Erection	97 days	Thu 15/7/21	Mon 22/11/21				
205	Construction 1/F RC Slab	14 days	Mon 20/9/21	Sun 3/10/21				
206	Construction 2/F RC Slab	7 days	Mon 27/9/21	Sun 10/10/21				
207	Construction 3/F RC Slab	18 days	Thu 30/9/21	Sun 17/10/21				
208	Construction 4/F RC Slab	7 days	Thu 7/10/21	Sun 24/10/21				
209	Construction 5/F RC Slab	44 days	Mon 25/10/21	Tue 7/12/21				
210	Construction 6/F RC Slab	14 days	Wed 1/12/21	Tue 14/12/21				
211	Construction Upper Roof RC Slab	10 days	Sun 12/12/21	Fri 24/12/21				
212	Construction Main Roof RC Slab	39 days	Tue 12/10/21	Fri 19/11/21				
213	Construction Defer Roof RC Slab (G.L. G-H)	16 days	Sun 28/11/21	Mon 13/12/21				
214	Construction of Staircase ST-01 & lift shaft & machine room	130 days	Fri 27/8/21	Mon 3/1/22				
215	Construction M/F RC Slab	14 days	Fri 1/10/21	Thu 14/10/21				
216	Lift Installation	90 days	Thu 9/2/23	Tue 9/5/23				
217	Construction of Staircase ST-02 except defer work	68 days	Mon 11/10/21	Fri 24/12/21				
218	Construction of RC plinth, kerbs & parapet Walls	40 days	Sat 20/11/21	Wed 29/12/21				
219	Erection of Skylight & Roof Features	50 days	Fri 26/11/21	Fri 14/1/22				
220	Waterproofing & Flooring at Roof	34 days	Thu 30/12/21	Thu 17/2/22				
221	ABFW Works	600 days	Fri 8/10/21	Tue 30/5/23				
222	Building Services Works	550 days	Tue 16/11/21	Fri 19/5/23				
223	Metal Cladding, Windows and Louvres incl. roof feature	535 days	Mon 23/8/21	Wed 8/2/23				
224	Removal of external scaffolding	460 days	Wed 1/12/21	Sun 5/3/23				
225	Installation of Catwalk at south elevation	90 days	Thu 1/9/22	Wed 14/12/22				
226	Cladding, ABWF & BS Works	60 days	Thu 15/12/22	Sun 12/2/23				
227	Removal of temporary works & clearance for plant erection contractor	30 days	Sat 14/1/23	Sun 12/2/23				
228	<b>Section C - (iii) Link Bridge between L11 and L12 MSB including their associated A&amp;A at L11 MSB</b>	<b>885 days</b>	<b>Fri 4/12/20</b>	<b>Sun 7/5/23</b>				
229	BD Consent	0 days	Fri 4/12/20	Fri 4/12/20				
230	Subletting / Fabrication / Delivery (For BS and ABWF)	250 days	Fri 25/12/20	Tue 31/8/21				
231	Clearing Works and plant set-up	30 days	Fri 3/12/21	Sat 1/1/22				
232	Dismantle of north scaffold for link bridge erection	0 days	Tue 25/1/22	Tue 25/1/22				
233	A&A works at South of L11 MSB	30 days	Fri 3/12/21	Sat 1/1/22				
234	Erection of link bridge structural steel	30 days	Sun 2/1/22	Mon 31/1/22				
235	Casting of bridge deck	11 days	Tue 1/2/22	Fri 11/2/22				
236	Metal roofing installation	30 days	Wed 22/2/23	Thu 23/3/23				
237	ABWF work	15 days	Fri 24/2/23	Fri 7/4/23				
238	BS Works	30 days	Sat 8/4/23	Sun 7/5/23				
239	Ready for power cable laying work by others	0 days	Sun 10/4/22	Sun 10/4/22				
240	<b>Section D - (ii) No. 5 Chimney with L12 Steel Flue Liner</b>	<b>902 days</b>	<b>Fri 1/1/21</b>	<b>Wed 21/6/23</b>				
241	Area Possession & Clearance	45 days	Fri 1/1/21	Sun 14/2/21				
242	Subletting / Fabrication / Delivery (For Civil and BS for Microwave Antenna and Equipment)	120 days	Fri 8/1/21	Fri 7/5/21				
243	Excavation & Pile Cap & Backfill	90 days	Sat 2/1/21	Thu 1/4/21				
244	Tower Crane erection	30 days	Tue 11/5/21	Wed 9/6/21				
245	Construction of Wind Shield + clearance for internal floors and flue+Ground slab	308 days	Fri 2/4/21	Mon 4/4/22				
246	Structural steel fabrication & Delivery for floors and staircase	415 days	Mon 3/1/22	Tue 21/2/23				
247	Erection of steel floors	79 days	Tue 19/4/22	Wed 6/7/22				
248	Construction of G/F room incl. Microwave Antenna Rm	45 days	Thu 7/7/22	Sat 20/8/22				
249	Construction of 1/F RC slab	8 days	Sat 13/8/22	Sat 20/8/22				
250	Construction of 2/F RC Slab	8 days	Fri 5/8/22	Fri 12/8/22				
251	Construction of 3/F RC slab	8 days	Thu 28/7/22	Thu 4/8/22				
252	Construction of 4/F RC slab	8 days	Thu 7/7/22	Thu 14/7/22				
253	Construction of Roof RC slab	61 days	Tue 21/6/22	Sat 20/8/22				
254	Removal of tower Crane	7 days	Sun 21/8/22	Sat 27/8/22				
255	Steel Flue fabrication and delivery	145 days	Sat 5/3/22	Wed 27/7/22				
256	Set up for steel flue installation	60 days	Tue 5/7/22	Fri 2/9/22				
257	Lift & install steel flue liner + cladding works	200 days	Thu 28/7/22	Sun 12/2/23				
258	Lift installation	120 days	Wed 22/2/23	Wed 21/6/23				
259	Installation Louvre & Doors	60 days	Mon 13/2/23	Thu 13/4/23				
260	Mis works. Demobilization and ready for gas duct connection	17 days	Thu 5/1/23	Sat 21/1/23				
261	<b>Section D (i) - ABWF and BS Works at Microwave Antenna Room and Chimney Windshield for installation of microwave and antenna</b>	<b>102 days</b>	<b>Tue 1/3/22</b>	<b>Fri 10/6/22</b>				
262	Completion of Microwave Antenna Room	0 days	Tue 1/3/22	Tue 1/3/22				
263	Remaining ABWF & BS Works	100 days	Thu 3/3/22	Thu 10/6/22				
264	<b>Section E - (i) Administration and Control Building (Transformer Room)</b>	<b>332 days</b>	<b>Fri 4/12/20</b>	<b>Sun 31/10/21</b>				
265	Area Possession & Clearance + BD consent	60 days	Fri 4/12/20	Mon 1/2/21				
266	Subletting / Fabrication / Delivery (For Civil+BS+ABWF)	100 days	Tue 2/2/21	Wed 12/5/21				

**Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12** **Master Programme**

ID	Task Name	Duration	Start	Finish	Mar	1st Quarter	Apr	May	Jun
267	Excavation works	45 days	Fri 4/12/20	Sun 17/1/21					
268	Main Earth Grid Installation	45 days	Sun 3/1/21	Tue 16/2/21					
269	Pile cap and Tie Beam	45 days	Sun 3/1/21	Tue 16/2/21					
270	Tower Crane Erection and modification works	49 days	Wed 10/2/21	Tue 30/3/21					
271	Substructure + Bearing walls + On grade slabs	115 days	Wed 17/2/21	Fri 11/6/21					
272	Construction of RC up to 1/F incl. staircases	69 days	Sat 12/6/21	Thu 19/6/21					
273	ABWF at G/F	52 days	Fri 10/9/21	Sun 31/10/21					
274	<b>Section E (ii) Handover G/F, 1/F, 2/F &amp; Hoisting Well</b>	<b>452 days</b>	<b>Fri 4/12/20</b>	<b>Mon 28/2/22</b>					
275	Cleaning Works and plant set-up	21 days	Sun 31/10/21	Sat 20/11/21					
276	Subletting / Fabrication / Delivery (For NSC Lift)	180 days	Sun 3/1/21	Sat 31/7/21					
277	Construction of RC up to 2/F incl. staircases	25 days	Sat 14/8/21	Mon 13/9/21					
278	Construction of RC up to 3/F incl. staircases	20 days	Thu 2/9/21	Tue 21/9/21					
279	Temporary Hoist erection	14 days	Wed 22/9/21	Tue 5/10/21					
280	Construction of RC up to 4/F incl. staircases	20 days	Thu 16/9/21	Tue 5/10/21					
281	Construction of RC up to R/F incl. staircases	25 days	Thu 30/9/21	Sun 24/10/21					
282	Construction of RC up to lift machine room	21 days	Mon 25/10/21	Sun 14/11/21					
283	Construction of RC up to UR/F	21 days	Mon 15/11/21	Sun 5/12/21					
284	External Wall Finish, Cladding + Windows and Louvres + Features	500 days	Thu 30/9/21	Sat 11/2/23					
285	ABWF at 1/F	95 days	Fri 8/10/21	Mon 10/1/22					
286	ABWF at 2/F	96 days	Fri 15/10/21	Tue 18/1/22					
287	Building Services Works at G/F, 1/F, 2/F & Hoisting Well	147 days	Tue 5/10/21	Mon 28/2/22					
288	<b>Section E (iii) Whole of Administration and Control Building</b>	<b>513 days</b>	<b>Sat 23/10/21</b>	<b>Sun 19/3/23</b>					
289	Subletting / Fabrication / Delivery (For BS+ABWF)	127 days	Sat 23/10/21	Sun 20/3/22					
290	Construction of New UG Grey Water Tank	60 days	Mon 21/3/22	Thu 19/5/22					
291	Submission of WW046 for commencement	60 days	Wed 19/1/22	Sat 19/3/22					
292	ABWF at 3/F	500 days	Mon 25/10/21	Wed 8/3/23					
293	ABWF at 4/F	470 days	Wed 24/11/21	Wed 8/3/23					
294	ABWF at R/F	470 days	Wed 24/11/21	Wed 8/3/23					
295	ABWF at UR/F + Lift Machine Room	35 days	Wed 1/2/23	Mon 13/3/23					
296	Bridge Erection & Connection	28 days	Wed 9/3/22	Wed 27/4/22					
297	Installation of Raised floors	60 days	Thu 9/12/21	Sun 6/2/22					
298	Removal of external scaffolding	45 days	Sat 21/1/23	Tue 14/3/23					
299	Waterproofing & screeding	440 days	Mon 6/12/21	Sat 18/2/23					
300	Removal of Tower Crane	7 days	Thu 31/3/22	Wed 6/4/22					
301	External utilities and road work	45 days	Fri 20/1/23	Tue 7/5/23					
302	Building Services Works	450 days	Sat 4/12/21	Sun 26/2/23					
303	False ceiling after BS works	54 days	Sun 15/1/23	Sat 11/3/23					
304	Submission of WW046 for completion	360 days	Wed 9/3/22	Fri 3/3/23					
305	Submission of FS inspection	14 days	Fri 3/3/23	Fri 17/3/23					
306	Submission for OP Inspection	14 days	Wed 8/3/23	Tue 21/3/23					
307	<b>Section F (i) - Gas Receiving Station and L12 Gas Receiving Station Equipment Room (GRS) Area Extension at Area F14</b>	<b>678 days</b>	<b>Tue 1/6/21</b>	<b>Sun 9/4/23</b>					
308	Area Possession & Clearance + BD consent	90 days	Tue 1/6/21	Sun 29/8/21					
309	Subletting / Fabrication / Delivery	30 days	Tue 22/6/21	Wed 21/7/21					
310	Installation of pipe pile at north of GRS (VO)	125 days	Mon 5/7/21	Sat 6/11/21					
311	Construction Equipment room extension	145 days	Sun 31/10/21	Thu 24/3/22					
312	Modification of existing drainage	45 days	Fri 25/3/22	Sun 8/5/22					
313	Excavation & earthing for Skid foundations	21 days	Mon 9/5/22	Sun 29/5/22					
314	Construction of Skid foundation	45 days	Mon 30/5/22	Wed 13/7/22					
315	Construct underground utilities and drainage	45 days	Thu 14/7/22	Sat 27/8/22					
316	Backfill and road works	200 days	Sun 28/8/22	Wed 15/3/23					
317	Relocate / install new fencing for completion	21 days	Sun 5/3/23	Sun 26/3/23					
318	Mis. Work and ready for OP inspection	14 days	Mon 27/3/23	Sun 9/4/23					
319	<b>Section F (ii) - Pipe and Cable rack and external work at Area F9A and F9B</b>	<b>941 days</b>	<b>Sat 21/21</b>	<b>Mon 31/7/23</b>					
320	BD consent + Site Possession at Area F9A & F9B	90 days	Sat 2/1/21	Thu 1/4/21					
321	Excavation & Plate load test	30 days	Mon 1/11/21	Tue 30/11/21					
322	Construction new footing for pipe rack	30 days	Wed 1/12/21	Mon 23/5/22					
323	Underground utilities and road works for completion	11 days	Thu 31/3/22	Tue 31/5/22					
324	Structural Steel fabrication & Delivery	90 days	Sat 21/10/21	Tue 31/5/22					
325	Erection of new pipe rack	70 days	Fri 31/12/21	Thu 10/3/22					
326	Mis. Work and ready for OP inspection	31 days	Sat 1/7/23	Mon 31/7/23					
327	<b>Section F (iii) - No. 5 CW Equipment Room, pipe and cable rack, external works at Area F10</b>	<b>765 days</b>	<b>Tue 1/6/21</b>	<b>Wed 5/7/23</b>					
328	Area Possession & Clearance + BD consent	90 days	Tue 1/6/21	Sun 14/11/21					
329	Subletting / Fabrication / Delivery For ABWF + BS	150 days	Wed 2/6/21	Fri 29/10/21					
330	Installation of Sheet Pile (VO)	85 days	Tue 1/6/21	Tue 24/8/21					
331	Consent for ELS Works	28 days	Wed 25/8/21	Tue 21/9/21					
332	Excavation & Plate load test	30 days	Wed 22/9/21	Thu 21/10/21					
333	Construction new footing for equipment room	68 days	Thu 23/12/21	Mon 28/2/22					
334	Superstructure for equipment room	60 days	Tue 1/3/22	Fri 29/4/22					
335	ABWF Works	45 days	Sat 30/4/22	Mon 13/6/22					
336	BS Works	400 days	Wed 1/6/22	Wed 5/7/23					
337	Construction RC Wall & plinths & drainage at Chlorinator area	280 days	Wed 30/3/22	Tue 3/1/23					
338	External wall finish & remove scaffolding	60 days	Sat 31/12/22	Tue 28/2/23					
339	Excavation & Plate load test for pipe rack extension (For F45-47 & F49)	30 days	Sat 16/10/21	Sun 14/11/21					
340	Construction new footing for pipe rack (For F45-47 & F49)	45 days	Mon 15/11/21	Wed 29/12/21					
341	Underground utilities and road works for completion	31 days	Wed 1/3/23	Fri 3/3/23					
342	Structural Steel fabrication & Delivery	90 days	Sun 12/12/21	Fri 11/3/22					
343	Backfilling and prepare for steel erection	12 days	Mon 28/2/22	Fri 11/3/22					
344	Excavation & Plate Load test for pipe rack extension (For F48 F56)	14 days	Wed 30/3/22	Tue 12/4/22					
345	Construction of new footing for pipe rack (For F48 & F56)	14 days	Wed 13/4/22	Tue 26/4/22					
346	Erection of new pipe rack (For F48 & F56)	65 days	Tue 3/5/22	Wed 6/7/22					
347	Erection of new pipe rack (For F45-47 & F49)	70 days	Sat 12/3/22	Fri 20/5/22					
348	Mis. Work and ready for OP inspection	56 days	Sun 7/5/23	Wed 5/7/23					
349	<b>Section G (i) - External Work surrounding Area F11</b>	<b>254 days</b>	<b>Mon 20/2/23</b>	<b>Tue 31/10/23</b>					
350	Area Possession & Clearance after handover from No. 5 Intake Contractor	31 days	Wed 1/3/23	Fri 31/3/23					
351	Subletting / Fabrication / Delivery	31 days	Mon 20/2/23	Wed 22/3/23					
352	Submission WW0046 for commencement	31 days	Wed 1/3/23	Fri 31/3/23					
353	Construct Underground utilities and drainage	150 days	Sat 1/4/23	Mon 28/8/23					
354	Install new FS Hydrant	20 days	Mon 10/7/23	Sat 29/7/23					
355	Submission WW0046 for completion	30 days	Sun 30/7/23	Mon 28/8/23					
356	Construction Road extension	58 days	Sun 30/7/23	Mon 25/9/23					
357	Construction road paving and install fencing	30 days	Tue 26/9/23	Wed 25/10/23					
358	Ready for OP inspection	14 days	Wed 18/10/23	Tue 31/10/23					
359	<b>Section G (ii) - External Works at Area F12 &amp; F13</b>	<b>961 days</b>	<b>Thu 4/3/21</b>	<b>Fri 20/10/23</b>					
360	Area Possession & Clearance after handover from other	45 days	Wed 17/5/23	Fri 30/6/23					
361	Subletting / Fabrication / Delivery	180 days	Thu 4/3/21	Mon 30/8/21					
362	Excavation	7 days	Sat 1/7/23	Fri 7/7/23					

**Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12** **Master Programme**

ID	Task Name	Duration	Start	Finish	Mar	1st Quarter	Apr	May	Jun
363	Submission WWO046 for commencement	30 days	Thu 8/6/23	Fri 7/7/23					
364	Construct Underground utilities and drainage	60 days	Sat 8/7/23	Tue 5/9/23					
365	Install new FS Hydrant	15 days	Wed 6/9/23	Wed 20/9/23					
366	Submission WWO046 for completion	30 days	Thu 21/9/23	Fri 20/10/23					
367	Construction Road extension	15 days	Thu 21/9/23	Thu 5/10/23					
368	Complete with M.S. Works for completion	15 days	Fri 6/10/23	Fri 20/10/23					
369	<b>Section G (iii) - FS Modification works along South Seafront Road at Area F15</b>	<b>183 days</b>	<b>Fri 1/4/22</b>	<b>Fri 30/9/22</b>					
370	Area Possession & Clearance after handover from other	45 days	Fri 1/4/22	Sun 15/5/22					
371	Subletting / Fabrication / Delivery	21 days	Fri 1/4/22	Thu 21/4/22					
372	Temporary Traffic Arrangement approval	14 days	Fri 1/4/22	Thu 14/4/22					
373	Utilities scanning and expose existing FS	14 days	Fri 15/4/22	Thu 28/4/22					
374	Determine new FS alignment	21 days	Fri 29/4/22	Thu 19/5/22					
375	Submission to FSD	14 days	Fri 20/5/22	Thu 2/6/22					
376	Modification of FS	60 days	Fri 3/6/22	Mon 1/8/22					
377	Backfill and reinstatement - report to FSD	60 days	Tue 2/8/22	Fri 30/9/22					
378	<b>Section G (iv) - 275kV cable trenches and External Works at Area F16</b>	<b>836 days</b>	<b>Sat 1/5/21</b>	<b>Mon 14/8/23</b>					
379	Area Possession & Clearance	60 days	Sat 1/5/21	Tue 29/6/21					
380	Subletting / Fabrication / Delivery	210 days	Wed 17/11/21	Tue 14/6/22					
381	Temporary Traffic Arrangement approval	60 days	Sat 1/5/21	Tue 29/6/21					
382	Removal of aboveground services	60 days	Wed 30/6/21	Sat 28/8/21					
383	Utilities scanning and expose existing UU	30 days	Sun 29/8/21	Mon 27/9/21					
384	Arrange of diversion existing UG utilities	90 days	Tue 28/9/21	Sun 26/12/21					
385	Construct new cable trenches	550 days	Mon 27/12/21	Thu 29/6/23					
386	Realign / install new UG utilities	30 days	Fri 23/6/23	Sun 23/7/23					
387	Backfill and reinstatement & ready for cable laying by others	45 days	Sat 1/7/23	Mon 14/8/23					
388	<b>Section G (v) - Shunt Reactor Compound and External Works at Area F17</b>	<b>912 days</b>	<b>Fri 4/12/20</b>	<b>Sat 3/6/23</b>					
389	Temporary Traffic Arrangement approval	45 days	Fri 4/12/20	Sun 17/1/21					
390	Subletting / Fabrication / Delivery	100 days	Fri 25/12/20	Sat 3/4/21					
391	BD approval & consent for pipe pile installation	90 days	Fri 4/12/20	Wed 3/3/21					
392	Area Possession & Clearance	14 days	Thu 4/3/21	Wed 17/3/21					
393	Removal of aboveground services	21 days	Thu 18/3/21	Wed 7/4/21					
394	Utilities scanning and expose existing UU	15 days	Thu 8/4/21	Thu 22/4/21					
395	Arrange of diversion existing UG utilities	45 days	Fri 23/4/21	Sun 6/6/21					
396	Install pipe piles	61 days	Sun 23/5/21	Thu 22/7/21					
397	BA14 for pipepile and BD consent for ELS	28 days	Fri 23/7/21	Thu 19/8/21					
398	Excavation & install earthing	35 days	Fri 20/8/21	Thu 23/9/21					
399	Construct Pipe Caps and Tie Beams	45 days	Fri 24/9/21	Sun 7/11/21					
400	Backfill & Erect scaffold	21 days	Mon 8/11/21	Sun 28/11/21					
401	Construction of SRC Walls	75 days	Mon 29/11/21	Fri 11/2/22					
402	Wall finish and remove scaffolding	380 days	Sat 12/2/22	Sun 26/2/23	fall finish and remove scaffolding				
403	Construct new cable trenches	60 days	Thu 9/2/23	Sun 9/4/23		Construct new cable trenches			
404	Install new UG Utilities, Backfill and reinstatement & ready for cable laying by Others for DAX1	55 days	Thu 7/4/22	Tue 31/5/22					
405	Realign / install new UG utilities (for DAX2, APX1 & APX3)	30 days	Tue 4/4/23	Thu 4/5/23					
406	Backfill and reinstatement & ready for cable laying by others (for DAX2, APX1, & APX3)	30 days	Thu 4/5/23	Sat 3/6/23					
407	<b>Section G (vi) - 275kV cable trenches and External Works at Area F18</b>	<b>397 days</b>	<b>Sat 1/5/21</b>	<b>Wed 1/6/22</b>					
408	Temporary Traffic Arrangement approval	45 days	Sat 1/5/21	Mon 14/6/21					
409	Subletting / Fabrication / Delivery	60 days	Tue 15/6/21	Fri 13/8/21					
410	Area Possession & Clearance	15 days	Sat 1/5/21	Sat 15/5/21					
411	Removal of aboveground services	30 days	Sun 16/5/21	Mon 14/6/21					
412	Utilities scanning and expose existing UU	45 days	Tue 15/6/21	Thu 23/7/21					
413	Arrange of diversion existing UG utilities	60 days	Fri 30/7/21	Mon 27/9/21					
414	Construct new cable trenches	172 days	Tue 28/9/21	Fri 18/3/22					
415	Realign / install new UG utilities	45 days	Sat 19/3/22	Mon 2/5/22					
416	Backfill and reinstatement & ready for cable laying by others	30 days	Tue 3/5/22	Wed 1/6/22					
417	<b>Section G (vii) - Flood wall at No. 5 CW Intake Area along HUA at Area F20A</b>	<b>803 days</b>	<b>Fri 4/12/20</b>	<b>Tue 14/2/23</b>					
418	Area Possession & Clearance	30 days	Fri 4/12/20	Sat 2/1/21					
419	Subletting / Fabrication / Delivery	60 days	Fri 25/12/20	Mon 22/2/21					
420	Temporary Traffic Arrangement approval	300 days	Fri 4/12/20	Wed 29/9/21					
421	ELS BD approval & consent	90 days	Fri 18/12/20	Wed 17/3/21					
422	Demolition of existing carriageway	30 days	Thu 11/1/21	Fri 10/12/21					
423	Removal of aboveground services	21 days	Thu 30/9/21	Wed 20/10/21					
424	Utilities scanning and expose existing UU	21 days	Thu 21/10/21	Wed 10/11/21					
425	Arrange of diversion existing UG utilities	30 days	Sat 11/12/21	Sun 9/1/22					
426	Excavation and construction of new Flood wall	65 days	Mon 10/1/22	Tue 15/3/22					
427	Realign / install new UG utilities	30 days	Wed 16/3/22	Thu 14/4/22					
428	Backfill and construct new carriageway	300 days	Fri 15/4/22	Wed 8/2/23					
429	Mis. Work for completion	6 days	Thu 9/2/23	Tue 14/2/23	hw carriageway completion				
430	<b>Section G (viii) - Flood wall at No. 5 CW Intake Area along HUA at Area F20B</b>	<b>729.5 days</b>	<b>Fri 1/10/21</b>	<b>Sat 30/9/23</b>					
431	Area Possession & Clearance	45 days	Fri 1/10/21	Sun 14/11/21					
432	Subletting / Fabrication / Delivery	90 days	Fri 22/10/21	Wed 19/1/22					
433	Temporary Traffic Arrangement approval	14 days	Fri 1/10/21	Thu 14/10/21					
434	ELS BD approval & consent	90 days	Fri 15/10/21	Wed 12/1/22					
435	Demolition of existing carriageway	630 days	Fri 1/10/21	Thu 22/6/23					Demolition
436	Removal of aboveground services	21 days	Tue 20/6/23	Tue 11/7/23					
437	Utilities scanning and expose existing UU	21 days	Wed 5/7/23	Wed 26/7/23					
438	Arrange of diversion existing UG utilities	30 days	Sun 23/7/23	Tue 22/8/23					
439	Install Sheetpiles	55 days	Thu 10/2/22	Tue 5/4/22					
440	BA14 for sheetpile and BD consent for ELS	28 days	Wed 6/4/22	Tue 3/5/22					
441	Excavation and construction of new Flood wall	30 days	Wed 26/7/23	Fri 25/8/23					
442	Realign / install new UG utilities	15 days	Fri 25/8/23	Sat 9/9/23					
443	Backfill and construct new carriageway	21 days	Thu 7/9/23	Thu 28/9/23					
444	Mis. Work for completion	9 days	Thu 21/9/23	Sat 30/9/23					
445	<b>Section G (ix) - Bund wall modification works at South Seafront Road at Area F21</b>	<b>316 days</b>	<b>Fri 4/12/20</b>	<b>Fri 15/10/21</b>					
446	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21					
447	Subletting / Fabrication / Delivery	90 days	Fri 25/12/20	Wed 24/3/21					
448	Temporary Traffic Arrangement approval	165 days	Fri 4/12/20	Mon 17/5/21					
449	ELS BD approval & consent	0 days	Thu 17/12/20	Thu 17/12/20					
450	Demolition of existing carriageway	14 days	Tue 18/5/21	Mon 31/5/21					
451	Removal of aboveground services	14 days	Tue 1/6/21	Mon 14/6/21					
452	Utilities scanning and expose existing UU	21 days	Tue 15/6/21	Mon 5/7/21					
453	Arrange of diversion existing UG utilities (include FS pipe under 17/8002)	40 days	Tue 6/7/21	Sat 14/8/21					
454	Excavation and expose existing bund wall & demolish	18 days	Wed 28/7/21	Sat 14/8/21					
455	Construction new bund wall for road junction	21 days	Sat 4/9/21	Fri 24/9/21					
456	Realign / install new UG utilities (include FS pipe under 17/8002)	60 days	Sun 1/8/21	Wed 29/9/21					
457	Backfill and construct new carriageway	16 days	Thu 30/9/21	Fri 15/10/21					
458	Mis. Work for completion	5 days	Mon 11/10/21	Fri 15/10/21					
459	<b>Section G (x) - DAX Cable Diversion Works (from Part I to Part IV)</b>	<b>955 days</b>	<b>Fri 4/12/20</b>	<b>Sun 16/7/23</b>					
460	Temporary Traffic Arrangement approval	14 days	Fri 4/12/20	Thu 17/12/20					
461	Subletting / Fabrication / Delivery	90 days	Fri 25/12/20	Wed 24/3/21					
462	Area Possession & Clearance	45 days	Fri 4/12/20	Sun 17/1/21					
463	Identification of existing cable trench	7 days	Mon 18/1/21	Sun 24/1/21					
464	Part 1 Re-excavation works incl construction of joint bay (at Water Reservoir Road)	246 days	Mon 25/1/21	Mon 27/9/21					
465	Part 1 Re-excavation works incl construction of joint bay (other than Reservoir road base on revised routing)	310 days	Mon 25/1/21	Tue 30/11/21					
466	Part 2 Re-excavation works incl. joint bay	120 days	Mon 1/11/21	Mon 28/2/22					
467	Part 3 Re-excavation works incl. joint bay	500 days	Mon 1/11/21	Wed 15/3/23					Part 3 Re-excavation works incl. joint bay

MASTER PROGRAMME  
Rev 1-B23 Aug 2021



Task Split Milestone Summary

**Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12 Master Programme**

ID	Task Name	Duration	Start	Finish	Mar	1st Quarter	Apr	May	Jun
468	Part 4 Re-excavation works incl. joint bay & new oil tank pits	92 days	Sat 1/10/22	Sat 31/12/22					
469	Backfill & Reinstatement Part 1	61 days	Mon 1/11/21	Fri 31/12/21					
470	Backfill & Reinstatement Part 2	61 days	Sun 1/5/22	Thu 30/6/22					
471	Backfill & Reinstatement Part 3	61 days	Wed 17/5/23	Sun 16/7/23					
472	<b>Section H - All remaining works shall be completed for reporting completion to BD and ready for OP inspection (PS1.4.4)</b>	<b>736.15 days</b>	<b>Wed 17/11/21</b>	<b>Thu 23/11/23</b>					
473	<b>Deferred works (MSB &amp; HRSG) Listed in PS 1.4.4</b>	<b>539 days</b>	<b>Wed 17/11/21</b>	<b>Tue 9/5/23</b>					
474	Construction of L12 MSB roof between GL12-G to 12-H and 12-2 to 12-6 after the overhead crane installation by the Employer's Specialist Contractors	38 days	Wed 17/11/21	Tue 4/1/22					
475	Construction of walls of L12 MSB below 1/F along GL 12-6 from GL12-B to 12-C and the associated staircases including the enclosure walls between G/F and 1/F. The Contractor shall allow access for the Employer's Specialist Contractors to use the hoisting we	92 days	Mon 16/5/22	Mon 15/8/22					
476	Provision in associated with hoisting well	21 days	Mon 6/6/22	Sun 26/6/22					
477	Construction of internal partition wall at 1/F of L12 MSB along GL 12-C from GL 12-2 to 12-3 AND North Façade at 1/F of L12 MSB along GL 12-1 from GL 12-B to 12-C	30 days	Wed 1/3/23	Thu 30/3/23					
478	Construction of metal fence and the associated Fire Services (F.S.) installations and installation of removable shelter at Transformer Area	120 days	Tue 10/1/23	Tue 9/5/23					
479	<b>Deferred works (DAX1 and DAX2 ) Listed in PS 1.4.4</b>	<b>151 days</b>	<b>Sun 1/1/23</b>	<b>Wed 31/5/23</b>					
480	Backfilling of whole DAX1 compartment inside existing joint bay "STJ12" and the new oil tank pit A located aside existing joint bay "STJ12".	59 days	Wed 12/2/23	Fri 31/3/23					
481	Re-excavation of whole DAX2 compartment inside existing joint bay "STJ12".	61 days	Sun 1/1/23	Thu 2/3/23					
482	Backfilling of whole DAX2 compartment inside existing joint bay "STJ12" and the new oil tank pit B located aside existing joint bay "STJ12".	61 days	Sat 1/4/23	Wed 31/5/23					
483	<b>Deferred works (External Work) Listed in PS 1.4.4</b>	<b>357.15 days</b>	<b>Thu 1/12/22</b>	<b>Thu 23/11/23</b>					
484	Final reinstatement of access roads and pavement surrounding and within L12 MSB and L12 HRSG area	320 days	Thu 1/12/22	Mon 16/10/23					
485	Installation of trench cover and road reinstatement of gas pipe and cable trenches within Area F5, F14, F16, F17 and F18.	30 days	Sun 1/1/23	Thu 28/9/23					
486	Backfilling and road reinstatement of 27.5kV cable trenches	60 days	Sun 1/1/23	Thu 23/11/23					
487	All Remaining work ready for OP inspection	0 days	Sat 1/7/23	Sat 1/7/23					
488	<b>STATUTORY SUBMISSION, INSPECTION &amp; APPROVAL</b>	<b>560 days</b>	<b>Tue 16/11/21</b>	<b>Mon 29/5/23</b>					
489	<b>WSD Statutory Submission, Inspection and Approval WWO Part I to III Submission / Approval</b>	<b>256 days</b>	<b>Tue 16/11/21</b>	<b>Fri 29/7/22</b>					
490	WSD : Submit to WSD Form WWO 046 Part I to II - FOR ACB Building (for Ext Works at later stage)	0 days	Tue 16/11/21	Tue 16/11/21					
491	WSD: Vetting Form WWO 046 Part I and II Submission	90 days	Wed 17/11/21	Mon 14/2/22					
492	WSD: Issued of Form WWO 046 Part III by WSD - FOR ACB Building	0 days	Tue 15/2/22	Tue 15/2/22					
493	WSD: Prepare for 1st Amendment for Plumbing Plan	60 days	Tue 15/2/22	Fri 15/4/22					
494	WSD: Submit to WSD 1st Amendment for Plumbing Plan	0 days	Fri 15/4/22	Fri 15/4/22					
495	WSD: Vetting of Plumbing Plan by WSD	60 days	Sat 16/4/22	Tue 14/6/22					
496	WSD: 1st Approval for Plumbing Plan by WSD	0 days	Tue 14/6/22	Tue 14/6/22					
497	WSD: Prepare and Submit for Final Amendment for Plumbing Plan	45 days	Wed 15/6/22	Fri 29/7/22					
498	WSD: Vetting and Final Approval for Plumbing Plan by WSD	0 days	Fri 29/7/22	Fri 29/7/22					
499	<b>WSD Statutory Submission, Inspection and Approval WWO Part IV to V Fire Services Water Submission / Approval</b>	<b>33 days</b>	<b>Fri 29/7/22</b>	<b>Wed 31/8/22</b>					
500	WSD: Form WWO 046 Part IV Submission (FS)	0 days	Fri 3/3/23	Fri 3/3/23					
501	WSD: WSD Received Form WWO046 Part IV and arrange for inspection (FS)	7 days	Fri 3/3/23	Thu 9/3/23					
502	WSD: WSD Inspection (FS)	7 days	Fri 10/3/23	Thu 16/3/23					
503	WSD: WWO 046 Part V Endorsement by WSD (FS)	12 days	Fri 17/3/23	Tue 28/3/23					
504	WSD: WSD Processing Water Supply Connection Certificate (FS)	7 days	Wed 29/3/23	Tue 4/4/23					
505	WSD: Issue by WSD Water Supply Connection Certificate (FS)	0 days?	Tue 4/4/23	Tue 4/4/23					
506	<b>WSD Statutory Submission, Inspection and Approval WWO Part IV to V Potable /Flush Water Submission / Approval</b>	<b>60 days</b>	<b>Fri 3/3/23</b>	<b>Mon 1/5/23</b>					
507	WSD: Form WWO 046 Part IV Submission (Fresh/Flush)	0 days	Fri 3/3/23	Fri 3/3/23					
508	WSD: WSD Acknowledge Form WWO 046	6 days	Fri 3/3/23	Wed 8/3/23					
509	WSD: WSD Inspection with Testing to lead (Fresh/Fluhs)	12 days	Thu 9/3/23	Mon 20/3/23					
510	WSD: Cleansing/Disinfecting Water Tanks / Piping System (Fresh/Flush)	6 days	Tue 21/3/23	Sun 26/3/23					
511	WSD: Collection of Sample for Testing at Accredited Lab (Fresh/Flush)	12 days	Mon 27/3/23	Fri 7/4/23					
512	WSD: Accredited Lab Testing Report of Sample to WSD	12 days	Sat 8/4/23	Wed 19/4/23					
513	WSD: Vetting of Test Report by WSD	6 days	Thu 20/4/23	Tue 25/4/23					
514	WSD: Issue of WWO 046 Part V (Fresh/Flush)	0 days	Tue 25/4/23	Tue 25/4/23					
515	WSD: WSD Processing WWO1005 Water Certification (Fresh/Flush)	6 days	Wed 26/4/23	Mon 1/5/23					
516	WSD: Issue by WSD WWO 1005 Water Certification (Fresh/Flush)	0 days	Mon 1/5/23	Mon 1/5/23					
517	<b>EMSD LIFT Statutory Submission, Inspection and Approval</b>	<b>45 days</b>	<b>Wed 15/2/23</b>	<b>Fri 31/3/23</b>					
518	EMSD: Submission of Lift Form LES to EMSD	12 days	Wed 15/2/23	Sun 26/2/23					
519	EMSD: EMSD Makes arrangement for Lift Installation	5 days	Mon 27/2/23	Fri 3/3/23					
520	EMSD: EMSD Inspection to Lift Installation	14 days	Sat 4/3/23	Fri 17/3/23					
521	EMSD: Processing Lift Certificate (Form LE6)	14 days	Sat 18/3/23	Fri 31/3/23					
522	EMSD: Lift Issuance of Form 6 (Lift Certificate)	0 days	Fri 31/3/23	Fri 31/3/23					
523	<b>HKE Transformer Final Inspection</b>	<b>120 days</b>	<b>Sat 30/7/22</b>	<b>Sat 26/11/22</b>					
524	TX Room: Invite HKE For Transformer Room Inspection	7 days	Sat 30/7/22	Fri 5/8/22					
525	TX Room: Give Access to Transformer Room for HKE Contractor	0 days	Fri 5/8/22	Fri 5/8/22					
526	TX Room: Move-IN HKE Transformer Equipments	5 days	Sat 6/8/22	Wed 10/8/22					
527	TX Room: Install HKE Transformer, MEP Works & Testing	90 days	Wed 11/8/22	Tue 8/11/22					
528	TX Room: HKE Power Energization / Inspection	6 days	Wed 9/11/22	Mon 14/11/22					
529	TX Room: Metering Installation	12 days	Tue 15/11/22	Sat 26/11/22					
530	TX Room: HKE Power-ON Date	0 days	Sat 26/11/22	Sat 26/11/22					
531	<b>DSD Drainage Completion Memo</b>	<b>65 days</b>	<b>Fri 30/6/23</b>	<b>Sat 2/9/23</b>					
532	DSD: CCTV Survey Report on Completed Drainage	30 days	Fri 30/6/23	Sat 29/7/23					
533	DSD: Submitted CCTV Report & Form HPB1 of Completed Drainage to DSD For Technical Audit	7 days	Sun 30/7/23	Sat 5/8/23					
534	DSD: Completed Drainage System including TMC Inspection/Technical Audit by DSD	14 days	Sun 6/8/23	Sat 19/8/23					
535	DSD: Preparation of Drainage Connection Completion Memo by DSD	14 days	Sun 20/8/23	Sat 2/9/23					
536	DSD: Issue of Drainage Connection Completion Memo by DSD	0 days	Sat 2/9/23	Sat 2/9/23					
537	<b>EPD Submission, Inspection and Approval</b>	<b>60 days</b>	<b>Wed 5/7/23</b>	<b>Sun 3/9/23</b>					
538	EPD: License Application to EPD under APCO (Cap 311) for Generator Sets	0 days	Wed 5/7/23	Wed 5/7/23					
539	EPD: Vetting of Application by EPD under APCO (Cap 311) for Generator Sets	60 days	Thu 6/7/23	Sun 3/9/23					
540	EPD: Approval from EPD under APCO (Cap 311) for Generator Sets Installation	0 days	Sun 3/9/23	Sun 3/9/23					
541	<b>FSD VAC Statutory Submission, Inspection and Approval</b>	<b>150 days</b>	<b>Wed 20/7/22</b>	<b>Fri 16/12/22</b>					
542	Preparation of FSD VAC Drawings and Submission to HEC	60 days	Wed 20/7/22	Sat 17/9/22					
543	HEC: Review and Approval	30 days	Sun 18/9/22	Mon 17/10/22					
544	Preparation of VAC Drawings and Submission to FSD	30 days	Tue 18/10/22	Wed 16/11/22					
545	FSD: Review and Approval	30 days	Thu 17/11/22	Fri 16/12/22					
546	<b>FSD Statutory Submission, Inspection and Approval</b>	<b>91 days</b>	<b>Sun 15/1/23</b>	<b>Sat 15/4/23</b>					
547	Testing and Commissioning (Individual System - FSI Related)	45 days	Sun 15/1/23	Tue 28/2/23					
548	FSD: All Sections FS Ingration Test by NSC_BS	15 days	Wed 1/3/23	Wed 15/3/23					
549	FSD: Completion of FS Integration Test by NSC_BS for FS314/501	0 days	Wed 15/3/23	Wed 15/3/23					
550	FSD: Submit Form 213/314 & Form 501 Request for Inspection	0 days	Wed 15/3/23	Wed 15/3/23					
551	FSD: FSD Makes Arrangement for Inspection	7 days	Thu 16/3/23	Wed 22/3/23					
552	FSD: FSD Inspection	12 days	Thu 23/3/23	Mon 3/4/23					
553	FSD: Completion of FS Inspection	0 days	Mon 3/4/23	Mon 3/4/23					
554	FSD: FSD Processing FS Certificate Form 172	12 days	Tue 4/4/23	Sat 15/4/23					
555	FSD: Issue of Fire Services FS Certificate Form 172	0 days	Sat 15/4/23	Sat 15/4/23					
556	<b>PRACTICAL COMPLETION</b>	<b>216 days</b>	<b>Sun 16/4/23</b>	<b>Fri 17/11/23</b>					
557	BD Inspection	97 days	Sun 16/4/23	Fri 21/7/23					
558	BD: Application Form BA13 for OP Application	21 days	Sun 16/4/23	Sat 6/5/23					
559	BD: BD Inspection Date	15 days	Sun 7/5/23	Sun 21/5/23					
560	BD: Reinspection date with defects and rectification works	60 days	Mon 22/5/23	Thu 20/7/23					

MASTER PROGRAMME  
Rev 1-B 23 Aug 2021



Task  Split  Milestone  Summary 

Page 6 of 7

**Contract No. 19/83002 Lamma Power Station Extension Civil and Building Works for Unit L12** **Master Programme**

ID	Task Name	Duration	Start	Finish	Mar	1st Quarter	Apr	May	Jun
561	<b>BD: Obtain Occupation Permit (OP) from BD</b>	<b>1 day</b>	<b>Fri 21/7/23</b>	<b>Fri 21/7/23</b>					
562	<b>As-Built Drawings &amp; Handover Documentation</b>	<b>120 days</b>	<b>Mon 1/5/23</b>	<b>Mon 28/8/23</b>					
563	Prepare and Submit As-Built Drawings & Handover Documentation	45 days	Mon 1/5/23	Wed 14/6/23					
564	Review and Approval	45 days	Thu 15/6/23	Sat 29/7/23					
565	As-Built Drawings & Handover Documentation - Revision by MC	30 days	Sun 30/7/23	Mon 28/8/23					
566	Revised As-Built Drawings & Handover Documentation - Final Submission	0 days	Mon 28/8/23	Mon 28/8/23					
567	<b>Completion of the Whole Contract Works</b>	<b>119 days</b>	<b>Sat 22/7/23</b>	<b>Fri 17/11/23</b>					
568	1st Client Inspection for Review and Comments	30 days	Sat 22/7/23	Sun 20/8/23					
569	Defects and Rectification works	60 days	Mon 21/8/23	Thu 19/10/23					
570	2nd Client Inspection	14 days	Fri 20/10/23	Thu 2/11/23					
571	Minor Defects Rectification Works and Final Inspection	15 days	Fri 3/11/23	Fri 17/11/23					
572	<b>PRACTICAL COMPLETION</b>	<b>0 days</b>	<b>Fri 17/11/23</b>	<b>Fri 17/11/23</b>					



ID	Task Name	Duration	Start	Finish	2nd Quarter		
					Apr	May	Jun
1	<b>19-83014 - Civil Works for No. 5 C.W. Intake and Cable Bridge at Lamma Power Station Extension</b>	<b>363 days</b>	<b>Fri 22/7/22</b>	<b>Fri 18/8/23</b>			
2	<b>No. 5 C.W. Intake</b>	<b>363 days</b>	<b>Fri 22/7/22</b>	<b>Fri 18/8/23</b>			
3	Delivery of Precast No. 5 Intake Chamber	3 days	Fri 22/7/22	Sun 24/7/22			
4	Installation of Precast No. 5 Intake Chamber	2 days	Mon 25/7/22	Tue 26/7/22			
5	Prepare formation level for reinstall culvert	18 days	Wed 27/7/22	Sat 13/8/22			
6	Reinstate of culvert	7 days	Mon 15/8/22	Sun 21/8/22			
7	Reinstate of seawall block	28 days	Mon 22/8/22	Sun 18/9/22			
8	Backfill at East Side	20 days	Mon 19/9/22	Sat 8/10/22			
9	Reinstate of seawall coping	30 days	Thu 3/11/22	Fri 2/12/22			
10	Temporary backfill for access at east of Intake Chamber	10 days	Sat 3/12/22	Mon 12/12/22			
11	Handover back from erection contractor at Intake Road	1 day	Mon 15/5/23	Mon 15/5/23			
12	UU works and reinstatement of Intake Road	66 days	Tue 16/5/23	Tue 15/8/23			
13	<b>Steel Parapet along seawall</b>	<b>37 days</b>	<b>Sat 4/3/23</b>	<b>Sun 9/4/23</b>			
14	Delivery of steel parapet (Removed for Chamber installation portion)	1 day	Sat 4/3/23	Sat 4/3/23			
15	Installation of steel parapet (Removed for chamber installation portion)	7 days	Sun 19/3/23	Sat 25/3/23			
16	Removal of existing steel parapet for replacement	7 days	Sun 26/3/23	Sat 1/4/23			
17	Installation of steel parapet (Replacement)	21 days	Sun 2/4/23	Sat 22/4/23			
18	<b>Steel Gantry Frame above Bar Screen Chamber</b>	<b>21 days</b>	<b>Sat 15/4/23</b>	<b>Fri 5/5/23</b>			
19	Delivery of steel members	1 day	Sat 15/4/23	Sat 15/4/23			
20	Installation of gantry frame	20 days	Sun 16/4/23	Fri 5/5/23			
21	<b>Bollard &amp; Fender</b>	<b>141 days</b>	<b>Wed 1/3/23</b>	<b>Fri 18/8/23</b>			
22	Confirmation and order of bollard and fender	1 day	Wed 1/3/23	Wed 1/3/23			
23	Fabrication and delivery of bollard & fender	90 days	Thu 2/3/23	Fri 9/6/23			
24	Installation of bollard (1 no.)	1 day	Mon 12/6/23	Mon 12/6/23			
25	Rebar fixing & Concreting	2 days	Tue 13/6/23	Wed 14/6/23			
26	Removal of existing fender	15 days	Mon 12/6/23	Fri 30/6/23			
27	Installation of fender	35 days	Mon 3/7/23	Fri 18/8/23			
28	<b>In-situ Construction Work for Intake Chamber</b>	<b>266 days</b>	<b>Sat 20/8/22</b>	<b>Tue 16/5/23</b>			
29	<b>Backfilling Work between Pipepile and Intake Chamber External Wall</b>	<b>19 days</b>	<b>Sat 20/8/22</b>	<b>Wed 7/9/22</b>			
33	Backfilling at Discharge Valve Chamber	10 days	Fri 9/9/22	Sun 18/9/22			
34	Installation of Concrete Block inside/ on intake chamber/ culvert	25 days	Tue 23/8/22	Fri 16/9/22			
35	Removal of Internal Strut/ King Post	28 days	Sat 20/8/22	Fri 16/9/22			
36	Dewatering in Chamber Internal Side	3 days	Tue 20/9/22	Thu 22/9/22			
37	Corrosion Protection of Rebar	8 days	Fri 23/9/22	Fri 30/9/22			
38	<b>Construction of Intake Chamber External Wall to Level +5.70mPD</b>	<b>189 days</b>	<b>Sun 28/8/22</b>	<b>Sat 4/3/23</b>			
39	<b>Erection of Scaffolding Supporting Bracket</b>	<b>48 days</b>	<b>Sun 28/8/22</b>	<b>Fri 14/10/22</b>			
44	<b>Installation of Scaffolding</b>	<b>51 days</b>	<b>Sat 3/9/22</b>	<b>Sun 23/10/22</b>			
45	<b>Chamber Internal Side</b>	<b>51 days</b>	<b>Sat 3/9/22</b>	<b>Sun 23/10/22</b>			
50	<b>Chamber External Side</b>	<b>51 days</b>	<b>Sat 3/9/22</b>	<b>Sun 23/10/22</b>			
55	<b>Rebar Fixing &amp; Formwork</b>	<b>58 days</b>	<b>Thu 8/9/22</b>	<b>Fri 4/11/22</b>			
59	<b>Concreting</b>	<b>18 days</b>	<b>Thu 29/9/22</b>	<b>Sun 16/10/22</b>			
63	<b>Wall construction at Penstock Chamber</b>	<b>132 days</b>	<b>Mon 24/10/22</b>	<b>Sat 4/3/23</b>			
64	External wall	14 days	Mon 24/10/22	Sun 6/11/22			
65	W29	5 days	Mon 7/11/22	Fri 11/11/22			
66	W26	5 days	Sat 12/11/22	Wed 16/11/22			
67	W4C	5 days	Mon 7/11/22	Fri 11/11/22			
68	W28	10 days	Thu 17/11/22	Sat 26/11/22			
69	W25	10 days	Sun 27/11/22	Tue 6/12/22			
70	W4B	10 days	Wed 7/12/22	Fri 16/12/22			
71	W27,W24 & W4A	10 days	Thu 23/2/23	Sat 4/3/23			
72	<b>Excavation and installation of CW culvert pipes</b>	<b>45 days</b>	<b>Sat 15/10/22</b>	<b>Mon 28/11/22</b>			
76	On grade slab & plinths construction at west of Intake Chamber	14 days	Tue 29/11/22	Mon 12/12/22			
77	<b>Construction of trash pit &amp; RC footings for hoist support</b>	<b>136 days</b>	<b>Wed 16/11/22</b>	<b>Fri 31/3/23</b>			


Project: 19-83014 - No. 5 Intake and Cable Br  
 Date: 26 Feb 2023  
 Rev. 9 - Programme for No. 5 C.W. Intake

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	2nd Quarter		
					Apr	May	Jun
78	Backfill to bottom level of trash pit at south of Intake Chamber	7 days	Wed 16/11/22	Tue 22/11/22			
79	RC works for trash pit & hoist support footings	30 days	Mon 6/2/23	Tue 7/3/23			
80	Backfill to ground level at south of Intake Chamber	4 days	Wed 8/3/23	Sat 11/3/23			
81	On grade slab & plinths construction at south of Intake Chamber	20 days	Sun 12/3/23	Fri 31/3/23			
82	North Chamber (L12)	91 days	Fri 23/9/22	Thu 22/12/22			
83	W11, W12 & W23	50 days	Fri 23/9/22	Fri 11/11/22			
84	1st Layer (-5.5mPD to -4.6mPD)	20 days	Fri 23/9/22	Wed 12/10/22			
89	2nd Layer (-4.8mPD to -0.875mPD)	10 days	Thu 13/10/22	Sat 22/10/22			
94	3rd Layer (-0.875mPD to 2.65mPD)	13 days	Sun 23/10/22	Fri 4/11/22			
99	4th Layer (2.65mPD to 5.7mPD)	7 days	Sat 5/11/22	Fri 11/11/22			
104	W10a-d & W20	46 days	Fri 30/9/22	Mon 14/11/22			
105	1st Layer (-5.5mPD to -4.6mPD)	13 days	Fri 30/9/22	Wed 12/10/22			
110	2nd Layer (-4.8mPD to -0.375mPD)	19 days	Thu 13/10/22	Mon 31/10/22			
115	3rd Layer (-0.375mPD to 3.15mPD)	8 days	Tue 1/11/22	Tue 8/11/22			
120	4th Layer (3.1mPD to 5.7mPD)	6 days	Wed 9/11/22	Mon 14/11/22			
124	Slab at Discharge Valve Chamber at Level +0.5mPD (G.L.1-7)	81 days	Thu 29/9/22	Sun 18/12/22			
129	Top Slab at Level +7.20mPD (G.L. 5-7)	47 days	Sun 30/10/22	Thu 15/12/22			
137	Ground Beam Along G.L. 7/D & 7/C	62 days	Fri 21/10/22	Wed 21/12/22			
146	Handover L12 Chamber and Discharge Valve Chamber	0 days	Thu 22/12/22	Thu 22/12/22			
147	W20 (Seal up L12 Box-out openings at discharge valve chamber)	15 days	Wed 15/3/23	Wed 29/3/23			
148	Handover to Paul Y for Sealing up work	1 day	Wed 15/3/23	Wed 15/3/23			
149	Rebar fixing, Formwork, Concreteing and Removal of Formwork	14 days	Thu 16/3/23	Wed 29/3/23			
150	L12 Bar Screen Chamber	48 days	Fri 24/2/23	Wed 12/4/23			
151	Drilled in anchor bolt at concrete recess of bar screen chamber	7 days	Fri 24/2/23	Thu 2/3/23			
152	Installation of Bar Screen Guide Channel (Bottom & Based Portion)	7 days	Fri 3/3/23	Thu 9/3/23			
153	Grouting (Bottom & Based Portion)	2 days	Fri 10/3/23	Sat 11/3/23			
154	Installation of Bar Screen Guide Channel (Remaining Portion)	7 days	Sun 12/3/23	Sat 18/3/23			
155	Grouting (Remaining Portion)	2 days	Sun 19/3/23	Mon 20/3/23			
156	Installation of temporary water gate (Use existing water gate from Intake 4)	1 day	Sat 25/3/23	Sat 25/3/23			
157	Infill Water and Water Leakage testing	1 day	Sun 26/3/23	Sun 26/3/23			
158	Removal Water	1 day	Mon 27/3/23	Mon 27/3/23			
159	Form Access Panel and pump out remaining water inside culvert	2 days	Tue 28/3/23	Wed 29/3/23			
160	Obsesrvation for any leakage from steel gate at culvert inlet	1 day	Thu 30/3/23	Thu 30/3/23			
161	Removal of Steel Gate (Friendly Benefit)	3 days	Fri 31/3/23	Sun 2/4/23			
162	Installation of Dosing Pipe	6 days	Mon 3/4/23	Sat 8/4/23			
163	Testing & Commissioning	2 days	Sun 9/4/23	Mon 10/4/23			
164	Removal of Steel Gate at Culvert Inlet L12 (WOD)	2 days	Tue 11/4/23	Wed 12/4/23			
165	Centre Chamber (Spare)	173 days	Tue 25/10/22	Sat 15/4/23			
166	W7, W8 & W22	54 days	Tue 25/10/22	Sat 17/12/22			
167	1st Layer (-5.5mPD to -4.6mPD)	13 days	Tue 25/10/22	Sun 6/11/22			
172	2nd Layer (-4.8mPD to -0.875mPD)	13 days	Mon 7/11/22	Sat 19/11/22			
177	3rd Layer (-0.875mPD to 2.65mPD)	13 days	Sun 20/11/22	Fri 2/12/22			
182	4th Layer (2.65mPD to 5.7mPD)	15 days	Sat 3/12/22	Sat 17/12/22			
187	W6a-b	120 days	Fri 28/10/22	Fri 24/2/23			
188	1st Layer (-5.5mPD to -4.6mPD)	22 days	Fri 28/10/22	Fri 18/11/22			
193	2nd Layer (-4.8mPD to -0.375mPD)	16 days	Sat 19/11/22	Sun 4/12/22			
198	3rd Layer (-0.375mPD to 3.15mPD)	16 days	Mon 5/12/22	Tue 20/12/22			
203	4th Layer (3.1mPD to 5.7mPD)	13 days	Wed 21/12/22	Mon 2/1/23			
207	Top Slab at Level +7.20mPD (G.L. 3-5)	57 days	Fri 30/12/22	Fri 24/2/23			
208	Removal of Concrete Block between G.L. 3-5/D-C)	4 days	Fri 30/12/22	Mon 2/1/23			
209	Erection of Soffit Formwork	14 days	Tue 3/1/23	Mon 16/1/23			
210	Rebar Fixing	18 days	Tue 17/1/23	Fri 3/2/23			
211	Concreting	1 day	Sat 4/2/23	Sat 4/2/23			
212	Builder's Work at Level +7.2mPD	20 days	Sun 5/2/23	Fri 24/2/23			


Project: 19-83014 - No. 5 Intake and Cable Br  
 Date: 26 Feb 2023  
 Rev. 9 - Programme for No. 5 C.W. Intake

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

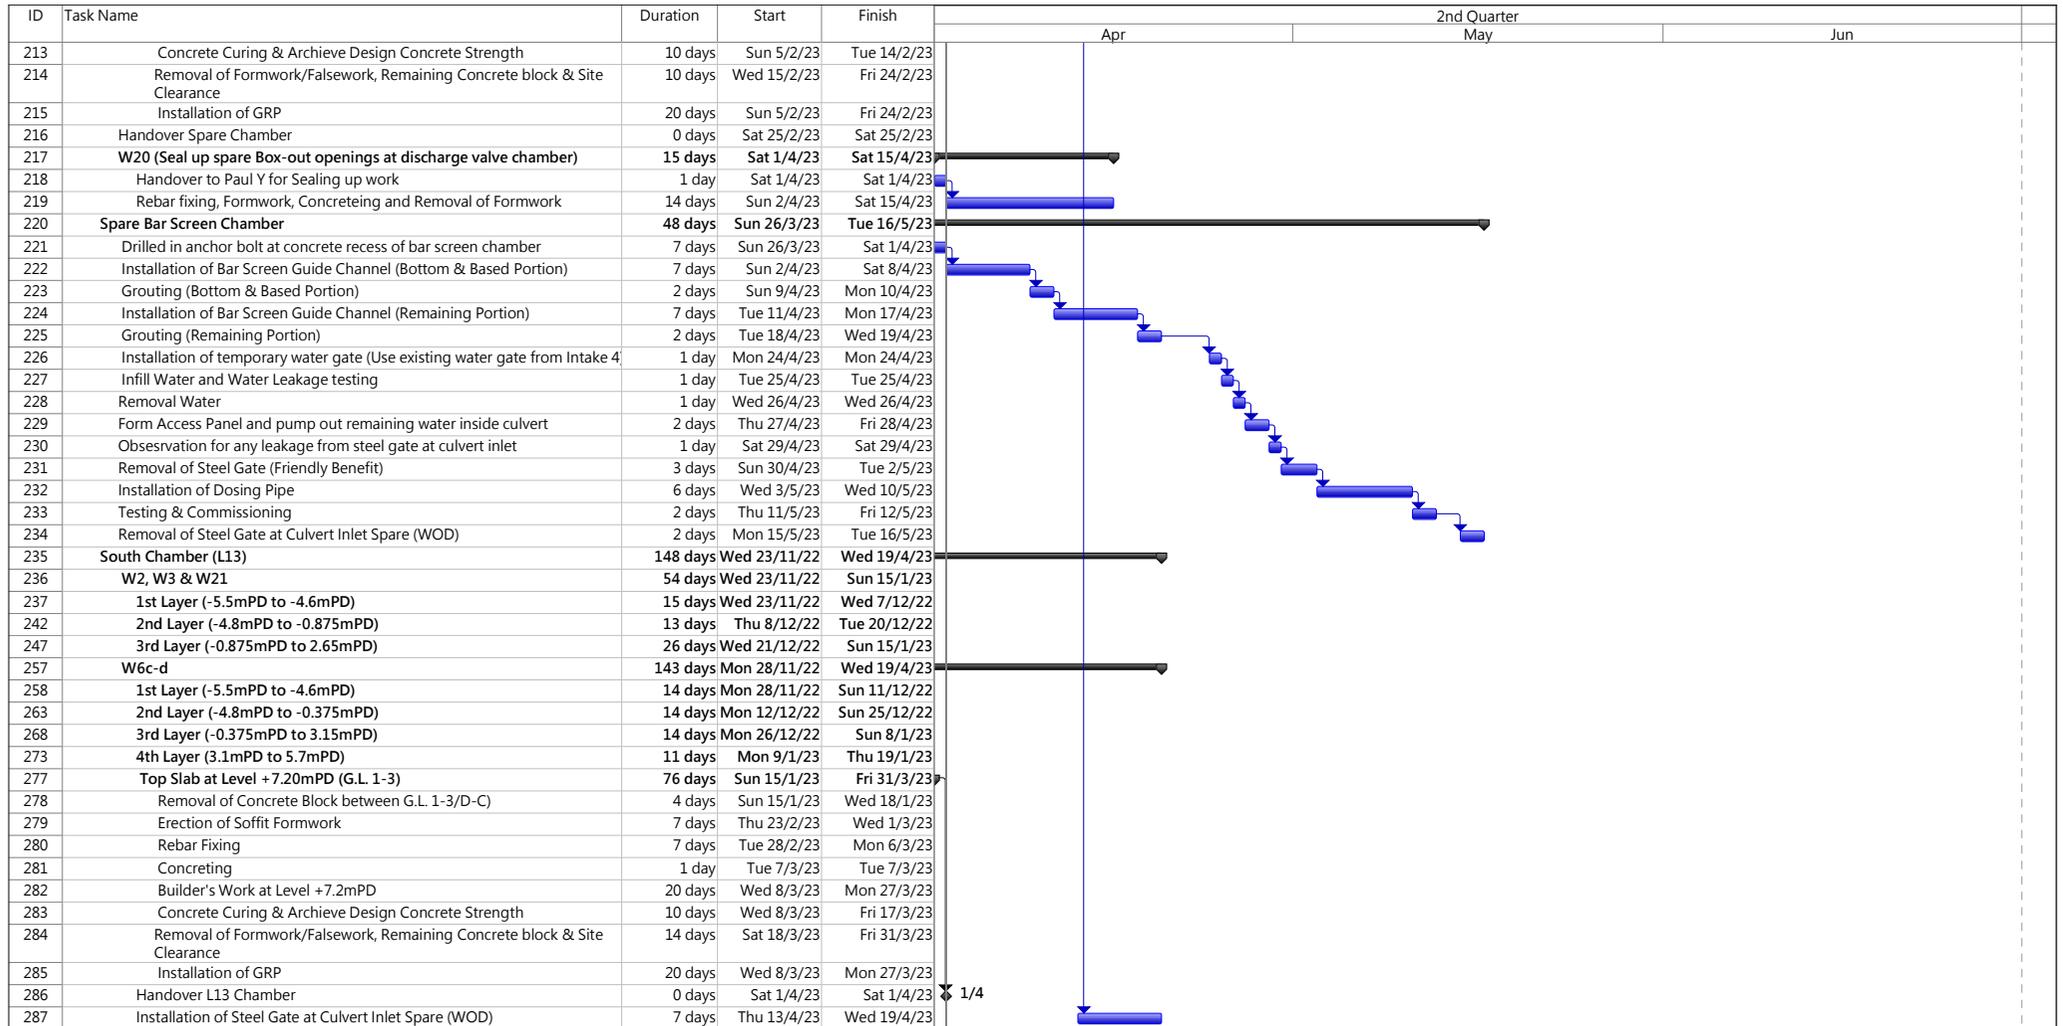

Project: 19-83014 - No. 5 Intake and Cable Br  
 Date: 26 Feb 2023  
 Rev. 9 - Programme for No. 5 C.W. Intake

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
Split		External Tasks		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

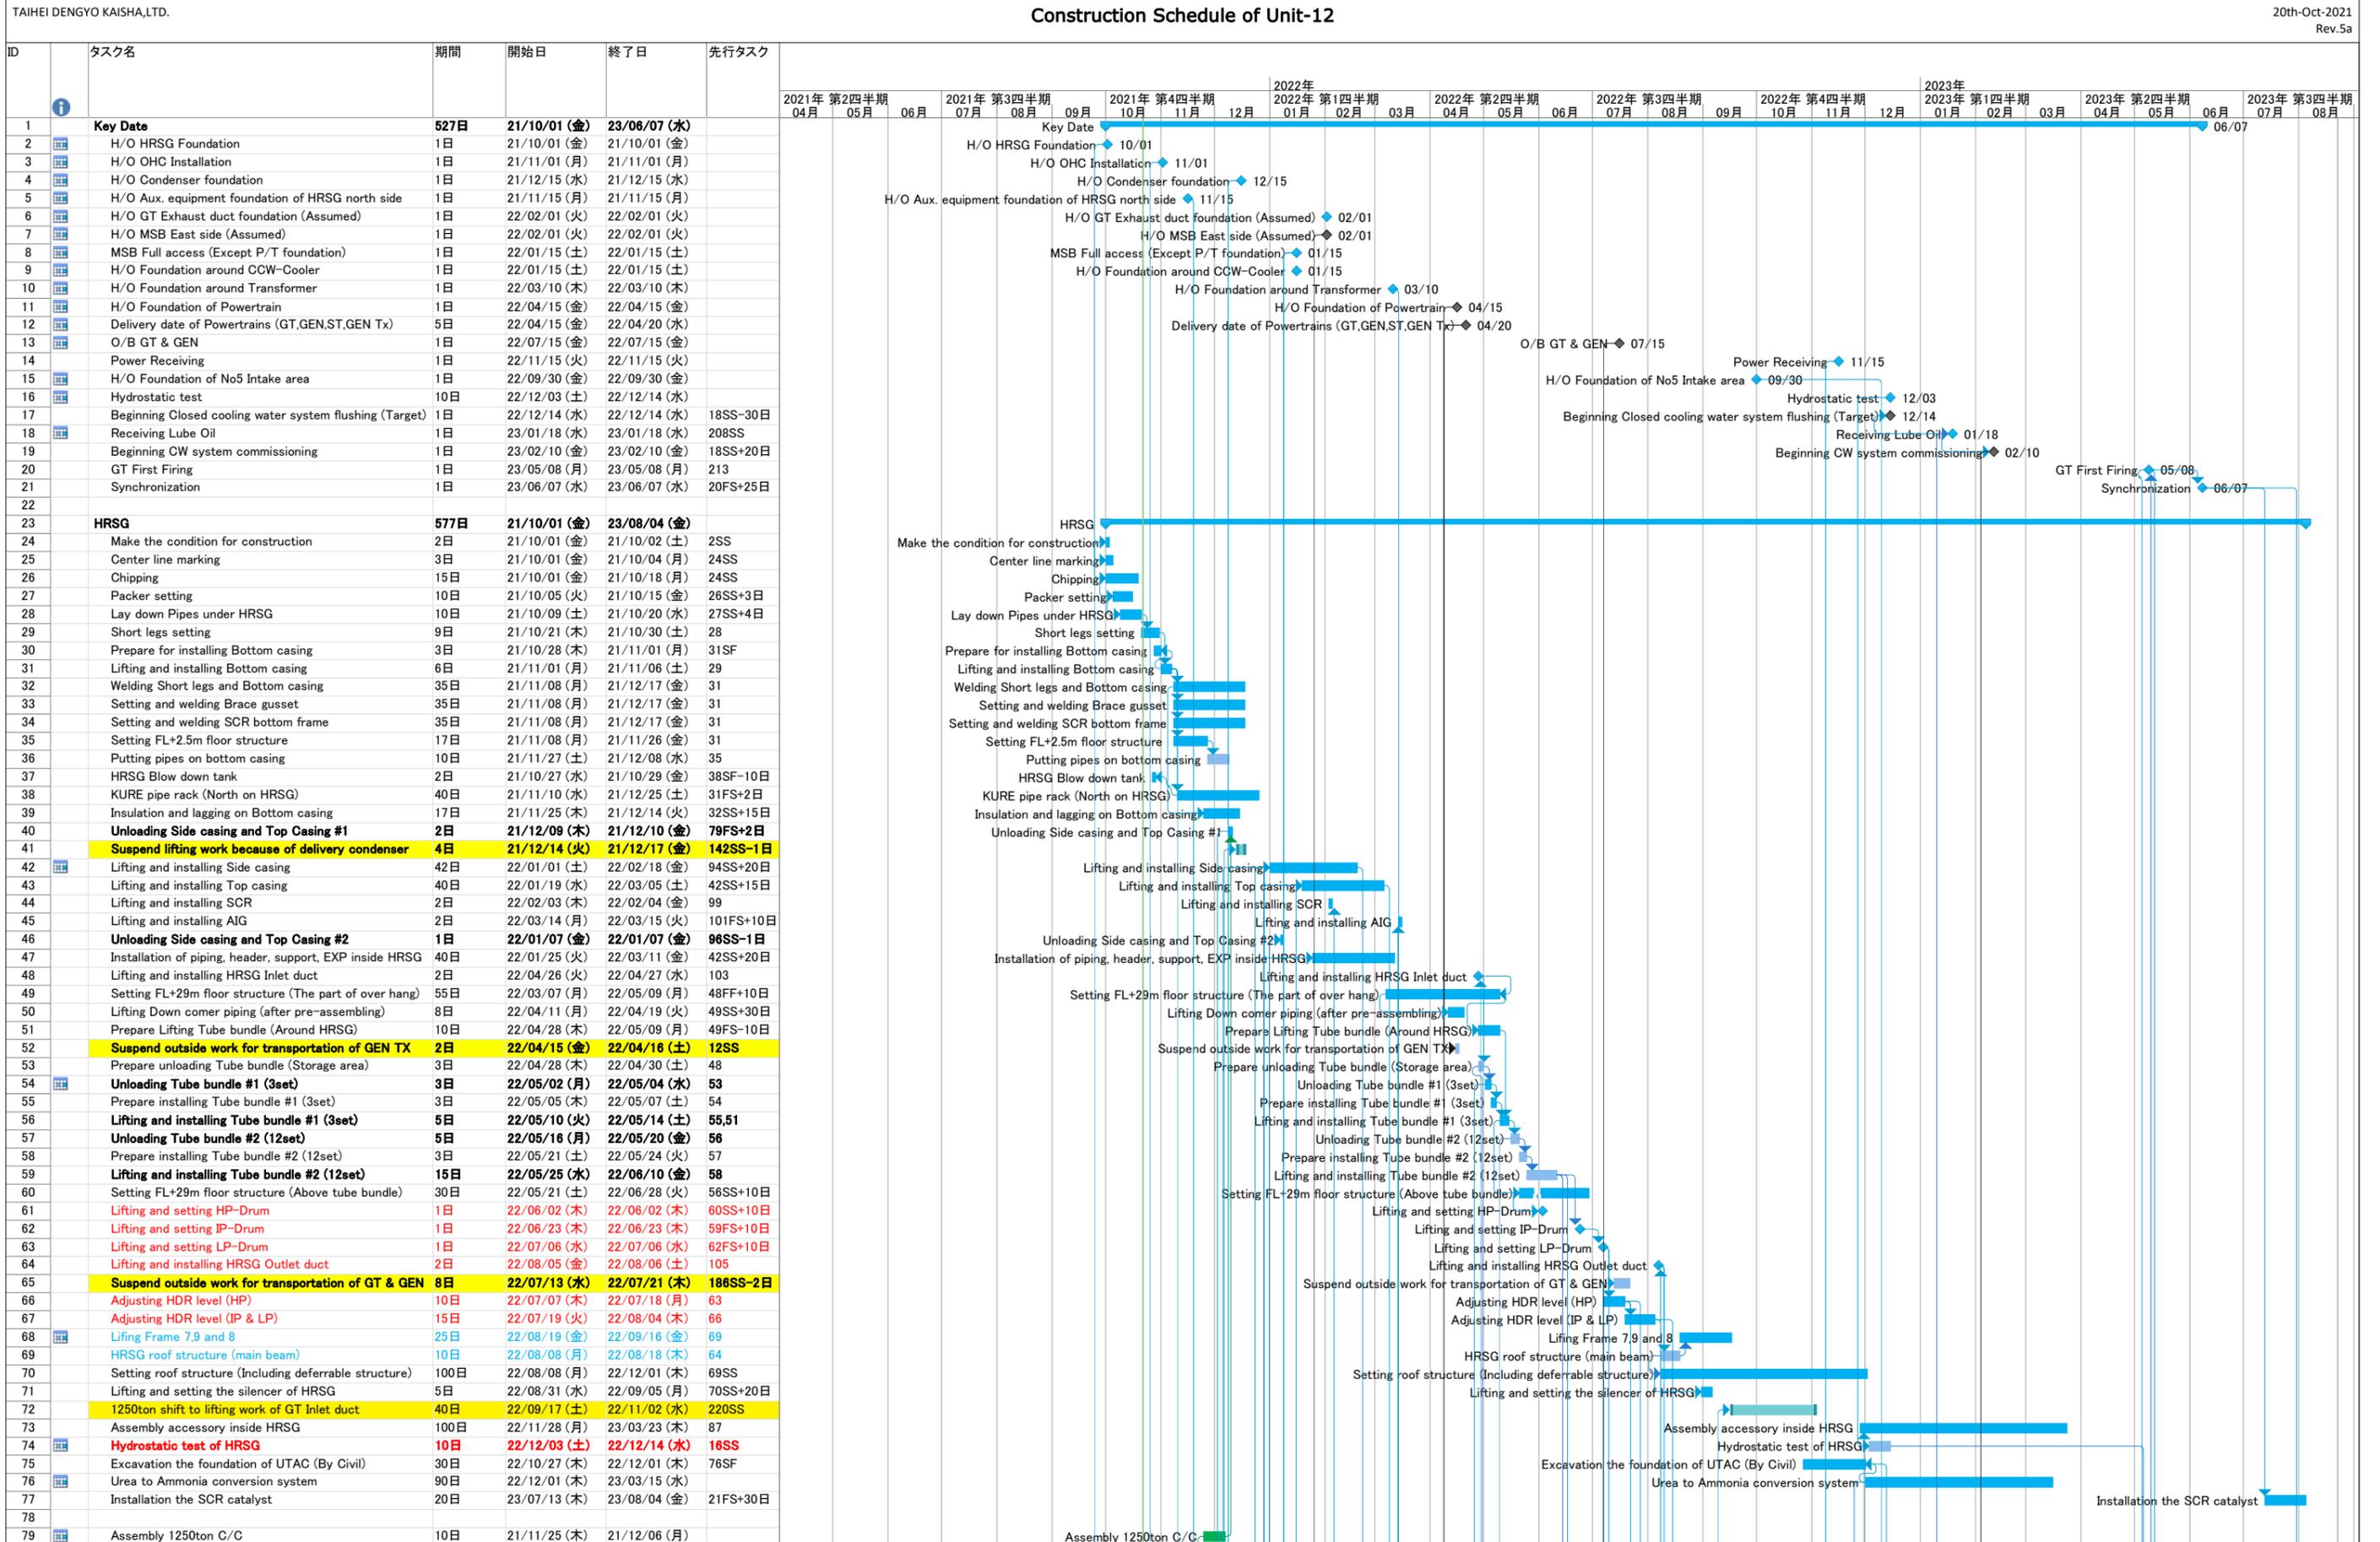

NOTE

1. The key date is subjected in the KOM held on 30th-Sep.

2. The east area on the MSB is assumed to be handovered before B-Feb-2022 according to the above key date changed.

3. Considered the affection of KURE's schedule belows;

i) Because of delaying the side casing, installation Inlet duct is postponed.

ii) Because of delivery 12 TBs in one time, no enough area for pre-ass'y Outlet duct and GT Inlet duct on schedule.











**Monthly Waste Flow Table for March 2023**

Project: Lamma Power Station Extension Civil and Building Works for Unit L12

Contractor: Paul Y. Construction Company, Limited

Record by: Ben Lam

Year of Record: 2020, 2021, 2022 & 2023

MM.YYYY	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of Non-inert C&D Materials Generated Monthly						
	Excavated Materials				Non-excavated Materials				Metals (steel bar / metal strip) <sup>(1)</sup>	Metals (aluminum can) <sup>(1)</sup>	Paper / cardboard packaging <sup>(1)</sup>	Plastics <sup>(1) &amp; (4)</sup>	Chemical waste (wasted lubricant oil/oil container)	Chemical waste (wasted lubricant oil/oil container)	Other, e.g. general refuse
	Disposed in Public Fill	Disposed in Sorting Facilities	Others (e.g Reused in the Contract/ Other Projects)	Broken Concrete or Construction Waste Collected by Recycled Company	Reused in the Contract	Reused in other Projects	Disposed in Public Fill	Disposed in Sorting Facilities							
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)							
Dec 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Jan 2021	0.00	0.00	21020.16	0.00	0.00	0.00	0.00	0.00	8.82	0.00	0.00	0.00	0.00	0.00	0.00
Feb 2021	0.00	0.00	18083.97	0.00	0.00	0.00	0.00	0.00	18.25	0.00	0.25	0.00	0.00	0.00	0.00
Mar 2021	0.00	0.00	9048.21	0.00	0.00	0.00	0.00	0.00	7.69	0.00	0.00	0.00	0.00	0.00	2.61
Apr 2021	0.00	0.00	3205.15	0.00	0.00	0.00	0.00	0.00	28.08	0.00	0.00	0.00	0.00	0.00	14.45
May 2021	0.00	0.00	6267.49	0.00	0.00	0.00	0.00	0.00	34.68	0.00	0.00	0.00	0.00	0.00	0.00
Jun 2021	0.00	0.00	6555.38	0.00	0.00	0.00	0.00	0.00	26.87	0.00	0.00	0.00	0.00	0.00	25.03
Jul 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.95	0.00	0.00	0.00	0.00	0.00	10.97
Aug 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	14.55	0.00	0.00	0.00	0.00	0.00	3.49
Sep 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.40	0.28	49.15	
Oct 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.47	0.00	0.00	0.00	0.00	0.00	62.08
Nov 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.08	0.00	0.00	0.00	0.00	0.00	34.17
Dec 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	10.36	0.00	0.00	0.00	0.00	0.00	52.18
Jan 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.93	0.00	0.00	0.00	0.00	0.00	42.73
Feb 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.62
Mar 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	24.21	0.00	0.000	0.00	0.00	0.00	25.70
Apr 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	5.51	0.00	0.00	0.00	0.00	0.00	0.00	52.83
May 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.36	0.00	0.00	0.00	0.00	0.00	38.60
Jun 2022	0.00	0.00	6645.22	0.00	0.00	0.00	0.00	5.70	0.00	0.00	0.000	0.00	0.00	0.00	37.38
Jul 2022	0.00	0.00	4710.98	0.00	0.00	0.00	0.00	6.58	11.55	0.00	0.000	0.00	0.00	0.00	25.22
Aug 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.60	0.42	21.74
Sep 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.64	0.00	0.000	0.00	0.00	0.00	48.57
Oct 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	44.71
Nov 2022	0.00	0.00	4930.52	0.00	0.00	0.00	0.00	0.00	6.67	0.00	0.000	0.00	0.00	0.00	12.15
Dec 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	6.21	0.00	0.000	0.00	0.00	0.00	62.32
Jan 2023	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	10.57	0.00	0.000	0.00	0.00	0.00	8.89
Feb 2023	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	7.39
Mar 2023	0.00	0.00	4910.49	0.00	0.00	0.00	0.00	0.00	17.09	0.00	0.000	0.00	0.00	0.00	28.59
Total	0.00	0.00	85377.56	0.00	0.00	0.00	0.00	17.79	312.03	0.00	0.25	0.00	1.00	0.70	719.57

Total Inert C&D Waste Materials Generated	Non-inert C&D Materials		
	C&D Materials Recycled	C&D Waste Disposed of at Landfill	Chemical Waste
85395.35 tonnes	312.28 tonnes	719.57 tonnes	0.70 tonnes

Where (A) Inert C&D materials include bricks, concrete, building debris, rubble and excavated spoil. In total, 85395.35 tonnes of inert C&D material were generated from the Project, of which 85377.56 tonnes were reused in this and other contracts, and the remaining 5.51 tonnes were disposed as public fill to Fill Banks / Sorting Facilities.

(b) Non-inert C&D materials (construction wastes) include metals, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Metals generated from the Project were grouped into construction wastes as the materials were not disposed of with others at the public fill.

(c) 17090 kg of metals, 0 kg of papers/ cardboard packing and 0 kg of plastics were sent to recyclers for recycling during the reporting period.

(d) Construction wastes other than metals, paper/cardboard packaging, plastics and chemicals were disposed of at Landfill.

- Notes:
- (1) metal, paper & plastic were collected by recycler
  - (2) The performance target of waste recycling are specified in the Contract.
  - (3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (4) Plastics refer to plastic bottles/ containers, plastic/ foam from packaging material.
  - (5) Broken concrete for recycling into aggregates.
  - (6) Disposal of inert waste to public fill or sorting facilities will NOT be considered as recycled waste.

**Monthly Waste Flow Table for March 2023**

Project: Civil Works for No. 5 C.W. Intake and Cable Bridge at Lamma Power Station Extension

Contractor: Paul Y. Construction Company, Limited

Record by: Ben Lam

Year of Record: 2020, 2021, 2022 & 2023

MM.YYYY	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of Non-inert C&D Materials Generated Monthly						
	Excavated Materials				Non-excavated Materials				Metals (steel bar / metal strip) <sup>(1)</sup>	Metals (aluminum can) <sup>(1)</sup>	Paper / cardboard packaging <sup>(1)</sup>	Plastics <sup>(1) &amp; (4)</sup>	Chemical waste (wasted lubricant oil/oil container)	Chemical waste (wasted lubricant oil/oil container)	Other, e.g. general refuse
	Disposed in Public Fill	Disposed in Sorting Facilities	Others (e.g Reused in the Contract / Other Projects)	Broken Concrete or Construction Waste Collected by Recycled Company	Reused in the Contract	Reused in other Projects	Disposed in Public Fill	Disposed in Sorting Facilities							
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)							
Oct 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Nov 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Dec 2020	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.21	0.00	0.00	0.00	0.00	0.00	0.00
Jan 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Feb 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Mar 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	7.49
Apr 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.60	0.42	4.85
May 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.61
Jun 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Jul 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Aug 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Sep 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	37.84
Oct 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	24.93
Nov 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Dec 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Jan 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	46.25
Feb 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.45
Mar 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	29.86
Apr 2022	0.00	0.00	15076.84	0.00	0.00	0.00	0.00	10.27	0.00	0.00	0.000	0.00	0.00	0.00	43.60
May 2022	0.00	0.00	29151.94	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	54.64
Jun 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	11.79
Jul 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	24.04	0.00	0.00	0.000	0.00	0.00	0.00	35.90
Aug 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	41.91
Sep 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	51.26
Oct 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	37.87
Nov 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	31.69
Dec 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	7.29	0.00	0.000	0.00	0.00	0.00	24.62
Jan 2023	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	0.00	0.00	0.00	39.90
Feb 2023	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.67	0.00	0.000	0.00	0.00	0.00	6.17
Mar 2023	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.59	0.00	0.000	0.00	0.00	0.00	35.13
Total	0.00	0.00	44228.78	0.00	0.00	0.00	0.00	34.31	36.76	0.00	0.00	0.00	0.60	0.42	601.76

Total Inert C&D Waste Materials Generated	Non-inert C&D Materials		
	C&D Materials Recycled	C&D Waste Disposed of at Landfill	Chemical Waste
44263.09 tonnes	36.76 tonnes	601.76 tonnes	0.42 tonnes

Where (A) Inert C&D materials include bricks, concrete, building debris, rubble and excavated spoil. In total, 44263.09 tonnes of inert C&D material were generated from the Project, of which 44228.78 tonnes were reused in this and other contracts, and the remaining 10.27 tonnes were disposed as public fill to Fill Banks / Sorting Facilities.

(b) Non-inert C&D materials (construction wastes) include metals, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Metals generated from the Project were grouped into construction wastes as the materials were not disposed of with others at the public fill.

(c) 16590 kg of metals, 0 kg of papers/ cardboard packing and 0 kg of plastics were sent to recyclers for recycling during the reporting period.

(d) Construction wastes other than metals, paper/cardboard packaging, plastics and chemicals were disposed of at Landfill.

- Notes:
- (1) metal, paper & plastic were collected by recycler
  - (2) The performance target of waste recycling are specified in the Contract.
  - (3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (4) Plastics refer to plastic bottles/ containers, plastic/ foam from packaging material.
  - (5) Broken concrete for recycling into aggregates.
  - (6) Disposal of inert waste to public fill or sorting facilities will **NOT** be considered as recycled waste.

### Monthly Waste Flow Table for March 2023

Project: LAMMA POWER STATION EXTENSION – Unit 12 Complete Erection, Inspection, Testing & Commissioning of Power Block Facilities

Contractor: Taihei Dengyo Kaisha, Ltd.

Record by: Stephen Sin

Year of Record: 2021, 2022, 2023

MM.YYYY	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of Non-inert C&D Materials Generated Monthly					
	Excavated Materials			Non-excavated Materials					Metals (steel bar / metal strip) <sup>(1)</sup>	Metals (aluminum can) <sup>(1)</sup>	Paper / cardboard packaging <sup>(1)</sup>	Plastics <sup>(1) &amp; (4)</sup>	Chemical waste (wasted lubricant oil/oil container)	Other, e.g. general refuse
	Disposed in Public Fill	Disposed in Sorting Facilities	Others (e.g. Reused in the Contract / Other Projects)	Broken Concrete or Construction Waste Collected by Recycled Company	Reused in the Contract	Reused in other Projects	Disposed in Public Fill	Disposed in Sorting Facilities						
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in L)	(in '000kg)	
Nov 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Dec 2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Jan 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	10.36
Feb 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	9.29
Mar 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.59
Apr 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	19.42
May 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	19.93
Jun 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	18.60
Jul 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.57
Aug 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	19.40
Sep 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.96
Oct 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	12.89
Nov 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.83
Dec 2022	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	14.58
Jan 2023	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.11
Feb 2023	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.50
Mar 2023	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.86
Total	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	243.89

Total Inert C&D Waste Materials Generated	Non-inert C&D Materials		
	C&D Materials Recycled	C&D Waste Disposed of at Landfill	Chemical Waste
0.00 tonnes	0.00 tonnes	243.89 tonnes	0 Liters

Where (A) Inert C&D materials include bricks, concrete, building debris, rubble and excavated spoil. In total, 0.00 tonnes of inert C&D material were generated from the Project, of which 0 tonnes were reused in this and other contracts, and the remaining 0.00 tonnes were disposed in Public Fill and Sorting Facilities.

(b) Non-inert C&D materials (construction wastes) include metals, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Metals generated from the Project were grouped into construction wastes as the materials were not disposed of with others at the public fill.

(c) 0 kg of metals, 0 kg of papers/ cardboard packing and 0 kg of plastics were sent to recyclers for recycling during the reporting period.

(d) Construction wastes other than metals, paper/cardboard packaging, plastics and chemicals were disposed of at Landfill.

Notes:

- (1) metal, paper & plastic were collected by recycler
- (2) The performance target of waste recycling are specified in the Contract.
- (3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (4) Plastics refer to plastic bottles/ containers, plastic/ foam from packaging material.
- (5) Broken concrete for recycling into aggregates.
- (6) Disposal of inert waste to public fill or sorting facilities will **NOT** be considered as recycled waste.
