DATA DATE: 01-Mar-25 | LAYOUT: 24-83005 UPDATE | PAGE 1 OF 11

#	Act ID	Activity Name	Duration	Start	Finish
1	**Contract No. 24-83005 Lamma Power Station Extention Civil and Building Works for Unit 13**		2281	01-Mar-25	29-May-31
2	**KEY DATES**		2171	19-Jun-25	29-May-31
3	KD1000	Tentative Date of Commencement (Hand over of Major Work Area)	0	19-Jun-25*	
4	KD1010	Full mobilization of Site Team	0		02-Jul-25
5	KD1020	Completion date for the whole of the works	0		30-May-30*
6	KD1030	Defect Liability Period	0		29-May-31
7	**SITE POSSESSION DATE & COMPLETION DATE**		1886	01-Apr-25	31-May-30
8	**WORKS AREA ACCESS DATE**		897	01-Apr-25	15-Sep-27
9	AD1010	Area G1 - L13 MSB & HRSG	0	19-Jun-25*	
10	AD1020	Area G2A - L13 MSB & HRSG	0	19-Jun-25*	
11	AD1030	Area G2B - L13 MSB & HRSG	0	19-Jun-25*	
12	AD1040	Area G3 - L13 MSB & HRSG	0	19-Jun-25*	
13	AD1050	Area G3A - L13 MSB & HRSG	0	30-Jun-25*	
14	AD1060	Area G1A - CW Outdoor Cooler Pump	0	19-Jun-25*	
15	AD1070	Area G4 - CW Culvert & External Works	0	19-Jun-25*	
16	AD1080	Area G5 - CW Culvert & External Works	0	19-Jun-25*	
17	AD1090	Area G6 (Stage 1) (Plan) - L13 GRS	0	15-Jul-25*	
18	AD1100	Area G6 (Stage 2) (Plan) - L13 GRS	0	15-Sep-27*	
19	AD1110	Area G7A (Stage 1) (Plan) - L13 GRS	0	15-Jul-25*	
20	AD1120	Area G7A (Stage 2) (Plan) - L13 GRS	0	15-Sep-27*	
21	AD1130	Area G7B (Stage 1) (Plan) - L13 GRS	0	15-Jul-25*	
22	AD1140	Area G7B (Stage 2) (Plan) - L13 GRS	0	15-Sep-27*	
23	AD1150	Area G8 (Stage 1) (Plan) - L13 GRS	0	15-Jul-25*	
24	AD1160	Area G8 (Stage 2) (Plan) - L13 GRS	0	15-Sep-27*	
25	AD1170	Area G10 - External Works	0	01-Oct-26*	
26	AD1180	Area G11 - APX Trenching Works at LMX	0	01-Jul-27*	
27	AD1190	Area G12 - External Works	0	01-Jan-27*	
28	AD1200	Area G13 (Plan) - No. 5 CW Pump Eqwuipment Room	0	15-Jul-25*	
29	AD1210	Area G14 - Light Oil Tank A&A And Associated Trenching Works	0	01-Oct-25*	
30	AD1220	Area G15 - 275kV s/s II	0	01-Oct-25*	
31	AD1230	Area G16 (Plan) - No. 5 CW Intake	0	15-Jul-25*	
32	AD1240	Area G16A (Plan) - No. 5 CW Intake	0	15-Jul-25*	
33	AD1250	Area G17A - Shunt Reactor Compound No. 7 & 8	0	01-Jan-27*	
34	AD1260	Area G17B - Shunt Reactor Compound No. 7 & 8	0	01-Jan-27*	
35	AD1270	Area G18 (Plan) - Site Toilet	0	15-Jul-25*	
36	AD1280	Area G22 (Plan) - Demolition Work of Urea Shelter	0	15-Jul-25*	
37	AD1290	Area G19 - ACB Modification Works	0	02-Jun-25*	
38	AD1300	Area G20 (Plan) - No.5 Chinmey	0	15-Jul-25*	
39	AD1310	Area G21 - L11 Inspection Manhole For CW Culvert	0	01-Sep-25*	
40	AD1320	Area G23 - L10 MSB (Shower Pit)	0	01-Sep-25*	
41	AD1330	Area G24 - L11 MSB (Shower Pit)	0	01-Nov-25*	
42	AD1340	Area G26 - DG Store	0	02-Jun-25*	
43	AD1350	Area B1A - External Works	0	01-Jan-27*	
44	AD1360	Area B1 - L13 Superstructure Storage Area	0	01-Apr-25*	
45	AD1370	Area B2 - L13 Superstructure Storage Area	0	01-Apr-25*	
46	AD1380	Area D2 - L13 Superstructure Storage Area	0	19-Jun-25*	
47	AD1390	Area D7 - L13 Superstructure Storage Area	0	23-Apr-25*	
48	AD1400	Area D8 (Plan) - L13 Superstructure Storage Area	0	15-Jul-25*	
49	**SECTION COMPLETION DATE**		1219	19-May-25	18-Sep-28
50	SC1010	Sect Ai - Supporting Structures for Overhead Cranes of L13 MSB incl. roof str except deferred wk	395	19-Jun-25*	18-Jul-26
51	SC1020	Sect Aii - Ext. Wks incl. CW Outlet Culvert Pipes	395	19-Jun-25*	18-Jul-26
52	SC1030	Sect Bi - Ext. Wk Incl. CW Inlet Culvert Pipes	306	19-Jun-25*	20-Apr-26
53	SC1040	Sect Bii - L13 Gas Rec. St Eqpt Rm - Stage 1 (Plan)	306	15-Jul-25*	16-May-26
54	SC1060	Sect Ci - Southern Part of L13 HRSG and its Surrounding	334	19-Jun-25*	18-May-26
55	SC1070	Sect Cii - Remaining Northern Part of L13 HRSG Area and its Surrounding	410	19-Jun-25*	02-Aug-26
56	SC1090	Sect Ciii - G/F of L13 MSB incl. Condenser Pit, etc fdn GL 13-B ~ C and 13-1 ~ 6 for installation of condenser	426	19-Jun-25*	18-Aug-26
57	SC1100	Sect Civ - No.5 CW Intake L13 Pump Chamber, Drum Screen Chamber, and Penstock Chamber (Plan)	334	15-Jul-25*	13-Jun-26
58	SC1110	Sect Di - CW Pump Equipment Room No. 5 and Its Surrounding (Plan)	699	15-Jul-25*	13-Jun-27
59	SC1120	Sect Dii - No. 5 CW Intake Remaining Works (Plan)	700	15-Jul-25*	14-Jun-27
60	SC1130	Sect Diii - 275kV Switch St. Phase II A & A Works	365	01-Oct-25*	30-Sep-26
61	SC1140	Sect Div - Plinth and Pipe Support for LMX Light Oil Tank Farm	396	01-Oct-25*	31-Oct-26
62	SC1150	Sect Dv - LMX Dangerous Goods Store Alterations and Additions Works	122	02-Jun-25*	01-Oct-25
63	SC1160	Sect Ei - Whole of L13 MSB incl. Pipe and Cable Rack along South Facade with Udr Grd Utilities	487	19-Jun-25*	18-Oct-26

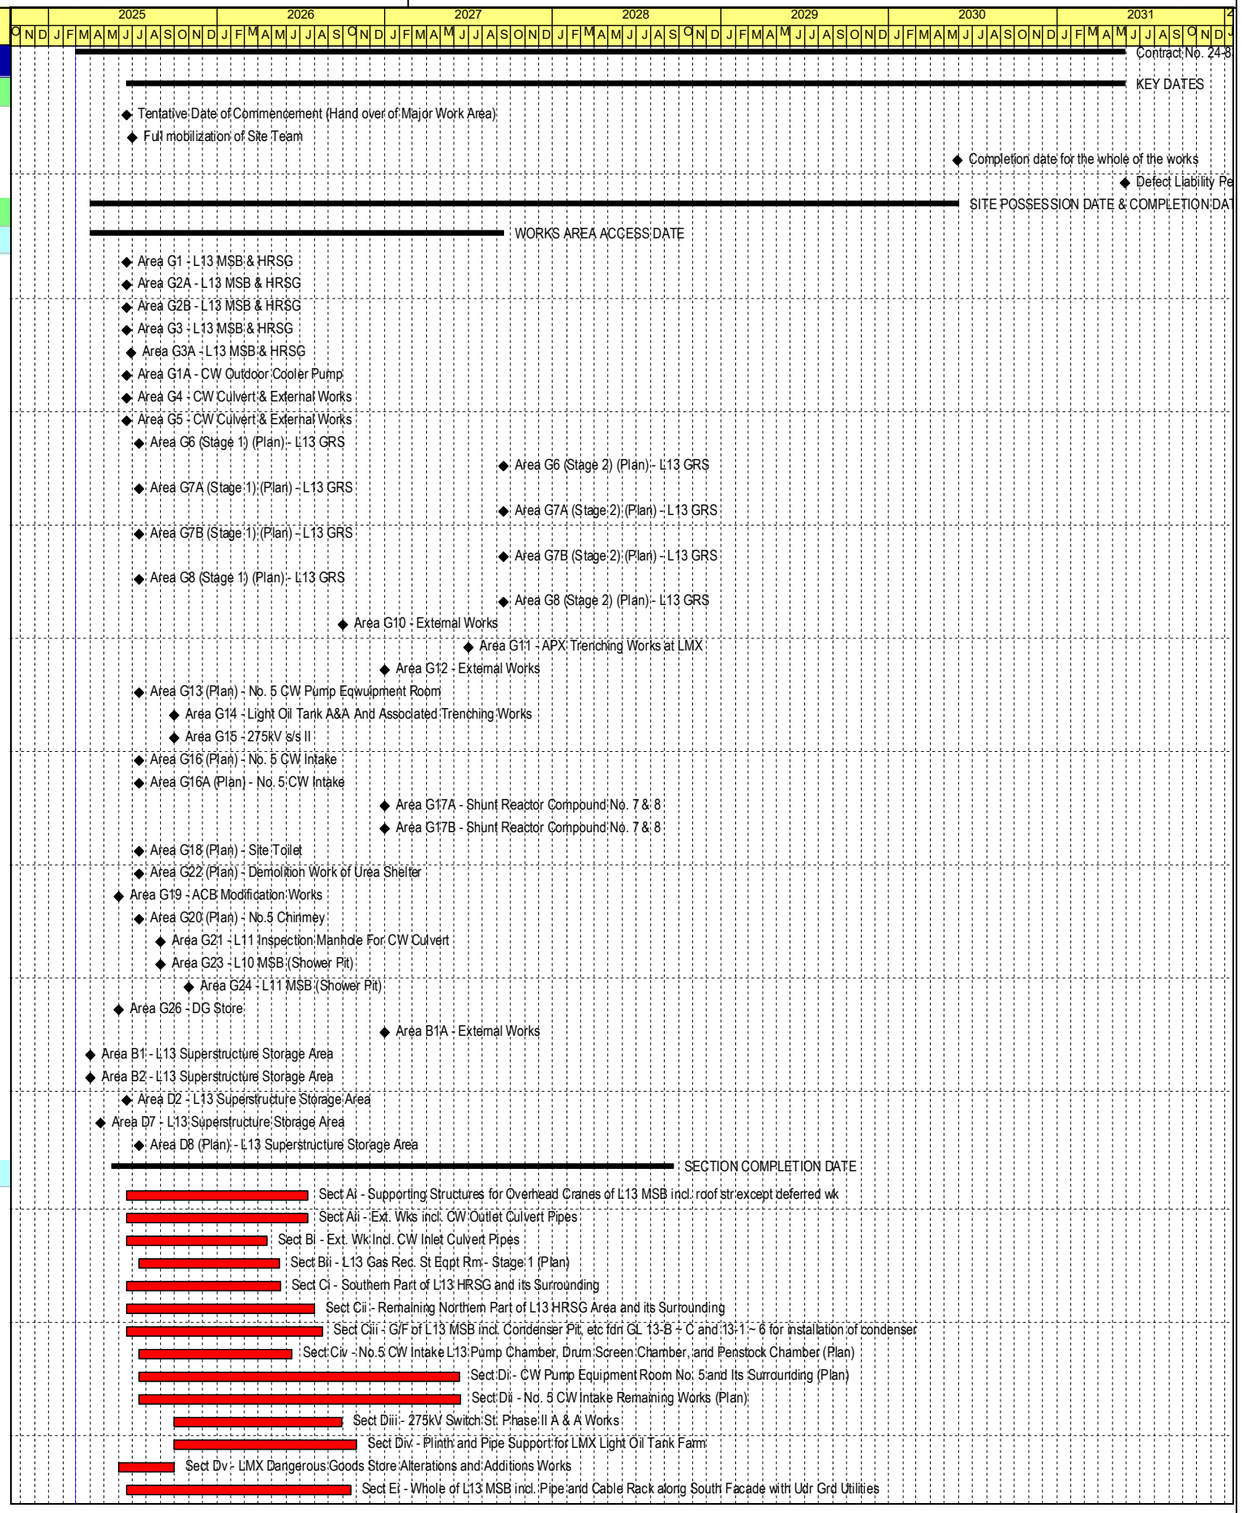

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Lamma Power Station Extension
Civl and Building Works for Unit 13
Contract No. 24-83005
Master Programme

Date	Revision	Checked	Approved

DATA DATE: 01-Mar-25 | LAYOUT: 24-83005 UPDATE | PAGE 2 OF 11

#	Act ID	Activity Name	Duration	Start	Finish
64	SC1170	Sect Eii - Link Bridge Between L12 & L13 MSB & Associate A&A Wk in L12 MSB (Plan)	487	15-Jul-25*	13-Nov-26
65	SC1180	Sect Eiii - L13 Turbo Block Foundation incl. L13 MSB Ground Flr with Eqpt Fdn Betwenn GL 13-D ~ H & GL 13-1 ~ 6	487	19-May-25*	17-Sep-26
66	SC1190	Sect Eiv - Cable Ducts Between L12 and L13 MSB for Temp Power Supply (Plan)	487	15-Jul-25*	13-Nov-26
67	SC1200	Sect Ev - L13 HRSG Equipment Room Building Service and Others Associated Works	487	19-Jun-25*	18-Oct-26
68	SC1210	Sect F1i - ACB Modification Wks at Area G19 - L9	517	02-Jun-25*	31-Oct-26
69	SC1220	Sect F1ii - ACB Modification Wks at Area G19 - L10 & L11	821	02-Jun-25*	31-Aug-27
70	SC1230	Sect F1iii - ACB Modification Wks at Area G19 - L13	486	02-Jun-25*	30-Sep-26
71	SC1240	Sect F2i - No. 5 Chinmeny Modification Works at Area G20 (Plan)	822	15-Jul-25*	14-Oct-27
72	SC1250	Sect F2ii - Completion of Exhaust Gas Duct Foundation at G3A (Plan)	609	30-Jun-25*	28-Feb-27
73	SC1260	Sect G - Station Toilet Fdn and Bldg Wk and Removal of Urea Plant Shelter in Area G18 & G22	640	15-Jul-25*	15-Apr-27
74	SC1270	Sect Hi - Ext Wks at Area G12	181	01-Jan-27*	30-Jun-27
75	SC1280	Sect Hii - Ext Wks at Area G10	273	01-Oct-26*	30-Jun-27
76	SC1290	Sect Hiii - L13 Shunt Reactor Modification at Bay 7 Area G17A	273	01-Jan-27*	30-Sep-27
77	SC1300	Sect Hiv - L13 Shunt Reactor Modification at Bay 8 Area G17B	424	01-Jan-27*	28-Feb-28
78	SC1310	Sect Ii - Trenches & Pits Surrounding Lf13 Gas Receiving St Eqpt Room in Area G6, G7A & G8	107	01-Jun-27*	15-Sep-27
79	SC1320	Sect Iii - Whole of L13 Gas Receiving St. Eqpy Rm - Stage 2, L13 GRS External Fdn, etc in ARea G6, G7A, G7B and G8	245	01-Jun-27*	31-Jan-28
80	SC1330	Sect Ji - Civil Works for APX Cable Div at LMX in Area G11	305	01-Jul-27*	30-Apr-28
81	SC1340	Sect Jii - APX Cable Div.Wk at LPS	547	01-Jan-27*	30-Jun-28
82	SC1350	Sect K - Improvement Wks for L11 CW Inlet Pipes at Area G21	123	01-Sep-25*	01-Jan-26
83	SC1360	Sect L - Refurbishment Wk on Existing Workshop Area Bet Generation Main Bldg & Training & Workshop Bldg	275	02-Jun-25*	03-Mar-26
84	SC1370	Sect M - Delivery of L13 HRSG Lift Shaft Precast Conc. Panels	0		01-Aug-27*
85	SC1380	Sect Ni - MSB Work (OP)	0		20-Apr-28*
86	SC1390	Sect Nii - Others Works Completed (OP) for Reporting Completion to Buildings Department	0		19-Jul-28*
87	SC1400	Sect Oi - Emergency Shower Pit at L10 MSB	91	01-Sep-25*	30-Nov-25
88	SC1410	Sect Oii - Emergency Shower pit at L11 MSB	92	01-Nov-25*	31-Jan-26
89	SC1420	Sect P - All Remaining Works Except Deferred Work	0		18-Sep-28*
90	SC1430	Sect Q1i - Fabrication of L12 Precast Panel with Stell Sub-Frame (Optionslk Work (1)) (Plan)	151	15-Jul-25*	12-Dec-25
91	SC1440	Sect Q1ii - Construction of In-Situ Roof Slab (Optional Works(1))	22	15-Oct-25*	05-Nov-25
92	SC1520	Sect Q2 - Improvement Works for Existing L11 CW Inlet Pipe inside L11 MSB	365	20-Sep-27	18-Sep-28*
93	**WORKS AREA COMPLETION DATE**		1838	18-May-25	31-May-30
94	AC1000	Area G1 - L13 MSB & HRSG	0		18-Jul-26*
95	AC1010	Area G2A - L13 MSB & HRSG	0		02-Aug-26*
96	AC1020	Area G2B - L13 MSB & HRSG	0		18-May-26*
97	AC1030	Area G3 - L13 MSB & HRSG	0		18-May-25*
98	AC1040	Area G3A - L13 MSB & HRSG (Plan)	0		28-Feb-27*
99	AC1050	Area G1A - C.W. Outdoor Cooler Pump	0		18-Jul-26*
100	AC1060	Area G4 - C.W. Culvert & External Works	0		18-Jul-26*
101	AC1070	Area G5 - C.W. Culvert & External Works	0		20-Apr-26*
102	AC1080	Area G6 - L13 GRS (Plan)	0		16-May-28*
103	AC1090	Area G7A - L13 GRS (Plan)	0		16-May-28*
104	AC1100	Area G7B - L13 GRS (Plan)	0		16-May-28*
105	AC1110	Area G8 - L13 GRS (Plan)	0		16-May-28*
106	AC1120	Area G10 - External Works	0		30-Jun-27*
107	AC1130	Area G11 - APX Trenching Works at LMX	0		30-Apr-28*
108	AC1140	Area G12 - External Works	0		30-Apr-28*
109	AC1150	Area G13 - No. 5 C.W. Pump Equipment Room	0		13-Jun-27*
110	AC1160	Area G14 - Light Oil Tank A&A And Associated Trenching Works	0		31-Oct-26*
111	AC1170	Area G15 - 257kV S/S II	0		30-Sep-26*
112	AC1180	Area G16 - No. 5 C.W. Intake	0		01-May-27*
113	AC1190	Area G16A - No. 5 C.W. Intake	0		01-May-26*
114	AC1200	Area G17A - Shunt Reactor Compound No. 7 & 8	0		30-Sep-27*
115	AC1210	Area G17B - Shunt Reactor Compound No. 7 & 8	0		28-Feb-28*
116	AC1220	Area G18 - Site Toilet (Plan)	0		15-Apr-27*
117	AC1230	Area G22 - Demilition Works of Urea Shelter (Plan)	0		31-Dec-26*
118	AC1240	Area G19 - ACB Modification Works - All Works Except Below	0		02-Dec-25*
119	AC1250	Area G19 - ACB Modification Works - L9	0		31-Oct-26*
120	AC1260	Area G19 - ACB Modification Works - L10 & L11	0		31-Aug-27*
121	AC1270	Area G19 - ACB Modification Works - L13	0		30-Sep-26*
122	AC1280	Area G20 - No. 5 Chimney (Plinth)(Plan)	0		15-Mar-27*
123	AC1290	Area G20 - No. 5 Chimney (Flue) (Plan)	0		14-Oct-27*
124	AC1300	Area G21 - L11 Inspection Manhole For CW Culvert	0		01-Jan-26*
125	AC1310	Area G23 - L10 MSB (Shower Pit)	0		30-Nov-25*
126	AC1320	Area G24 - L11 MSB (Shower Pit)	0		31-Jan-26*
127	AC1330	Area G26 - DG Store	0		01-Oct-25*
128	AC1340	Area B1A - External Works	0		15-Sep-27*
129	AC1350	Area B1 - L13 Superstructure Storage Area	0		31-May-30*
130	AC1360	Area B2 - L13 Superstructure Storage Area	0		31-Jul-26*
131	AC1370	Area D2 - L13 Superstructure Storage Area	0		18-May-26*
132	AC1380	Area D7 - L13 Superstructure Storage Area	0		31-May-30*
133	AC1390	Area D8 - L13 Superstructure Storage Area	0		31-May-25*
134	WA1278	Area G25	0		06-Nov-25*
135	**STATUTORY SUBMISSION**		1072	15-May-25	20-Apr-28
136	SS1100	Unit 13 ELS, Pile Cap & Tie-Beam - Consent Application	0	15-May-25*	

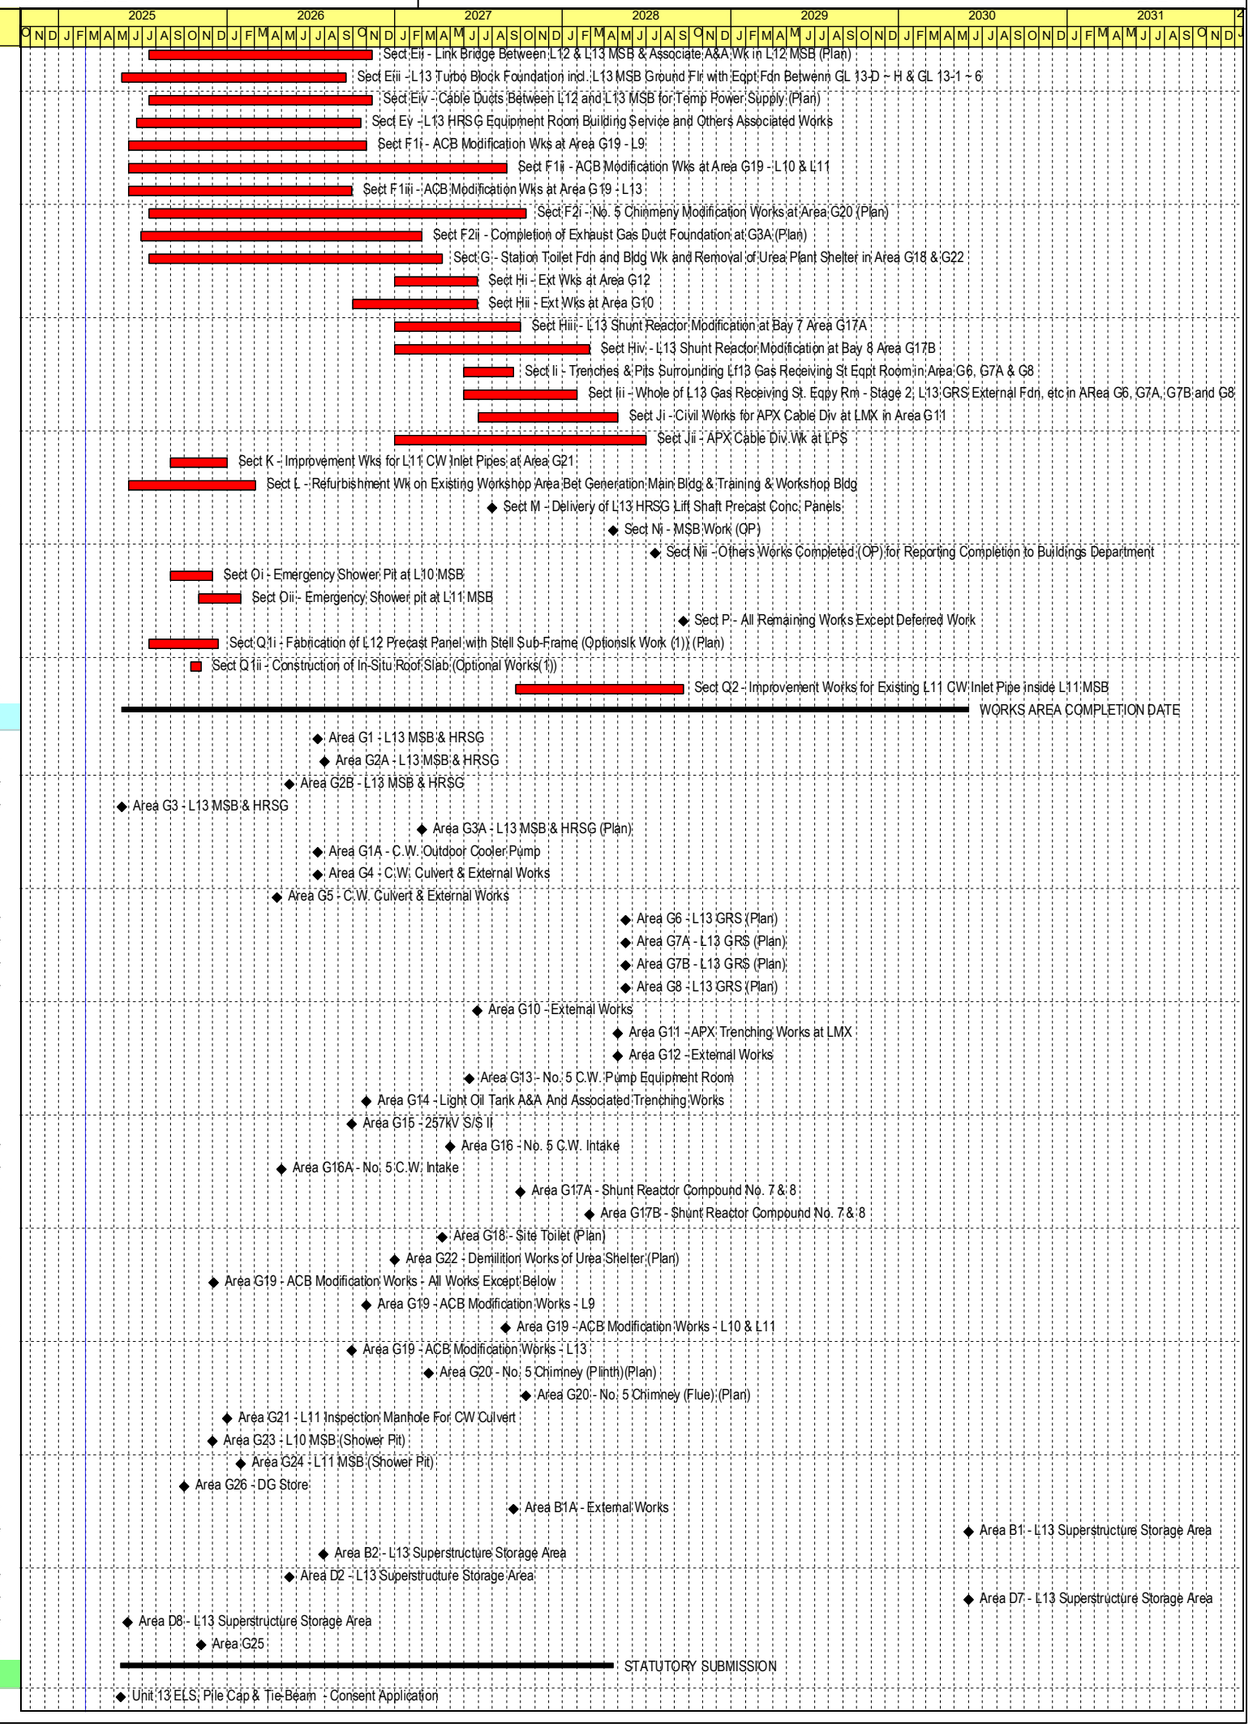

DATA DATE: 01-Mar-25 | LAYOUT: 24-83005 UPDATE | PAGE 3 OF 11

#	Act ID	Activity Name	Duration	Start	Finish
137	SS1110	Unit 13 ELS Works - BA10 Submission	0	17-Jun-25*	
138	SS1140	Unit 13 MSB BA13 Submission	0		20-Apr-28*
139	**CONTRACTOR'S DESIGN SUBMISSION**		235	19-Jun-25	09-Feb-26
140	**CLADDING WALL DESIGN AND DRAWINGS**		133	19-Jun-25	30-Oct-25
141	DES1000	Cladding & Str. Steel Design Submission - Interface Coordination with NSC	45	19-Jun-25	02-Aug-25
142	DES1010	Cladding & Str. Steel Design Submission - Drawing and Calculation Prepare for BD Submission	45	19-Jun-25	02-Aug-25
143	DES1020	Cladding & Str. Steel Design Submission - BD 1st Submission	0	03-Aug-25	
144	DES1030	Cladding & Str. Steel Design Submission - BD Approval	0	02-Oct-25	
145	DES1040	Cladding & Str. Steel - Consent Application	0	02-Oct-25	
146	DES1050	Cladding & Str. Steel - Consent Issuance	0	30-Oct-25	
147	DES1060	Cladding & Str. Steel - Submission of BA10	0	30-Oct-25	
148	DES1070	Cladding & Str. Steelwork - Shop Drawing Submission to HEC	28	03-Aug-25	30-Aug-25
149	DES1080	Cladding & Str. Steelwrok - Shop Drawing Approval by HEC	28	31-Aug-25	27-Sep-25
150	**TOWER CRANE**		88	19-Jun-25	15-Sep-25
151	DES1090	Selection and Confirmation of Tower Crane	14	19-Jun-25	02-Jul-25
152	DES1100	Tower Crane - Design Preparation Submission	30	03-Jul-25	01-Aug-25
153	DES1110	Tower Crane - Engineer Review and Approval	30	02-Aug-25	31-Aug-25
154	DES1120	Tower Crane - Revise Design and Resubmit for Approval	30	16-Aug-25	14-Sep-25
155	DES1130	Tower Crane - Tower Crane Base Delivery (TC-01)	0	15-Sep-25*	
156	DES1140	Tower Crane - Tower Crane Base Delivery (TC-02)	0	15-Sep-25*	
157	**ELS FOR CABLE TRENCH**		154	18-Aug-25	19-Jan-26
158	DES1240	ELS - Design preparation	30	18-Aug-25	16-Sep-25
159	DES1250	ELS - Submit to Engineer for review	28	17-Sep-25	14-Oct-25
160	DES1260	ELS - Update Submission to incorporate Engineer's comments	6	15-Oct-25	20-Oct-25
161	DES1270	ELS - BD submission and approval	60	21-Oct-25	19-Dec-25
162	DES1280	ELS - BD consent to commence excavation	30	20-Dec-25	18-Jan-26
163	DES1290	ELS - BD10 submission	0	19-Jan-26	
164	**STEEL FLUE FOR UNIT 13**		235	19-Jun-25	09-Feb-26
165	DES1610	Steel Flue Unit 13 - Submission of Steel Flue Design Specialist for Approval	0	19-Jun-25	
166	DES1620	Steel Flue Unit 13 -HEC Review and Approval	30	19-Jun-25*	18-Jul-25
167	DES1630	Steel Flue Unit 13 - Design Preparation and Submission	45	19-Jul-25*	01-Sep-25
168	DES1640	Steel Flue Unit 13 - HEC Review and Approval	45	02-Sep-25*	16-Oct-25
169	DES1650	Steel Flue Unit 13 -Design Review and Approval	30	16-Sep-25*	15-Oct-25
170	DES1660	Steel Flue Unit 13 - Design Submit to BD	0	16-Oct-25	
171	DES1670	Steel Flue Unit 13 -BD Approval	0	15-Dec-25	
172	DES1680	Steel Flue Unit 13 -Consent Application	0	15-Dec-25	
173	DES1690	Steel Flue Unit 13 -Consent Approval	0	14-Jan-26*	
174	DES1700	Steel Flue Unit 13 -BA10 Submission	0	09-Feb-26*	
175	**SUPPORTING RACKS (LMX L9, L10, L11 & L13)**		60	19-Jun-25	17-Aug-25
176	DES1190	LMX Supporting Rack - Design preparation	30	19-Jun-25	18-Jul-25
177	DES1200	LMX Supporting Rack - Submit to Engineer for review and approval	30	19-Jul-25	17-Aug-25
178	**REFURBISHMENT WRKS. ON EXISTING WORKSHOP AREAS BET. GEN. MAINT. BLDG. & TRAIN. WORKSHOP BLDG.**		54	19-Jun-25	11-Aug-25
179	DES1210	Refurbishment Works - Design preparation (horading and roof replacement)	24	19-Jun-25	12-Jul-25
180	DES1220	Refurbishment Works - Submission to Engineer for review and approval	30	13-Jul-25	11-Aug-25
181	**CONTRACTOR'S PROCUREMENT AND OFF SITE FABRICATION**		643	19-Jun-25	23-Mar-27
182	**L13 STRUCTURAL STEEL**		228	03-Aug-25	18-Mar-26
183	**OFF-SITE FABRICATION**		228	03-Aug-25	18-Mar-26
184	PRO1230	Confirm Drawing and Method for Materials Ordering	30	03-Aug-25	01-Sep-25
185	PRO1250	1st Batch - Off-site Fabrication	42	30-Oct-25	10-Dec-25
186	PRO1260	1st Batch - Inspection	28	20-Nov-25	17-Dec-25
187	PRO1270	1st Batch - Delivery	7	18-Dec-25	24-Dec-25
188	PRO1280	2nd Batch - Off-site Fabrication	42	11-Dec-25	21-Jan-26
189	PRO1290	2nd Batch - Inspection	28	01-Jan-26	28-Jan-26
190	PRO1300	2nd Batch - Delivery	7	29-Jan-26	04-Feb-26
191	PRO1310	3rd Batch - Off-Site Fabrication	35	22-Jan-26	25-Feb-26
192	PRO1320	3rd Batch - Inspection	28	12-Feb-26	11-Mar-26
193	PRO1330	2rd Batch - Delivery	7	12-Mar-26	18-Mar-26
194	**STEEL FLUE FOR UNIT 13**		217	16-Oct-25	20-May-26
195	**SHOP DRAWINGS**		85	16-Oct-25	08-Jan-26
196	PRO2170	Steel Flue Design and Shop Drawings - Preparation and Submission	49	16-Oct-25	03-Dec-25
197	PRO2180	Steel Flue Design and Shop Drawing - Approval	49	21-Nov-25	08-Jan-26
198	**OFFSITE FABRICATION**		146	26-Dec-25	20-May-26
199	PRO2210	Steel Flue - Material Confirmation, Ordering and Delivery	84	26-Dec-25	19-Mar-26
200	PRO2220	Steel Flue - Off-Site Assemble and Fabrication	49	20-Mar-26	07-May-26
201	PRO2230	Steel Flue - Inspection	32	04-Apr-26	06-May-26
202	PRO2240	Steel Flue - Delivery to Site	14	07-May-26	20-May-26
203	**PRECAST UNITS**		643	19-Jun-25	23-Mar-27
204	**MSB PRECAST STAIR**		294	19-Jun-25	08-Apr-26
205	**SHOP DRAWING**		120	19-Jun-25	16-Oct-25
206	PRO1140	Shop Drawings- Preparation	48	19-Jun-25	05-Aug-25

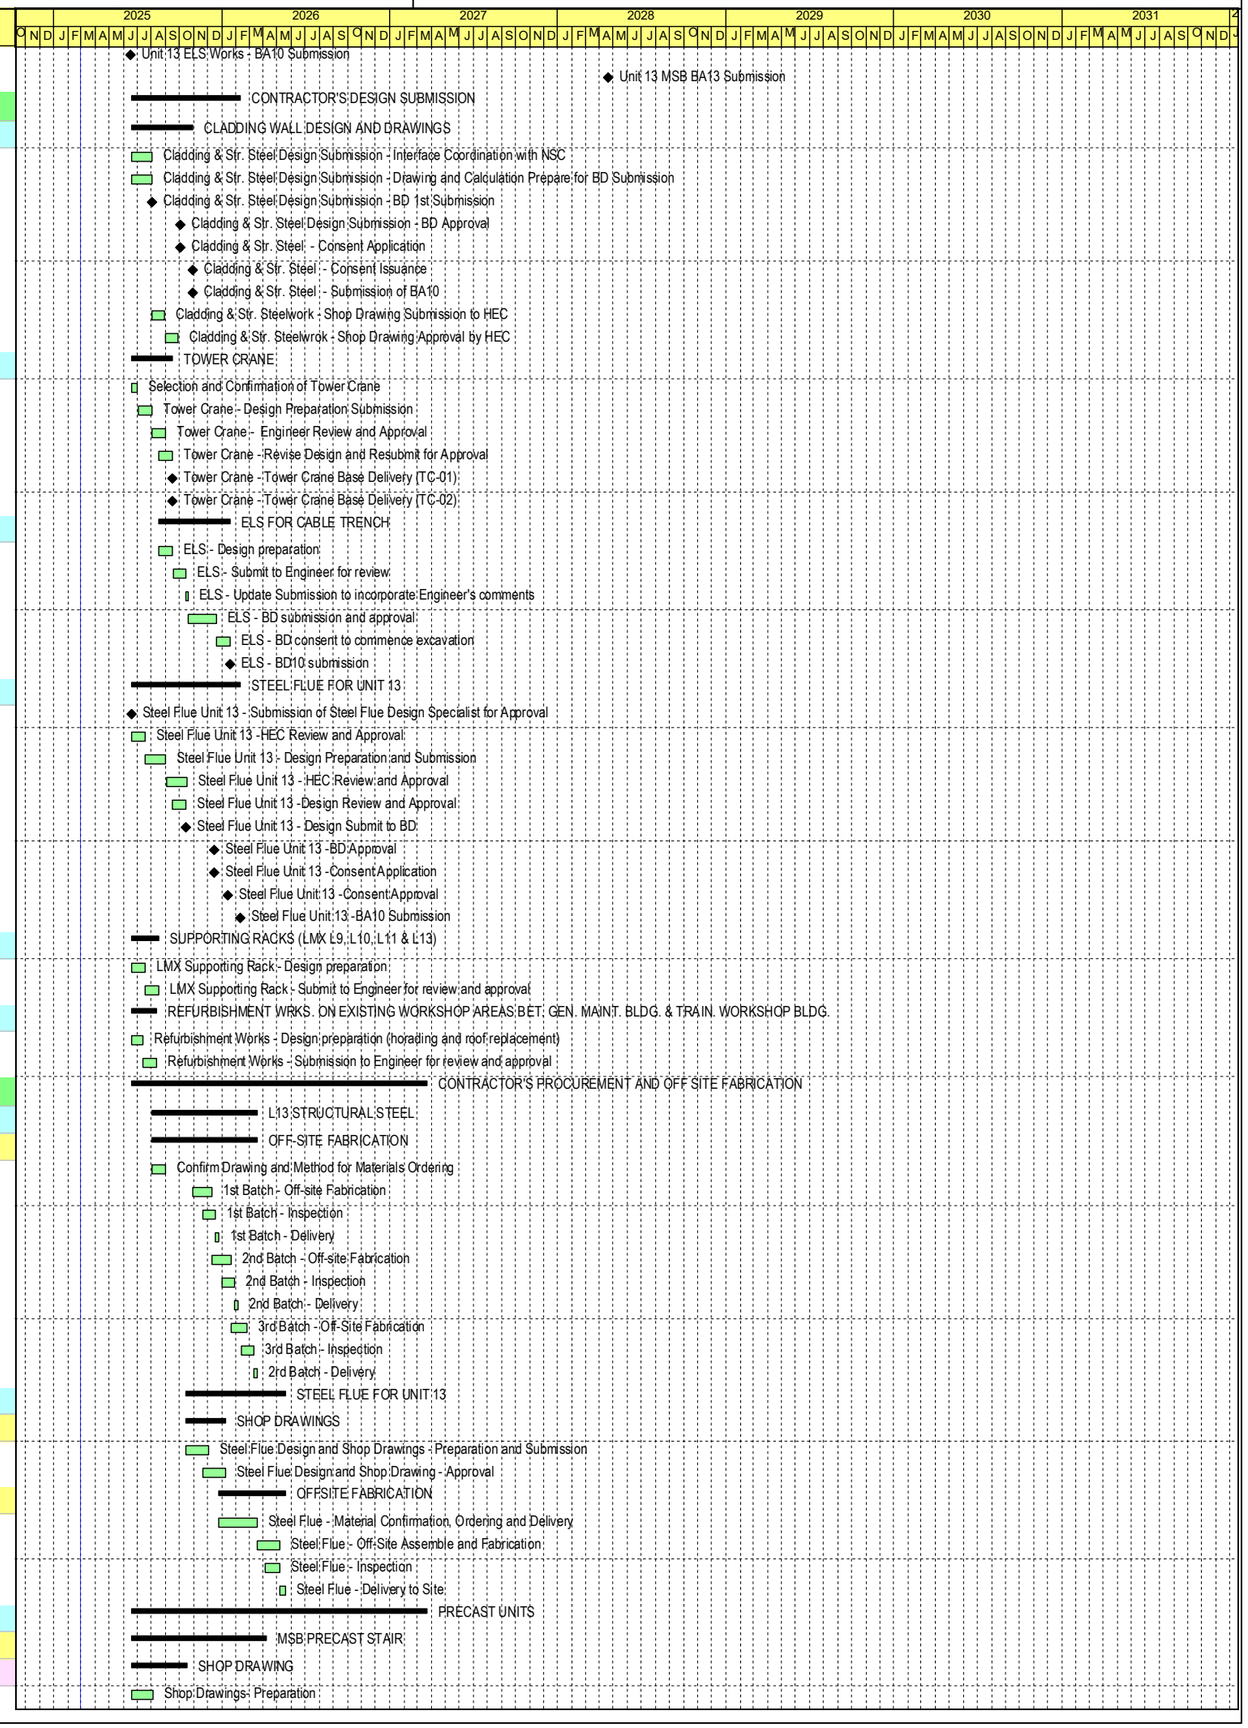

DATA DATE: 01-Mar-25 | LAYOUT: 24-83005 UPDATE | PAGE 4 OF 11

#	Act ID	Activity Name	Duration	Start	Finish
207	PRO1150	Shop Drawings- Submission, Review and RtoC twice	48	06-Aug-25	22-Sep-25
208	PRO1160	Shop Drawings- Approvals	24	23-Sep-25	16-Oct-25
209	**OFF-SITE FABRICATION**		174	17-Oct-25	08-Apr-26
210	PRO1170	Manufacture- Fabrication	48	17-Oct-25	03-Dec-25
211	PRO1180	Manufacture- Inspections	6	04-Dec-25	09-Dec-25
212	PRO1190	Manufacture- Production and delivery	120	10-Dec-25	08-Apr-26
213	**PRECAST R.C. COVER (200mm)**		246	19-Jun-25	19-Feb-26
214	**SHOP DRAWING**		96	19-Jun-25	22-Sep-25
215	PRO2340	Shop Drawings- Preparation	24	19-Jun-25	12-Jul-25
216	PRO2350	Shop Drawings- Submission, Review and RtoC twice	48	13-Jul-25	29-Aug-25
217	PRO2360	Shop Drawings- Approvals	24	30-Aug-25	22-Sep-25
218	**OFF-SITE FABRICATION**		150	23-Sep-25	19-Feb-26
219	PRO2370	Manufacture- Fabrication	48	23-Sep-25	09-Nov-25
220	PRO2380	Manufacture- Inspections	6	10-Nov-25	15-Nov-25
221	PRO2390	Manufacture- Production and delivery	96	16-Nov-25	19-Feb-26
222	**L13 HRSG SERVICE LIFT SHAFT PRECAST WALL PANELS ON STEEL FRAME**		252	15-Jul-26	23-Mar-27
223	**SHOP DRAWING**		112	15-Jul-26	03-Nov-26
224	PRO2080	Shop Drawings - Preparation	72	15-Jul-26*	24-Sep-26
225	PRO2090	Shop Drawings - Submission, Review and RtoC twice	60	12-Aug-26	10-Oct-26
226	PRO2100	Shop Drawings - Approvals	24	11-Oct-26	03-Nov-26
227	**OFF-SITE FABRICATION**		140	04-Nov-26	23-Mar-27
228	PRO2110	Manufacture - Production	140	04-Nov-26	23-Mar-27
229	PRO2120	Manufacture - Inspections	133	11-Nov-26	23-Mar-27
230	PRO2140	Manufacture - Delivery to designated location on site	0		23-Mar-27
231	**SUPPORTING RACKS (LMX L9, L10, L11 & L13)**		336	18-Aug-25	19-Jul-26
232	**SHOP DRAWINGS**		48	18-Aug-25	04-Oct-25
233	PRO2280	Shop Drawings- Preparation	24	18-Aug-25	10-Sep-25
234	PRO2290	Shop Drawings- Submission, Review and Approval	24	11-Sep-25	04-Oct-25
235	**OFF-SITE FABRICATION**		144	26-Feb-26	19-Jul-26
236	PRO2020	Supporting Rack LMX L9 - Fabrication and delivery	36	26-Feb-26	02-Apr-26
237	PRO2250	Supporting Rack LMX L10 - Fabrication and delivery	36	03-Apr-26	08-May-26
238	PRO2260	Supporting Rack LMX L11 - Fabrication and delivery	36	09-May-26	13-Jun-26
239	PRO2270	Supporting Rack LMX L113 - Fabrication and delivery	36	14-Jun-26	19-Jul-26
240	**CONTRACTOR PRELIMINARIES**		1806	19-Jun-25	29-May-30
241	CP1000	Preparation of site layout including hoarding, haul road, office, storage yard and site drainage	24	19-Jun-25	12-Jul-25
242	CP1010	Submission of layout of site set-up for Engineer's Approval	24	13-Jul-25	05-Aug-25
243	CP1020	Implementation of the plan and system	1758	06-Aug-25	29-May-30
244	CP1025	Site Clearing	24	01-Jul-25	24-Jul-25
245	CP1030	Surveys, Instrumnentation (CGM1, NGM, V1a, SP1-SP2, TMa, DW, OW, Long Term Settement Markers) and Monitoring	24	01-Jul-25	24-Jul-25
246	CP1050	Installation of Hoardings, gates and drainage to Work Areas (Dwg No. 554/03/024/2054)	12	19-Jun-25	30-Jun-25
247	CP1060	Installation of temproray site utilities (water, electricity, communication, internet, etc)	12	19-Jun-25	30-Jun-25
248	CP1070	Submission of Safety Plan, EIA submission, Env. Plan, BEP and SHEPP	12	19-Jun-25	30-Jun-25
249	KD1040	Submission of BA10 notifying BD the commencement of the works	7	19-Jun-25	25-Jun-25
250	**CONSTRUCTION**		1918	01-Mar-25	31-May-30
251	**BILL NO.2 - MAIN STATION BUILDING UNIT 13**		1372	19-Jun-25	21-Mar-29
252	**ELS FOR UT13**		168	19-Jun-25	03-Dec-25
253	**STAGE 1a**		24	19-Jun-25	12-Jul-25
254	MB1010	Piling Plant Mobilisation	14	19-Jun-25	02-Jul-25
255	MB1020	Installation of King Post	10	03-Jul-25	12-Jul-25
256	MB1030	Plant Mobilisation and Set Up for Excavation	5	19-Jun-25	23-Jun-25
257	MB1040	Excavation from +7.0mPD to +6.7~6+6.9mPD in HRSG Gas Duct Area	10	24-Jun-25	03-Jul-25
258	MB1050	Excavation from +7.0mPD to +4.0mPD in HRSG, MSB and TX Area	10	24-Jun-25	03-Jul-25
259	MB1060	Excavation from +7.0mPD to +5.2mPD in Zone 4A	10	24-Jun-25	03-Jul-25
260	**STAGE 1b**		48	04-Jul-25	20-Aug-25
261	MB1070	Excavation from 4.0mPD to +3.425mPD & +2.425mPD in Zone 5	7	04-Jul-25	10-Jul-25
262	MB1080	ELS from +6.9mPD to -2.8mPD in Zone 3A	21	13-Jul-25	02-Aug-25
263	MB1090	ELS from 4.0mPD to +1.10mPD in Zone 4	39	13-Jul-25	20-Aug-25
264	**Zone 2**		21	13-Nov-25	03-Dec-25
265	MB1410	Zone 2 - ELS to -3.325mPD	21	13-Nov-25	03-Dec-25
266	**Zone 4 ,Zone 6A and Zone 6**		90	21-Aug-25	18-Nov-25
267	MB1502	Zone 3A - Additional work for ELS Modification	40	21-Aug-25*	29-Sep-25
268	MB1504	Zone 4 - Additional work for ELS Modification	44	21-Aug-25*	03-Oct-25
269	MB1510	Zone 4 - Installation of Remedial Works for ELS Pipe pile Openings at Zone 4	5	29-Sep-25*	03-Oct-25
270	MB1520	Zone 4- Concreting for Additional Blinding Layer due to Raising Level of CW Pipe(middle level from +2.8mPD to +3.05mPD)	1	04-Oct-25	04-Oct-25
271	MB1530	Zone 6A - Excavation of Zone 6A for CW Pipe installation (Stage 1)	6	06-Oct-25	11-Oct-25
272	MB1570	Zone 6A- Excavation of Zone 6A for CW Pipe installation,Breaking of Existing Doghouse and Blinding Laying	7	28-Oct-25	03-Nov-25
273	MB1580	Zone 6A- Excavation of Zone 6A for CW Pipe installation (Stage 2) and Blinding Laying	6	13-Nov-25	18-Nov-25
274	**Zone 5 - Excavation,Pile Head Treatment, Earthing, HRSG RC**		19	02-Oct-25	20-Oct-25
275	MB1702	Zone 5 - Excavation to FEL and Pile Head Treatment between Gridline 13-1 to 13-3	19	02-Oct-25	20-Oct-25

#	Act ID	Activity Name	Duration	Start	Finish
276	MB1710	Excavation for formation & earthing (+3.3mPD) for Gridline 13-H-B to 13-H-E and SPa to 13H4	6	14-Oct-25	19-Oct-25
277	**Plate Load Tests for GRS and HRSG (after Backfill of Zone 4 - Item 1.7)**		10	13-Nov-25	22-Nov-25
278	MB1810	Excavation for formation of 2 NOs. PLTs at GRS & HRSG	5	13-Nov-25	17-Nov-25
279	MB1820	Preparation works for PLTs	2	18-Nov-25	19-Nov-25
280	MB1830	Plate Load Tests for GRS and HRSG	3	20-Nov-25*	22-Nov-25
281	**SUBSTRUCTURE CONSTRUCTION**		181	26-Sep-25	25-Mar-26
282	MB2008	Earthing System Installation	137	26-Sep-25	09-Feb-26
283	MB2010	Tower Crane Base Installation (TC-01)	4	11-Oct-25*	14-Oct-25
284	MB2012	Tower Crane Erection (TC-01)	7	14-Nov-25	20-Nov-25
285	MB2013	Tower Crane Testing (TC-01)	2	21-Nov-25	22-Nov-25
286	MB2022	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 1	28	03-Oct-25*	30-Oct-25
287	MB2024	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 2	14	24-Oct-25	06-Nov-25
288	MB2026	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 3	17	28-Oct-25	13-Nov-25
289	MB2028	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 4	19	31-Oct-25	18-Nov-25
290	MB2030	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 5	17	07-Nov-25	23-Nov-25
291	MB2032	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 6	31	31-Oct-25	30-Nov-25
292	MB2034	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 7	13	21-Nov-25	03-Dec-25
293	MB2036	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 8	21	14-Nov-25	04-Dec-25
294	MB2038	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 9	12	01-Dec-25	12-Dec-25
295	MB2040	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 10	14	05-Dec-25	18-Dec-25
296	MB2042	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion11	12	22-Jan-26	02-Feb-26
297	MB2044	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 12	13	29-Jan-26	10-Feb-26
298	MB2046	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 13	14	14-Dec-25*	27-Dec-25
299	MB2048	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 14	33	13-Dec-25	14-Jan-26
300	MB2050	Pit for Inlet Pipe	10	10-Dec-25*	19-Dec-25
301	MB2052	TDK Inlet Pipe Installation	21	20-Dec-25	09-Jan-26
302	MB2054	Pit for Inlet Pipe Rem	7	10-Jan-26	16-Jan-26
303	MB2056	Pit for Outlet Pipe	10	17-Jan-26	26-Jan-26
304	MB2058	TDK Outlet Pipe	7	27-Jan-26	02-Feb-26
305	MB2059	Pit for Outlet Pipe Rem	7	03-Feb-26	09-Feb-26
306	MB2060	Pile Head Treatment, Const of Pile Cap & Tie Beam Portion 15	14	10-Feb-26	23-Feb-26
307	MB2070	Tower Crane Base Installation (TC-02)	1	05-Nov-25*	05-Nov-25
308	MB2072	Tower Crane Erection (TC-02)	7	28-Nov-25	04-Dec-25
309	MB2074	Tower Crane Testing (TC-02)	2	05-Dec-25	06-Dec-25
310	MB2130	Const of Column, Plinth and Wall at GL13A ~ B / 13-1 ~ 4	17	19-Nov-25	05-Dec-25
311	MB2140	Const of Column, Plinth and Wall at GL13B ~ E / 13-1 ~ 2	17	04-Dec-25	20-Dec-25
312	MB2150	Const of Column, Plinth and Wall at GL13A ~ B / 13-4 ~ 6	17	28-Dec-25	13-Jan-26
313	MB2160	Const of Column, Plinth and Wall at GL13B ~ E / 13-2 ~ 6	14	24-Feb-26	09-Mar-26
314	MB2170	Const of Column, Plinth and Wall at GL13E ~ H / 13-1 ~ 3	35	14-Nov-25	18-Dec-25
315	MB2180	Const of Column, Plinth and Wall at GL13H ~ HB / 13-1 ~ 3	18	01-Dec-25	18-Dec-25
316	MB2190	Const of Column, Plinth and Wall at GL13E ~ H / 13-4 ~ 6	18	13-Dec-25	30-Dec-25
317	MB2191	Const of Column, Plinth and Wall at GL13HB ~ HH / 13-1 ~ 3	18	07-Nov-25	24-Nov-25
318	MB2192	Const of Column, Plinth and Wall at GL13H ~ HE / 13-4 ~ 6	18	11-Feb-26	28-Feb-26
319	MB2200	Const of Column, Plinth and Wall at GL13HC ~ HG / 13-H4 ~ H9	18	24-Nov-25	11-Dec-25
320	MB2230	Const of Ground Beam & On-grade Slab at GL13A ~ B/GL13-1 ~ 4	56	06-Dec-25	30-Jan-26
321	MB2240	Const of Ground Beam & On-grade Slab at GL13B ~ E / 13-1 ~ 2	14	21-Dec-25	03-Jan-26
322	MB2250	Const of Ground Beam & On-grade Slab at GL13A ~ B / 13-4 ~ 6	14	14-Jan-26	27-Jan-26
323	MB2260	Const of Ground Beam & On-grade Slab at GL13B ~ E / 13-2 ~ 6	14	10-Mar-26	23-Mar-26
324	MB2270	Const of Ground Beam & On-grade Slab at GL13E ~ H / 13-1 ~ 3	14	19-Dec-25	01-Jan-26
325	MB2280	Const of Ground Beam & On-grade Slab at GL13H ~ HB / 13-1 ~ 3	21	19-Dec-25	08-Jan-26
326	MB2290	Const of Ground Beam & On-grade Slab at GL13E ~ G / 13-4 ~ 6	21	31-Dec-25	20-Jan-26
327	MB2291	Const of Ground Beam & On-grade Slab at GL13HB ~ HH /13-1 ~ 3	21	25-Nov-25	15-Dec-25
328	MB2292	Const of Ground Beam & On-grade Slab at GL13H ~ HE /13-4 ~ 6	21	01-Mar-26	21-Mar-26
329	MB2300	Const of Ground Beam & On-grade Slab at GL13HC ~ HG /13-H4 ~ H9	28	12-Dec-25	08-Jan-26
330	MB2310	Const of Plumbing and Drainage System within MSB	110	06-Dec-25	25-Mar-26
331	**SUPERSTRUCTURE CONSTRUCTION**		225	04-Jan-26	16-Aug-26
332	MB3010	Erection of Columns & Beams from +7.0mPD to +36.5 mPD at GL13B ~ D / 13-1 ~ 3	14	04-Jan-26	17-Jan-26
333	MB3020	Erection of Columns & Beams from +7.0mPD to +36.5 mPD at GL13D ~ G / 13-1 ~ 3	14	18-Jan-26	31-Jan-26
334	MB3030	Erection of Columns & Beams from +7.0mPD to +36.5mPD at GL13G ~ H / 13-1 ~ 3	14	01-Feb-26	14-Feb-26
335	MB3032	Erection of Columns & Beams from +7.0mPD to +36.5mPD at GL13 H / 13-1 ~ 5	14	15-Feb-26	28-Feb-26
336	MB3040	Erection of Columns & Beams from +7.0mPD to +36.5 mPD at GL13B ~ D / 13-3 ~ 6	10	24-Mar-26	02-Apr-26
337	MB3150	Erection of Columns & Beams from +7.0mPD to +36.5mPD at GL13D ~ H / 13-3 ~ 6	10	03-Apr-26	12-Apr-26
338	MB3155	Erection of Columns & Beams from +7.0mPD to +36.5mPD at GL13G ~ H / 13-3 ~ 6	10	13-Apr-26	22-Apr-26
339	MB3158	Erection of Columns & Beams from +36.5mPD to +52.62mPD	14	23-Apr-26	06-May-26
340	MB3160	Construction of Column Base in HRSG Area	48	09-Jan-26	25-Feb-26
341	MB3182	Erection of Roof Truss	45	24-Mar-26	07-May-26
342	MB3188	Installation of External Cladding & Roof Cladding (Except Temp Opening)	35	24-Apr-26	28-May-26
343	MB3190	Installation of Maintenance Platform at +10.0mPD &+13.0mPD	21	27-Jul-26	16-Aug-26
344	MB3230	Const of Lift Shaft and RC Wall of Staircase ST1 &ST2 from +7.0mPD to +54.5mPD	42	18-Apr-26	29-May-26
345	MB3240	Lift Car Installation, Testing & Commissioning	49	30-May-26	17-Jul-26
346	MB3250	Const of RC Slab at +10.15/+13.0/+19.0/+24.5/+29.4/+34.6/+36.78/+40.3mPD	66	18-Apr-26	22-Jun-26
347	MB3270	Installation of Precast Stairs from +7.0mPD to +54.5mPD	28	09-Apr-26	06-May-26
348	MB3300	Internal &External Finishing, E&M, FS and etc.	87	22-Apr-26	17-Jul-26

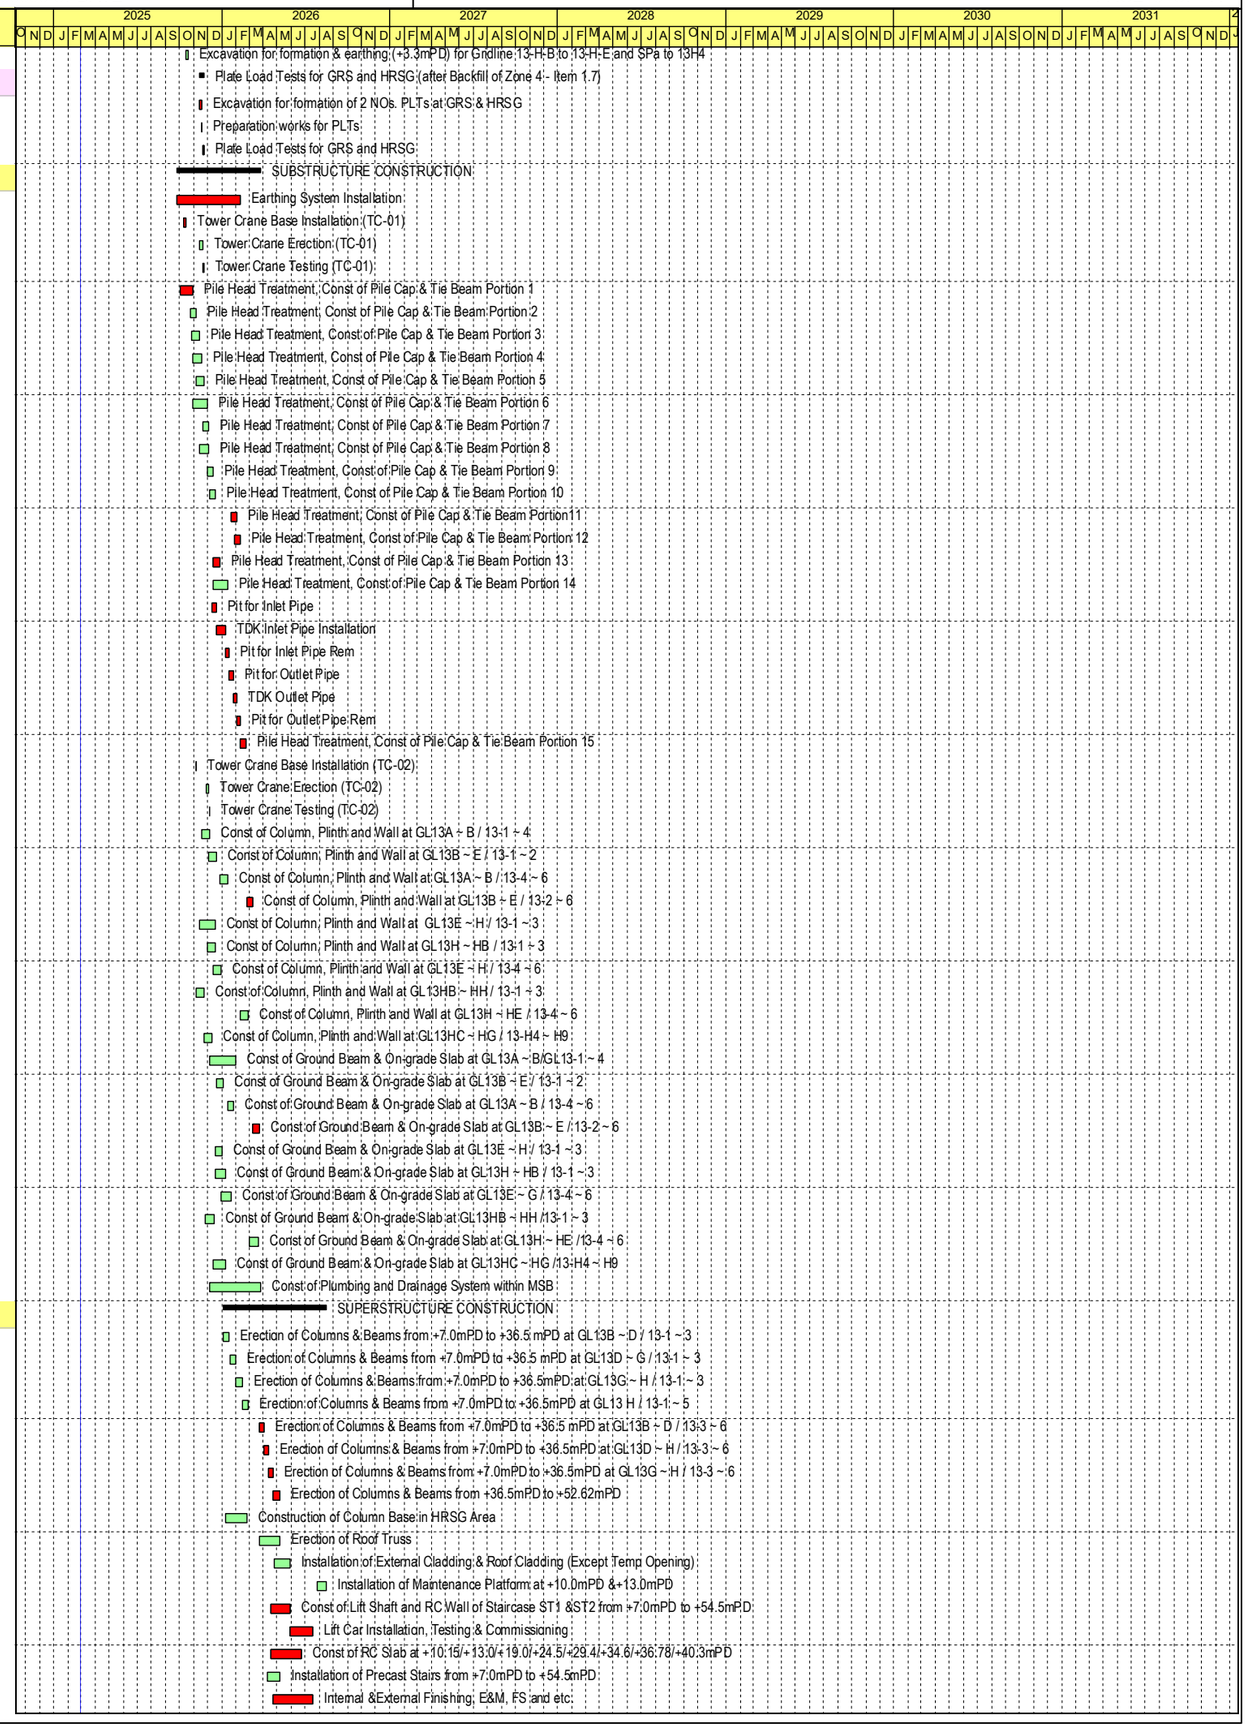

#	Act ID	Activity Name	Duration	Start	Finish
349		**WORK INTERFACE WITH OTHER**	245	19-Jun-26	18-Feb-27
350	MB4130	Template Setting at L13 Turbo Block Foundation	45	20-Jul-26*	02-Sep-26
351	MB4140	Template Setting of Holding Down Bolt at HRSG Column Base	45	19-Jun-26*	02-Aug-26
352	MB4150	Installation of I-Beam/ Channel Base on Tx Fdn at Tx Area	45	20-Nov-26*	03-Jan-27
353	MB4160	Installation of Overhead Crane - Rail Setting	30	20-Jun-26*	19-Jul-26
354	MB4170	Installation of Overhead Crane - Crane Girders	7	20-Jul-26*	26-Jul-26
355	MB4180	Assembly and Erection of Condenser & Access through Temp Facade Opening	153	20-Aug-26*	19-Jan-27
356	MB4190	Installation of Power Train Equipment Including Air Inlet Duct through Temp Facade Opening	122	20-Oct-26*	18-Feb-27
357		**DEFERRED WORKS**	969	27-Jul-26	21-Mar-29
358	DW1000	1 - Construct L13 MSB roof bet GL13-G ~ H and 13-2 ~ 6 after the OH crane installation by the Employer¡¦s SC	38	27-Jul-26*	02-Sep-26
359	DW1010	2 - Construction of walls of L13 MSB below 1/F at GL 13-6 from GL13-B ~ C & ass. precast stair incl. enclosure wall	90	19-Feb-27*	19-May-27
360	DW1020	3 - Construction of internal partition wall at 1/F of L13 MSB along GL 13 -C from GL 13-2 ~ 3	32	12-Mar-27*	12-Apr-27
361	DW1030	4 - Construction of L13 MSB GF slab in corridor as shown in plan 554/03/022/2047	30	20-Nov-26*	19-Dec-26
362	DW1040	5a - Construction of IPB support and sunshade support at transformer area	45	20-Jun-27*	03-Aug-27
363	DW1050	5b - Construction of metal fence and asso F.S. install & install of removable shelter at transformer area	458	20-Dec-27*	21-Mar-29
364	DW1060	6a - Construction of Concrete Plinths for Eqpt and Plants in Southern Parts of L13 HRSG	91	20-May-27*	18-Aug-27
365	DW1070	6b - Completion of East Side Facade Cladding at GL 13-H and GL 13-5 ~ 6	61	20-May-27*	19-Jul-27
366	DW1080	7a - Construction of Roof Slab and its Associated Works on L13 HRSG Lift Shaft after Completion of Erection	30	19-Feb-28*	19-Mar-28
367	DW1090	7b - Construction of Associated Building Service Works (MVAC, FS and Lift Works by NSC)	152	21-Mar-28*	19-Aug-28
368	DW1210	8 - Construction of gas pipe protective barrier and utility platform from +6.85 to +30.12	90	19-Feb-27*	19-May-27
369	DW1220	9i - Final reinst of access rd & pave surrounding and w/in L13 MSB & L13 HRSG area (incl Area G3,G4,G5)	184	15-Oct-27*	15-Apr-28
370		**BILL NO.3 - UNIT 13 HRSG EQUIPMENT ROOM AND ITS ASSOCIATED WORKS**	119	18-Jan-26	16-May-26
371		**SUBSTRUCTURE**	119	18-Jan-26	16-May-26
372	HRSG1000	Formation at +6.025 mPD	14	18-Jan-26*	31-Jan-26
373	HRSG1010	Construction of Foundation F01	14	01-Feb-26	14-Feb-26
374	HRSG1020	Construction of Superstructure	42	15-Feb-26	28-Mar-26
375	HRSG1030	Construction of Roof Plinth and Parapet	14	29-Mar-26	11-Apr-26
376	HRSG1040	Internal Finishing	28	29-Mar-26	25-Apr-26
377	HRSG1050	Raised Floor Installation	21	12-Apr-26	02-May-26
378	HRSG1060	BS installation	35	12-Apr-26	16-May-26
379	HRSG1070	External Finishing	28	12-Apr-26	09-May-26
380	HRSG1080	Roofing System	21	12-Apr-26	02-May-26
381	HRSG1090	Water Testing	14	19-Apr-26	02-May-26
382		**BILL NO.4 - UNIT 13 GAS RECEIVING STATION EQUIPMENT ROOM & GAS RECEIVING STATION**	1070	15-Jan-26	19-Dec-28
383		**Unit 13 GAS Receiving Station Equipment Room**	122	15-Jan-26	16-May-26
384	GRS1000	Excavation to Formation Level	7	15-Jan-26*	21-Jan-26
385	GRS1010	Installation of Earth Grid	14	22-Jan-26	04-Feb-26
386	GRS1015	Plate Load Test (F1)	14	22-Jan-26	04-Feb-26
387	GRS1030	Pad Footing and Substructure Construction Up to +5.57mPD	14	05-Feb-26	18-Feb-26
388	GRS1040	Construction of Superstructure Up to +12.15mPD	35	19-Feb-26	25-Mar-26
389	GRS1050	Construction of Parapet and Dog House	14	26-Mar-26	08-Apr-26
390	GRS1060	Internal Finishing	28	30-Mar-26	26-Apr-26
391	GRS1070	BS Installation	35	12-Apr-26	16-May-26
392	GRS1080	External Finish Including Cat Ladder	27	26-Mar-26	21-Apr-26
393	GRS1090	Roofing System	28	09-Apr-26	06-May-26
394	GRS1100	Water Test	7	16-Apr-26	22-Apr-26
395		**GRS Equipment and Pipe Support**	182	15-Jan-26	15-Jul-26
396	GRS2000	Excavation to Formation level +4.625 mPD / +5.625 mPD	7	15-Jan-26	21-Jan-26
397	GRS2010	Installation of Earthing Grid	35	22-Jan-26	25-Feb-26
398	GRS2020	Plate Load Test (F5 & F19)	14	22-Jan-26	04-Feb-26
399	GRS2040	Foundation Construction to +7.0 mPD	42	26-Feb-26	08-Apr-26
400	GRS2042	Foundation B1 Construction	14	09-Apr-26	22-Apr-26
401	GRS2044	Fenceing Foundation Construction	14	09-Apr-26	22-Apr-26
402	GRS2046	Pipe Cable Support	14	23-Apr-26	06-May-26
403	GRS2048	Fenceing Installation	21	23-Apr-26	13-May-26
404	GRS2050	Equipment Plinth Construction	14	14-May-26	27-May-26
405	GRS2052	Installation of Ladder and Mentenance Plattform for Dry Gas Filter	49	28-May-26	15-Jul-26
406	GRS2060	Backfill to Ground Level	14	21-May-26	03-Jun-26
407	GRS2070	Const of Cable Trench	49	21-May-26	08-Jul-26
408	GRS2100	Drainage Works	35	28-May-26	01-Jul-26
409		**Pipe Rack**	91	29-May-26	27-Aug-26
410	GRS2080	Pipe Rack Foundation	49	29-May-26	16-Jul-26
411	GRS2090	Pipe Rack Installation	28	17-Jul-26	13-Aug-26
412	GRS2110	Railing Installation	14	14-Aug-26	27-Aug-26
413		**DW-Final reinstatement of access roads and pavement for Area G6**	92	19-Sep-28	19-Dec-28
414	DW1230	9ii - Final reinstatement of access roads and pavement for Area G6	92	19-Sep-28*	19-Dec-28
415		**BILL NO.5 - UNIT 13 C.W. CULVERT SYSTEM**	108	06-Oct-25	21-Jan-26
416	CW1000	Zone 4 & 6A -Installation of CW Pipe from A57 to A37 (Stage 1)	22	06-Oct-25	27-Oct-25
417	CW1002	Zone 4 & 6A - Haunching Concreting (with Thrust Block)	10	23-Oct-25	01-Nov-25
418	CW1004	Zone 4 & 6A - Water test for CW Pipe - Stage 1 - Erection, Testing and Removal (from A57 to A37)	8	02-Nov-25	09-Nov-25
419	CW1006	Zone 4 & 6A - Backfilling for Diversion of Site Haul Road (Temporary)	3	10-Nov-25	12-Nov-25

#	Act ID	Activity Name	Duration	Start	Finish
420	CW1010	Zone 3 & 3A - Installation of CW Pipe from A57 to A37	14	02-Nov-25	15-Nov-25
421	CW1012	Zone 3 & 3A - Haunching Concreting (with Thrust Block)	8	09-Nov-25	16-Nov-25
422	CW1014	Zone 3 & 3A - Water test for CW Pipe - Erection, Testing and Removal (from A57 to A37)	8	17-Nov-25	24-Nov-25
423	CW1016	Zone 3 & 3A - Backfilling for Diversion of Site Haul Road (Temporary)	3	25-Nov-25	27-Nov-25
424	CW1020	Zone 6A & 6 - Installation of CW Pipe from A37 to A1 (Stage 2)	20	19-Nov-25	08-Dec-25
425	CW1022	Zone 6A & 6 - Haunching Concreting (with Thrust Block)	10	24-Nov-25	03-Dec-25
426	CW1023	Zone 6A & 6 - M/H - 17 Construction	10	24-Nov-25	03-Dec-25
427	CW1024	Zone 6A & 6 - Water test for CW Pipe - Stage 2 - Erection, Testing and Removal (from A57 to A37)	14	04-Dec-25	17-Dec-25
428	CW1026	Zone 6A & 6 - Backfilling and Removal of Struts & Wailing	35	18-Dec-25	21-Jan-26
429	**BILL NO.6 - CABLE TRENCHES**		1562	20-Feb-26	31-May-30
430	**EXISTING CABLE TRENCH RE-EXCAVATION (EXTERNAL WORKS*)**		627	01-Jan-27	18-Sep-28
431	CT1000	Trench Re-excavation - Trench No. 275-31 (dwg.no. 554/03/024/2081)	60	16-Oct-27*	15-Dec-27
432	CT1010	Trench Re-excavation - Trench No. 275-31 cable laying by Employer" Specialist Contractor (dwg.no. 554/03/024/2081)	90	16-Dec-27	15-Mar-28
433	CT1020	Trench Re-excavation - Trench No. 275-31 backfilling and reinstatement works (dwg.no. 554/03/024/2081) (deferred work)	59	16-Mar-28	15-May-28
434	CT1030	Trench Re-excavation - Trench No. 275-32 (dwg.no. 554/03/024/2081)	56	16-Mar-28*	10-May-28
435	CT1040	Trench Re-excavation - Trench No. 275-32 cable laying by Employer" Specialist Contractor (dwg.no. 554/03/024/2081)	91	12-May-28	10-Aug-28
436	CT1050	Trench Re-excavation - Trench No. 275-32 backfilling and reinstatement works (dwg.no. 554/03/024/2081) (deferred work)	38	12-Aug-28	18-Sep-28
437	CT1060	Trench Re-Excavation - Trench No. 275-28 & -30 along Area G11 (dwg.no. 554/03/024/2080 - 81)	247	01-Jul-27	04-Mar-28
438	CT1070	Trench Re-Excavation - Trench No. 275-18 along Areaa G12 (dwg.no. 554/03/024/2081 - 85)	140	01-Jan-27	20-May-27
439	**NEW CABLE TRENCH (EXTERNAL WORKS*)**		441	20-Feb-26	06-May-27
440	CT1080	New Trench - Construction of cable/pipe trench at Area G1, G1a and G4 (dwg no. 554/03/024/2085)	69	20-Feb-26	29-Apr-26
441	CT1090	New Trench - Construction of cable trench at Area B1A (dwg no. 554/03/024/2086)	96	01-Jan-27	06-Apr-27
442	CT1100	New Trench - Construction of cable trench at Area G7A, G6 and G8 (dwg no. 554/03/024/2085, 87A & 88A)	72	30-Apr-26	10-Jul-26
443	CT1110	New Trench - Construction of cable trench at Area G10 (dwg no. 554/03/024/2088 - 89)	218	01-Oct-26	06-May-27
444	**DEFERRED WORK**		1216	01-Feb-27	31-May-30
445	DW1270	12i - Re-exc existing trenches, construct new trench for cable replace work nearby Shunt Reactor No. 1 (ALC1) at LPS	214	01-Jun-29*	31-Dec-29
446	DW1280	12ii - B/F & rd reinstat of 275kV cable trenches for cable replacement work nearby Shunt Reactor No.1 (ALC1) at LPS	92	01-Mar-30*	31-May-30
447	DW1290	13 - B/F, install trench cover and road-reinstatement of 275kV cable trenches within Area G11 at LMX	92	01-Oct-28*	31-Dec-28
448	DW1300	13 - B/F, install trench cover and road-reinstatement of 275kV cable trenches within Area G12 at LMX	92	01-Nov-27*	31-Jan-28
449	DW1310	14 - Installation of trench cover and road reinstatement of existing trenches within Area G14	58	01-Feb-27*	30-Mar-27
450	**BILL NO.7 - DEMOLITION OF STEEL SHELTER AT UREA PLANT AREA**		317	11-Jan-26	23-Nov-26
451	**BD SUBMISSION**		135	11-Jan-26	25-May-26
452	BD1010	Demolition - Preparation documentation for submission	28	11-Jan-26	07-Feb-26
453	BD1020	Demolition - Submit to Engineer for Review	28	08-Feb-26	07-Mar-26
454	BD1030	Demolition - Updated Submission to Incorporate Engineer's Comments	12	08-Mar-26	19-Mar-26
455	BD1040	Demolition - BD review and consent	60	20-Mar-26	18-May-26
456	BD1050	Demolition - BA10 Submission	7	19-May-26	25-May-26
457	**DEMOLITION WORKS**		182	26-May-26	23-Nov-26
458	DE1050	Demolition - Hoarding erection	28	26-May-26	22-Jun-26
459	DE1060	Demolition - Install temprary steel proping to existing structure	14	23-Jun-26	06-Jul-26
460	DE1070	Demolition - Removal of archiutectural finishes, BS and other non-bearing elements	21	07-Jul-26	27-Jul-26
461	DE1080	Demolition - Demolish shelter in sections by cut and lift method	21	28-Jul-26	17-Aug-26
462	DE1090	Demolition - Demolish steel column, beams and base plate	21	18-Aug-26	07-Sep-26
463	DE1100	Demolition - Open cut excavation from G/F level down to +5.70mPD	14	08-Sep-26	21-Sep-26
464	DE1110	Demolition - Demolish R.C piers and works for ventilating pipe	28	22-Sep-26	19-Oct-26
465	DE1120	Demolition - Backfill up to ground level at +6.00mPD	35	20-Oct-26	23-Nov-26
466	**BILL NO.8 - CIVIL WORKS FOR LMX LIGHT OIL TANK FARM**		262	01-Oct-25	19-Jun-26
467	LO1000	Hoarding Erection	42	01-Oct-25	11-Nov-25
468	LO1020	Const. of Pipe Support Footing	115	12-Nov-25	06-Mar-26
469	LO1030	Removal of Existing Railing and R.C Curb & Installation of New Cat Ladder	3	07-Mar-26	09-Mar-26
470	LO1040	Erection of New Steel Platform	12	10-Mar-26	21-Mar-26
471	LO1060	Breaking/Removal of Road Pavement / Blocks and Excavation along Area G14 (dwg.no. 554/03/024/2080 - 81)	48	22-Mar-26	08-May-26
472	LO1070	Construction of New Trench	24	09-May-26	01-Jun-26
473	LO1080	Hoarding - Removal of Hoarding and Reinstatement Works	18	02-Jun-26	19-Jun-26
474	**BILL NO.9 - UNIT L13 STATION TOILET**		231	04-Jun-26	20-Jan-27
475	ST1010	Unit 13 Station Toilet - Excavation to Formation level (+4.225mPD)	14	04-Jun-26	17-Jun-26
476	ST1020	Unit 13 Station Toilet - Construction of Footing (RF1)	14	18-Jun-26	01-Jul-26
477	ST1022	Unit 13 Station Toilet - Construction of Drainage Underneth On Grade Slab	21	02-Jul-26	22-Jul-26
478	ST1024	Unit 13 Station Toilet - Construction of On Grade Slab	7	23-Jul-26	29-Jul-26
479	ST1030	Unit 13 Station Toilet - Construct of Superstructure Up to +10mPD	21	30-Jul-26	19-Aug-26
480	ST1032	Unit 13 Station Toilet - Construction of Parapet and Dog House	14	20-Aug-26	02-Sep-26
481	ST1050	Unit 13 Station Toilet - Internal Finishing	42	03-Sep-26	14-Oct-26
482	ST1060	Unit 13 Station Toilet - BS Installation	42	15-Oct-26	25-Nov-26
483	ST1070	Unit 13 Station Toilet - External Finishing	28	26-Nov-26	23-Dec-26
484	ST1080	Unit 13 Station Toilet - Waterproofing	28	24-Dec-26	20-Jan-27
485	ST1090	Unit 13 Station Toilet - Water Test	7	07-Jan-27	13-Jan-27
486	**BILL NO.10 - APX CABLE DIVERSION**		881	01-Jul-27	27-Nov-29
487	ACD1000	Removal of planter box, traffic diversion and other prep works	14	01-Jul-27	15-Jul-27
488	ACD1010	APX Cable Diversion (Part 1) - Re-excavate trench between Joint Bays SJ3 and SJ2 (along Stacker Rd.)	30	15-Jul-27	14-Aug-27
489	ACD1020	APX Cable Diversion (Part 1) - Re-excavate trench for APX1 & 3 up to new cable trench along Stacker Rd.	14	14-Aug-27	28-Aug-27
490	ACD1030	APX Cable Diversion (Part 1) - Installation of temporary decking	14	28-Aug-27	11-Sep-27

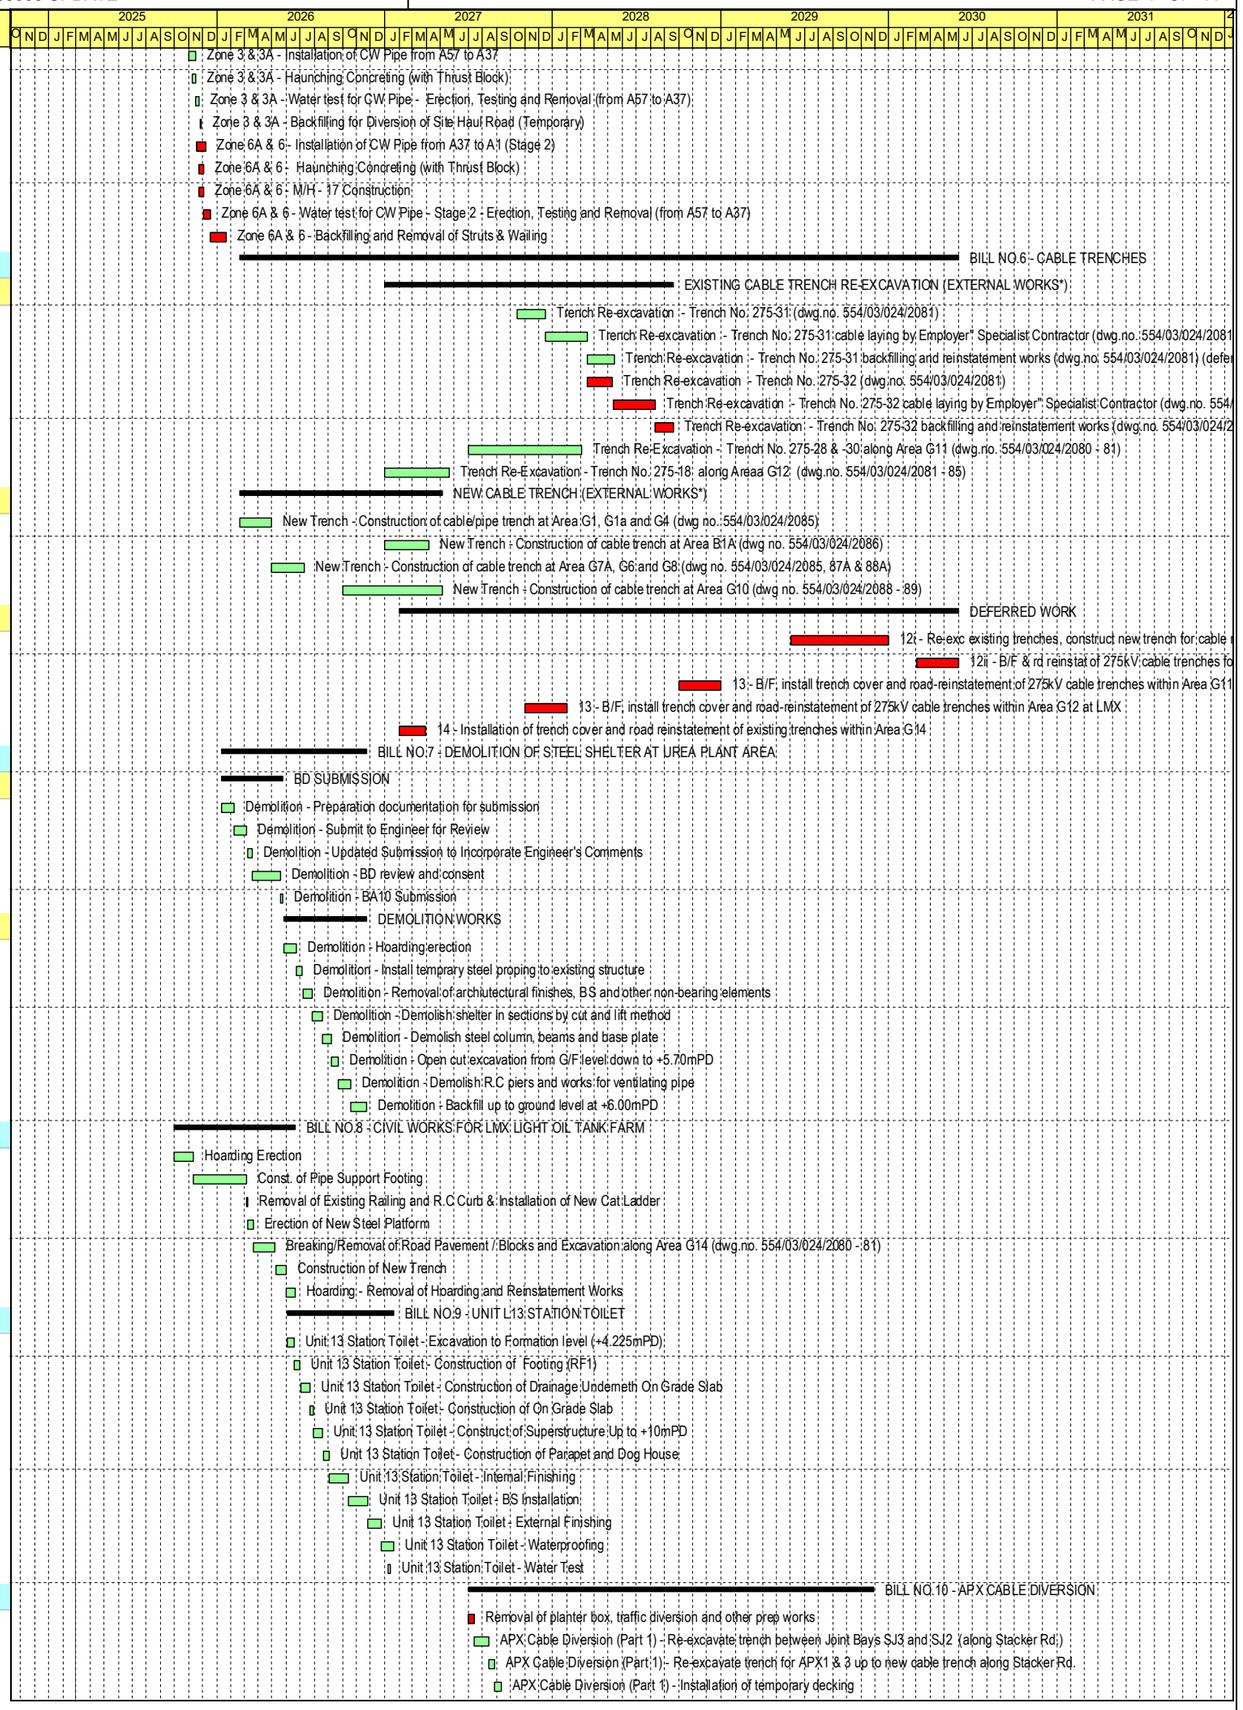

#	Act ID	Activity Name	Duration	Start	Finish
491	ACD1040	TTA Set Up & Close west lane on Coal Yard Road	3	11-Sep-27	14-Sep-27
492	ACD1050	Construct new cable trench and trench crossings along the west lane	48	14-Sep-27	01-Nov-27
493	ACD1060	Install temporary decking to completed cable trench and divert traffic	14	01-Nov-27	15-Nov-27
494	ACD1070	TTA Set Up & Close east lane on Coal Yard Road	0	15-Nov-27	
495	ACD1080	Construct new cable trench adjacent to east lane and 2nos. trench road crossings (remaining section)	48	15-Nov-27	02-Jan-28
496	ACD1090	Install temporary decking to completed cable trench road crossing and open road traffic	14	02-Jan-28	16-Jan-28
497	ACD1100	Excavate and install temporary support to existing cable trough (Section 'B'-'B' of Dwg. 500/03/020/2441)	24	16-Jan-28	09-Feb-28
498	ACD1110	Construct new cable trough (Section 'B'-'B' of Dwg. 500/03/020/2441)	36	09-Feb-28	16-Mar-28
499	**PART 1 (STACKER ROAD TO CONNECTION TO NEW JOINT BAY)**		440	01-Jul-27	13-Sep-28
500	**MAIN ROAD (PART 1)**		151	01-Jul-27	29-Nov-27
501	ACD1120	Constract new cable trench	89	01-Jul-27	28-Sep-27
502	ACD1130	TTA Set Up & Close north lane (west end of Main Rd)	2	28-Sep-27	30-Sep-27
503	ACD1140	Construct new cable trench road crossings along north lane (west end of Main Rd.)	24	30-Sep-27	24-Oct-27
504	ACD1150	Install temporary decking to completed cable trench and divert traffic	6	24-Oct-27	30-Oct-27
505	ACD1160	TTA Set Up & Close south lane (west end of Main Rd)	0	30-Oct-27	
506	ACD1170	Construct new cable trench road crossings (remaining section)	24	30-Oct-27	23-Nov-27
507	ACD1180	Install temporary decking to completed cable trench road crossing and open road to traffic	6	23-Nov-27	29-Nov-27
508	**MACHINE SHOP, WEST STATION ROD, FS/SECURITY BUILDING**		224	15-Jul-27	24-Feb-28
509	ACD1190	Construct new cable trench above/below ground	24	15-Jul-27	08-Aug-27
510	ACD1200	TTA Set Up & Close north lane of Precipitation Rd	2	08-Aug-27	10-Aug-27
511	ACD1210	Construct new cable trench road crossings along north lane of Precipitation Rd	36	10-Aug-27	15-Sep-27
512	ACD1220	Install temporary decking to completed cable trench and divert traffic	6	15-Sep-27	21-Sep-27
513	ACD1230	TTA Set Up & Close south lane of Precipitation Rd	0	21-Sep-27	
514	ACD1240	Construct new cable trench road crossings along south lane of Precipitation Rd	36	21-Sep-27	27-Oct-27
515	ACD1250	Install temporary decking to completed cable trench road crossing and open road to traffic	6	27-Oct-27	02-Nov-27
516	ACD1260	Construct new cable trench	48	02-Nov-27	20-Dec-27
517	ACD1270	Excavate and install temporary support to existing cable trough (Section 'F'-'F' of Dwg. 500/03/020/2442A)	24	20-Dec-27	13-Jan-28
518	ACD1280	Construct new cable trough (Section 'F'-'F' of Dwg. 500/03/020/2442A)	36	13-Jan-28	18-Feb-28
519	ACD1290	Install temporary decking	6	18-Feb-28	24-Feb-28
520	**PART 1 - CABLE LAYING BY ENGINEER'S SPECIALIST CONTRACTOR**		181	16-Mar-28	13-Sep-28
521	ACD1300	APX Cable Diversion (Part 1) - Cable laying by Employer's Specialist Contractor	181	16-Mar-28*	13-Sep-28
522	**PART 2 (NEW JOINT BAY TO WATERFRONT ROAD)**		594	15-Jul-27	28-Feb-29
523	ACD1310	APX Cable Diversion (Part 2) - Construct new Joint Bay adjacent to FS/Security Bldg.	96	15-Jul-27	19-Oct-27
524	**JOINT BAY (SOUTH OF FS SECURITY BUILDING)**		36	19-Oct-27	24-Nov-27
525	ACD1320	Construct new cable trench	36	19-Oct-27	24-Nov-27
526	**TREATMENT PLANT ROAD**		97	24-Nov-27	29-Feb-28
527	ACD1330	TTA Set Up & Close Treatment Plant Road for cable trench construction by tunnelling method	5	24-Nov-27	29-Nov-27
528	ACD1340	Excavate and install temporary support to existing cable/pipe/drainage pipe (Section 'H'-'H' of Dwg. 500/03/020/2443)	48	29-Nov-27	16-Jan-28
529	ACD1350	Installation of duct bank and backfill with mass concrete (Section 'H'-'H' of Dwg. 500/03/020/2443)	24	16-Jan-28	09-Feb-28
530	ACD1360	Backfilling and cast concrte slab (including curing)	18	09-Feb-28	27-Feb-28
531	ACD1370	Open Treatment Plant Road to traffic	2	27-Feb-28	29-Feb-28
532	**AMITY ROAD**		182	15-Jul-27	13-Jan-28
533	ACD1380	Construct new cable trench (including traffic diversion)	90	15-Jul-27	13-Oct-27
534	ACD1390	Excavate and install temporary support to existing utilities (Section 'H1'-'H1' of Dwg. 500/03/020/2443)	48	13-Oct-27	30-Nov-27
535	ACD1400	Installation of duct bank and backfill with mass concrete (Section 'H1'-'H1' of Dwg. 500/03/020/2443)	24	30-Nov-27	24-Dec-27
536	ACD1410	Backfilling and cast concrte slab (including curing)	18	24-Dec-27	11-Jan-28
537	ACD1420	Open Treatment Plant Road to traffic	2	11-Jan-28	13-Jan-28
538	**JUNCTION OF AMITY ROAD AND WEST WHARF ROAD**		110	13-Jan-28	02-May-28
539	ACD1430	TTA Set Up & Close north lane of junction	2	13-Jan-28	15-Jan-28
540	ACD1440	Construct new cable trench road crossings (2nos) along north lane	48	15-Jan-28	03-Mar-28
541	ACD1450	Install temporary decking to completed cable trench and divert traffic	6	03-Mar-28	09-Mar-28
542	ACD1460	TTA Set Up & Close south lane of junction	0	09-Mar-28	
543	ACD1470	Construct new cable trench road crossing	48	09-Mar-28	26-Apr-28
544	ACD1480	Install temporary decking to completed cable trench road crossing and open road to traffic	6	26-Apr-28	02-May-28
545	**WEST WHARF ROAD**		72	20-Apr-28	01-Jul-28
546	ACD1490	APX Cable Diversion (Part 2) - Re-excavate material inside existing preform trench (along West Wharf Rd.)	72	20-Apr-28	01-Jul-28
547	**PART 2 - CABLE LAYING BY ENGINEER'S SPECIALIST CONTRACTOR**		242	01-Jul-28	28-Feb-29
548	ACD1500	APX Cable Diversion (Part 2) - Cable laying by Employer's Specialist Contractor	242	01-Jul-28*	28-Feb-29
549	**WINCH PLATFORM**		127	29-Nov-27	04-Apr-28
550	ACD1510	Winch Platform - Installation of steel platform W1 - W7	35	29-Nov-27	03-Jan-28
551	ACD1520	Winch Platform - Installation of steel platform W8 - W11	35	03-Jan-28	07-Feb-28
552	ACD1530	Winch Platform - Installation of steel platform W12 - W17	35	29-Feb-28	04-Apr-28
553	**DW-install of trench cover and rd reinstate of 275kV cable trenches for APX cable diversion (Part 1)**		164	01-Jul-28	11-Dec-28
554	DW1250	11) B/F, installation of trench cover and rd reinstate of 275kV cable trenches for APX cable diversion at LPS (Part 1)	164	01-Jul-28*	11-Dec-28
555	**DW-install of trench cover and rd reinstate of 275kV cable trenches for APX cable diversion (Part 2)**		272	01-Mar-29	27-Nov-29
556	DW1260	11) B/F, installation of trench cover and rd reinstate of 275kV cable trenches for APX cable diversion at LPS (Part 2)	272	01-Mar-29*	27-Nov-29
557	**BILL NO.11 - ROAD, DRAINAGE, UTILITIES AND EXTERNAL WORKS**		1173	01-Mar-25	16-May-28
558	B11_1000	Road diversion and installation of temporary supports for open cut excavation along Area G4, G5 and G6	24	20-Dec-25*	12-Jan-26
559	B11_5000a10	Fire Hydrant - Construction of plinth and FH box (G6 and G8)	18	13-Jan-26	30-Jan-26
560	B11_7020	Storm Drain - Removal of existing storm drain MH607 - MH625 (G4 & G5)	21	13-Jan-26	02-Feb-26

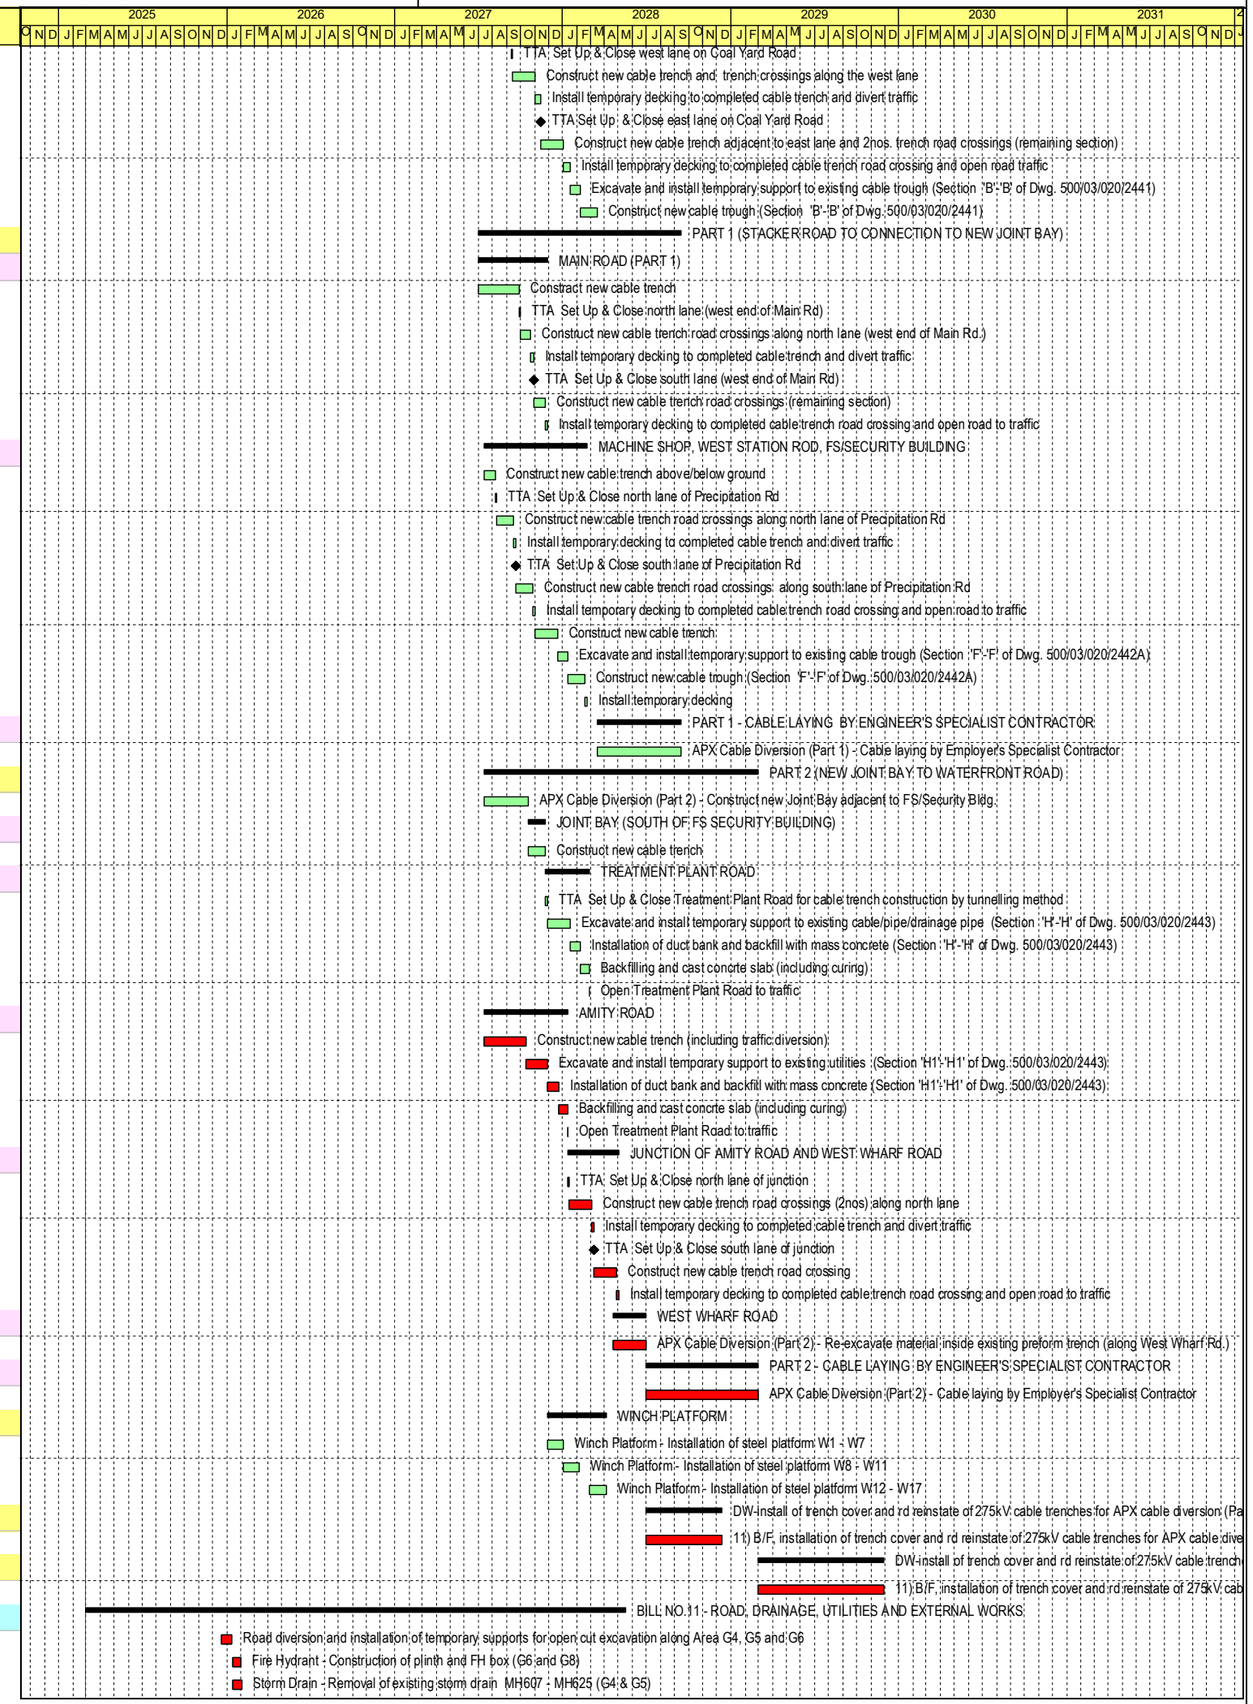

#	Act ID	Activity Name	Duration	Start	Finish
561	B11_7040	Storm Drain - Road gullies and pipe works (G4 , G5 & G6)	18	03-Feb-26	20-Feb-26
562	B11_7050	Storm Drain - Construct drainage manhole (G5 ,G6 & G8)	20	03-Feb-26	22-Feb-26
563	B11_7060	Sewage Drain - Removal of existing sewage drain SM218 to SM219 (G4)	7	23-Feb-26	01-Mar-26
564	B11_7070	Sewage Drain - Reconstruction of sewage drain SM218 to SM219 (G4)	14	16-Feb-26	01-Mar-26
565	B11_7075	Catchpit - Construct CP-22 and u-channel (G6)	14	02-Mar-26	15-Mar-26
566	B11_7090	Sewage Drain - Construct pipe works connecting (G4 & G5)	16	16-Mar-26	31-Mar-26
567	B11_7100	Catchpit - Construct CP-21 to CP-20 inlcuding u-channels (G7B & G8)	14	23-Mar-26	05-Apr-26
568	B11_7110	Catchpit - Construct 150 u-channel with grating from GRS Stream L13 to CP-21(G7B)	14	30-Mar-26	12-Apr-26
569	B11_7130	Catchpit - Construct CP-05A with 300dia drain pipe to MH617 (G5)	14	06-Apr-26	19-Apr-26
570	B11_7140	Drawpit - Construct drawpits and cable ducts from U13 MSB to U12 MSB (Dwg No. 554/03/024/2090)	24	13-Jan-26	05-Feb-26
571	B11_7150	Drawpit - Construct drawpits along Area G4	14	13-Jan-26	26-Jan-26
572	B11_7160	Drawpit - Construct drawpits along Area G5	14	20-Jan-26	02-Feb-26
573	B11_7170	Drawpit - Construct drawpits along Area G5 & G8	14	03-Feb-26	16-Feb-26
574	B11_7180	Drawpit - Construct drawpits along Area G7A & G7B	14	17-Feb-26	02-Mar-26
575	B11_7190	Drawpit - Construct drawpits along Area G7	14	03-Mar-26	16-Mar-26
576	B11_7200	Drawpit - Construct drawpits along Area G16A	14	17-Mar-26	30-Mar-26
577	B11_7210	Street Light - Construct concrete footings (kerbs and blocks) (as per dwg. no. 554/03/024/2050 and /2072) (G4)	21	13-Jan-26	02-Feb-26
578	B11_7220	Street Light - Construct concrete footings (kerbs and blocks) (as per dwg. no. 554/03/024/2050 and /2072) (G5)	21	13-Jan-26	02-Feb-26
579	B11_7230	Street Light - Construct concrete footings (kerbs and blocks) (as per dwg. no. 554/03/024/2050 and /2072) (G6 and G8)	21	17-Feb-26	09-Mar-26
580	B11_7240	Street Light - Construct concrete footings (kerbs and blocks) (as per dwg. no. 554/03/024/2050 and /2072) (G8)	21	10-Mar-26	30-Mar-26
581	B11_7250	Fire Hydrant - Construction of plinth and FH box (G5)	18	03-Feb-26	20-Feb-26
582	B11_7260	FS pipe installation (including FS valve pits) and associated cable conduits	36	03-Feb-26	10-Mar-26
583	B11_7310	Lean Concrete - 100mm concrete pavement (B1, B2, D2, D8, G8 and D7)	48	28-Feb-26	16-Apr-26
584	B11_7320	Concrete Slab - 200mm concrete slab (GRS) (G7A and G7B)	1173	01-Mar-25	16-May-28
585	**BILL NO.12 - MODIFICATION WORK TO EXISTING 275 KV SWITCHING STATION (PHASE II)**		233	01-Oct-25	21-May-26
586	**NEW SUPPPORTING RACK**		142	01-Oct-25	19-Feb-26
587	SS1000	275KV SS Modification - Form opening to existing raised floor inside RTU / ICP Room (9A-9B, 17A-17D)	30	01-Oct-25	30-Oct-25
588	SS1010	275KV SS Modification - Form opening to existing raised floor inside Cable Alarm Room (9A-9B, 27A-27D)	28	31-Oct-25	27-Nov-25
589	SS1020	275KV SS Modification - Form opening to existing raised floor inside 275k-V Switching Control Room	14	28-Nov-25	11-Dec-25
590	SS1030	275KV SS Modification - Installation of new supporting racks inside RYU / ICP Room	28	12-Dec-25	08-Jan-26
591	SS1040	275KV SS Modification - Installation of new supporting racks inside Cable Alarm Room	21	09-Jan-26	29-Jan-26
592	SS1050	275KV SS Modification - Installation of new supporting racks inside 275k-V Switching Control Room	21	30-Jan-26	19-Feb-26
593	**CABLE LADDER**		91	20-Feb-26	21-May-26
594	SS1060	Cable Ladder - Erection of working platform (scaffoldongs) (ground to +24.41mPD)	21	20-Feb-26	12-Mar-26
595	SS1070	Cable Ladder - Installation of ladder brackets (support Type S1)	28	13-Mar-26	09-Apr-26
596	SS1080	Cable Ladder - Installation of cable ladder (Unistrut)	42	10-Apr-26	21-May-26
597	**BILL NO.13 - MODIFICATION WORK TO EXISTING SHUNT REACTOR COMPOUND EXTENSION**		527	01-May-27	09-Oct-28
598	**SHUNT REACTOR BAY 7**		141	01-May-27	18-Sep-27
599	SR1000	Shunt Reactor Compound Bay 7 - Clearing site and take down existing 2500mm high wire mesh fence and gate (G17A)	12	01-May-27	12-May-27
600	SR1010	Shunt Reactor Compound Bay 7 - Remove existing concrete fill from R.C. platform	36	13-May-27	17-Jun-27
601	SR1020	Shunt Reactor Compound Bay 7 - Construct new R.C slab with pocket, embeded plat and steel frame	72	18-Jun-27	28-Aug-27
602	SR1030	Shunt Reactor Compound Bay 7 - Handover and move-in by Engineer's Speciallist Contractor	0	09-Jul-27	
603	SR1040	Shunt Reactor Compound Bay 7 - Receiver working area from Engineer's Specialist Contractor	0		29-Jul-27
604	SR1050	Shunt Reactor Compound Bay 7 - Reinstate wire mesh fence and gate	21	29-Aug-27	18-Sep-27
605	**SHUNT REACTOR BAY 8**		141	29-Aug-27	16-Jan-28
606	SR1060	Shunt Reactor Compound Bay 8 - Clearing site and take down existing 2500mm high wire mesh fence and gate (G17B)	12	29-Aug-27	09-Sep-27
607	SR1070	Shunt Reactor Compound Bay 8 - Remove existing concrete fill from R.C. platform	36	10-Sep-27	15-Oct-27
608	SR1080	Shunt Reactor Compound Bay 8 - Construct new R.C slab with pocket, embeded plate and steel frame	72	16-Oct-27	26-Dec-27
609	SR1090	Shunt Reactor Compound Bay 8 - Handover and move-in by Engineer's Speciallist Contractor	0	13-Nov-27	
610	SR1100	Shunt Reactor Compound Bay 8 - Receiver working are from Engineer's Specialist Contractor	0		10-Dec-27
611	SR1110	Shunt Reactor Compound Bay 8 - Reinstate wire mesh fence and gate	21	27-Dec-27	16-Jan-28
612	**DW-B/F, install trench cover & rd reinstt of 275kV cable trenches link bet Shunt Reactor Bay 7**		53	16-Mar-28	08-May-28
613	DW1240	10) B/F, install trench cover & rd reinstt of 275kV cable trenches link bet Shunt Reactor Bay 7 LMX 275kV SS LMX	53	16-Mar-28*	08-May-28
614	**DW-B/F, install trench cover & rd reinstt of 275kV cable trenches link bet Shunt Reactor Bay 8**		54	16-Aug-28	09-Oct-28
615	DW1245	10) B/F, install trench cover & rd reinstt of 275kV cable trenches link bet Shunt Reactor Bay 8 LMX 275kV SS LMX	54	16-Aug-28*	09-Oct-28
616	**BILL NO.14 - MODIFICATION WORKS TO EXISTING NO. 5 CHIMNEY**		301	18-May-26	14-Mar-27
617	CH1000	Remove Existing Door & Erection of Safety Barrier/ Protective Barrier	21	18-May-26	08-Jun-26
618	CH1010	Install steel track trolley directly below the steel flue with entry from the Ground Gate	21	08-Jun-26	29-Jun-26
619	CH1020	Removal of metal roof cover and installation of heavy duty lifting system (strand jack)	25	22-Jun-26	17-Jul-26
620	CH1040	Erect temporary working platform for Liner Can alignment and anti-corrosion painting	28	11-Jul-26	08-Aug-26
621	CH1050	Set Up Strand Jack	28	02-Aug-26	30-Aug-26
622	CH1060	Lifting and installation of Can No. 1 to No. 21C	122	30-Aug-26*	30-Dec-26
623	CH1070	Installation of lateral restraint of steel flue	25	30-Dec-26	24-Jan-27
624	CH1080	Removal of existing metal cover of Entry Duct	6	24-Jan-27	30-Jan-27
625	CH1090	Installation of Entry Duct (Can No. 22A - 22D)	6	30-Jan-27	05-Feb-27
626	CH1100	Installation of insulation and external protective cladding	25	30-Jan-27	24-Feb-27
627	CH1110	Installation of maintenance and access paltforms with doors at the bottom of steel flue	25	18-Feb-27	14-Mar-27
628	**BILL NO.15 - MODIFICATION WORK TO EXISTING L11 C.W. CULVERT PIPE**		84	01-Sep-25	23-Nov-25
629	**L11 INSPECTION MANHOLE FOR C.W. INLET PIPE**		84	01-Sep-25	23-Nov-25
630	CC1000	Accestance of site (L11 ST-2) and clearing away any item and fencing the site prior to commencing the works	6	01-Sep-25	06-Sep-25
631	CC1010	Reinstatement of opened slab and temporary seal up the floor opening for the proposed manhole cover for BD inspection	12	07-Sep-25	18-Sep-25

#	Act ID	Activity Name	Duration	Start	Finish
632	CC1020	Arrange BD inspection	24	19-Sep-25	12-Oct-25
633	CC1030	Removal of concrete cover, excavation and contruction of new manhole (blocks and steel) with permanent CI manhole cover	36	13-Oct-25	17-Nov-25
634	CC1040	Clearing site after construction	6	18-Nov-25	23-Nov-25
635	**BILL NO.16 - MODIFICATION WORK TO EXISTING NO. 5 C.W. INTAKE AND C.W. PUMP EQUIPMENT ROOM NO. 5**		318	15-Jul-25	29-May-26
636	CWP1000	Equipment Room - Removal of mass fill concrete panels	10	15-Jul-25	24-Jul-25
637	CWP1010	Discharge Valve Chamber - Construction of plinths for L13 pipes/valves	36	25-Jul-25	29-Aug-25
638	CWP1020	Discharge Valve Chamber - Removal of existing block wall	14	30-Aug-25	12-Sep-25
639	CWP1030	Discharge Valve Chamber - installation of puddle pipe (by Others)	28	13-Sep-25	10-Oct-25
640	CWP1040	Discharge Valve Chamber - Seal up wall opening by concrete	14	11-Oct-25	24-Oct-25
641	CWP1050	Discharge Valve Chamber - Installation of GRP ladder and modification of existing GRP railing and security wire mesh	18	25-Oct-25	11-Nov-25
642	CWP1060	Discharge Valve Chamber - Laying cement sand screeding	14	12-Nov-25	25-Nov-25
643	CWP1070	Pump Chamber - Removal of existing precast cover and installation of GMS railing	28	26-Nov-25	23-Dec-25
644	CWP1080	Pump Chamber - Removal of cement sand seal up material inside existing pocket holes	10	24-Dec-25	02-Jan-26
645	CWP1090	Pump Chamber - Make good of fall surface of existing concrete topping by grinding to achieve fall requirment	10	03-Jan-26	12-Jan-26
646	CWP1100	Mesh Screen Chamber - Removal of precast cover and disposal	14	13-Jan-26	26-Jan-26
647	CWP1110	Mesh Screen Chamber - Breaking non-struct conc. topping for conduits installation then reinatate trench cover/topping	28	27-Jan-26	23-Feb-26
648	CWP1120	Mesh Screen Chamber - Installation of GRP ladder with safety loops, railing with security wire mesh and GRP grating	18	24-Feb-26	13-Mar-26
649	CWP1130	Mesh Screen Chamber - Removal of cement sand seal up material inside existing opening and pocket holes	6	14-Mar-26	19-Mar-26
650	CWP1140	Mesh Screen Chamber - Unplug existing drain pipe towards existing L13 chamber	6	20-Mar-26	25-Mar-26
651	CWP1150	Mesh Screen Chamber - Installation of permanent isolation valve to existing trash basket pit and trash pit	6	26-Mar-26	31-Mar-26
652	CWP1160	Bar Screen & Penstock Chamber - Removal of precast cover	12	30-Aug-25	10-Sep-25
653	CWP1170	Bar Screen & Penstock Chamber - Installation of L13 Bar Screen SS Channel	28	11-Sep-25	08-Oct-25
654	CWP1180	Bar Screen & Penstock Chamber - Break up 200mm non-struct conc. topping and install dowel bars at L13 penstock support	28	09-Oct-25	05-Nov-25
655	CWP1190	Bar Screen & Penstock Chamber - Install GRP ladder with safety loops and GMS grating	28	06-Nov-25	03-Dec-25
656	CWP1200	Bar Screen & Penstock Chamber - Modify existing plinth for penstock install. & seal up gap bet. stop gate/intake (dw)	35	04-Dec-25*	07-Jan-26
657	CWP1210	Bar Screen & Penstock Chamber - Concrete scrabbling to form recess for grating cover installation	14	08-Jan-26	21-Jan-26
658	CWP1220	Intake Culvert - Remove and disposal of temporary watergate and steel end plate	28	22-Jan-26	18-Feb-26
659	CWP1230	Intake Culvert - Diving inspection and desilting	28	19-Feb-26	18-Mar-26
660	CWP1240	Intake Culvert - Installation of chlorination pipes	14	19-Mar-26	01-Apr-26
661	**DW-Construction of concrete plinth for penstock within L13 Penstock Chamber inside No.5 C.W. Intake**		28	01-May-26	29-May-26
662	DW1320	15) Construction of concrete plinth for penstock within L13 Penstock Chamber inside No.5 C.W. Intake	28	01-May-26*	29-May-26
663	**BILL NO.17 - MODIFICATION WORK TO EXISTING LMX ADMINISTRATION AND CONTROL BUILDING**		771	01-Apr-25	11-May-27
664	LACB1000	LMX L9 - Form opening to existing raised floor & Installation of supporting rack	36	03-Apr-26	08-May-26
665	LACB1010	LMX L10 - Form opening to existing raised floor & Installation of supporting rack	36	01-Mar-27*	05-Apr-27
666	LACB1020	LMX L11 - Form opening to existing raised floor & Installation of supporting rack	36	06-Apr-27	11-May-27
667	LACB1030	LMX L13 - Installation of supporting rack	36	20-Jul-26*	24-Aug-26
668	LACB1040	ACB modification works at Area G19 as shown in drawing no. 554/03/024/2040 (Except works in drawing no. 554/03/033/2000)	149	01-Apr-25*	27-Aug-25
669	**BILL NO.18 - REFURB. WRKS. ON EXISTING WORKSHOP AREAS BET. GEN. MAINT. BLDG & TRAIN. WORKSHOP BLDG.**		184	02-Jun-25	02-Dec-25
670	**WATER TANK REMEDIAL WORKS**		53	26-Jun-25	17-Aug-25
671	RW1000	Water Tank - Hack off existing internal finishes including existing waterproofing layer to sound concrete substrate	12	26-Jun-25	07-Jul-25
672	RW1010	Water Tank - Sealing of visible cracks with repair mortar	8	08-Jul-25	15-Jul-25
673	RW1020	Water Tank - Apply Optimix BP126 Plaster" to floor, walls and ceiling soffit	6	16-Jul-25	21-Jul-25
674	RW1030	Water Tank - Apply waterproofing	10	22-Jul-25	31-Jul-25
675	RW1040	Water Tank - Carry out water test	5	01-Aug-25	05-Aug-25
676	RW1050	Water Tank - Install tiles to floor, walls and ceiling soffit	12	06-Aug-25	17-Aug-25
677	**REPLACEMENT OF EXISTING METAL ROOF SYSTEM**		184	02-Jun-25	02-Dec-25
678	RW1100	Metal Roof - Design Prepration	28	02-Jun-25	29-Jun-25
679	RW1110	Metal Roof - BD Submission & Approval	60	30-Jun-25	28-Aug-25
680	RW1120	Metal Roof - BD Consent Application	30	29-Aug-25	27-Sep-25
681	RW1130	Metal Roof - BA10 Submission	7	28-Sep-25	04-Oct-25
682	RW1150	Metal Roof - Erection corrogated metal hoarding	14	28-Sep-25	11-Oct-25
683	RW1160	Metal Roof - Removal of existing roofing system	14	11-Oct-25	25-Oct-25
684	RW1170	Metal Roof - Temporary removal of affected electrical installation, FS installation and mech ventilation installations	14	11-Oct-25	25-Oct-25
685	RW1180	Metal Roof - Installation of new roofing system including skylight, capping, gutters and and rain water outlet,	28	15-Oct-25	12-Nov-25
686	RW1190	Metal Roof - Installation of fall arrest system and 150dia epoxy coated CI pilpes	14	12-Nov-25	25-Nov-25
687	RW1200	Metal Roof - Install repalcement of damaged fire rated ceiling	14	12-Nov-25	25-Nov-25
688	RW1210	Metal Roof - Repaint the entire fire ated ceiling with polyurethane coating	7	26-Nov-25	02-Dec-25
689	**BILL NO.18A - A&A WORKS AT DG STORE**		97	26-Jun-25	01-Oct-25
690	DG1000	DG Store - Notification to commence A&A works	14	26-Jun-25	09-Jul-25
691	DG1010	DG Store - Construct new 560(H) R.C curb at the entrance and louver areas of DG Store "A" incl. painting to wall/floor	8	09-Jul-25	17-Jul-25
692	DG1020	DG Store - Construct temp. fire rated enclosure for new partition wall opening at DG Store "A"	14	17-Jul-25	30-Jul-25
693	DG1030	DG Store - Re-locate all ammonium hydroxide at existing DG Store "D" to DG Stare "A" (with prior approval from FSD)	8	30-Jul-25	07-Aug-25
694	DG1040	DG Store - Construct R.C. ramp, srtaircase, railings and curbs at DG Store "D"	24	07-Aug-25	31-Aug-25
695	DG1050	DG Store - Painting works to wall and floors (RUSTOLEUM 9100)	11	31-Aug-25	11-Sep-25
696	DG1060	DG Store - Statutory Inspection	14	12-Sep-25	25-Sep-25
697	DG1070	DG Store - Restore all Ammonium Hydroxide to DG Store "D" from DG Store "A"	6	25-Sep-25	01-Oct-25
698	**BILL NO.18B - EMERGENCY SHOWER AT L10 & L11 MSB**		138	01-Sep-25	16-Jan-26
699	ES1000	L10 Shower - Break existing on-grade slab and excavation	14	01-Sep-25	14-Sep-25
700	ES1010	L10 Shower - Construct RC emrgency shower pit including 300mmx300mm D trench	28	15-Sep-25	12-Oct-25
701	ES1020	L10 Shower - Backfill and reintate on-grade slab	21	13-Oct-25	02-Nov-25
702	ES1030	L10 Shower - Installation of unheated emergency safety shower set incl. plumbings	14	03-Nov-25	16-Nov-25
703	ES1040	L11 Shower - Break existing on-grade slab and excavation	14	01-Nov-25	14-Nov-25

DATA DATE: 01-Mar-25 | LAYOUT: 24-83005 UPDATE | PAGE 11 OF 11
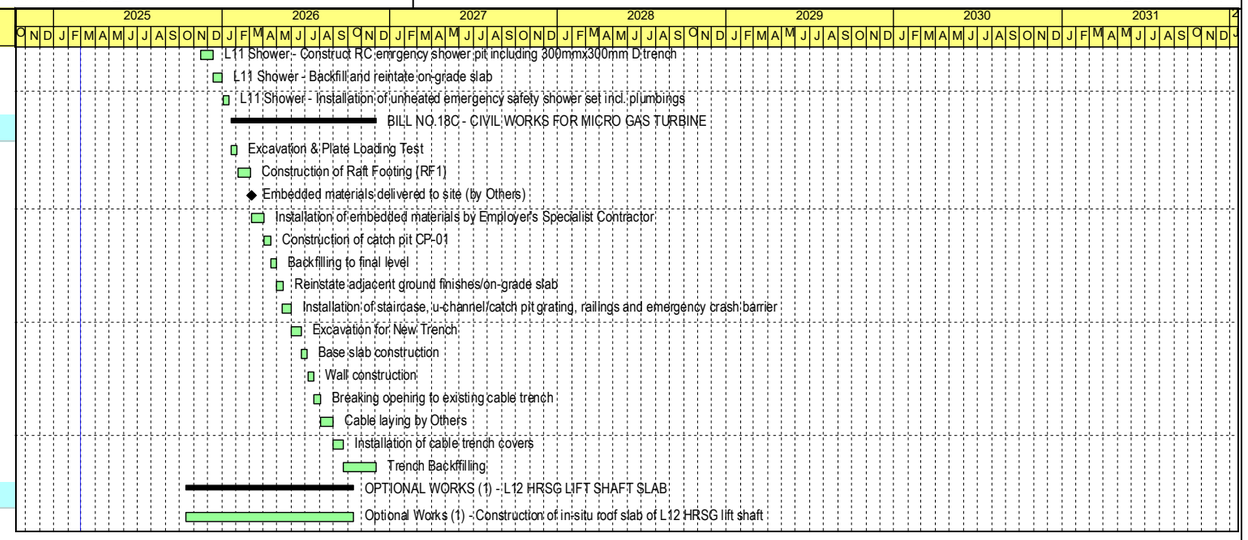
#	Act ID	Activity Name	Duration	Start	Finish
704	ES1050	L11 Shower - Construct RC emrgency shower pit including 300mmx300mm D trench	28	15-Nov-25	12-Dec-25
705	ES1060	L11 Shower - Backfill and reintate on-grade slab	21	13-Dec-25	02-Jan-26
706	ES1070	L11 Shower - Installation of unheated emergency safety shower set incl. plumbings	14	03-Jan-26	16-Jan-26
707	**BILL NO.18C - CIVIL WORKS FOR MICRO GAS TURBINE**		316	21-Jan-26	02-Dec-26
708	MGT1000	Excavation & Plate Loading Test	14	21-Jan-26	03-Feb-26
709	MGT1010	Construction of Raft Footing (RF1)	28	04-Feb-26	03-Mar-26
710	MGT1020	Embedded materials delivered to site (by Others)	0		06-Mar-26*
711	MGT1030	Installation of embedded materials by Employer's Specialist Contractor	28	06-Mar-26	02-Apr-26
712	MGT1040	Construction of catch pit CP-01	14	03-Apr-26	16-Apr-26
713	MGT1050	Backfilling to final level	14	17-Apr-26	30-Apr-26
714	MGT1060	Reinstate adjacent ground finishes/on-grade slab	14	01-May-26	14-May-26
715	MGT1070	Installation of staircase, u-channel/catch pit grating, railings and emergency crash barrier	21	12-May-26	01-Jun-26
716	MGT1080	Excavation for New Trench	21	02-Jun-26	22-Jun-26
717	MGT1090	Base slab construction	14	23-Jun-26	06-Jul-26
718	MGT1100	Wall construction	14	07-Jul-26	20-Jul-26
719	MGT1110	Breaking opening to existing cable trench	14	21-Jul-26	03-Aug-26
720	MGT1120	Cable laying by Others	28	04-Aug-26	31-Aug-26
721	MGT1130	Installation of cable trench covers	21	01-Sep-26	21-Sep-26
722	MGT1140	Trench Backfilling	72	22-Sep-26	02-Dec-26
723	**OPTIONAL WORKS (1) - L12 HRSG LIFT SHAFT SLAB**		365	15-Oct-25	14-Oct-26
724	OPW1_1000	Optional Works (1) - Construction of in-situ roof slab of L12 HRSG lift shaft	365	15-Oct-25*	14-Oct-26
